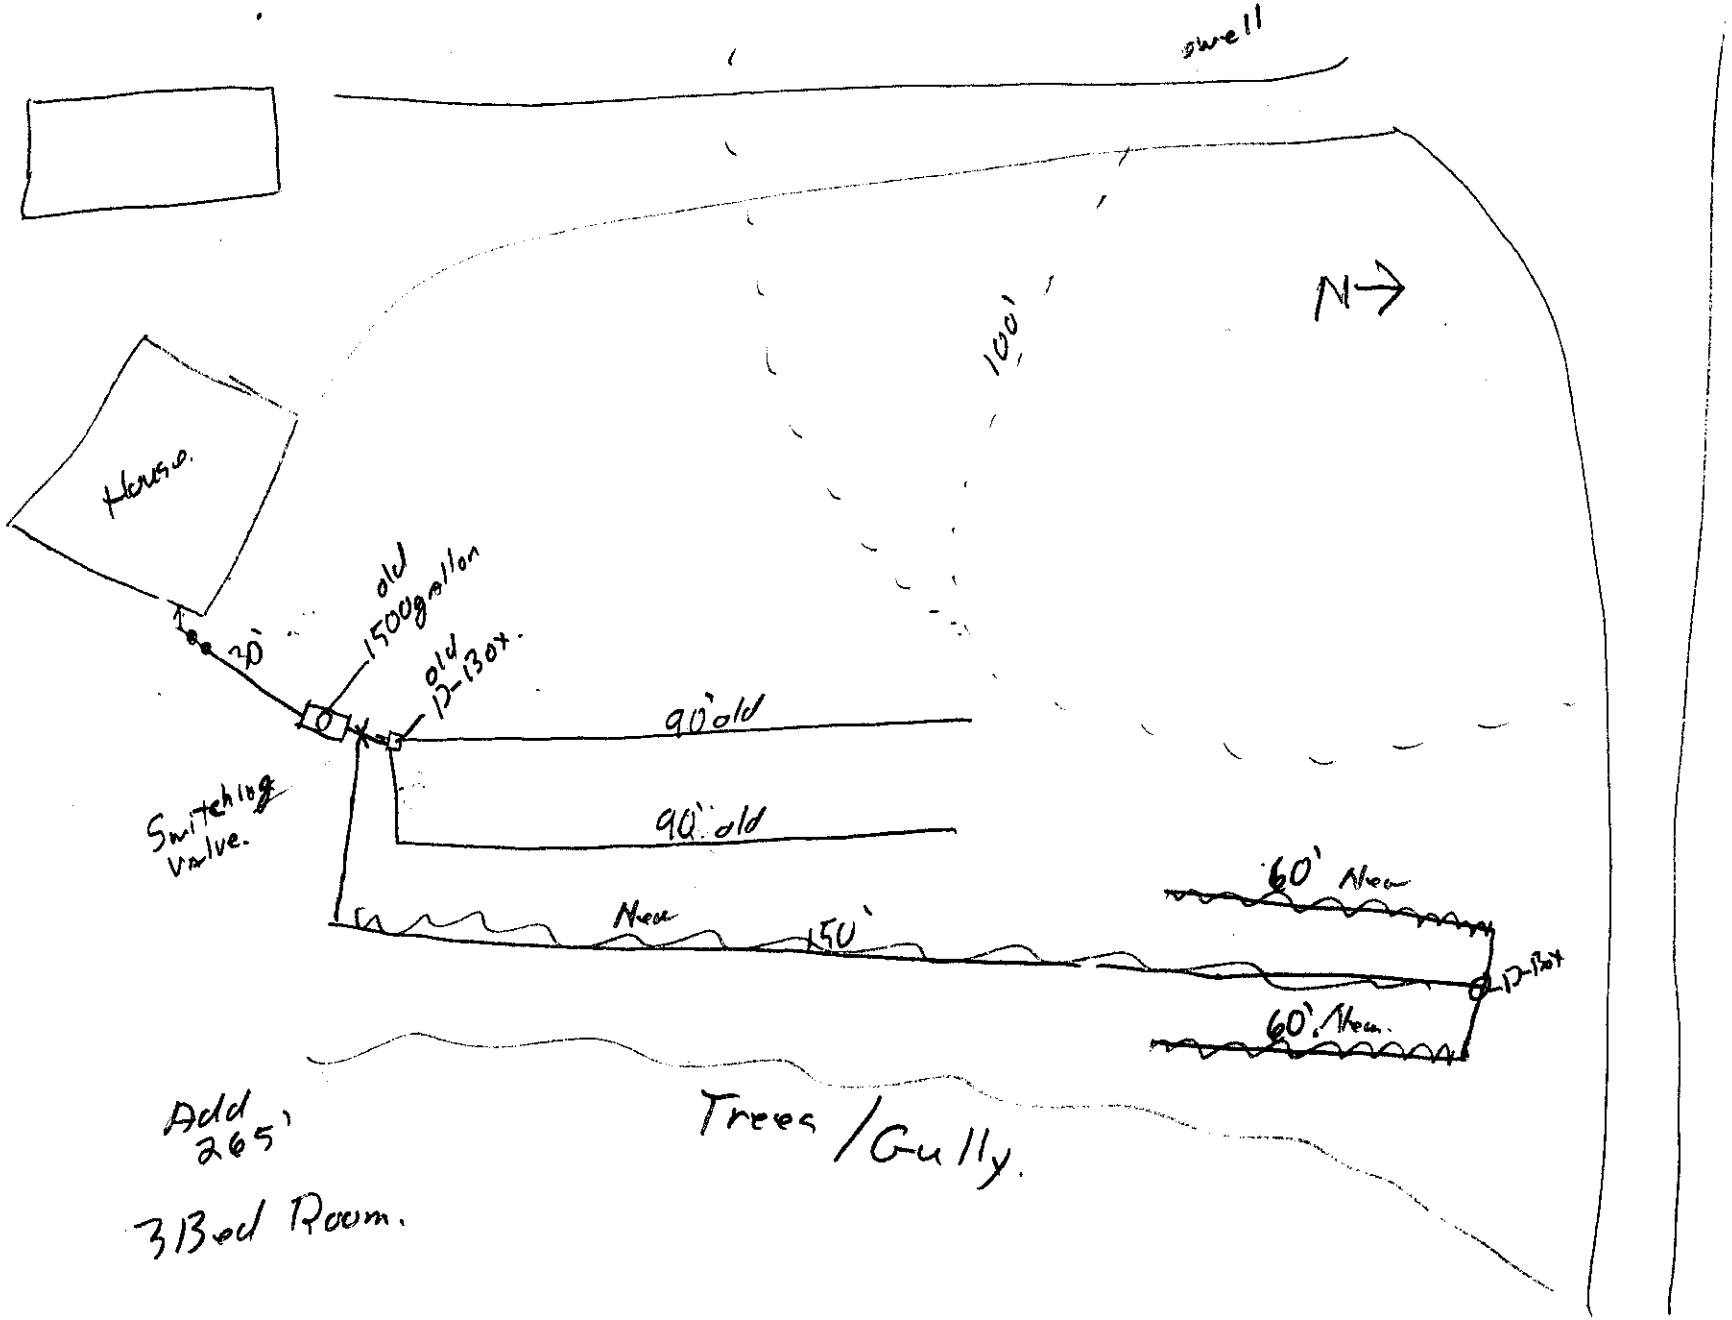


LLCHD HS000489

5-5-2011. 8:14:42

Lincoln-Lancaster County Health Department
Environmental Public Health Division (402) 441-8027
3140 N Street Lincoln, NE 68510-1514

ON-SITE WASTE WATER SYSTEM
REPAIR PERMIT

No. HS000489

System Type: STANDARD

Situs: 7233 W RANGER RIDGE RD

Legal Description: T09N-R05E-S02-3-Lot 1

Owner: FRYE, DAVID L & DEBORAH J
7233 W RANGER RIDGE RD
LINCOLN NE
68532

Permit Fee:	$185.00
Total Fees:	$185.00
Issued:	05/03/2011
Expires	05/02/2012

Judith A Halstead

Judith A. Halstead, MS, Health Director

Dear Applicant:

The above document is your permit to repair an existing On-site Waste Water System at the location listed. Please contact this office once repairs are complete to obtain final approval before use.

Judith A Halstead

Judith A. Halstead, MS
Health Director

RAYMOND CONTRACTING
13800 NW 70TH
RAYMOND NE 68428

LLCHD HS000489

MAR 03 2011

Application to Alter, Extend or Repair an Onsite Wastewater Treatment System

☐ Municipal Code 24.38 ☐ County Resolution Number 02-30

HS000489

The undersigned hereby applies for a permit to: ☐ **ALTER** ☑ **EXTEND** ☐ **REPAIR** an existing wastewater treatment system, complying with appropriate Ordinance or Resolution, as marked above with drawings attached.

1. **Legal description of property:**
   Township 9 Range 5 1/4 ____ 1/4 NE Section 2
   Block 3 Lot 1 Addition Ridge Park 1st Add
   Parcel ID 03-02-209-001-000 (i.e. 99-99-999-999-999)
   Street Address (no rural route) 7233 W Ranger Ridge Rd Lincoln, NE 68532

2. **Property use:** ☒ residential ☐ commercial ☐ other use
   Number of bedrooms 3 Describe ____

3. **Type of Present Individual Disposal System** ☒ septic system ☐ lagoon ☐ other

4. **Description of proposed alteration, extension or repair** replace existing drainfield 265' based on a perc rate of 60 mpi

5. **Work to be done by:** ☐ owner ☒ contractor's name Lloyd Jakauber Raymond Contracting Inc

6. **Estimated project:** a. Repair, replace, or minor extension with a cost less than $400 (no fee required).
   b. Total cost is greater than $400 (Return fee with this application)
   c. A permit is required if the use, operation, location, or type of system is changed.

Print Name David Fryc Address 7233 W Ranger Ridge Rd Phone: 402-610-2185
Lincoln, NE 68532

* Applicant Signature (owner or lessee) Lloyd J. Jakauber for David Fryc

Please contact LLCHD for the permit fee for this application
Fee must be included before the application will be processed. Incomplete information will delay processing

---

HEALTH DEPARTMENT USE ONLY

Date received 5/3/11 REVIEW: ☑ Approved ☐ Disapproved By: ____

Site visits
Date ____/____/____ By ____
Date ____/____/____ By ____
Date ____/____/____ By ____

Installation final written approval
Date ____/____/____ By ____

Return application to:
Lincoln-Lancaster County Health Department
Environmental Public Health Division
3140 "N" Street, Lincoln, NE 68510
Phone: 441-8643

Business Office Use Only

Received: Date: 5/3/11 Amount 185 Check No. 7623 Initials ____

Revised 3-09

5-4-2011 14:23:55

Lincoln-Lancaster County Health Department
Environmental Health Division
3140 "N" Street • Lincoln, NE 68510-1514
Phone: 402-441-8022

B

Permit Number:

Sewage Disposal System

Soil Absorption Test Data Report

Annex to Application

PLEASE PRINT OR TYPE

System Location (Indicate correct number and street)

Address 7233 W Ranger Ridge Rd (no rural route) City Lincoln NE, Zip 68532

Owner David Frye Addresss Same

Soil Type (SCS): Wymore Silty Clay Loam Percolation Rate: 60 min./inch

Date of Tests 4/12/11 to 4/13/11 Weather: Precipitation 0 Temperature 65°

Percolation Test Data Table

A.	B.	C. D. E. F. Pre-Saturation Period				G. H. I. J. K. Percolation Readings					L. M. N. Results		
		Start		End		Start			End				
Hole No.	Hole Depth (in)	Date (Mo/Da)	Time (Hr/Min)	Date (Mo/Da)	Time (Hr/Min)	Date (Mo/Da)	Time (Hr/Min)	Water Lev (in.)	Date (Mo/Da)	Time (Hr/Min)	Elapsed Time (Min)	Water Level Drop (in)	Percolation Rates (Min/in)
1	30	4/12	1:00p	4/12	5:00p	4/13	4:00p	6	4/13	4:30p	30	15/16	32
2	28	"	"	"	"	"	"	"	"	"	"	1	30
3	26	"	"	"	"	"	"	"	"	"	"	1/2	60

Sum of Percolation Rates: 122

Average of Rates: 41

Rate Used for Calculation: 60 (20 min Variance)

Person Conducting Percolation Tests

Name: Terri L. Jahnebek, Raymond Contracting, Inc.

Phone: 402-783-2003 or 402-890-3870

Address 13800 NW 70th St

Raymond, NE 68428 # C1198


DO NOT WRITE BELOW THIS LINE

Reviewing Action

Remarks _____

Signature of Reviewing Official _____ Date _____

FORM 23-101 10-96
5-4-2011 14:23:57

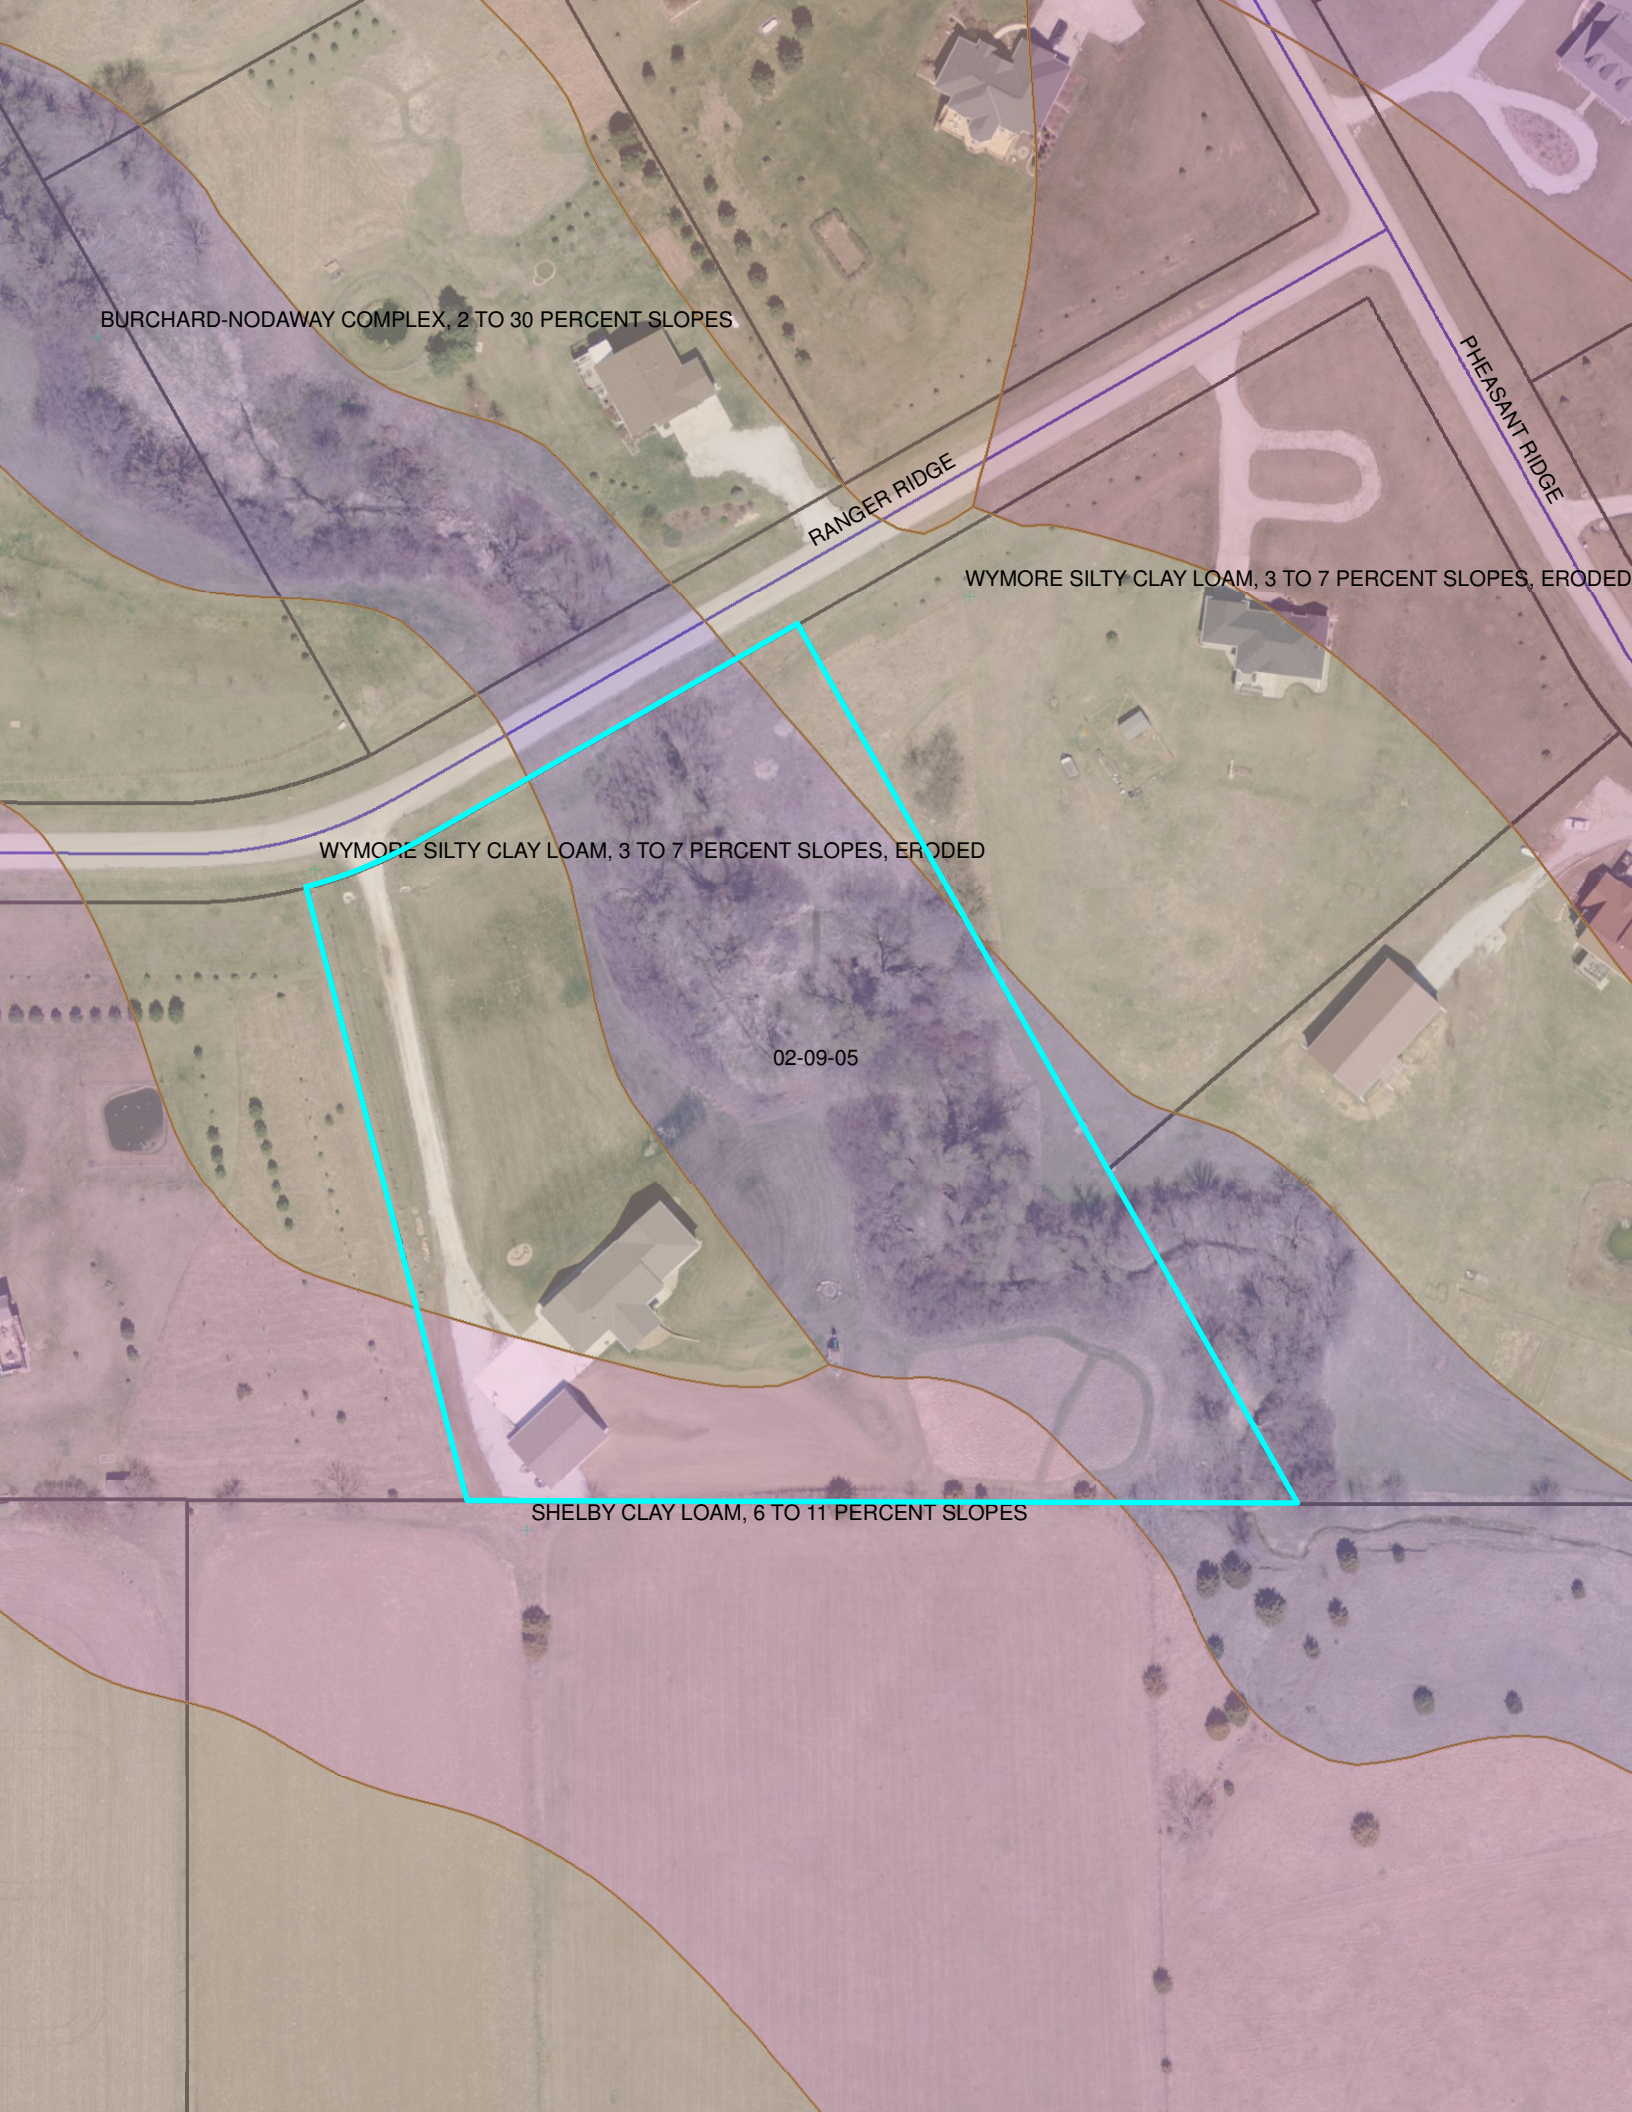
BURCHARD-NODAWAY COMPLEX, 2 TO 30 PERCENT SLOPES
RANGER RIDGE
PHEASANT RIDGE
WYMORE SILTY CLAY LOAM, 3 TO 7 PERCENT SLOPES, ERODED
WYMORE SILTY CLAY LOAM, 3 TO 7 PERCENT SLOPES, ERODED
02-09-05
SHELBY CLAY LOAM, 6 TO 11 PERCENT SLOPES
