
LLCHD HS000667

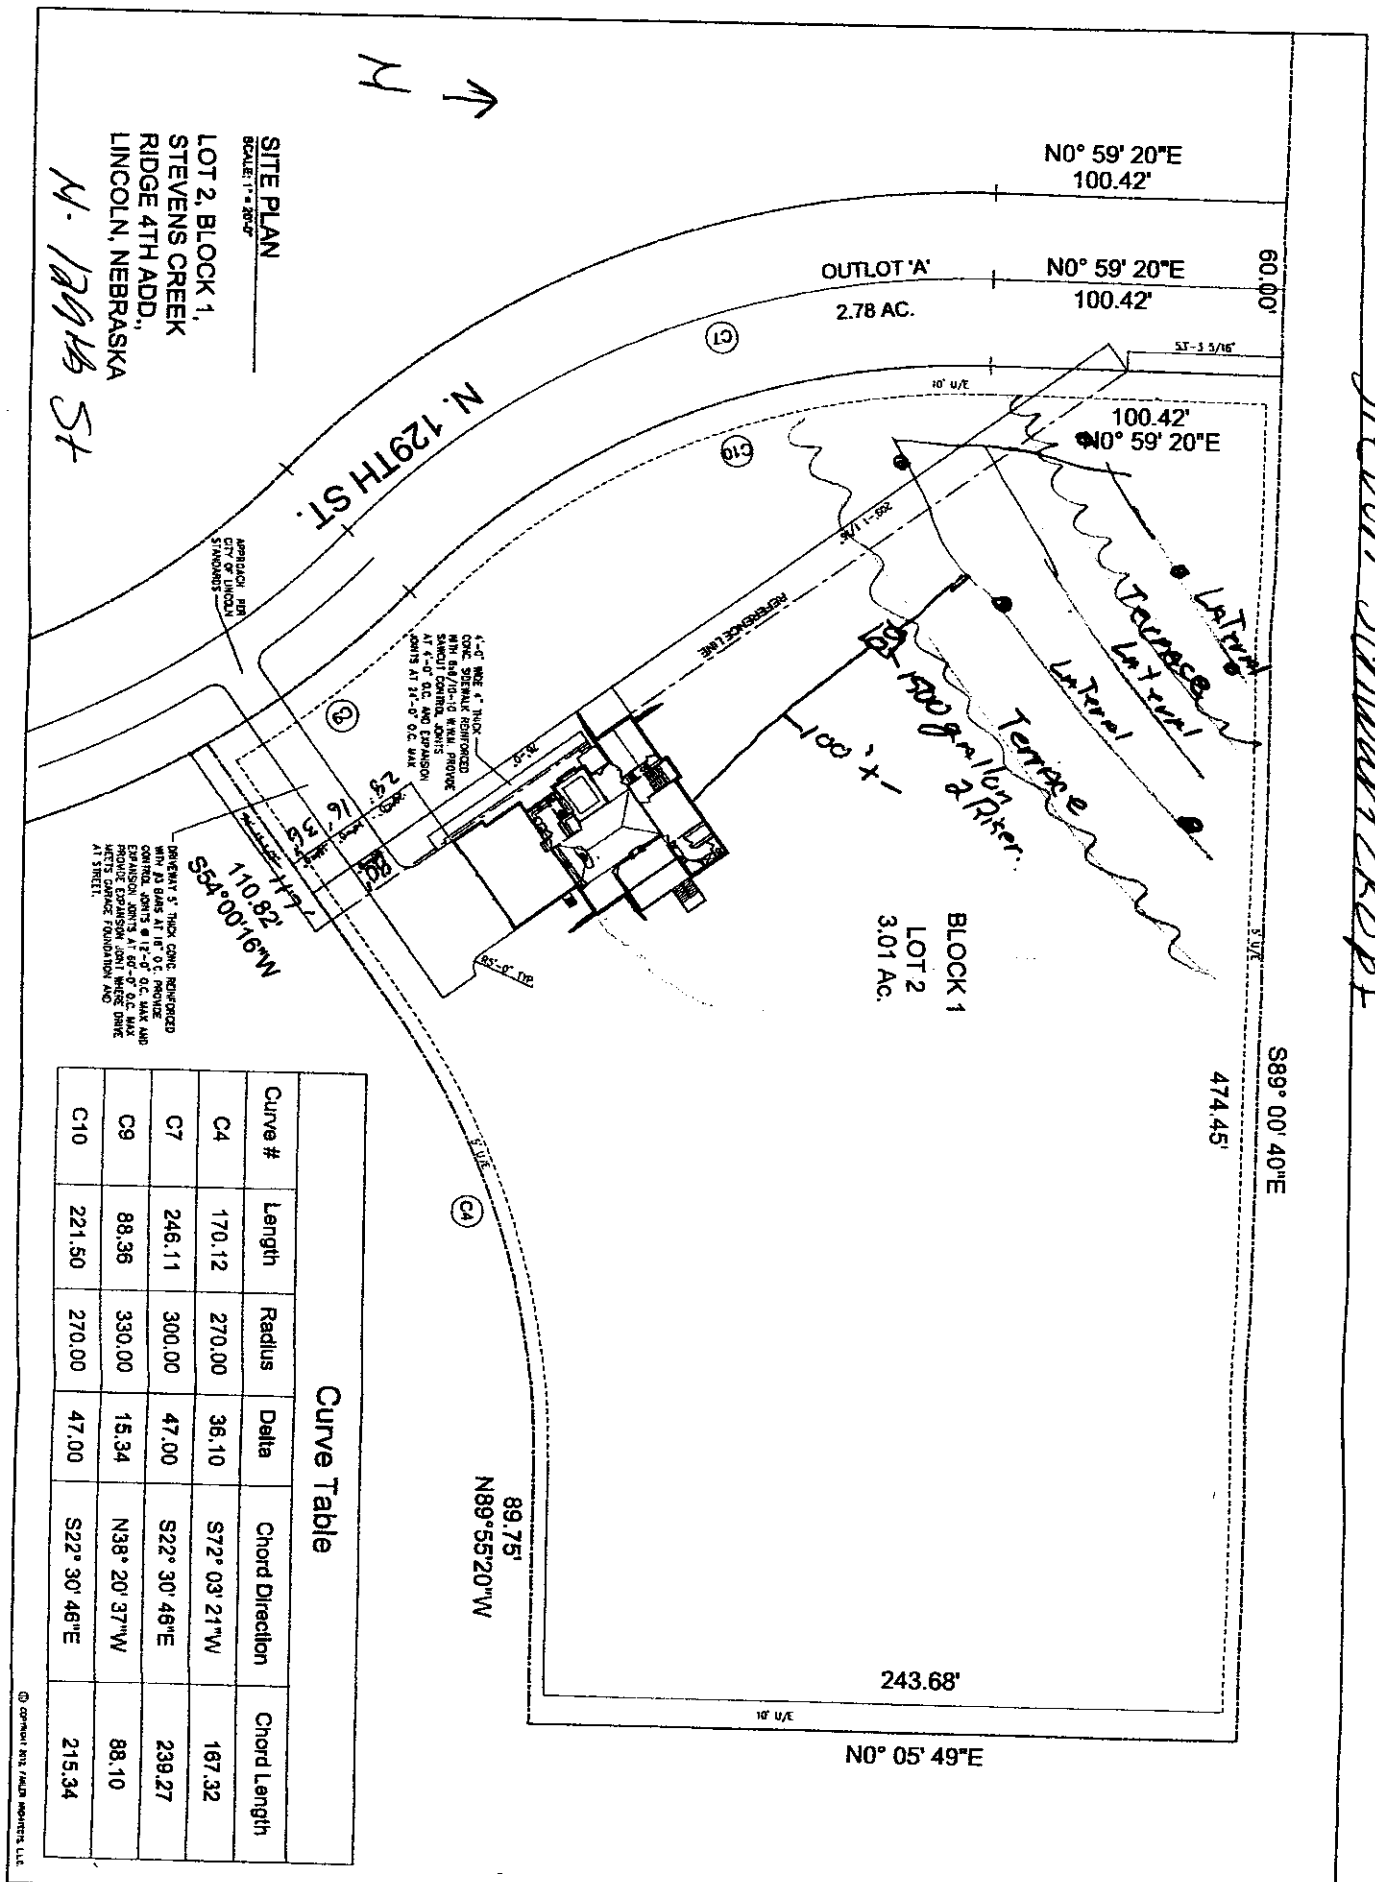

Curve Table					
Curve #	Length	Radius	Delta	Chord Direction	Chord Length
C4	170.12	270.00	36.10	S72° 03' 21"W	167.32
C7	246.11	300.00	47.00	S22° 30' 46"E	239.27
C9	88.36	330.00	15.34	N38° 20' 37"W	88.10
C10	221.50	270.00	47.00	S22° 30' 46"E	215.34

© COPYRIGHT 2012, FAKLER ARCHITECTS, L.L.C.

SITE PLAN

A-0

REVISIONS

PRELIMINARY ISSUE 8/21/2012

BID ISSUE 9/20/2012

PERMIT ISSUE 10/2/2012

CONST. ISSUE

Steve & Sandi Schwartzkopf Residence

N. 129th St., Lincoln, Nebraska

FAKLER ARCHITECTS, L.L.C.
421 W. PARK ST., BEATRICE, NE 68310
PH 402-228-3020 FAX 402-228-3018
E-MAIL michael@faklerarchitects.com

Steven Schwartzkopf

10-2-2012 14: 8:59

Lincoln-Lancaster County Health Department
Environmental Public Health Division (402) 441-8027
3140 N Street Lincoln, NE 68510-1514

ON-SITE WASTE WATER SYSTEM
CONSTRUCTION - INSTALLATION PERMIT

No. HS000667

System Type: STANDARD

Situs:

Legal Description: T10N-R08E-S17-1-Lot 2

Owner:

Permit Fee:	$345.00
Variance Fee:	$0.00
Extension Fee:	$0.00
Total Fees:	$345.00

Issued:	10/02/2012
Expires:	10/02/2013

Judith A Halstead

Judith A. Halstead, MS, Health Director


On-site Waste System Permit Holder:

The above document is your permit to construct a new On-site Waste Water System at the location listed. Please contact this office once the sytem is complete in order to schedule a final inspection before use.

Judith A Halstead

Judith A. Halstead, MS
Health Director

RAYMOND CONTRACTING
13800 NW 70TH
RAYMOND NE 68428

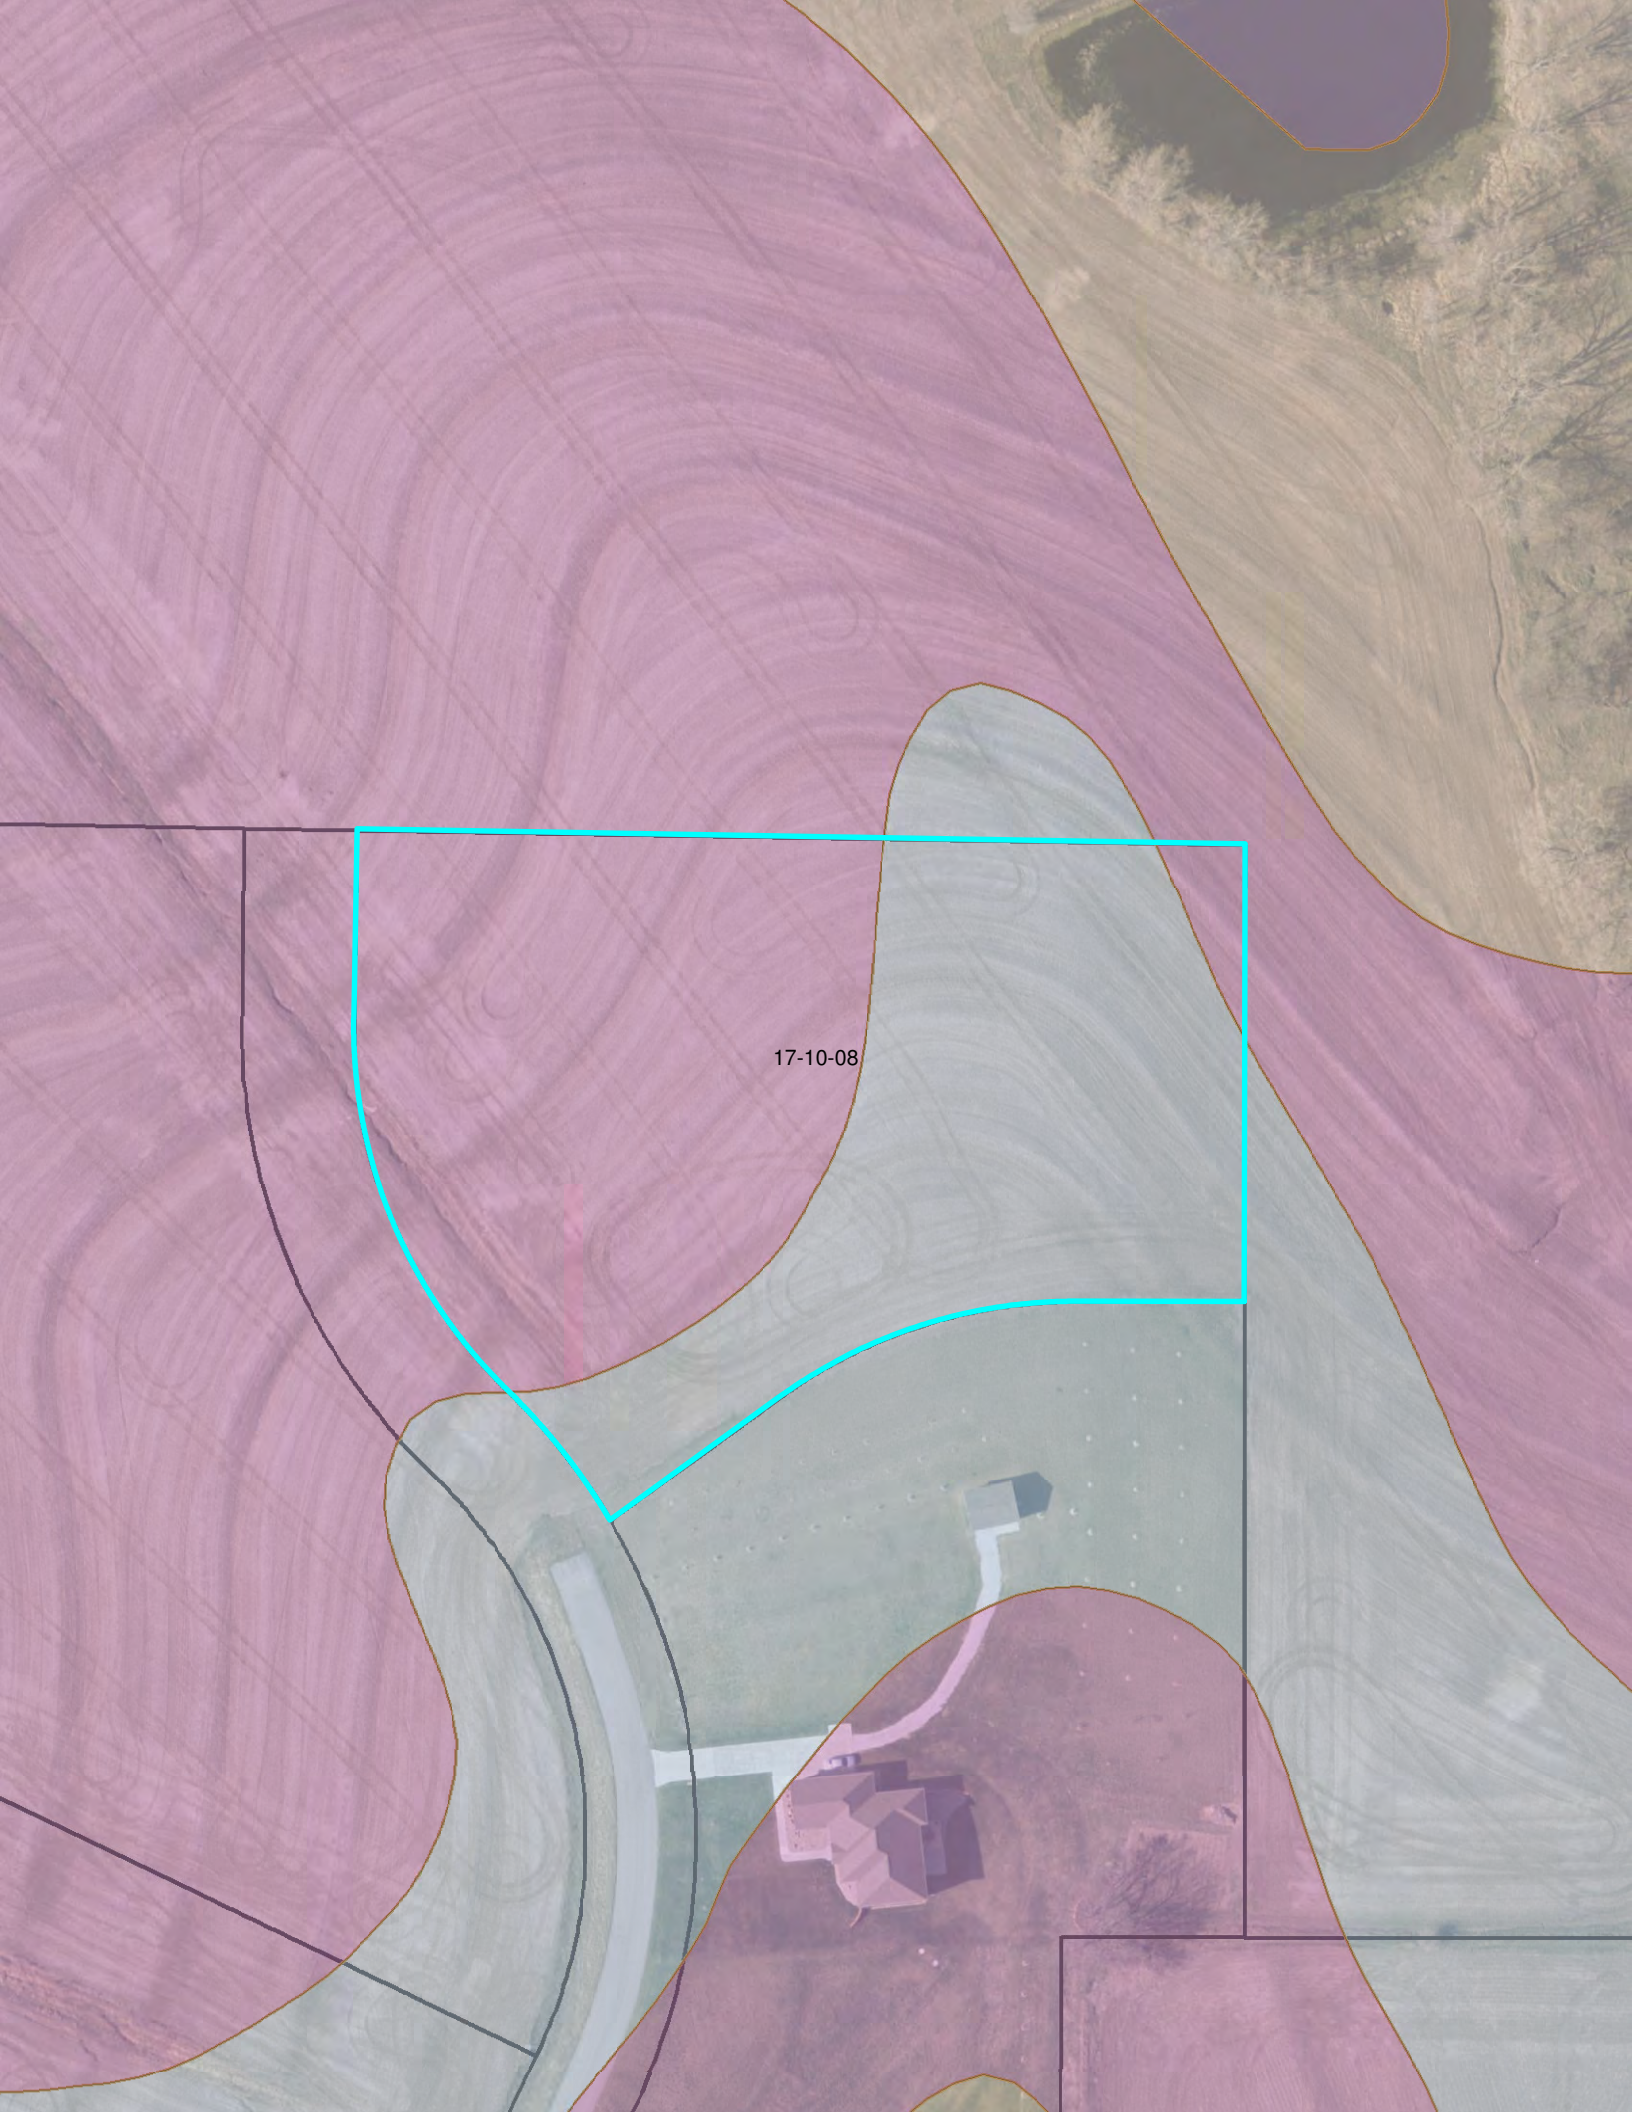
17-10-08

LLCHD HS000667

OCT 01 2012

Lincoln-Lancaster County Health Department
Environmental Public Health Division
3140 N Street • Lincoln NE 68510-1514
Phone: 402-441-8643

A

Permit Number HS000667

Onsite Wastewater Treatment System
Request for Site Clearance and Permit

Include Form B and C. Submit correct fee with this Application

3 acres or more required for: ☑ Septic System ☐ Lagoon ☐ Other (Refer to Form C)

The undersigned hereby requests site clearance and permit to construct a Wastewater Treatment System in conformance with appropriate regulations.

PLEASE PRINT OR TYPE

A. Onsite System Location

Address 1830 N. 129th St (no rural route) City Lincoln, NE Zip 68527

Legal Description SE 17 10 8 Stevens Creek Ridge 4th 1 2
(1/4 | 1/4 | Section | Township | Range | Subdivison | Addition | Block | Lot)

Geographical Location (if known): Lat/Long: PID 23-17-405-002-000

B. Owner

Name Steven Schwartzkopf Signature

Address 824 Sawyer St City/State/Zip Lincoln NE 68505

Home Phone Work Phone

C. Certified Installer

Name: Lloyd Jakoubek, Raymond Contracting Signature

Address 13800 NW 70th St City/State/Zip Raymond, NE 68428

Work Phone 402-890-6009

D. Engineer

☐ Check and complete if engineer designed system P.E. License Number:

Designer Name Firm Work Phone

E. This system will serve a + Garbage Disposal

☑ Residential Dwelling Number of Bedrooms 3 Is there a Whirlpool Bathtub? ☑ Yes ☐ No Total Acres 3.01

☐ Commercial Establishment/Other Facility Specify Design flow in gallons per day

Type of Wastewater ☐ Domestic ☐ Non-Domestic Well Permit Applied for ☐ Yes ☐ No ☑ Not Applicable

DO NOT WRITE BELOW THIS LINE

Approval Process ☐ Municipal Code 24.38 ☐ County Resolution No. 02-30

1. Health Department
Site visits
Date rec'd 10/2/12
Date frwd 10/2/12
ACTION ☑ Approved ☐ Disapproved
Signature

2. Supt. Bldg. Insp. or Village Clerk
Comments
Date rec'd 10-2-2012
Date frwd 10-2-2012
ACTION ☑ Approved ☐ Disapproved
Signature

3. City or County Engineer
Comments
Date rec'd 10-2-2012
Date frwd 10-2-2012
ACTION ☑ Approved ☐ Disapproved
Signature Kenneth D. Schroeder

Installation Final Written Approval
By
Date

Business Office Use Only
Date Received 10-2-12 Amount Paid 346.00
Received By BA Cash/Check No. 1971

White - Health Department Yellow - Engineer Pink - Building & Safety

Form A Updated: 5/10

10-2-2012 14: 8: 9

LLCHD HS000667

Lincoln-Lancaster County Health Department
Environmental Health Division
3140 "N" Street • Lincoln, NE 68510-1514
Phone: 402-441-8022

B

Permit Number:

Sewage Disposal System
Soil Absorption Test Data Report
Annex to Application

PLEASE PRINT OR TYPE

System Location (Indicate correct number and street)

Address M. 12th St (no rural route) City Lincoln NE, Zip 68527

Owner Steve Schwartzkopf Addresss 1424 Sawyer St Lincoln NE 68505

Soil Type (SCS): Silty Clay Loam Percolation Rate: 48 min./inch

Date of Tests 9/25/2012 to 9/26/2012 Weather: Precipitation 0 Temperature 78°

Percolation Test Data Table

A.	B.	C. D. E. F. Pre-Saturation Period				G. H. I. J. K. Percolation Readings					L. M. N. Results		
		Start		End		Start			End				
Hole No.	Hole Depth (in)	Date (Mo/Da)	Time (Hr/Min)	Date (Mo/Da)	Time (Hr/Min)	Date (Mo/Da)	Time (Hr/Min)	Water Lev (in.)	Date (Mo/Da)	Time (Hr/Min)	Elapsed Time (Min)	Water Level Drop (in)	Percolation Rates (Min/in)
1	36	9/25	3:00p	9/25	7:00p	9/26	4:30p	10	9/26	5:10p	20	5/8	48
2	30	"	"	"	"	"	"	"	"	"	"	1 1/2	20
3	27	"	"	"	"	"	"	"	"	"	"	1 3/16	25
4	27	"	"	"	"	"	"	"	"	"	"	1 3/16	37
5	38	"	"	"	"	"	"	"	"	"	"	7/8	34
10	26	"	"	"	"	"	"	"	"	"	"	5/8	48

Person Conducting Percolation Tests

Name: Terri Jakubek, Raymond Construction Inc

Phone: 402-890-3870 or 402-783-2663

Address 13800 NW 70th St

Raymond, NE 68428 HC1198

Sum of Percolation Rates: 212

Average of Rates: 35

Rate Used for Calculation: 48 (20 min Variance)

DO NOT WRITE BELOW THIS LINE

Reviewing Action

Remarks

Signature of Reviewing Official Date

FORM 23-101 10-96

10-2-2012 14: 8:10

Lincoln-Lancaster County Health Department
Environmental Health Division
3140 "N" Street • Lincoln, NE 68510-1514
Phone: 402-441-8022


C

Permit Number:

Sewage Disposal System

Preliminary Plan Specifications

Draw a plot plan showing system location, lines, distribution box, tank and laterals, percolation test hole locations, well, residence, compass direction and property lines. Indicate on drawing if residence and well are existing or proposed.

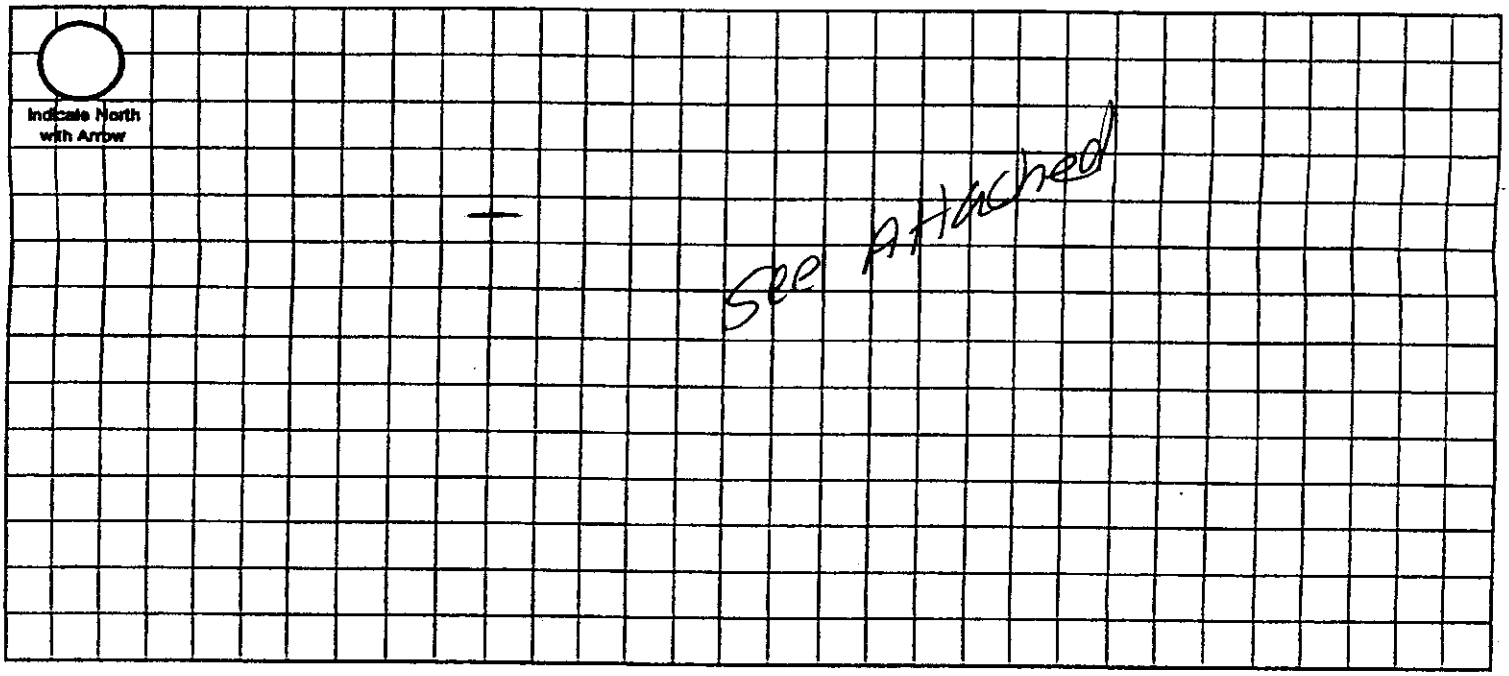

Approximate Scale: _____ ft. = _____ grid line/s

A. System Location (Indicate correct number and street)

Address (no rural route) M.129 St City Lincoln NE, Zip 68527

B. Proposed Septic Tank/s

Tank Material: ☒ Concrete ☐ Plastic ☐ Other _____

C. Proposed Absorption System (See Form B for Percolation Information)

Percolation Rate 48 (min. per inch) Soil Type: Silty Clay loam Land Slope: _____ %

Type of Absorption System: ☒ Trench ☐ Bed ☐ Other _____

Total Square Feet of Field Required: 990 sq. ft.

Type of Lateral: ☐ Half-Moon ☐ Perforated Pipe ☒ Other Lateral Material: ADS Graveless Chambers

Capacity of Septic Tank 1,500 gals Number of Absorption Beds: _____ Number of Distribution Laterals per Bed _____

Total Length of Laterals 250 ft. Number of Trenches 3 Trench Width 40"

D. Setbacks Check the Boxes Below if the Required Setback has been Satisfied

Distance From	Private Well	Public Well	Surface Water	Gound Water	Pressure Water Lines	Property Lines	Foundations Yours	Foundations Neighbors	All Other Setbacks
Tank (ft)	50 ☐	500 ☐	50 ☐	NA ☐	25 ☐	20 ☐	15 ☐	25 ☐	☐
Field (ft)	100 ☐	500 ☐	50 ☐	4 ☐	30 ☐	20 ☐	30 ☐	40 ☐	☐
Lagoon (ft)	100 ☐	500 ☐	50 ☐	N/A ☐	30 ☐	50 ☐	100 ☐	200 ☐	☐

E. Required Signatures

Home Building Contractor _____ Date 9-27-12

Installer _____ Date 9/27/12

FORM 23-102 10-96

Lincoln-Lancaster County Health Department
Environmental Public Health Division (402) 441-8027
3140 N Street Lincoln, Nebraska 68510-1514

ON-SITE WASTE WATER SYSTEM
CONSTRUCT/ INSTALL EXTENSION PERMIT
No. HS000667

System Type: Standard

Situs: 1970 N 129 CT, RURAL, NE

Issued: 10/2/2013

Expires: 4/7/2014

Description: 1970 N. 129thT10N-R08E-S17-1-Lot 2

Owner:

Judith A Halstead

Judith A. Halstead, MS, Health Director

Dear Applicant:

The above document is your permit to construct a new On-site Waste Water System at the location listed. Please contact this office once the sytem is complete in order to schedule a final inspection before use.

Judith A Halstead

Judith A. Halstead, MS
Health Director

RAYMOND CONTRACTING
13800 NW 70TH
RAYMOND, NE 68428

Lincoln-Lancaster County Health Department
Environmental Public Health Division (402) 441-8027
3140 N Street Lincoln, Nebraska 68510-1514

ON-SITE WASTE WATER SYSTEM
CONSTRUCT/ INSTALL EXTENSION PERMIT
No. HS000667

System Type: Standard

Situs: 1970 N 129 CT, RURAL, NE

Issued: 10/2/2013

Expires: 4/7/2014

Description: 1970 N. 129thT10N-R08E-S17-1-Lot 2

Owner: STEVEN SCHWARTZKOPF
1924 SAWYER ST
LINCOLN, NE 68505

Judith A Halstead
Judith A. Halstead, MS, Health Director

Dear Applicant:

The above document is your permit to construct a new On-site Waste Water System at the location listed. Please contact this office once the sytem is complete in order to schedule a final inspection before use.

Judith A Halstead
Judith A. Halstead, MS
Health Director

RAYMOND CONTRACTING
13800 NW 70TH
RAYMOND, NE 68428

Lincoln-Lancaster County Health Department
Environmental Public Health Division (402) 441-8027
3140 N Street Lincoln, Nebraska 68510-1514

ON-SITE WASTE WATER SYSTEM
CONSTRUCT/ INSTALL EXTENSION PERMIT
No. HS000667

System Type: Standard

Situs: 1970 N 129 CT, RURAL, NE

Issued: 10/7/2013

Expires: 4/7/2014

Description: 1970 N. 129thT10N-R08E-S17-1-Lot 2

Owner: STEVEN SCHWARTZKOPF
1924 SAWYER ST
LINCOLN, NE 68505

Judith A Halstead
Judith A. Halstead, MS, Health Director

Dear Applicant:

The above document is your permit to construct a new On-site Waste Water System at the location listed. Please contact this office once the sytem is complete in order to schedule a final inspection before use.

Judith A Halstead
Judith A. Halstead, MS
Health Director

RAYMOND CONTRACTING
13800 NW 70TH
RAYMOND, NE 68428

018478

-Lancaster County Health Department
onmental Public Health Division (402) 441-8027
N Street Lincoln, Nebraska 68510-1514

ON-SITE WASTE WATER SYSTEM
CONSTRUCT/ INSTALL EXTENSION PERMIT
No. HS000667

System Type: Standard

Situs: 1970 N 129 CT, RURAL, NE

Issued: 10/7/2013

Expires: 4/7/2014

Description: 1970 N. 129thT10N-R08E-S17-1-Lot 2

Owner: STEVEN SCHWARTZKOPF
1924 SAWYER ST
LINCOLN, NE 68505

Judith A Halstead
Judith A. Halstead, MS, Health Director

Dear Applicant:

The above document is your permit to construct a new On-site Waste Water System at the location listed. Please contact this office once the sytem is complete in order to schedule a final inspection before use.

Judith A Halstead

Judith A. Halstead, MS
Health Director

Receipt # 8278460

Invoice # 974854

RAYMOND CONTRACTING
13800 NW 70TH
RAYMOND, NE 68428

Lincoln-Lancaster County Health Department
Environmental Public Health Division (402) 441-8027
3140 N Street Lincoln, Nebraska 68510-1514

ON-SITE WASTE WATER SYSTEM
CONSTRUCT/ INSTALL EXTENSION PERMIT
No. HS000667

System Type: Standard

Situs: 1970 N 129 CT, RURAL, NE

Issued: 4/7/2014

Expires: 12/4/2014

Description: 1970 N. 129thT10N-R08E-S17-1-Lot 2

Owner: STEVEN SCHWARTZKOPF
1924 SAWYER ST
LINCOLN, NE 68505

Judith A Halstead
Judith A. Halstead, MS, Health Director

Dear Applicant:

The above document is your permit to construct a new On-site Waste Water System at the location listed. Please contact this office once the sytem is complete in order to schedule a final inspection before use.

Judith A Halstead
Judith A. Halstead, MS
Health Director

RAYMOND CONTRACTING
13800 NW 70TH
RAYMOND, NE 68428

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
LAGOON/SEPTIC INSPECTION REPORT

Permit No. HS000667 Certified Installer: J. Koubek

Address: 1970 N 129th

Circle compliance status for each item. **IN = in compliance OUT = not in compliance NA = not applicable NO = not observed**

LAGOON SETBACKS

				Item	MIN. SETBACK DISTANCE – FT. (METERS)	COMMENTS
IN	OUT	NA	NO	Surface Wtr. Distance from Wtr. Mark	50 ft. (15.2 m)	
IN	OUT	NA	NO	Private Drinking Water Wells	100 ft. (30.5 m)	
IN	OUT	NA	NO	Public Drinking Water Supply Wells:		
IN	OUT	NA	NO	Non-Community	100 ft. (30.5 m)	
IN	OUT	NA	NO	Community	Evaluated by a professional engineer for potential impact on the well and submitted to the Dept. for approval l if less than 1000 ft. (304.8 m)	
IN	OUT	NA	NO	All Other Water Wells	100 ft. (152.4 m)	
IN	OUT	NA	NO	Water Lines:		
IN	OUT	NA	NO	Pressure Main	25 ft. (7.6 m)	
IN	OUT	NA	NO	Pressure-Service Connection	25 ft. (7.6 m)	
IN	OUT	NA	NO	Suction Line	100 ft. (30.5 m)	
IN	OUT	NA	NO	Property Lines	50 ft. (15.2 m)	
IN	OUT	NA	NO	Trees and Brush	50 ft. (15.2 m)	
IN	OUT	NA	NO	Foundations: (see definition above)		
IN	OUT	NA	NO	Except Neighbor's Foundation:		
IN	OUT	NA	NO	Class 1	100 ft. (30.5 m)	
IN	OUT	NA	NO	Class 2	100 ft. (30.5 m)	
IN	OUT	NA	NO	Class 3	50 ft. (15.2 m)	
IN	OUT	NA	NO	Neighbor's Foundation:		
IN	OUT	NA	NO	Class 1	200 ft. (61.0 m)	**Lagoon Dimensions:**
IN	OUT	NA	NO	Class 2	200 ft. (61.0 m)	
IN	OUT	NA	NO	Class 3	100 ft. (30.5 m)	

TANK AND SOIL ABSORPTION SYSTEM SETBACKS

				Item	MIN. SETBACK DISTANCE – FT. (METERS) Tanks	Absorption, Infiltrative & Evaporative Systems	COMMENTS
IN	OUT	NA	NO	Surface Water	50 ft. (15.2 m)	50 ft. (15.2 m)	
IN	OUT	NA	NO	Private Drinking Water Wells	50 ft. (15.2 m)	100 ft. (30.5 m)	
IN	OUT	NA	NO	Public Drinking Water Supply Wells:			
IN	OUT	NA	NO	Non-Community System	50 ft. (15.2 m)	100 ft. (30.5 m)	
IN	OUT	NA	NO	Community System	500 ft. (152.4 m)	500 ft. (152. 4 m)	
IN	OUT	NA	NO	Community System when a septic system or soil absorption system of > 1000 gpd is proposed	500 ft. (152.4 m)	Evaluated by professional engineer for potential impact on the well and submitted to the Depart. for approval if less than 1000 ft.	
IN	OUT	NA	NO	All Other Water Wells	50 ft. (15.2 m)	100 ft. (30.5 m)	
IN	OUT	NA	NO	Water Lines:			
IN	OUT	NA	NO	Pressure-Main	10 ft. (3.1 m)	25 ft. (7.6 m)	
IN	OUT	NA	NO	Pressure-Service – Connection	10 ft. (3.1 m)	25 ft. (7.6 m)	
IN	OUT	NA	NO	Suction Lines	50 ft. (15.2 m)	100 ft. (30.5 m)	
IN	OUT	NA	NO	Property Lines	5 ft. (1.5 m)	5 ft. (1.5 m)	
IN	OUT	NA	NO	Parking area, driveway, sidewalk or other impermeable surface or cover	5 ft. (1.5 m)	5 ft. (1.5 m)	Not completed at time of Inspection
IN	OUT	NA	NO	Foundations: (see definitions above)			
IN	OUT	NA	NO	Except Neighbor's Foundation:			
IN	OUT	NA	NO	Class 1	15 ft. (4.6 m)	30 ft. (9.1 m)	
IN	OUT	NA	NO	Class 2	10 ft. (3.1 m)	20 ft. (6.1 m)	**Septic Tank Size:** 1500 installed
IN	OUT	NA	NO	Class 3	7 ft. (2.1 m)	10 ft. (3.1 m)	
IN	OUT	NA	NO	Neighbor's Foundation:			
IN	OUT	NA	NO	Class 1	25 ft. (7.6 m)	40 ft. (12.2 m)	**Lateral Sq. Footage:** each 100' plus
IN	OUT	NA	NO	Class 2	20 ft. (6.1 m)	30 ft. (9.1 m)	
IN	OUT	NA	NO	Class 3	15 ft. (4.6 m)	20 ft. (6.1 m)	

Inspected By: Doug Amos **Date:** 6/16/14

OCT 01 2012

SCANNED

Lincoln-Lancaster County Health Department
Environmental Public Health Division
3140 N Street • Lincoln NE 68510-1514
Phone: 402-441-8643

A

Permit Number HS000667

Onsite Wastewater Treatment System
Request for Site Clearance and Permit

Include Form B and C. Submit correct fee with this Application

3 acres or more required for: ☒ Septic System ☐ Lagoon ☐ Other (Refer to Form C)

The undersigned hereby requests site clearance and permit to construct a Wastewater Treatment System in conformance with appropriate regulations.

PLEASE PRINT OR TYPE

A. Onsite System Location

Address 1930 N. 129th St (no rural route) City Lincoln, NE Zip 68527

Legal Description SE 17 10 8 Stevens Creek Ridge 4th 1 2
(1/4 | 1/4 | Section | Township | Range | Subdivison | Addition | Block | Lot)

Geographical Location (if known): Lat/Long: _____ PID 23-17-405-002-000

B. Owner

Name Steven Schwartzkopf Signature [signature]

Address 924 Sawyer St City/State/Zip Lincoln, NE 68505

Home Phone _____ Work Phone _____

C. Certified Installer

Name: Lloyd Jakobuske, Raymond Contracting Signature _____

Address 13800 NW 70th St City/State/Zip Raymond, NE 68428

Work Phone 402-890-6009

D. Engineer

☐ Check and complete if engineer designed system P.E. License Number: _____

Designer Name _____ Firm _____ Work Phone _____

E. This system will serve a + Garbage Disposal

☒ Residential Dwelling Number of Bedrooms 3 Is there a Whirlpool Bathtub? ☒ Yes ☐ No Total Acres 3.01

☐ Commercial Establishment/Other Facility Specify _____ Design flow in gallons per day _____

Type of Wastewater ☐ Domestic ☐ Non-Domestic Well Permit Applied for ☐ Yes ☐ No ☒ Not Applicable

DO NOT WRITE BELOW THIS LINE

Approval Process ☐ Municipal Code 24.38 ☐ County Resolution No. 02-30

1. Health Department
Site visits _____
Date rec'd 10/2/12
Date frwd 10/2/12
ACTION ☒ Approved ☐ Disapproved
Signature [signature]

2. Supt. Bldg. Insp. or Village Clerk
Comments _____
Date rec'd 10-2-2012
Date frwd 10-2-2012
ACTION ☒ Approved ☐ Disapproved
Signature [signature]

3. City or County Engineer
Comments _____
Date rec'd 10-2-2012
Date frwd 10-2-2012
ACTION ☒ Approved ☐ Disapproved
Signature [signature]

Installation Final Written Approval
By [signature]
Date 6/16/14

Business Office Use Only
Date Received 10-2-12 Amount Paid 346.00
Received By BAL Cash/Check No. 7971
10-4-13 BAL 105.00 CK# 8228

White - Health Department Yellow - Engineer Pink - Building & Safety

Form A Updated: 5/10

JUN 19 2014

D

Lincoln-Lancaster County Health Department
Environmental Public Health Division
3140 "N" Street • Lincoln, NE 68510-1514
Phone: 402-441-8022

Permit Number: HS0006067

Onsite Wastewater Treatment System 4th Mod

As Built Plans & Specifications Stevens Creek Ridge Block 1

Date 6/16/2014 Legal Description SE 1/4 17 1/4 Section 10N Township Range 8E Range Lot 2

Onsite System Location

Address (no rural route) 1970 N. 129th St City Lincoln NE, Zip 68527

Owner Steven Schwartzkopf Address 1924 Sawyer St Lincoln, NE 68506

A. Sewer Pipe

1. Material: SDR26 Plastic
   Diameter: 4 in.
2. Distance above basement floor: _____ in.
   or distance below basement floor: 16 in.
3. Distance between dwelling and septic tank: 70 ft.
4. Number of clean-outs: one
5. Distances to: well or suction line 100 ft.
   stream 100 ft.
   pressure line 100 ft.
   property line 50 ft.

B. Septic Tank

☑ Label with Manufacturer, address and gallon capacity

1. Material: Concrete
   Number of compartments: one
2. Capacity: 1500 gal.
3. Factory built: ☑ Yes ☐ No
4. Manholes: Over inlet, diameter 24 in.
   Over outlet, diameter 24 in.
   Riser: ☐ above ☐ below grade NT in.
5. Inlet: ☑ baffle ☐ tee ☐ 6" dia. inspection pipe
6. Outlet: ☑ baffle ☐ tee ☐ 6" dia. inspection pipe
7. Depth to top of tank, below unfinished grade: 18-12 in.
8. Distances to: Well or suction line 100 ft.
   Stream 100 ft.
   Pressure line 100 ft.
   Property line 100 ft.

C. ☐ Distribution Box ☑ Drop Boxes

(≥ 12" inspection opening) (removable lid to inspect)

1. Material: End caps, Plastic
   Number available outlets: 2 per cap
2. Factory built: ☑ Yes ☐ No
3. Distance from septic tank: 19-14 ft.


D. Drainfield Absorption

☑ Trench ☐ Bed ☐ Level Bottom


1. Type: ☐ Half rounds ☐ Perforated pipe ☐ Chambers
   Diameter or width: _____
   Number of distribution lines in bed _____
   Material: ☐ fiberglass ☑ plastic ☐ concrete
   ☐ other _____
2. Drainfield Laterals: Number 2
   Length of each line: 125 ft. 125 ft.
   _____ ft. _____ ft., _____ ft.
3. Drainfield dimensions: Width 40 ft.
   Distribution Pipe Slope 2" Drop in/100 ft.
   Average depth 22-24 in
4. Filter material: Soil
   Depth of material 22-24 in.
5. Distances to: Well or suction line 100 ft.
   Pressure line 100 ft.
   Property line 50 ft.
   House or building 70 ft.
   Lake or Stream 100 ft.

Complete As-Built drawing on the back fo this form.

Onsite Wastewater System Design (Example)

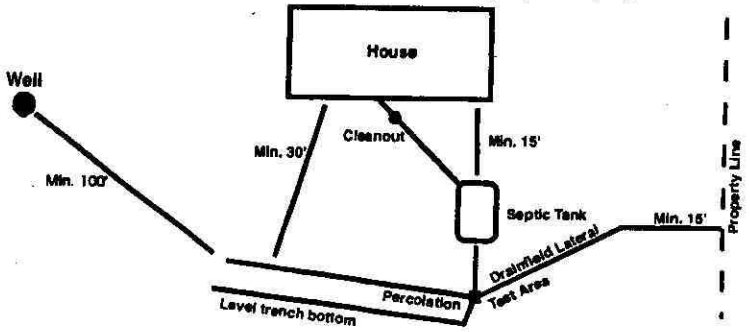

Indicate North with Arrow

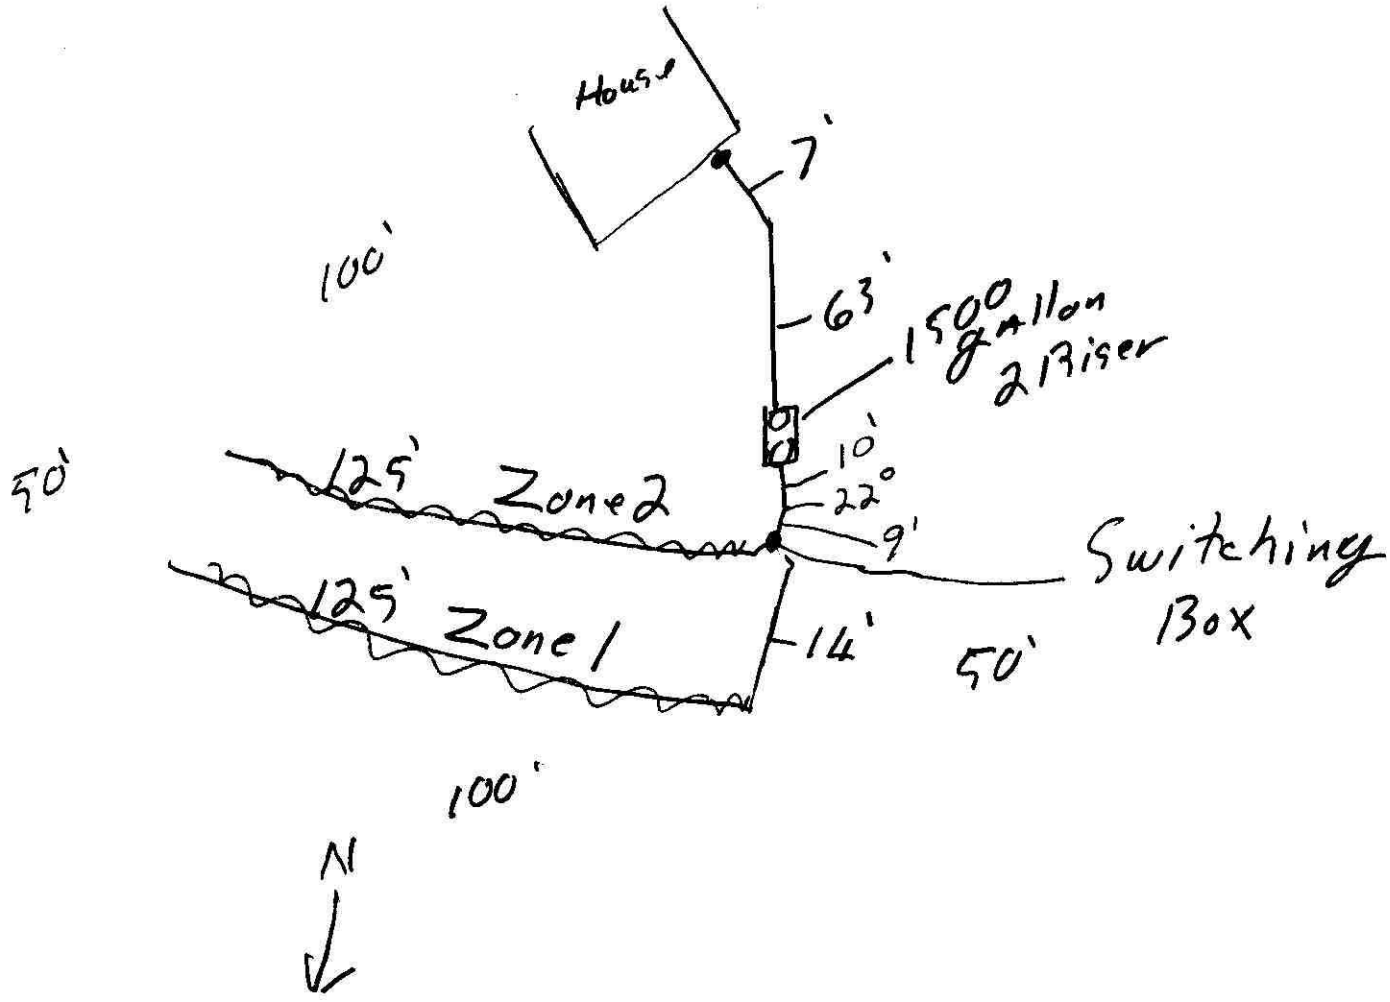

6/16/2014

Raymond Contracting, Inc.
Lloyd J Jakoubek
13800 NW 70th St
Raymond, NE 68428
402-783-2663
