SCANNED

Lincoln-Lancaster County Health Department
Environmental Public Health Division
3140 N Street • Lincoln NE 68510-1514
Phone: 402-441-8643

A

Permit Number
HS001020

Onsite Wastewater Treatment System Request for Site Clearance and Permit

Fees paid

Include Form B and C. Submit correct fee with this Application

3 acres or more required for: ☒ Septic System ☒ Lagoon ☐ Other (Refer to Form C)

The undersigned hereby requests site clearance and permit to construct a Wastewater Treatment System in conformance with appropriate regulations.

PLEASE PRINT OR TYPE

A. Onsite System Location

Address 14122 Brush Creek Place (no rural route) City Roca NE Zip 68430

Legal Description 9 8 7 Brush Creek Estates Lot 11 & 12
1/4 1/4 Section Township Range Subdivison Addition Block Lot

Geographical Location (if known): Lat/Long: PID 1509-301-011-000 & 15-09-301-012-000

B. Owner

Name Joey Haussmann Signature NA

Address 14301 Brush Creek Pl City/State/Zip Roca Ne 68430

Home Phone Work Phone 438-3230

C. Certified Installer

Name: Kurt T Virgil Signature

Address 1620 W Mary Lucia Ln City/State/Zip Lincoln, Ne, 68528

Work Phone 402-525-6601

D. Engineer

☐ Check and complete if engineer designed system P.E. License Number:

Designer Name Firm Work Phone

E. This system will serve a

☒ Residential Dwelling Number of Bedrooms 8 Is there a Whirlpool Bathtub? ☒ Yes ☐ No Total Acres 6.02

☐ Commercial Establishment/Other Facility Specify Design flow in gallons per day

Type of Wastewater ☐ Domestic ☐ Non-Domestic Well Permit Applied for ☐ Yes ☐ No ☐ Not Applicable

DO NOT WRITE BELOW THIS LINE

Approval Process ☐ Municipal Code 24.38 ☐ County Resolution No. 02-30

1. Health Department
Site visits
Date rec'd 1/20/15
Date frwd 1/20/15
ACTION ☒ Approved ☐ Disapproved
Signature

2. Supt. Bldg. Insp. or Village Clerk
Comments
Date rec'd
Date frwd
ACTION ☒ Approved ☐ Disapproved
Signature

3. City or County Engineer
Comments
Date rec'd
Date frwd
ACTION ☒ Approved ☐ Disapproved
Signature

Installation Final Written Approval
By
Date 10/12/15

Business Office Use Only
Date Received 1-16-15 Amount Paid $375.00
Received By SB Cash/Check No. 14905

White - Health Department Yellow - Engineer Pink - Building & Safety

Form A Updated: 5/10

Nate C. Hartman

From: Ken D. Schroeder
Sent: Tuesday, January 20, 2015 3:43 PM
To: Nate C. Hartman
Cc: Pamela L. Dingman
Subject: sewage disposal system for PID #15 09 301 001 000 & #15 09 301 012 000
Attachments: part of sec 9-8-7.pdf

Nate,
Lancaster County Engineering Department indicates approval for a sewage disposal system for lot 11 (14122 Brush Creek Place) and lot 12, "BRUSH CREEK ESTATES" located in the S 1/2 of Section 9, T8N, R7E of the 6th P.M., Lancaster County, Nebraska. *(see attached part of sec 9-8-7)*
As always, subject to confirmation of and compliance with any floodplain elevation requirements prior to construction.
Ken

Kenneth D. Schroeder, RLS
Lancaster County Surveyor
444 Cherrycreek Road, Bldg. "C"
Lincoln, Nebraska 68528
kschroeder@lancaster.ne.gov
Phone (402) 441-7681
Fax (402) 441-8692


LOT 19
25.00 ± Ac. Total
24.93 ± Ac. Net
#2007-25613
#2011-33214
NO SURVEY
LOT 16
18.52 ± Ac.
#71-15648
#79-1267
#79-1268
#89-3119
#94-23393
#95-42773
#2006-51260
#2006-51288
NO SURVEY
LOT 17
39.48 ± Ac.
#71-15648
#79-1267
#79-1268
#89-3119
#94-23393
#95-42773
#2006-51260
#2006-51288
14122 Brush Creek Place
LOT 20
61.79 ± Ac. Total
61.09 ± Ac. Net
DEED BOOK #546, Pgs 229-230
#84-14834
#87-37619
#85-4299
#89-16008
#2001-2176
#2007-25613
#2011-43642
#2012-43101
#2012-47060
NO SURVEY
LOT 18
34.19 ± Ac. Total
33.26 ± Ac. Net
#71-15648
#79-1268
#83-279
#91-32644
#92-55349
#92-56940
#92-56941
#93-799
#93-800
#93-801
#2006-51288
COUNTY ROAD #445
S 54th St
BRUSH CREEK PLACE
OUTLOT "A"
BRUSH
CREEK
ESTATES
1ST ADD.
ESTATES 2
OUTLOT "A"
COUNTY ROAD #585
Wittstruck Rd
LOT 6
3.28
± Ac.
Sec. 9 (8-7)


Nate C. Hartman

From: Todd A. Stutzman
Sent: Tuesday, January 20, 2015 2:00 PM
To: Nate C. Hartman
Subject: 14122 Brush Creek Pl

Nate,

Brush Creek Estates lots 1& 12, 14122 Brush Creek Pl . Is a buildable lot

Todd

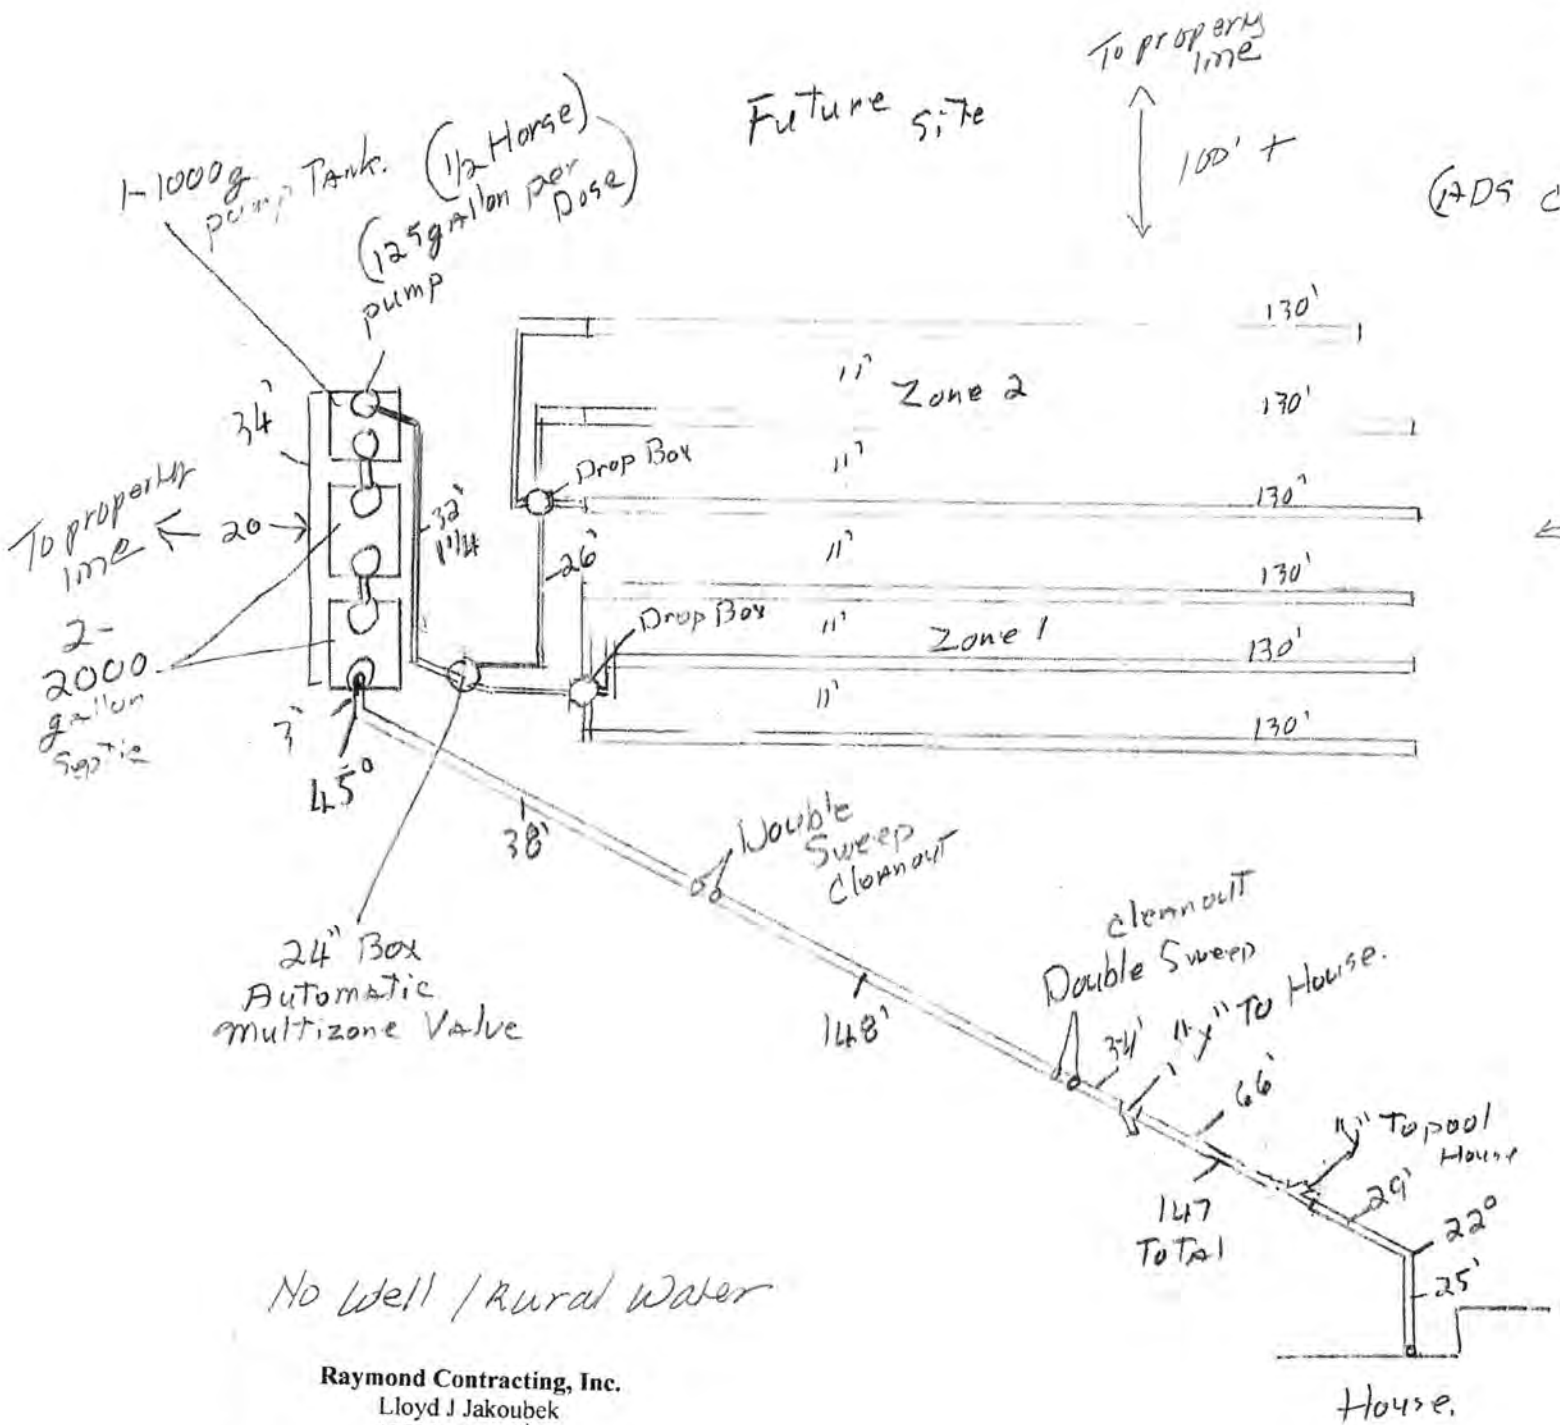

No Well / Rural Water

Raymond Contracting, Inc.
Lloyd J Jakoubek
13800 NW 70th St
Raymond, NE 68428
402-783-2663

Lincoln-Lancaster County Health Department (LLCHD)
Environmental Public Health Division
3140 "N" Street • Lincoln, NE 68510-1514
Phone: 402-441-8022

B

Permit Number:

Onsite Wastewater Treatment System
Soil Evaluation Report

PLEASE PRINT OR TYPE

Onsite System Location

Address 14122 Brush Creek Place (no rural route) City Roca NE, Zip 68430

Owner Joe Hausmann Address 14301 Brush Creek Pl, Roca, NE 68430

Date of Tests 8/31/15 to 9/1/15 Weather: Precipitation 0 Temperature 84°

Percolation Test Data Table

A.	B.	C.	D.	E.	F.	G.	H.	Water Level Drop I.	J.	K.	L.	M.	N.
		Saturation/Swelling Time				Last 30 mins of 4 hr or last 10 mins of 1 hr					Results		
		Start		End		Start		Initial	End				
Hole No.	Hole Depth (in)	Date (Mo/Da)	Time (Hr/Min)	Date (Mo/Da)	Time (Hr/Min)	Date (Mo/Da)	Time (Hr/Min)	Water Lev (in.)	Date (Mo/Da)	Time (Hr/Min)	Elapsed Time Interval	Water Level Drop (in)	Percolation Rates (Min/in = mpi)
1	26	8/31	11:30a	8/31	3:30p	9/1	12:30p	6	9/1	1:00p	30	5/8	48
2	21	"	"	"	"	"	"	6	"	"	"	1-5/8	18
3	39	"	"	"	"	"	"	6	"	"	"	2-1/16	15
4	22	"	"	"	"	"	"	6	"	"	"	1/2	60
5	35	"	"	"	"	"	"	6	"	"	"	1-5/8	18
6	26	"	"	"	"	"	"	6	"	"	"	5/8	48
								6					
								6					

Person Conducting Percolation Test

Name: Terri L Jakoubek, Raymond Contracting, Inc.
Phone: 402-783-2663 or 402-890-6009
Address 13800 NW 70th St
Raymond, NE 68428 Cert #1198

Sum of Percolation Rates: 207
Average of Rates: 35
Rate Used for Calculation: 60 (20 mpi variance)

Soil type (NRCS Maps/Other) Wymore Silty Clay Loam
Groundwater Depth >8.5'

DO NOT WRITE BELOW THIS LINE

Reviewing Action

Comments (Soil type, groundwater, floodplain, etc.)

Signature of Reviewing Official Date

"Quality Pumps Since 1939"

Product information presented here reflects conditions at time of publication. Consult factory regarding discrepancies or inconsistencies.

SECTION: 3.20.175
FM1732
1204
Supersedes
0603

MAIL TO: P.O. BOX 16347 • Louisville, KY 40256-0347
SHIP TO: 3649 Cane Run Road • Louisville, KY 40211-1961
(502) 778-2731 • 1 (800) 928-PUMP • FAX (502) 774-3624

visit our web site:
www.zoeller.com

ZOELLER ON-SITE WASTEWATER PRODUCTS

ZOELLER SEPTIC SYSTEM ACCESSORIES

Automatic Multizone Valves

The Zoeller 4000 Series distribution valve offers an easy, reliable and economical way to automate multiple zoned residential and small commercial disposal fields. The simplicity of design ensures ease of maintenance and long service life. These patented valves are ideally suited for pump fed applications using reclaimed or dirty water.


The Zoeller 6000 Series is the foundation of distributing valves. Patented for its ability to manifold multiple zones with only one moving part, this valve offers exceptional reliability and durability under dirty water conditions. With its metal die cast body, the 6000 Series valve is capable of high pressure applications and is recommended for use on pump fed systems.



4000 Series



6000 Series

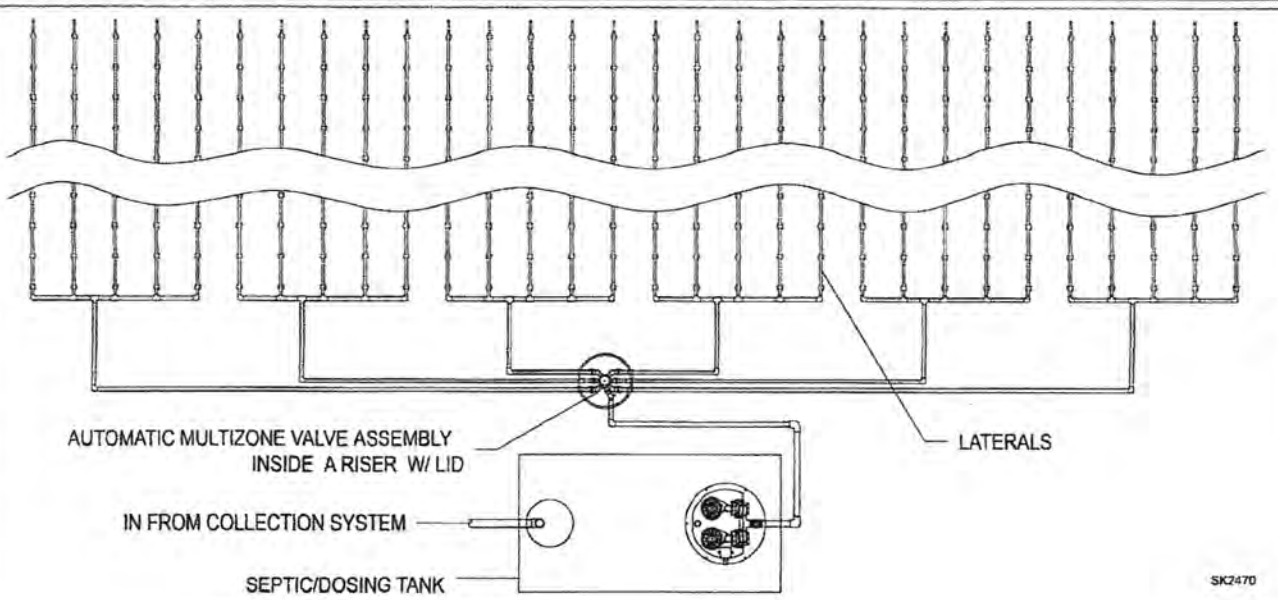

© Copyright 2004 Zoeller Co. All rights reserved.

4000 & 6000 Automatic Multizone Valves

SPECIFICATIONS	4000 SERIES	6000 SERIES
Flow Range: (Minimum flow of 10 gpm for the 4000 Series and 15 gpm for the 6000 Series must be maintained in order for the valve to index properly.)	4 Outlet Valve: 10 - 50 GPM 6 Outlet Valve: 10 - 40 GPM	4 Outlet Valve: 15 - 150 GPM 6 Outlet Valve: 15 - 150 GPM
Pressure Rating:	2½ - 75 PSI	2½ - 150 PSI
Pressure Loss - 4 Outlet Valve:	Flow (GPM): 10 20 30 40 50 PSI Loss: 2.0 3.0 4.5 6.4 10.0	Flow (GPM): 15 30 60 90 120 150 PSI Loss: 2.0 3.0 5.0 9.0 11.0 13.0
Pressure Loss - 6 Outlet Valve:	Flow (GPM): 10 20 30 40 PSI Loss: 2.5 4.5 7.5 11.5	Flow (GPM): 15 30 60 90 120 150 PSI Loss: 2.0 3.5 6.0 10.0 12.0 14.0
Inlet:	Slip and glue connections to 1¼" PVC pipe	Threaded 1½" NPT Connection.
Outlets:	Slip and glue connections. 4 Outlet Valve: To 1¼" PVC Pipe 6 Outlet Valve: To 1" PVC Pipe	Slip and glue connections to 1½" PVC Pipe.
Construction:	High strength noncorrosive ABS polymer.	Die Cast Metal Housing High strength noncorrosive ABS Polymer Outlets
Dimensions:	Height: 5¾" Width: 5¾"	Height: 7" Width: 8"

4000 SERIES:

4 Outlet Models

P/N 170-0064	Model 4402 - For 2 Zone operation.
P/N 170-0065	Model 4403 - For 3 Zone operation.
P/N 170-0066	Model 4404 - For 4 Zone operation.

6 Outlet Models

P/N 170-0067	Model 4605 - For 5 Zone operation.
P/N 170-0068	Model 4606 - For 6 Zone operation.

6000 SERIES:

4 Outlet Models

P/N 170-0069	Model 6402 - For 2 Zone operation.
P/N 170-0070	Model 6403 - For 3 Zone operation.
P/N 170-0071	Model 6404 - For 4 Zone operation.

6 Outlet Models


P/N 170-0072	Model 6605 - For 5 Zone operation.
P/N 170-0073	Model 6606 - For 6 Zone operation.

New Automatic Multizone Valve Assemblies

Featuring 6000 Series Automatic Multizone Valves


- Easy to install -
  Slip ends are ready to glue.
- Easy to maintain -
  Unions allow for simple removal. Shutoff ball valve included.
- Convenient to test -
  Clear PVC "Windows" indicate current flow path instantly.
- Compact -
  Assemblies fit easily in a Zoeller 30" Deluxe Riser.


P/N 5053-0001	2 Outlet Multizone Assembly.
P/N 5053-0002	3 Outlet Multizone Assembly.
P/N 5053-0003	4 Outlet Multizone Assembly.
P/N 5053-0004	5 Outlet Multizone Assembly.
P/N 5053-0005	6 Outlet Multizone Assembly.



6 Outlet Multizone Valve Assembly Shown

SK2489





6" Clear PVC Pipe

P/N 170-0074	(4) 1¼" Dia. Pieces For 4400 2-4 Zone.	P/N 170-0076	(4) 1½" Dia. Pieces For 6400 2-4 Zone.
P/N 170-0075	(6) 1" Dia. Pieces For 4600 5-6 Zone.	P/N 170-0077	(6) 1½" Dia. Pieces For 6600 5-6 Zone.

ALL ZOELLER ON-SITE WASTEWATER PRODUCTS MUST BE INSTALLED IN ACCORDANCE WITH LOCAL AND/OR STATE PLUMBING AND/OR HEALTH DEPARTMENT CODES.

© Copyright 2004 Zoeller Co. All rights reserved.

Lincoln-Lancaster County Health Department
Environmental Public Health Division
3140 N Street • Lincoln NE 68510-1514
Phone: 402-441-8643

D Exhibit 4

Permit Number:

Onsite Wastewater Treatment System
As-Built Description and Drawing

Type of Onsite Wastewater System: ☐ Lagoon (Skip to Back Page) ☒ Subsurface Septic ☐ Mound

Onsite Wastewater System Location

15-09-301-011-000

Address or Legal Description or Parcel Identification Number (PID) 14122 Brush Creek Pl, Roca, NE 68430

Owner: Jay Hasselmann Address 14301 Brush Creek Pl Roca, NE 68430

A. Wastewater Piping

1. Material: SDR 26 Diameter: 4 in.
2. Distance between dwelling and septic tank: 336 ft.

B. Septic Tank

1. Material Concrete
2. Capacity: 2-2000 1-1000 pump
3. Depth to top of tank, below unfinished grade: 24" in.
4. Distance to:
   Well 100+ ft.
   Pressure line 100+ ft
   Property Line 20+ ft.
   Foundation 300+ ft.

C Distribution Box or Drop Box

Distance and Direction from septic tank: 32' ft. South East

D. Drainfield/Absorption Field

☒ Trench ☐ Bed

1. Type: ☐ Perforated Pipe ☑ Chamberless ☐ Other
   Material brand and inside width of Chamberless: ADS 29"
2. Number of Laterals: 6 All→130
3. Length of each lateral (linear): ft. ft. 2-Zones Dosed
   ft. ft.
4. Drainfield size: 2831 sq. ft.
5. Distance to:
   Well 100+ ft.
   Pressure line 100 ft.
   Property line 30 ft.
   Depth of Groundwater 24"-48"

Was the Onsite Wastewater System covered prior to LLCHD inspection? ☒ Yes ☐ No (partial)

If Yes, the Certified Professional must sign below for final approval:

I swear and affirm that the system complies with Lincoln Municipal Code (LMC) 24.38 and/or County Resolution R-13-0062 requirements and that the information and documentation submitted are true and accurate.

Certified Professional Signature: Kevin L Johnson Date: 10/12/15

Complete As-Built drawing on the back of this form.

Lincoln-Lancaster County Health Department
Environmental Public Health Division
3140 N Street • Lincoln NE 68510-1514
Phone: 402-441-8643

A

Permit Number
HS001020

Onsite Wastewater Treatment System
Request for Site Clearance and Permit

Include Form B and C. Submit correct fee with this Application

3 acres or more required for: ☐ Septic System ☒ Lagoon ☐ Other (Refer to Form C)

The undersigned hereby requests site clearance and permit to construct a Wastewater Treatment System in conformance with appropriate regulations.

PLEASE PRINT OR TYPE

A. Onsite System Location

Address 14122 Brush Creek Place (no rural route) City Roca NE Zip 68430

Legal Description _____ Brush Creek Estates Lot 11 & 12

1/4 1/4 Section Township Range Subdivison Addition Block Lot

Geographical Location (if known): Lat/Long: _____ PID 1509-301-011-000 & 15-09-301-012-000

B. Owner

Name Joey Hausmann Signature NA

Address 14201 Brush Creek Pl City/State/Zip Roca Ne 68430

Home Phone _____ Work Phone 438-3230

C. Certified Installer

Name: Kurt T Virgil Signature _____

Address 1620 W Mary Lucia Ln City/State/Zip Lincoln, Ne, 68528

Work Phone 402-525-6601

D. Engineer

☐ Check and complete if engineer designed system P.E. License Number: _____

Designer Name _____ Firm _____ Work Phone _____

E. This system will serve a

☒ Residential Dwelling Number of Bedrooms 8 Is there a Whirlpool Bathtub? ☒ Yes ☐ No Total Acres 6.02

☐ Commercial Establishment/Other Facility Specify _____ Design flow in gallons per day _____

Type of Wastewater ☐ Domestic ☐ Non-Domestic Well Permit Applied for ☐ Yes ☐ No ☐ Not Applicable

DO NOT WRITE BELOW THIS LINE

Approval Process ☐ Municipal Code 24.38 ☐ County Resolution No. 02-30

1. Health Department
Site visits _____
Date rec'd _____ Date frwd _____
ACTION ☐ Approved ☐ Disapproved
Signature _____

2. Supt. Bldg. Insp. or Village Clerk
Comments _____
Date rec'd _____ Date frwd _____
ACTION ☐ Approved ☐ Disapproved
Signature _____

3. City or County Engineer
Comments _____
Date rec'd _____ Date frwd _____
ACTION ☐ Approved ☐ Disapproved
Signature _____

Installation Final Written Approval
By _____
Date _____

Business Office Use Only
Date Received 1-16-15 Amount Paid $375.00
Received By SB Cash/Check No. 14905

White - Health Department Yellow - Engineer Pink - Building & Safety

Form A Updated: 5/10

Lincoln-Lancaster County Health Department (LLCHD)
Environmental Public Health Division
3140 "N" Street • Lincoln, NE 68510-1514
Phone: 402-441-8022

B

Permit Number: HS 001020

Onsite Wastewater Treatment System

Soil Evaluation Report

late winter

PLEASE PRINT OR TYPE Will perc in SPRING after ground thaw

Onsite System Location

Address _____ (no rural route) City _____ NE, Zip _____

Owner _____ Address _____

Date of Tests _____ to _____ Weather: Precipitation _____ Temperature _____

Percolation Test Data Table

A.	B.	C. D. E. F. Saturation/Swelling Time				G. H. I. J. K. Water Level Drop Last 30 mins of 4 hr or last 10 mins of 1 hr					L. M. N. Results		
		Start		End		Start		Initial	End				
Hole No.	Hole Depth (in)	Date (Mo/Da)	Time (Hr/Min)	Date (Mo/Da)	Time (Hr/Min)	Date (Mo/Da)	Time (Hr/Min)	Water Lev (in.)	Date (Mo/Da)	Time (Hr/Min)	Elapsed Time Interval	Water Level Drop (in)	Percolation Rates (Min/in = mpi)
								6					
								6					
								6					
								6					
								6					
								6					
								6					
								6					
								6					

Person Conducting Percolation Test

Name: _____

Phone: _____

Address _____

_____

Soil type (NRCS Maps/Other) _____

Groundwater Depth _____

Sum of Percolation Rates: _____

Average of Rates: _____

Rate Used for Calculation: _____

DO NOT WRITE BELOW THIS LINE

Reviewing Action

Comments (Soil type, groundwater, floodplain, etc.) _____

_____

_____

_____

_____

Signature of Reviewing Official _____ Date _____

Lincoln-Lancaster County Health Department
Environmental Public Health Division
3140 "N" Street • Lincoln, NE 68510-1514
Phone: 402-441-8022


C

Permit Number: HS001020

Onsite Wastewater Treatment System

Preliminary Plan Specifications

Draw a plot plan showing onsite system sewer lines, drop of distribution boxes, tank, drainfields, percolation test holes, well, residence, direction of groundwater flow, property lines, and reserve area for replacement onsite system.

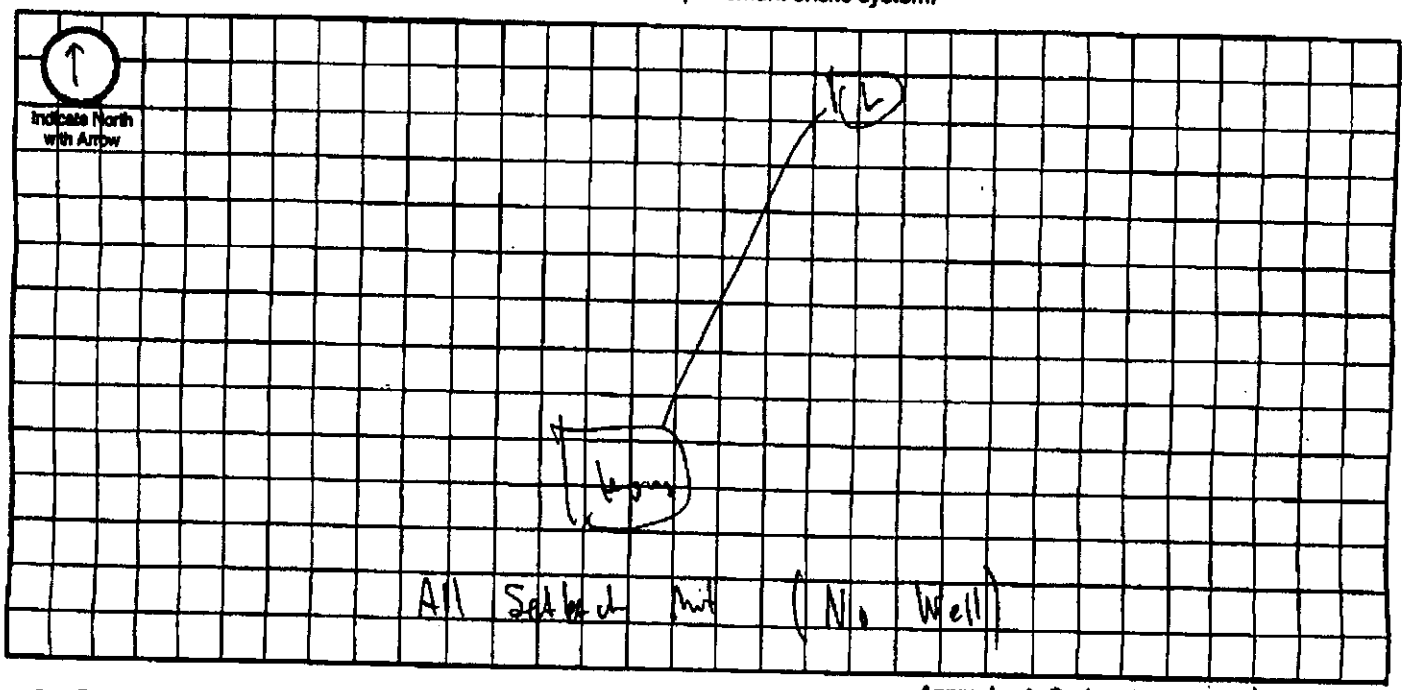

Approximate Scale: 10 ft. = 1 grid line/s

A. Onsite System Location

Address (no rural route) 14132 Brush Creek Est. City Roca NE, Zip 68430

B. Proposed Septic Tank/s

Septic Tank Cap._____ gals Tank Material: ☐ Concrete ☐ Plastic ☐ Other_____ ☐ Lagoon(Max. seepage 1/8" per day)

C. Reserve Area for Replacement Onsite System

☐ Drainfield Absorption Area (percolation test required) ☑ Lagoon

D. Drainfield Absorption System

Percolation Rate____ (min/inch = mpi) No. of Bedrooms_____ Soil Type_____ Land Slope_____%

☐ Trench ☐ Bed ☐ Non-Standard (engineer designed and NDEQ approved Total Square feet of drainfield_____sq.ft.

Total length of laterals_____ Type of distribution: ☐ Perforated pipe ☐ Half-Round ☐ Chamber ☐ Other

No. of absorption trenches_____ Width_____ No. of drop boxes_____ Distrubtion Box_____

No. of absorption beds_____ Width_____ No of Distribution lines per bed_____

E. Setbacks Check the Boxes Below if the Required Setback has been Satisfied

Distance From	Private Well	Public Well	Surface Water	Gound Water	Pressure Water Lines	Property Lines	Foundations Yours	Foundations Neighbors	All Other Setbacks
Tank (ft)	50 ☐	500 ☐	50 ☐	NA ☐	25 ☐	20 ☐	15 ☐	25 ☐	☐
Field (ft)	100 ☐	500 ☐	50 ☐	4 ☐	30 ☐	20 ☐	30 ☐	40 ☐	☐
Lagoon (ft)	100 ☑	500 ☑	50 ☑	N/A ☑	30 ☑	50 ☐	100 ☑	200 ☑	☐

F. Required Signatures

Home Building Contractor_____ Date_____

Installer_____ Date 1-12-15

Onsite Form C 12_08

Lincoln-Lancaster County Health Department
Environmental Public Health Division (402) 441-8027
3140 N Street Lincoln, Nebraska 68510-1514

ON-SITE WASTE WATER SYSTEM
CONSTRUCTION - INSTALLATION PERMIT
No. HS001020

System Type: Lagoon

Situs: 14122 BRUSH CREEK PLACE, RURAL NE

Issued: 1/21/2015

Expires: 1/21/2016

Description: BRUSH CREEK ESTATES, Lot 11

Owner: HAUSMANN, JOEY & REBECCA
14301 BRUSH CREEK PL
ROCA, NE 68430

Judith A Halstead
Judith A. Halstead, MS, Health Director

Dear Applicant:

The above document is your permit to construct a new On-site Waste Water System at the location listed. Please contact this office once the sytem is complete in order to schedule a final inspection before use.

Judith A Halstead
Judith A. Halstead, MS
Health Director

HAUSMANN & SONS CONSTRUCTION
8545 EXECUTIVE WOODS DR SUITE 1
LINCOLN, NE 68512

Lincoln-Lancaster County Health Department
Environmental Public Health Division
3140 N Street • Lincoln NE 68510-1514
Phone: 402-441-8643

Exhibit 5

Permit Number: H500 to 20

Onsite Wastewater Treatment System

Inspection Sheet

Date 10/12/15 Legal Description Brush Creek Est Lot 3 11a R
¼ ¼ Section/Township/Range

Onsite System Location

Address (no rural route) 1472 Brush Creek Pl City Roca

Owner Hartmann Address

Mark One: ☒ Dwelling ☐ Non-dwelling

☒ New System ☐ Alteration [☐ Tank Only ☐ Trench Only] ☐ Lateral Only

☐ Temporary modification (Describe problem causing discharge and reason for temporary modification): _____

Drainfield Absorption System:

☒ Lateral ☐ Bed ☐ Non-standard (engineer-designed and NDEQ approved) ☐ Holding Tank ☐ Trench

Total square feet of drainfield [redacted] Sq. Ft. Tank Size 2000 x 2 gals w/ 1000 gal pump/Dose

Total length of laterals 780 2827.5 Type of Distribution: ☒ Chamber ☐ Perforated Pipe ☐ Other (describe)_____

No. of Absorption Laterals 7 Width 3 No. of Drop Boxes 0 Distribution Box 3 N/O

Leveling Method Used Level

Setbacks (Check the Boxes Below if the Required Setback has been Satisfied):

Distance From	Private Well	Public Well	Surface Water	Ground water	Pressure Water Lines	Property Lines
Tank (ft)	50 ☒	500 ☒	50 ☒	NA ☒	10 ☒	5 ☒
Field (ft)	100 ☒	500 ☒	50 ☒	4 ☒	25 ☒	5 ☒

Geographical Coordinates to 6 Decimals:

Tank_____

Lateral #1_____ N/O Lateral #3_____

Lateral #2_____ Lateral #4_____

Comments:
Partial Inspection, some covered see Sketch for Real Info

Inspections prior to Final Approval
Initial DH Date 10/12/15

Follow-Up_____ Date _____

Follow-Up_____ Date _____

Installation Final Written Approval
By _____

Date 10/12/15

Field Note Drawing (See Reverse Side):
