AUG 19 2015

Lincoln-Lancaster County Health Department
Environmental Public Health Division
3140 N Street • Lincoln NE 68510-1514
Phone: 402-441-8643

A

Permit Number
HS001120

Onsite Wastewater Treatment System
Request for Site Clearance and Permit

Include Form B and C. Submit correct fee with this Application

3 acres or more required for: ☒ Septic System ☐ Lagoon ☐ Other (Refer to Form C)

The undersigned hereby requests site clearance and permit to construct a Wastewater Treatment System in conformance with appropriate regulations.

PLEASE PRINT OR TYPE

A. Onsite System Location

Address 5000 W Sumner Cir (no rural route) City Lincoln, NE Zip 68522

Legal Description NW (1/4) 1/4 31 (Section) 10N (Township) 6E (Range) High Ridge West Acres (Subdivison) 1 (Addition) 1 (Block) (Lot)

PID 10-31-101-001-000

B. Owner

Name Gregory & Shauna Byelick Signature Shauna J Byelick

Address 5000 W Sumner Cir City/State/Zip Lincoln, NE 68522

Home Phone 402-580-6453 (Shauna) Work Phone 402-580-6503 (Greg)

C. Certified Installer

Name: Lloyd Jakoubek, Raymond Contracting Inc Signature

Address 13800 NW 70th St City/State/Zip Raymond, NE 68428

Work Phone 402-890-6009 or 402-783-2663

D. Engineer

☐ **Check and complete if engineer designed system** P.E. License Number:

Designer Name Firm Work Phone

E. This system will serve a

☒ Residential Dwelling Number of Bedrooms 3 Whirlpool Bathtub? ☐ Yes ☒ No Total Acres 3.35

Garbage Grinder? ☒ Yes ☐ No

☐ Commercial Establishment/Other Facility Specify Design flow in gallons per day

Type of Wastewater ☐ Domestic ☐ Non-Domestic

DO NOT WRITE BELOW THIS LINE

Approval Process ☐ Municipal Code 24.38 ☐ County Resolution No. 02-30

1. Health Department
Site visits
Comments
Date rec'd
Date frwd
ACTION ☐ Approved ☐ Disapproved
Signature

2. Supt. Bldg. Insp. or Village Clerk
Comments
Date rec'd
Date frwd
ACTION ☐ Approved ☐ Disapproved
Signature

3. City or County Engineer
Comments
Date rec'd
Date frwd
ACTION ☐ Approved ☐ Disapproved
Signature

Installation Final Written Approval
By
Date

Business Office Use Only
Date Received 8-19-15 Amount Paid $375.00
Received By SB Cash/Check No. 8714

White - Health Department Yellow - Engineer Pink - Building & Safety

Form A Updated: 1/13

Lincoln-Lancaster County Health Department (LLCHD)
Environmental Public Health Division
3140 "N" Street • Lincoln, NE 68510-1514
Phone: 402-441-8022

B

Permit Number: HS001120

Onsite Wastewater Treatment System

Soil Evaluation Report

PLEASE PRINT OR TYPE

Onsite System Location

Address 5000 W Sumner Cir (no rural route) City Lincoln NE, Zip 68522

Owner Greg & Shauna Byelick Address Same

Date of Tests 7/8/15 to 7/9/15 Weather: Precipitation 0 Temperature 78°

Percolation Test Data Table

A.	B.	C.	D.	E.	F.	G.	H.	I.	J.	K.	L.	M.	N.
		Saturation/Swelling Time				Water Level Drop Last 30 mins of 4 hr or last 10 mins of 1 hr					Results		
		Start		End		Start		Initial	End				
Hole No.	Hole Depth (in)	Date (Mo/Da)	Time (Hr/Min)	Date (Mo/Da)	Time (Hr/Min)	Date (Mo/Da)	Time (Hr/Min)	Water Lev (in.)	Date (Mo/Da)	Time (Hr/Min)	Elapsed Time Interval	Water Level Drop (in)	Percolation Rates (Min/in = mpi)
1	27	7/8	9:00a	7/8	1:00p	7/9	12:15p	6	7/9	12:45p	30	1/2	60
2	25	"	"	"	"	"	"	6	"	"	"	9/16	53
3	27	"	"	"	"	"	"	6	"	"	"	3/4	48
								6					
								6					
								6					
								6					
								6					

Person Conducting Percolation Test

Name: Terri L Jakoubek, Raymond Contracting, Inc.

Phone: 402-783-2663 or 402-890-6009

Address 13800 NW 70th St

Raymond, NE 68428 Cert #1198

Sum of Percolation Rates: 161

Average of Rates: 54

Rate Used for Calculation: 54

Soil type (NRCS Maps/Other) SCL

Groundwater Depth >7'

DO NOT WRITE BELOW THIS LINE

Reviewing Action

Comments (Soil type, groundwater, floodplain, etc.) _____

Signature of Reviewing Official _____ Date _____

Lincoln-Lancaster County Health Department
Environmental Public Health Division
3140 "N" Street • Lincoln, NE 68510-1514
Phone: 402-441-8022


C

Permit Number: HS00 1120

Onsite Wastewater Treatment System

Preliminary Plan Specifications

Draw a plot plan showing onsite system sewer lines, drop of distribution boxes, tank, drainfields, percolation test holes, well, residence, direction of groundwater flow, property lines, and reserve area for replacement onsite system.

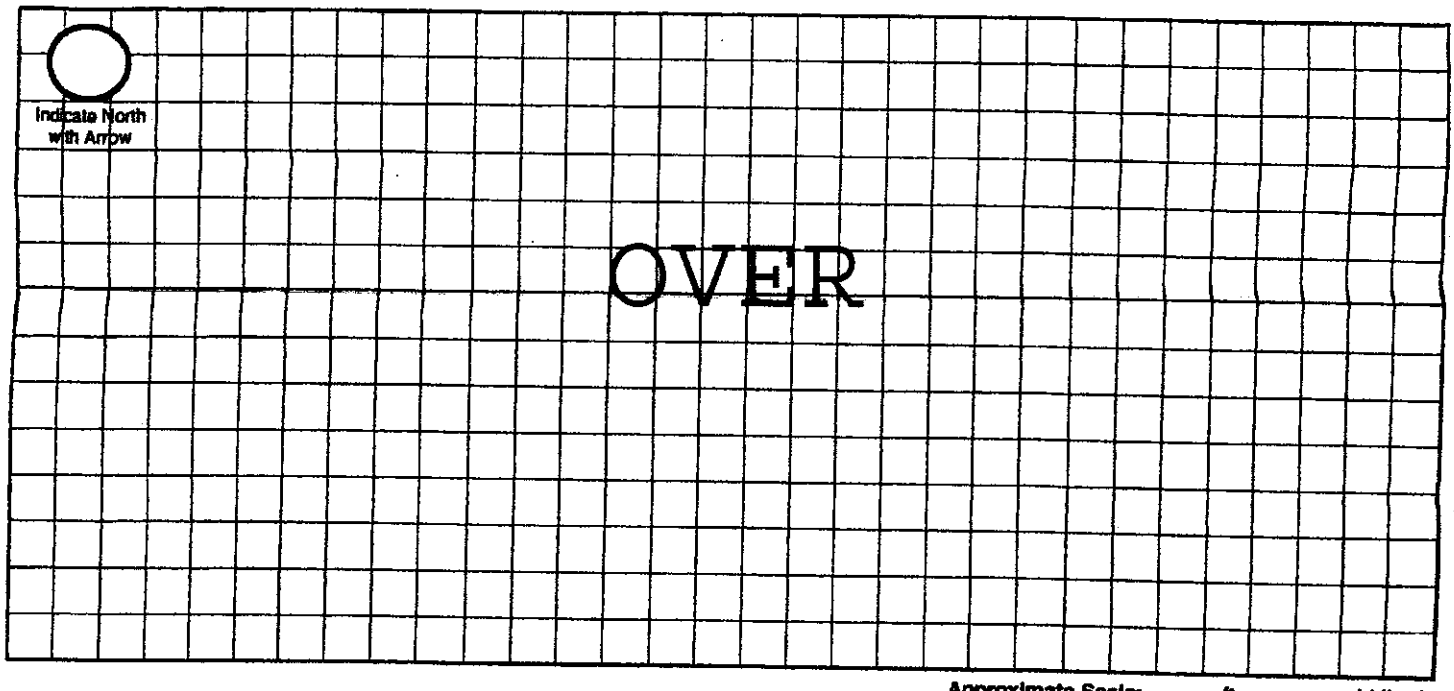

Approximate Scale: _____ft. = _____ grid line/s

A. Onsite System Location

Address (no rural route) 5000 W Sumner Cir City Lincoln NE, Zip 68522

B. Proposed Septic Tank/s

Septic Tank Cap. 1,500 gals Tank Material: ☒ Concrete ☐ Plastic ☐ Other_____ ☐ Lagoon(Max. seepage 1/8" per day)

C. Reserve Area for Replacement Onsite System

☐ Drainfield Absorption Area (percoloation test required) ☒ Lagoon

D. Drainfield Absorption System

Percolation Rate 54 (min/inch = mpi) No. of Bedrooms 3 Soil Type Silt Loam/Silty Clay Loam Land Slope 2-6 %

☒ Trench ☐ Bed ☐ Non-Standard (engineer designed and NDEQ approved Total Square feet of drainfield 1,060 sq.ft.

Total length of laterals 265 Type of distribution: ☐ Perforated pipe ☐ Half-Round ☒ Chamber ☐ Other

No. of absorption trenches 3 Width 40" No. of drop boxes_____ Distrubtion Box 1

No. of absorption beds_____ Width_____ No of Distribution lines per bed_____


E. Setbacks Check the Boxes Below if the Required Setback has been Satisfied

Distance From	Private Well	Public Well	Surface Water	Gound Water	Pressure Water Lines	Property Lines	Foundations Yours	Foundations Neighbors	All Other Setbacks
Tank (ft)	50 ☒	500 ☒	50 ☒	NA ☒	25 ☒	20 ☒	15 ☒	25 ☒	☒
Field (ft)	100 ☒	500 ☒	50 ☒	4 ☒	30 ☒	20 ☒	30 ☒	40 ☒	☒
Lagoon (ft)	100 ☐	500 ☐	50 ☐	N/A ☐	30 ☐	50 ☐	100 ☐	200 ☐	☐

F. Required Signatures

Home Building Contractor EXISTING Date _____

Installer [signature] Date 8/7/2015

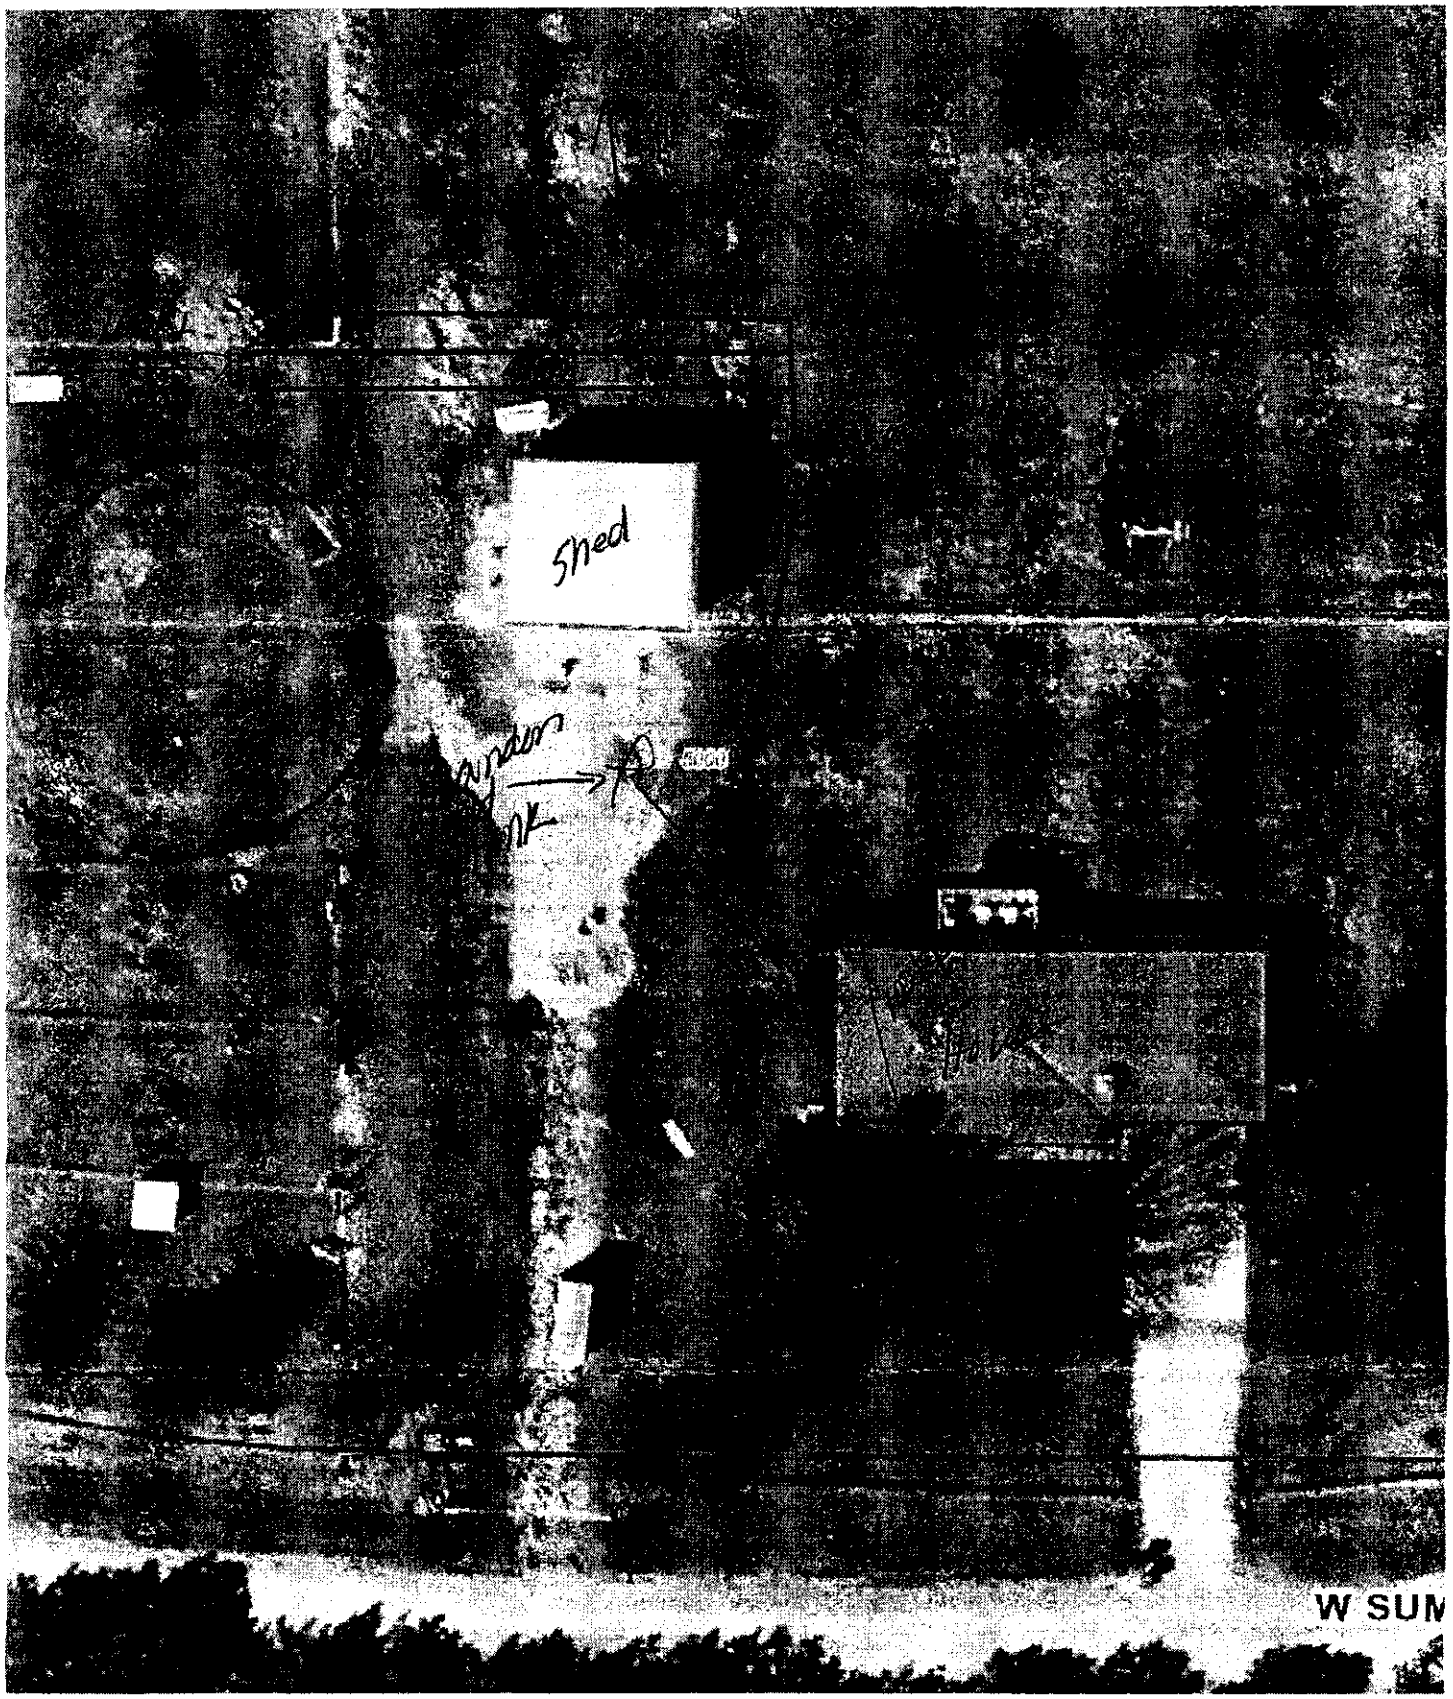

Lancaster County/City of Lincoln GIS Map

N
W E
S

Printed: Aug 06, 2015

5600 W Summer Cir Lincoln, NE 68522

DISCLAIMER: The information is presented on a best-efforts basis, and should not be relied upon for making financial, survey, legal or other commitments. If you have questions or comments regarding the data displayed on this map, please email ags@lincoln.ne.gov and you will be directed to the appropriate department.

Lincoln-Lancaster County Health Department
Environmental Public Health Division (402) 441-8027
3140 N Street Lincoln, Nebraska 68510-1514

ON-SITE WASTE WATER SYSTEM
CONSTRUCTION - INSTALLATION PERMIT
No. HS001120

System Type: Standard

Situs: 5000 W SUMNER CIR, RURAL, NE

Issued: 8/21/2015

Expires: 8/21/2016

Description: HIGH RIDGE WEST ACRES, BLOCK 1, Lot 1

Owner: BYELICK, GREGORY C & SHAUNA L
5000 W SUMNER CIR
LINCOLN, NE 68522

Judith A Halstead
Judith A. Halstead, MS, Health Director

Dear Applicant:

The above document is your permit to construct a new On-site Waste Water System at the location listed. Please contact this office once the sytem is complete in order to schedule a final inspection before use.

Judith A Halstead
Judith A. Halstead, MS
Health Director

RAYMOND CONTRACTING
13800 NW 70TH ST
RAYMOND, NE 68428

Lincoln-Lancaster County Health Department
Environmental Public Health Division
3140 N Street • Lincoln NE 68510-1514
Phone: 402-441-8643

Exhibit 5

Permit Number: HS001120

Onsite Wastewater Treatment System

Inspection Sheet

Date 9/25/15 Legal Description ¼ ¼ 31/10/6 Section/Township/Range BLK 1 LOT 1

Onsite System Location

Address (no rural route) 5000 N. Sumner City

Owner Address

Mark One: ❑ Dwelling ❑ Non-dwelling

☒ New System ❑ Alteration [❑ Tank Only ❑ Trench Only] ❑ Lateral Only

❑ Temporary modification (Describe problem causing discharge and reason for temporary modification):

Drainfield Absorption System:

☒ Lateral ❑ Bed ❑ Non-standard (engineer-designed and NDEQ approved) ❑ Holding Tank ❑ Trench

Total square feet of drainfield 1,060 Sq. Ft. Tank Size 1,500 gals

Total length of laterals 290' Type of Distribution: ☒ Chamber ❑ Perforated Pipe ❑ Other (describe)

No. of Absorption Laterals 3 Width 3.66 factor No. of Drop Boxes 0 Distribution Box 1

Leveling Method Used Laser

Setbacks (Check the Boxes Below if the Required Setback has been Satisfied):

Distance From	Private Well	Public Well	Surface Water	Ground water	Pressure Water Lines	Property Lines
Tank (ft)	50 ☒	500 ☒	50 ☒	NA ☒	10 ☒	5 ☒
Field (ft)	100 ☒	500 ☒	50 ☒	4 ☒	25 ☒	5 ☒

Geographical Coordinates to 6 Decimals:

Tank 1,500

Lateral #1 Lateral #3

Lateral #2 Lateral #4

Comments:

Inspections prior to Final Approval
Initial DC Date 9/15/15

Follow-Up Date

Follow-Up Date

Installation Final Written Approval
By Doug Ahlman
Date 9/25/15

Field Note Drawing (See Reverse Side):
