Lincoln-Lancaster County Health Department
Environmental Public Health Division
3140 N Street • Lincoln NE 68510-1514
Phone: 402-441-8643

A

Permit Number HS001519

Existing Shed

Onsite Wastewater Treatment System
Request for Site Clearance and Permit

Include Form B and C. Submit correct fee with this Application

3 acres or more required for: ☒ Septic System ☐ Lagoon ☐ Other (Refer to Form C)

The undersigned hereby requests site clearance and permit to construct a Wastewater Treatment System in conformance with appropriate regulations.

PLEASE PRINT OR TYPE

A. Onsite System Location

Address 7700 W Waverly Rd (no rural route) City Malcolm, NE Zip 68402

Legal Description SW 11 11N 5E 7
(1/4 | 1/4 | Section | Township | Range | Subdivison | Addition | Block | Lot)

PID 05-11-300-007-000

B. Owner

Name Terry & Jeri Maxson Signature Jeri Maxson

Address 7700 W Waverly Rd City/State/Zip Malcolm

Home Phone 402-802-4955 Work Phone

C. Certified Installer

Name: Lloyd Jakoubek, Raymond Contracting Inc Signature

Address 13800 NW 70th St City/State/Zip Raymond, NE 68428

Work Phone 402-890-6009 or 402-783-2663

D. Engineer

☐ Check and complete if engineer designed system P.E. License Number:

Designer Name Firm Work Phone

E. This system will serve a

☐ Residential Dwelling Number of Bedrooms Whirlpool Bathtub? ☐ Yes ☐ No Total Acres 8.82
Garbage Grinder? ☐ Yes ☐ No

☒ Commercial Establishment/Other Facility Specify Shed with Restroom Design flow in gallons per day <100

Type of Wastewater ☒ Domestic ☐ Non-Domestic

DO NOT WRITE BELOW THIS LINE

Approval Process ☐ Municipal Code 24.38 ☐ County Resolution No. 02-30

1. Health Department
Site visits
Comments
Date rec'd
Date frwd
ACTION ☐ Approved ☐ Disapproved
Signature

2. Supt. Bldg. Insp. or Village Clerk
Comments
Date rec'd
Date frwd
ACTION ☐ Approved ☐ Disapproved
Signature

3. City or County Engineer
Comments
Date rec'd
Date frwd
ACTION ☐ Approved ☐ Disapproved
Signature

Installation Final Written Approval
By
Date

Business Office Use Only
Date Received 8-18-14 Amount Paid 395.00
Received By LC Cash/Check No. cc

7152

White - Health Department Yellow - Engineer Pink - Building & Safety

Form A Updated: 1/13

Lincoln-Lancaster County Health Department (LLCHD)
Environmental Public Health Division
3140 "N" Street • Lincoln, NE 68510-1514
Phone: 402-441-8022

B

Permit Number:

Onsite Wastewater Treatment System
Soil Evaluation Report

PLEASE PRINT OR TYPE

Onsite System Location

Address 7700 W Waverly Rd (no rural route) City Malcolm NE, Zip 68402

Owner Terry & Jeri Maxson Address Same

Date of Tests 8/1/17 to 8/2/17 Weather: Precipitation 0 Temperature 87 °

Percolation Test Data Table

A.	B.	C.	D.	E.	F.	G.	H.	I.	J.	K.	L.	M.	N.
		Saturation/Swelling Time				Water Level Drop Last 30 mins of 4 hr or last 10 mins of 1 hr					Results		
		Start		End		Start		Initial	End				
Hole No.	Hole Depth (in)	Date (Mo/Da)	Time (Hr/Min)	Date (Mo/Da)	Time (Hr/Min)	Date (Mo/Da)	Time (Hr/Min)	Water Lev (in.)	Date (Mo/Da)	Time (Hr/Min)	Elapsed Time Interval	Water Level Drop (in)	Percolation Rates (Min/in = mpi)
1	26	8/1	1:00p	8/1	4:00p	8/2	4:30p	6	8/2	5:00p	30	1/2	60
2	24	"	"	"	"	"	"	6	"	"	"	9/16	53
3	24	"	"	"	"	"	"	6	"	"	"	1/2	60
								6					
								6					
								6					
								6					
								6					

Person Conducting Percolation Test

Name: Terri L Jakoubek, Raymond Contracting, Inc.
Phone: 402-783-2663 or 402-890-6009
Address 13800 NW 70th St
Raymond, NE 68428 Cert #1198

Sum of Percolation Rates: 173
Average of Rates: 58
Rate Used for Calculation: 58

Soil type (NRCS Maps/Other) Yutan SCL / Ponsarem SCL
Groundwater Depth >8'

DO NOT WRITE BELOW THIS LINE

Reviewing Action

Comments (Soil type, groundwater, floodplain, etc.)

Signature of Reviewing Official Date

Lincoln-Lancaster County Health Department
Environmental Public Health Division
3140 "N" Street • Lincoln, NE 68510-1514
Phone: 402-441-8022


C

Permit Number:

Onsite Wastewater Treatment System

Preliminary Plan Specifications

Draw a plot plan showing onsite system sewer lines, drop of distribution boxes, tank, drainfields, percolation test holes, well, residence, direction of groundwater flow, property lines, and reserve area for replacement onsite system.

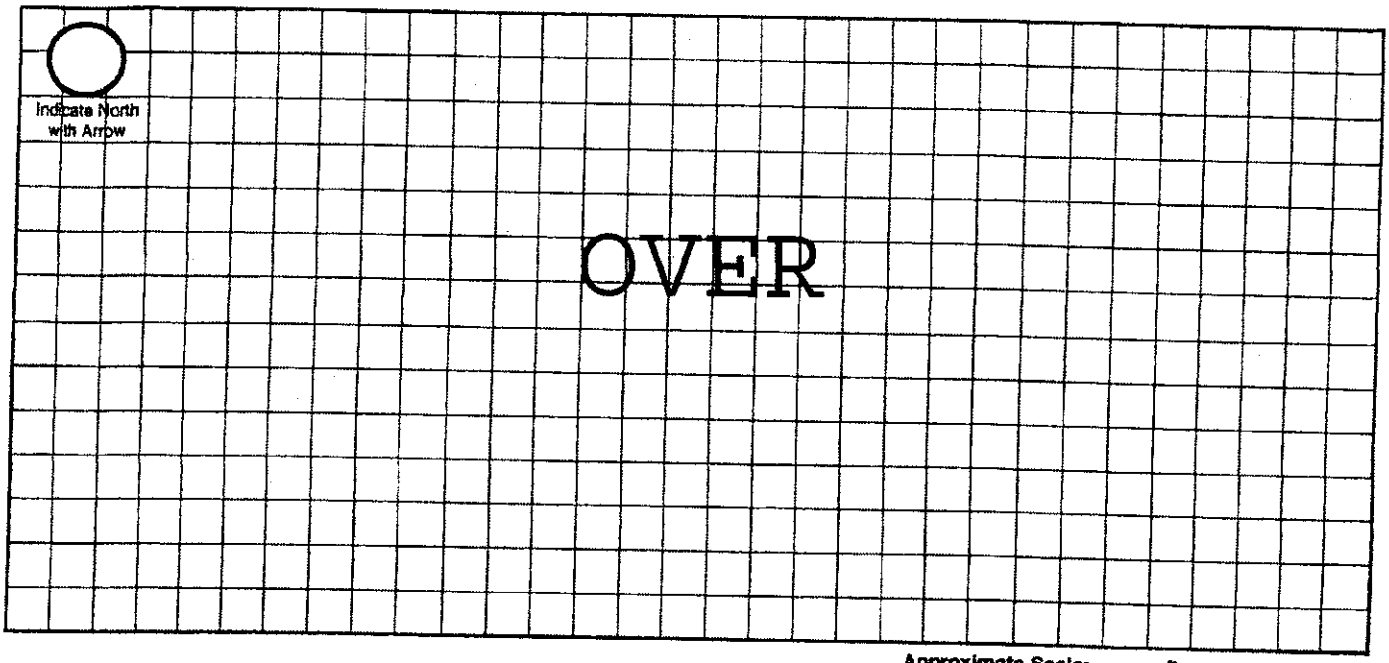

Approximate Scale: _____ ft. = _____ grid line/s

A. Onsite System Location

Address (no rural route) 7700 W Waverly Rd City Malcolm NE, Zip 68402

B. Proposed Septic Tank/s

Septic Tank Cap. 1,000 gals Tank Material: ☒ Concrete ☐ Plastic ☐ Other_____ ☐ Lagoon(Max. seepage 1/8" per day)

C. Reserve Area for Replacement Onsite System

☐ Drainfield Absorption Area (percolation test required) ☒ Lagoon

D. Drainfield Absorption System (Shed with restroom)

Percolation Rate 58 (min/inch = mpi) No. of Bedrooms N/A Soil Type Aksarben SCL Land Slope_____%

☒ Trench ☐ Bed ☐ Non-Standard (engineer designed and NDEQ approved Total Square feet of drainfield 450 sq.ft.

Total length of laterals 100' Type of distribution: ☐ Perforated pipe ☐ Half-Round ☐ Chamber ☒ Other EZFlow 1203H

No. of absorption trenches_____ Width 40" No. of drop boxes 1 Distrubtion Box_____

No. of absorption beds_____ Width_____ No of Distribution lines per bed_____


E. Setbacks Check the Boxes Below if the Required Setback has been Satisfied

Distance From	Private Well	Public Well	Surface Water	Gound Water	Pressure Water Lines	Property Lines	Foundations Yours	Foundations Neighbors	All Other Setbacks
Tank (ft)	50 ☒	500 ☒	50 ☒	NA ☒	25 ☒	20 ☒	15 ☒	25 ☒	☒
Field (ft)	100 ☒	500 ☒	50 ☒	4 ☒	30 ☒	20 ☒	30 ☒	40 ☒	☒
Lagoon (ft)	100 ☐	500 ☐	50 ☐	N/A ☐	30 ☐	50 ☐	100 ☐	200 ☐	☐

F. Required Signatures

Home Building Contractor Existing Shed Date_____

Installer Ronald L. Jakowbek Date 8/17/17

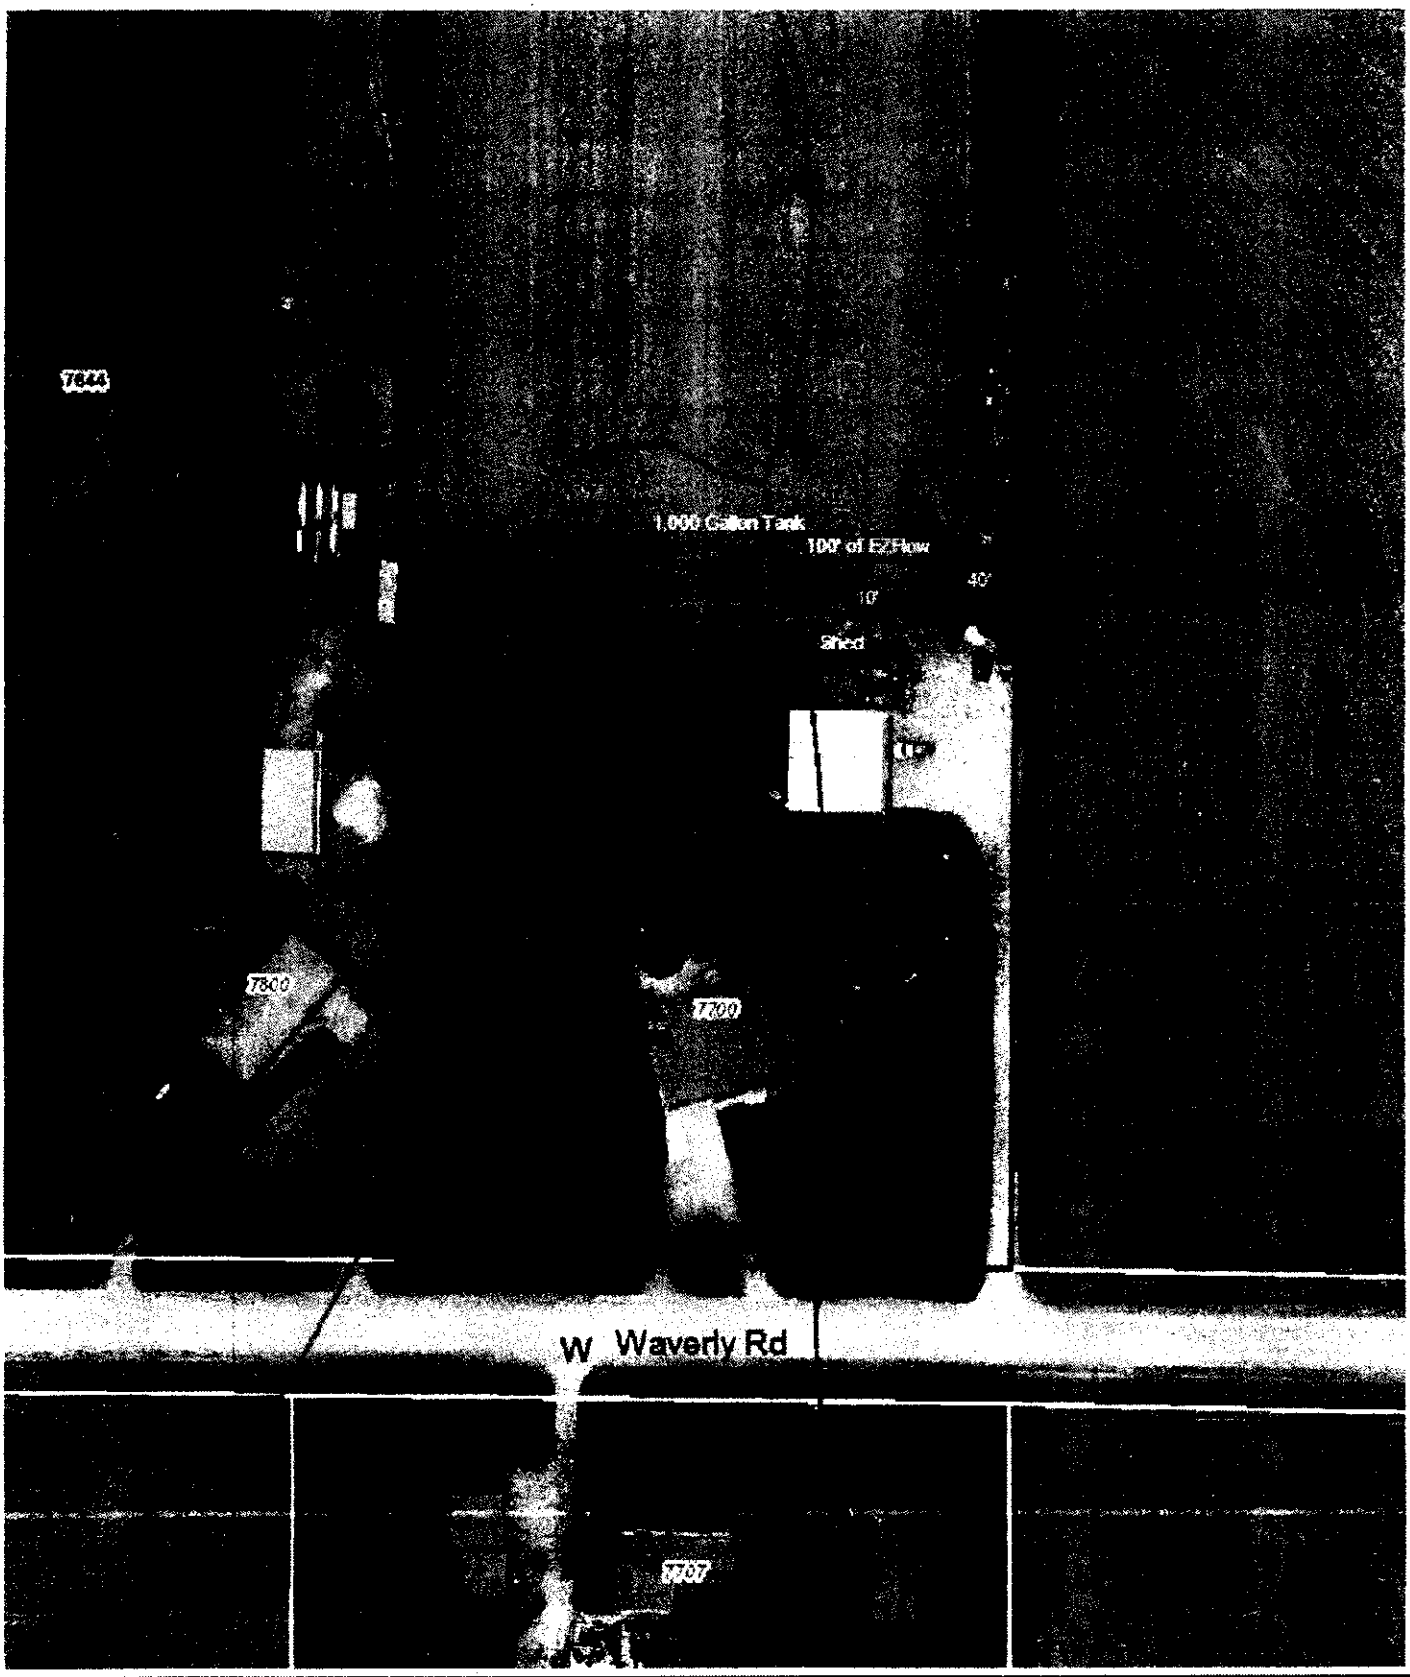

Lancaster County/City of Lincoln GIS Map

Terry & Jeri Maxson 7700 W Waverly Rd, Malcolm, NE 68402

N
W E
S

Printed: Aug 17, 2017

DISCLAIMER: The information is presented on a best-efforts basis, and should not be relied upon for making financial, survey, legal or other commitments. If you have questions or comments regarding the data displayed on this map, please email ags@lincoln.ne.gov and you will be directed to the appropriate department.

Lincoln-Lancaster County Health Department
Environmental Public Health Division (402) 441-8027
3140 N Street Lincoln, Nebraska 68510-1514

ON-SITE WASTE WATER SYSTEM
CONSTRUCTION - INSTALLATION PERMIT
No. HS001519

System Type: Standard

Situs: 7700 W WAVERLY RD, RURAL, NE

Issued: 8/18/2017

Expires: 8/18/2018

Description: S11, T11, R5, 6th Principal Meridian, LOT 7 SW

Owner: MAXSON, TERRY E & JERI L
7700 W WAVERLY RD
MALCOLM, NE 68402

Charlotte Burke, MS, RD, Interim Health Director

Dear Applicant:

The above document is your permit to construct a new On-site Waste Water System at the location listed. Please contact this office once the sytem is complete in order to schedule a final inspection before use.

Charlotte Burke, MS, RD
Interim Health Director

RAYMOND CONTRACTING INC
13800 NW 70 ST
RAYMOND, NE 68428
