H5001561

Application to Alter or Repair an Onsite Wastewater Treatment System

The applicant is applying for a permit to: ☐**ALTER** ☐**REPAIR** an existing Onsite Wastewater Treatment System, and agrees to comply with LMC 24.38 or County Resolution 02-0030.

1. **Street Address (No Rural Route):** 2005 112th Lincoln NE, 68508

   Legal Description of Property: Township: 10 Range: 8 Section: 30

   Block _____ Lot 49 SubDivsion 6th Principal Meridian Add: _____

   ***Parcel ID** 23 - 30 - 200 - 005 - 000 (i.e. 99-99-999-999-999)

2. **Property use:** ■ Residential ☐ Commercial ☐ Other use (Describe: _____)
   Number of bedrooms 3 Does the system have a: ☐ Garbage Grinder ☐ Large Capacity Tub

3. **Type of Present Individual Disposal System** ■ septic system ☐ lagoon ☐ other

4. **Description of proposed alteration or repair:** Add 00 ft. of laterals to acomidate with Title 124 Standards.

5. **Current Type of Lateral-** Chamber **Current Linear Ft. Of Lateral -** 100'

   Current Tank Gallonage- 1000

6. Print Name Steven Lewis Address 4810 w. Claire Ave Lincoln NE, 68523 Phone: (402) 310-9160

   Applicant Signature: _____

Please contact LLCHD for the current permit fee for this application
Fee must be included before the application will be processed. Incomplete information will delay processing.

HEALTH DEPARTMENT USE ONLY

☐Municipal Code 24.38 ☐County Resolution Number 02-30

Date received ____/____/____ REVIEW: ☐ Approved ☐ Disapproved By: _____

Comments (if any): _____

Site visits
Date ____/____/____ By _____
Date ____/____/____ By _____

Installation final written approval
Date ____/____/____ By _____

Return application to:

Lincoln-Lancaster County Health Department
Environmental Public Health Division
3140 "N" Street, Lincoln, NE 68510
Phone: (402) 441-8643

Business Office Use Only

Received: Date: 11/1/17 Amount 220.00 Check No. 8651 Initials LC

Revised 4/8/13

Lincoln-Lancaster County Health Department (LLCHD)
Environmental Public Health Division
3140 "N" Street • Lincoln, NE 68510-1514
Phone: 402-441-8022

B

Permit Number:

Onsite Wastewater Treatment System
Soil Evaluation Report

PLEASE PRINT OR TYPE

Onsite System Location

Address 200 s. 112th Street (no rural route) City Lincoln NE, Zip 68508

Owner Jack & Karen Chlupek Address 6301 Normal Blvd #316, Lincoln, NE 68506

Date of Tests 10-30-17 to 10-31-17 Weather: Precipitation Ø none Temperature 34°

Percolation Test Data Table

A.	B.	C.	D.	E.	F.	G.	H.	I.	J.	K.	L.	M.	N.
		Saturation/Swelling Time				Water Level Drop Last 30 mins of 4 hr or last 10 mins of 1 hr					Results		
		Start		End		Start			End				
Hole No.	Hole Depth (in)	Date (Mo/Da)	Time (Hr/Min)	Date (Mo/Da)	Time (Hr/Min)	Date (Mo/Da)	Time (Hr/Min)	Initial Water Lev (in.)	Date (Mo/Da)	Time (Hr/Min)	Elapsed Time Interval	Water Level Drop (in)	Percolation Rates (Min/in = mpi)
1	12"-14"	10/30	9:30	10/31	10:30	10/31	10:30	6	10/31	11:00	30	.5	60
2	"	"	"	"	"	"	"	6	"	"	"	.5	60
3	"	"	"	"	"	"	"	6	"	"	"	1.5	20
4	"	"	"	"	"	"	"	6	"	"	"	1"	30
5	"	"	"	"	"	"	"	6	"	"	"	1.5	20
								6					
								6					
								6					

Person Conducting Percolation Test

Name: Steven C Lewis
Phone: 402 802 0788
Address 4810 w. Claire Ave.
Lincoln NE. 68523

Sum of Percolation Rates: 5" total
Average of Rates: 1", 30 min
Rate Used for Calculation: 60 min

Soil type (NRCS Maps/Other)

Groundwater Depth

DO NOT WRITE BELOW THIS LINE

Reviewing Action

Comments (Soil type, groundwater, floodplain, etc.)


Signature of Reviewing Official Date

READ THOROUGHLY


DIAGRAM OF PERCOLATION TEST PROCEDURE

Finished Grade or Natural Ground Level

I. Size, Number, and Location or Test Holes
   - A. Dig six or more holes spaced uniformly over proposed lateral field site.
   - B. Scratch smeared spots on sides of hole.
   - C. Remove loose material from hole.
   - D. Add 2" of gravel to hole.

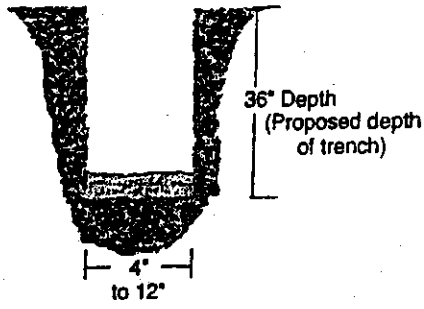


II. Saturation of Soil (Pre-soak)
   - A. Fill hole with 12" or more of water.
   - B. MAINTAIN THIS WATER LEVEL FOR 4 HOURS.
   - C. Record on Form B columns a thru f.

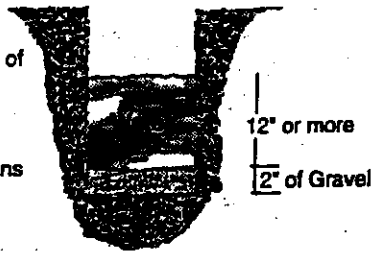


24 Hours Later

III. Percolation-rate Measurement **(refer to instructions 5a, 5b, or 5c.)**
   - A. Add 6" of water.
   - B. Measure from fixed reference point (nail) to water.
   - C. Record measurement and time on front of Form B.

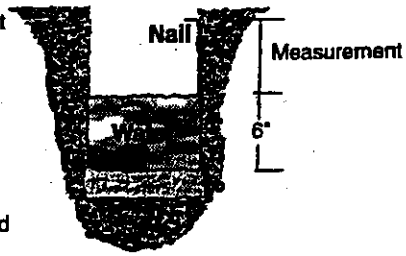

½ hour later
(30 minutes)

   - D. 30 minutes later remeasure and record time.
   - E. If water will be too low for another reading 30 minutes later, adjust to 6" of water and remeasure and record time.

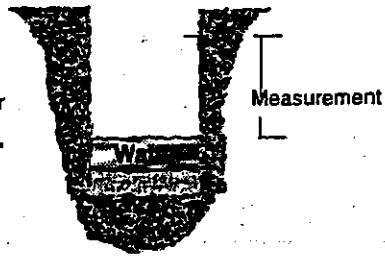

   - F. Continue for 3½ hours taking readings every 30 minutes.
   - G. Last 30 minute reading is used in filling out Form B. Record date, time, intervals and water level drops in column g thru m.

Instructions

1. **Number and location of tests.** Percolation tests shall be made in 6 or more separate test holes which shall be spaced uniformly over the proposed lateral field site.
2. **Type of test hole.** Dig or bore a hole 3 feet deep with a diameter of 4 to 12 inches. (To save time, labor and the volume of water required per test, a 4-inch auger hole is recommended).
3. **Preparation of the test hole.** Scratch or roughen any smeared spots on the sides of the hole with a knife blade or sharp pointed instrument to provide a natural soil interface into which water may percolate. Remove all loose material from the hole. Add 2 inches of gravel to protect the bottom from scouring when water is poured into the hole.
4. **Saturation and swelling of the soil.** Fill the hole with clear water to a depth of 12 inches or more above the gravel and maintain this water level at least 4 hours and preferably overnight. The accuracy and true value of the percolation data depends on thorough saturation and swelling of the soil.
5. **Percolation-rate measurement.** Percolation-rate measurements shall be made 24 hours after starting the saturation and swelling procedure described above. Record results on the front of this form and complete all calculations.
   a. If water remains in the test hole after the overnight swelling period, adjust the depth to approximately 6 inches over the gravel. From a fixed reference point, measure the drop in water level over a 30 minute period to the nearest 1/8 of an inch. This drop is used to calculate the percolation rate.
   b. If no water remains in the test hole after the overnight swelling period, add clear water to bring the depth to approximately 6 inches over the gravel. From a fixed point, measure the drop in water level to the nearest 1/8 of an inch at 30-minute intervals for 4 hours. Refill to the 6 inch level over the gravel as often as necessary. The drop that occurs during the final 30 minutes is used to calculate the percolation rate.
   c. In sandy soils (or other soils in which the first 6 inches of water seeps away in less than 30 minutes after the overnight swelling period) the time interval between measurements shall be 10 minutes instead of 30 minutes and the test run for 1 hour instead of 4 hours. The drop that occurs during the final 10 minutes is used to calculate the percolation rate.
6. **Record the test results and complete all calculations on the front of this form.** The average of the percolation rates calculated for all holes in the last 30 (10) minutes will normally be the rate used for calculations to size the system. ***Exceptions are the use of the greatest percolation rate when rates vary more than 20 min/in between holes or when other soil analysis indicates potential percolation problems.***

LLCHD reserves the right to require additional testing based on knowledge of soil types, percolation tests results on nearby properties, or due to concerns with procedures followed. In some situations, LLCHD staff will require and perform on-site observation of percolation tests.

Lincoln-Lancaster County Health Department
Environmental Public Health Division
3140 "N" Street • Lincoln, NE 68510-1514
Phone: 402-441-8022


C

Permit Number:

Onsite Wastewater Treatment System

Preliminary Plan Specifications

Draw a plot plan showing onsite system sewer lines, drop of distribution boxes, tank, drainfields, percolation test holes, well, residence, direction of groundwater flow, property lines, and reserve area for replacement onsite system.

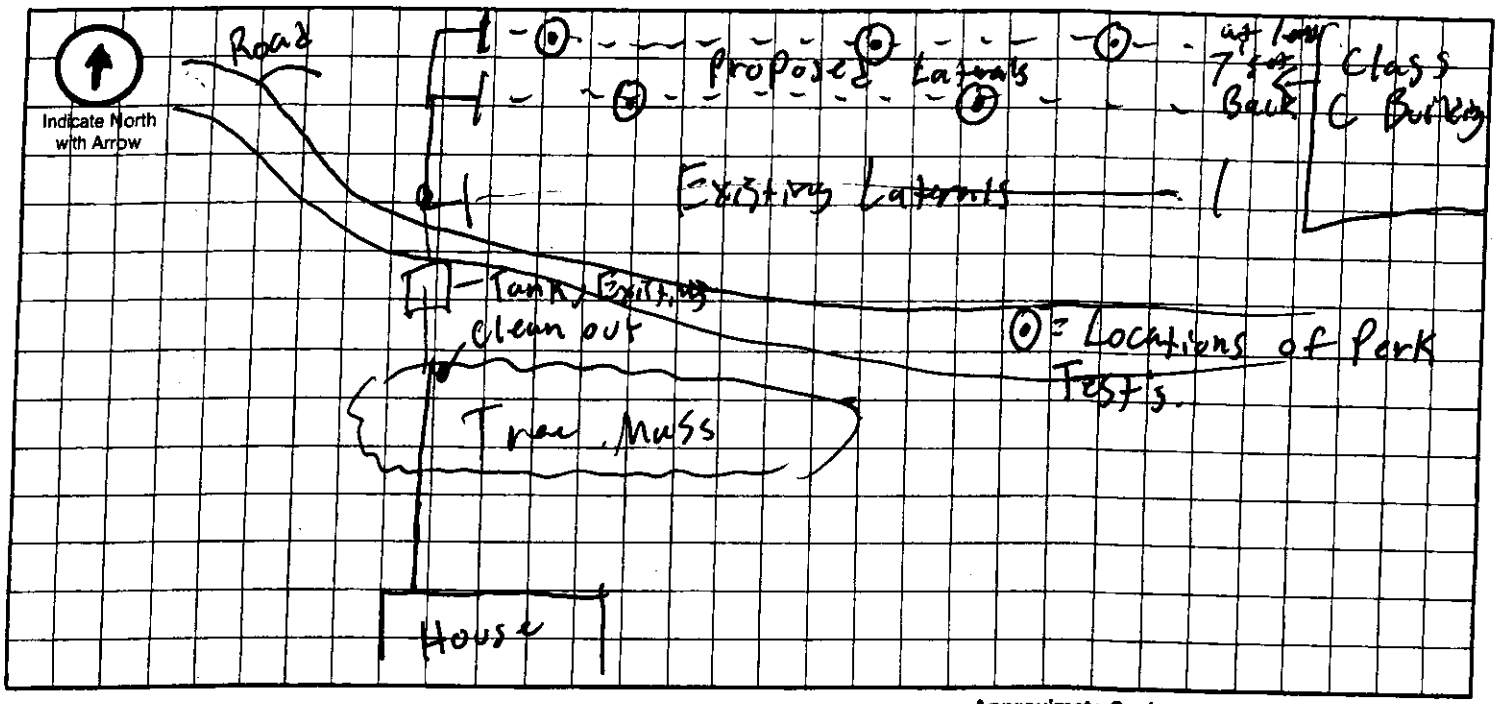

Approximate Scale: _____ ft. = _____ grid line/s

A. Onsite System Location

Address (no rural route) 200 s 112th Street City Lincoln NE, Zip 68508

B. Proposed Septic Tank/s

Septic Tank Cap._____ gals Tank Material: ☐ Concrete ☐ Plastic ☐ Other_____ ☐ Lagoon(Max. seepage 1/8" per day)

C. Reserve Area for Replacement Onsite System

☒ Drainfield Absorption Area (percolation test required) ☐ Lagoon

D. Drainfield Absorption System

Percolation Rate 60 (min/inch = mpi) No. of Bedrooms 3 Soil Type_____ Land Slope ~0 %

☐ Trench ☐ Bed ☐ Non-Standard (engineer designed and NDEQ approved Total Square feet of drainfield_____sq.ft.

Total length of laterals_____ Type of distribution: ☐ Perforated pipe ☐ Half-Round ☐ Chamber ☐ Other

No. of absorption trenches_____ Width_____ No. of drop boxes_____ Distrubtion Box_____

No. of absorption beds_____ Width_____ No of Distribution lines per bed_____

E. Setbacks Check the Boxes Below if the Required Setback has been Satisfied

Distance From	Private Well	Public Well	Surface Water	Gound Water	Pressure Water Lines	Property Lines	Foundations Yours	Foundations Neighbors	All Other Setbacks
Tank (ft)	50 ☐	500 ☐	50 ☐	NA ☐	25 ☒	20 ☒	15 ☒	25 ☐	☐
Field (ft)	100 ☐	500 ☐	50 ☐	4 ☐	30 ☒	20 ☒	30 ☒	40 ☐	☐
Lagoon (ft)	100 ☐	500 ☐	50 ☐	N/A ☐	30 ☐	50 ☐	100 ☐	200 ☐	☐

F. Required Signatures

Home Building Contractor_____ Date_____

Installer_____ Date_____
