Lincoln-Lancaster County Health Department
Environmental Public Health Division (402) 441-8027
3131 O Street Lincoln, Nebraska 68510-1514

ON-SITE WASTE WATER SYSTEM
CONSTRUCTION - INSTALLATION PERMIT
No. HS001891

System Type: Standard

Situs: 5001 W A ST, LINCOLN, NE 68522

Issued: 9/17/2019

Expires: 9/17/2020

Description: S31, T10, R6, 6th Principal Meridian, LOT 10 NW

Owner: ROACH, LESLIE D & CHERYL L
5001 W A ST
LINCOLN, NE 68510

Patricia D. Lopez

Patricia D. Lopez, RN, MSN, Interim Health Director

Dear Applicant:

The above document is your permit to construct a new On-site Waste Water System at the location listed. Please contact this office once the sytem is complete in order to schedule a final inspection before use.

Patricia D. Lopez

Patricia D. Lopez, RN, MSN
Interim Health Director

RAYMOND CONTRACTING INC
13800 NW 70TH ST
RAYMOND, NE 68428

SCANNED

SEP 16 2019

A

Lincoln-Lancaster County Health Department
Environmental Public Health Division
3140 N Street • Lincoln NE 68510-1514
Phone: 402-441-8643

Existing Home

Permit Number
#5001891

Onsite Wastewater Treatment System Request for Site Clearance and Permit

Include Form B and C. Submit correct fee with this Application

3 acres or more required for: ☑ Septic System ☐ Lagoon ☐ Other (Refer to Form C)

The undersigned hereby requests site clearance and permit to construct a Wastewater Treatment System in conformance with appropriate regulations.

PLEASE PRINT OR TYPE

A. Onsite System Location

Address 5001 W A St (no rural route) City Lincoln, NE Zip 68522

Legal Description NW 31 10N 6E 10
1/4 1/4 Section Township Range Subdivison Addition Block Lot

PID 10-31-100-004-000

B. Owner

Name Leslie & Cheryl Roach Signature Leslie Roach Cheryl Roach

Address 5001 W A St City/State/Zip Lincoln, NE 68522

Home Phone 402-429-1225 Work Phone

C. Certified Installer

Name: Lloyd Jakoubek, Raymond Contracting Inc Signature

Address 13800 NW 70th St City/State/Zip Raymond, NE 68428

Work Phone 402-890-6009 or 402-783-2663

D. Engineer

☐ **Check and complete if engineer designed system** P.E. License Number:

Designer Name Firm Work Phone

E. This system will serve a

☑ Residential Dwelling Number of Bedrooms 4 Whirlpool Bathtub? ☐ Yes ☑ No Total Acres 3.16
Garbage Grinder? ☑ Yes ☐ No

☐ Commercial Establishment/Other Facility Specify Design flow in gallons per day

Type of Wastewater ☐ Domestic ☐ Non-Domestic

DO NOT WRITE BELOW THIS LINE

Approval Process ☐ Municipal Code 24.38 ☑ County Resolution No. 02-30

1. Health Department
Site visits
Comments
Date rec'd 9/17/19
Date frwd 9/17/19
ACTION ☑ Approved ☐ Disapproved
Signature

2. Supt. Bldg. Insp. or Village Clerk
Comments
Date rec'd
Date frwd
ACTION ☐ Approved ☐ Disapproved
Signature

3. City or County Engineer
Comments
Date rec'd
Date frwd
ACTION ☐ Approved ☐ Disapproved
Signature

Installation Final Written Approval
By
Date 11/6/19

Business Office Use Only
Date Received 9-16-19 Amount Paid $430.00
Received By JAO Cash/Check No. 9723

White - Health Department Yellow - Engineer Pink - Building & Safety

Form A Updated: 1/13

Nate C. Hartman

From: Terri Jakoubek <jakoubek63@windstream.net>
Sent: Tuesday, November 05, 2019 8:38 PM
To: Nate C. Hartman
Cc: Doug R. Smith
Subject: 5001 W A St D-Sheet
Attachments: 5001 A St D-Sheet.pdf

HS001891 is attached.

Thanks,

Terri Jakoubek
Raymond Contracting, Inc.
13800 NW 70th St
Raymond, NE 68428
402-783-2663 (Office)
402-783-2341 (Fax)
402-890-3870 (Mobile)
jakoubek63@windstream.net

Lincoln-Lancaster County Health Department
Environmental Public Health Division
3140 N Street • Lincoln NE 68510-1514
Phone: 402-441-8643

D Exhibit 4

Permit Number: HS001891

Onsite Wastewater Treatment System
As-Built Description and Drawing

Type of Onsite Wastewater System: ☐ Lagoon (Skip to Back Page) ☒ Subsurface Septic ☐ Mound

Onsite Wastewater System Location PID = 10-31-100-004-000

Address or Legal Description or Parcel Identification Number (PID) 5001 W A St, Lincoln, NE 68522

Owner: Leslie & Cheryl Roach Address Same

A. Wastewater Piping

1. Material: SDR26 Diameter: 4 in.
2. Distance between dwelling and septic tank: 45 ft.

B. Septic Tank

1. Material: Concrete
2. Capacity: 1,500
   Plus a 1,000g pump tank - Lifting effluent to drainfield
3. Depth to top of tank, below unfinished grade: 60 in.
4. Distance to:
   Well 100 ft.+
   Pressure line N/A ft
   Property Line 100 ft.+
   Foundation 45 ft.+

C Distribution Box or Drop Box

Distance and Direction from septic tank: 195 ft. S
(Defuser D-Box)

D. Drainfield/Absorption Field

☒ Trench ☐ Bed

1. Type: ☐ Perforated Pipe ☐ Chamberless ☒ Other
   Material brand and inside width of Chamberless:
   EZFlow 1203H Bundles
2. Number of Laterals: 4
3. Length of each lateral (linear): ft. 80 ft. 80 ft. 80 ft. 80 ft. 80
4. Drainfield size: 1,440 sq. ft.
5. Distance to:
   Well 100 ft.+
   Pressure line N/A ft.
   Property line 30 ft.+
   Depth of Groundwater >10'

2 laterals dropped per approval

Was the Onsite Wastewater System covered prior to LLCHD inspection? ☒ Yes ☐ No
(Partially)


If Yes, the Certified Professional must sign below for final approval:

I swear and affirm that the system complies with Lincoln Municipal Code (LMC) 24.38 and/or County Resolution R-13-0062 requirements and that the information and documentation submitted are true and accurate.

Certified Professional Signature: [signature] Date: 10/30/19

Complete As-Built drawing on the back of this form.

Updated 4/15

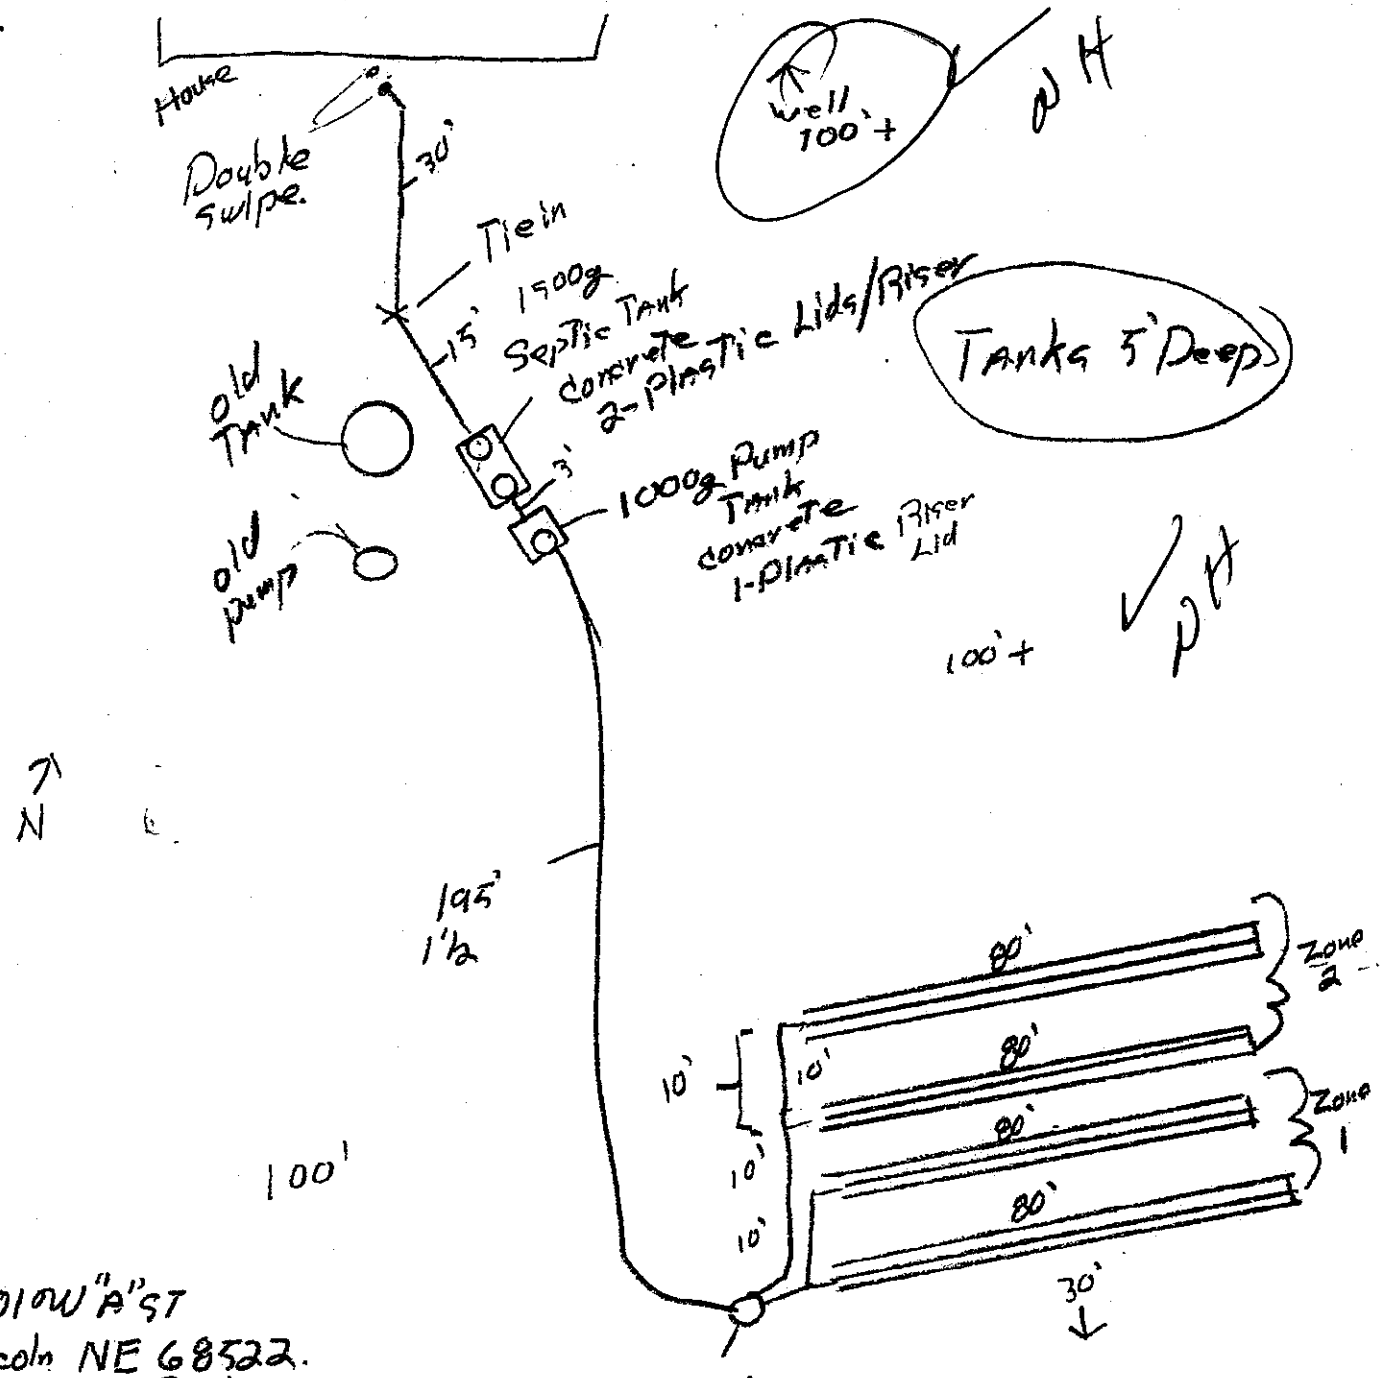

5001 OW "A" ST
Lincoln NE 68522.
Les / Cheryl Roach.
10/30/19

Raymond Contracting, Inc.
Lloyd J Jakoubek
13800 NW 70th St
Raymond, NE 68428
402-783-2663

24" De Fuser Box
D-Box
zone 1 & 2
Controlled by capping the line in the D-Box

Lateral
24"-32" Deep.
