Lincoln-Lancaster County Health Department
Environmental Public Health Division
3140 N Street • Lincoln NE 68510-1514
Phone: 402-441-8643

A

Permit Number
#3001931

Onsite Wastewater Treatment System Permit Application

Include Form B and C. Submit correct fee with this Application

☐ Septic System ☐ Lagoon ☐ Other (Refer to Form C)

PLEASE PRINT OR TYPE

A. Onsite System Location

Address* 6521 SW 32 St (no rural route) City Lincoln, NE Zip 68523

Legal Description SE 17 9 4 Twin Pines Addition 1 2
1/4 | 1/4 | Section | Township | Range | Subdivison | Addition | Block | Lot

PID 0917401002000 *Approx. Address (If to be determined)

B. Owner

Name Oleh Tyshkov Signature Oleh Tyshkov

Address 909 W Walter Dr City/State/Zip Lincoln, Ne 68522

Home Phone 402 610 5554 Work Phone Same

C. Certified Installer

Name: H.L. Muhlbach Signature Harry Muhlbach

Address 14277 N 56 St City/State/Zip Linkoln, Ne 68514

Work Phone 402 - 430 - 7304

D. Engineer

☐ **Check and complete if engineer designed system** P.E. License Number:

Designer Name Firm Work Phone

E. This system will serve a

☑ Residential Dwelling Number of Bedrooms 5 Whirlpool Bathtub? ☐ Yes ☒ No Total Acres 3
Garbage Grinder? ☒ Yes ☐ No

☐ Commercial Establishment/Other Facility Specify Design flow in gallons per day 400

Type of Wastewater ☒ Domestic ☐ Non-Domestic

DO NOT WRITE BELOW THIS LINE

Approval Process

1. Health Department
Site visits
Comments
Date rec'd
Date frwd
ACTION ☐ Approved ☐ Disapproved
Signature

2. Supt. Bldg. Insp. or Village Clerk
Comments
Date rec'd
Date frwd
ACTION ☐ Approved ☐ Disapproved
Signature

3. City or County Engineer
Comments
Date rec'd
Date frwd
ACTION ☐ Approved ☐ Disapproved
Signature

Installation Final Written Approval
By
Date

Business Office Use Only
Date Received Amount Paid
Received By Cash/Check No.

White - Health Department Yellow - Engineer Pink - Building & Safety

Lincoln-Lancaster County Health Department (LLCHD)
Environmental Public Health Division
3140 "N" Street • Lincoln, NE 68510-1514
Phone: 402-441-8022

B

Permit Number:

Onsite Wastewater Treatment System
Soil Evaluation Report

PLEASE PRINT OR TYPE

Onsite System Location

Address 6521 SW 32St (no rural route) City Lincoln NE, Zip 68523

Owner Olch Tyshkow Address 909 W WelterDr Lincoln, Ne 68522

Date of Tests 10-7-19 to 10-7-19 Weather: Precipitation Damp Temperature 49°

Percolation Test Data Table

A.	B.	C. D. E. F. Saturation/Swelling Time				G. H. I. J. K. Water Level Drop Last 30 mins of 4 hr or last 10 mins of 1 hr					L. M. N. Results		
		Start		End		Start			End				
Hole No.	Hole Depth (in)	Date (Mo/Da)	Time (Hr/Min)	Date (Mo/Da)	Time (Hr/Min)	Date (Mo/Da)	Time (Hr/Min)	Initial Water Lev (in.)	Date (Mo/Da)	Time (Hr/Min)	Elapsed Time Interval	Water Level Drop (in)	Percolation Rates (Min/in = mpi)
1	36	None				10-7	8:00	6	10-7	11.30	30	.50	60,0
2	36					"	8:05	6	"	11.35	"	.50	60,0
3	36	Rainy Days				"	8:10	6	"	11.40	"	.60	50,0
4	36	Before Test				"	8:13	6	"	11.43	"	.52	58,0
								6					
								6					
								6					
								6					

Person Conducting Percolation Test

Name: Harry Muhlbach

Phone: 402-430-7304

Address 14277 N 56 St Lincoln, Ne 68514

Sum of Percolation Rates: 228

Average of Rates: 57,0

Rate Used for Calculation: 40,00

Soil type (NRCS Maps/Other) Wymore silty clay loam, 1-7% Slop

Groundwater Depth Appear to be more than 8 Plus ft Well above flood Plain

DO NOT WRITE BELOW THIS LINE

Reviewing Action

Comments (Soil type, groundwater, floodplain, etc.)


Signature of Reviewing Official Date

READ THOROUGHLY


DIAGRAM OF PERCOLATION TEST PROCEDURE

Finished Grade or Natural Ground Level

I. Size, Number, and Location or Test Holes
   - A. Dig six or more holes spaced uniformly over proposed lateral field site.
   - B. Scratch smeared spots on sides of hole.
   - C. Remove loose material from hole.
   - D. Add 2" of gravel to hole.

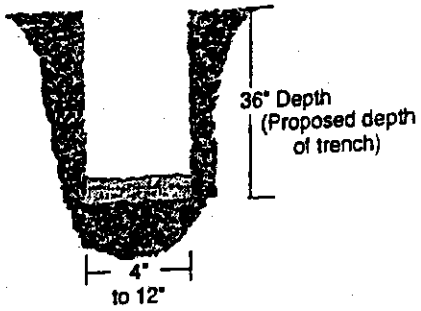


II. Saturation of Soil (Pre-soak)
   - A. Fill hole with 12" or more of water.
   - B. MAINTAIN THIS WATER LEVEL FOR 4 HOURS.
   - C. Record on Form B columns a thru f.

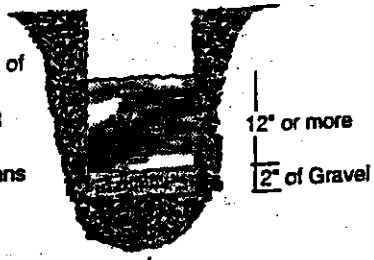


24 Hours Later

III. Percolation-rate Measurement **(refer to Instructions 5a, 5b, or 5c.)**
   - A. Add 6" of water.
   - B. Measure from fixed reference point (nail) to water.
   - C. Record measurement and time on front of Form B.

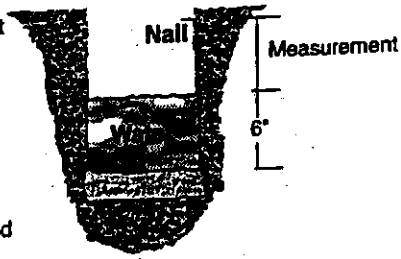

½ hour later (30 minutes)

   - D. 30 minutes later remeasure and record time.
   - E. If water will be too low for another reading 30 minutes later, adjust to 6" of water and remeasure and record time.

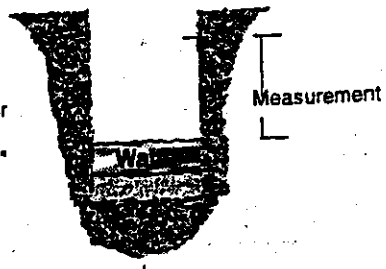

   - F. Continue for 3½ hours taking readings every 30 minutes.
   - G. Last 30 minute reading is used in filling out Form B. Record date, time, intervals and water level drops in column g thru m.

Instructions

1. **Number and location of tests.** Percolation tests shall be made in 6 or more separate test holes which shall be spaced uniformly over the proposed lateral field site.
2. **Type of test hole.** Dig or bore a hole 3 feet deep with a diameter of 4 to 12 inches. (To save time, labor and the volume of water required per test, a 4-inch auger hole is recommended).
3. **Preparation of the test hole.** Scratch or roughen any smeared spots on the sides of the hole with a knife blade or sharp pointed instrument to provide a natural soil interface into which water may percolate. Remove all loose material from the hole. Add 2 inches of gravel to protect the bottom from scouring when water is poured into the hole.
4. **Saturation and swelling of the soil.** Fill the hole with clear water to a depth of 12 inches or more above the gravel and maintain this water level at least 4 hours and preferably overnight. The accuracy and true value of the percolation data depends on thorough saturation and swelling of the soil.
5. **Percolation-rate measurement.** Percolation-rate measurements shall be made 24 hours after starting the saturation and swelling procedure described above. Record results on the front of this form and complete all calculations.
   a. If water remains in the test hole after the overnight swelling period, adjust the depth to approximately 6 inches over the gravel. From a fixed reference point, measure the drop in water level over a 30 minute period to the nearest 1/8 of an inch. This drop is used to calculate the percolation rate.
   b. If no water remains in the test hole after the overnight swelling period, add clear water to bring the depth to approximately 6 inches over the gravel. From a fixed point, measure the drop in water level to the nearest 1/8 of an inch at 30-minute intervals for 4 hours. Refill to the 6 inch level over the gravel as often as necessary. The drop that occurs during the final 30 minutes is used to calculate the percolation rate.
   c. In sandy soils (or other soils in which the first 6 inches of water seeps away in less than 30 minutes after the overnight swelling period) the time interval between measurements shall be 10 minutes instead of 30 minutes and the test run for 1 hour instead of 4 hours. The drop that occurs during the final 10 minutes is used to calculate the percolation rate.
6. **Record the test results and complete all calculations on the front of this form.** The average of the percolation rates calculated for all holes in the last 30 (10) minutes will normally be the rate used for calculations to size the system. ***Exceptions are the use of the greatest percolation rate when rates vary more than 20 min/in between holes or when other soil analysis indicates potential percolation problems.***

LLCHD reserves the right to require additional testing based on knowledge of soil types, percolation tests results on nearby properties, or due to concerns with procedures followed. In some situations, LLCHD staff will require and perform on-site observation of percolation tests.

Lincoln-Lancaster County Health Department
Environmental Public Health Division
3140 "N" Street • Lincoln, NE 68510-1514
Phone: 402-441-8022


C

Permit Number:

Onsite Wastewater Treatment System

Preliminary Plan Specifications

Draw a plot plan showing onsite system sewer lines, drop of distribution boxes, tank, drainfields, percolation test holes, well, residence, direction of groundwater flow, property lines, and reserve area for replacement onsite system.

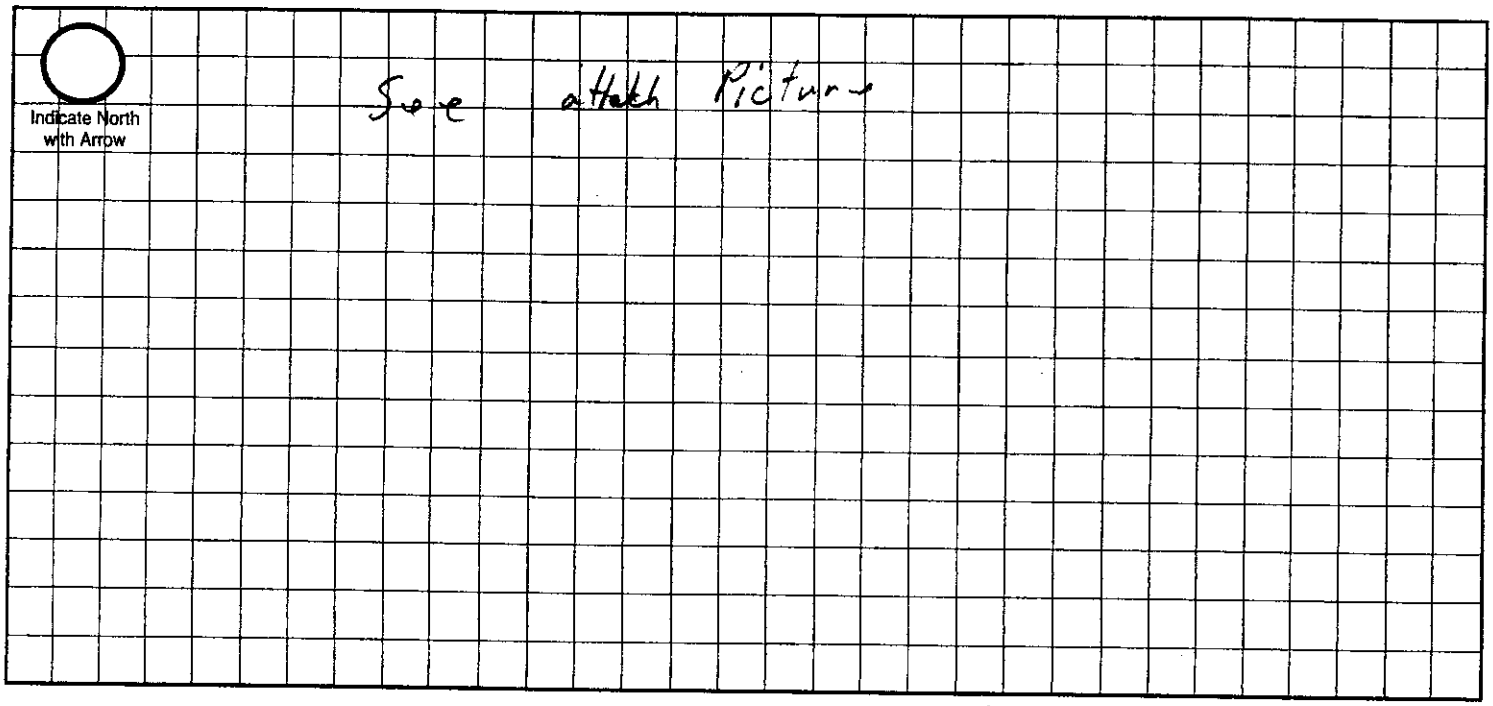

Approximate Scale: _____ft. = _____ grid line/s

A. Onsite System Location

Address (no rural route) 6521 SW 32 St City Lincoln NE, Zip 68523

B. Proposed Septic Tank/s

Septic Tank Cap. 2000 gals Tank Material: ☒ Concrete ☐ Plastic ☐ Other_____ ☐ Lagoon(Max. seepage 1/8" per day)

C. Reserve Area for Replacement Onsite System

☑ Drainfield Absorption Area (percoloation test required) ☐ Lagoon

D. Drainfield Absorption System

Percolation Rate 57 (min/inch = mpi) No. of Bedrooms 5 Soil Type Wymore Silt Loam, Gil Land Slope 1-7 %

☑ Trench ☐ Bed ☐ Non-Standard (engineer designed and NDEQ approved Total Square feet of drainfield_____sq.ft.

Total length of laterals 390 Type of distribution: ☐ Perforated pipe ☐ Half-Round ☐ Chamber ☒ Other Ez flow

No. of absorption trenches 4 Width 3' No. of drop boxes_____ Distrubtion Box 1

No. of absorption beds_____ Width_____ No of Distribution lines per bed_____


E. Setbacks Check the Boxes Below if the Required Setback has been Satisfied

Distance From	Private Well	Public Well	Surface Water	Gound Water	Pressure Water Lines	Property Lines	Foundations Yours	Foundations Neighbors	All Other Setbacks
Tank (ft)	50 ☑	500 ☑	50 ☑	NA ☑	25 ☑	20 ☑	15 ☑	25 ☑	☑
Field (ft)	100 ☑	500 ☑	50 ☑	4 ☑	30 ☑	20 ☑	30 ☑	40 ☑	☐
Lagoon (ft)	100 ☐	500 ☐	50 ☐	N/A ☐	30 ☐	50 ☐	100 ☐	200 ☐	☐

F. Required Signatures

Home Building Contractor_____ Date 11-14-19

Installer Harry Millard Date _____

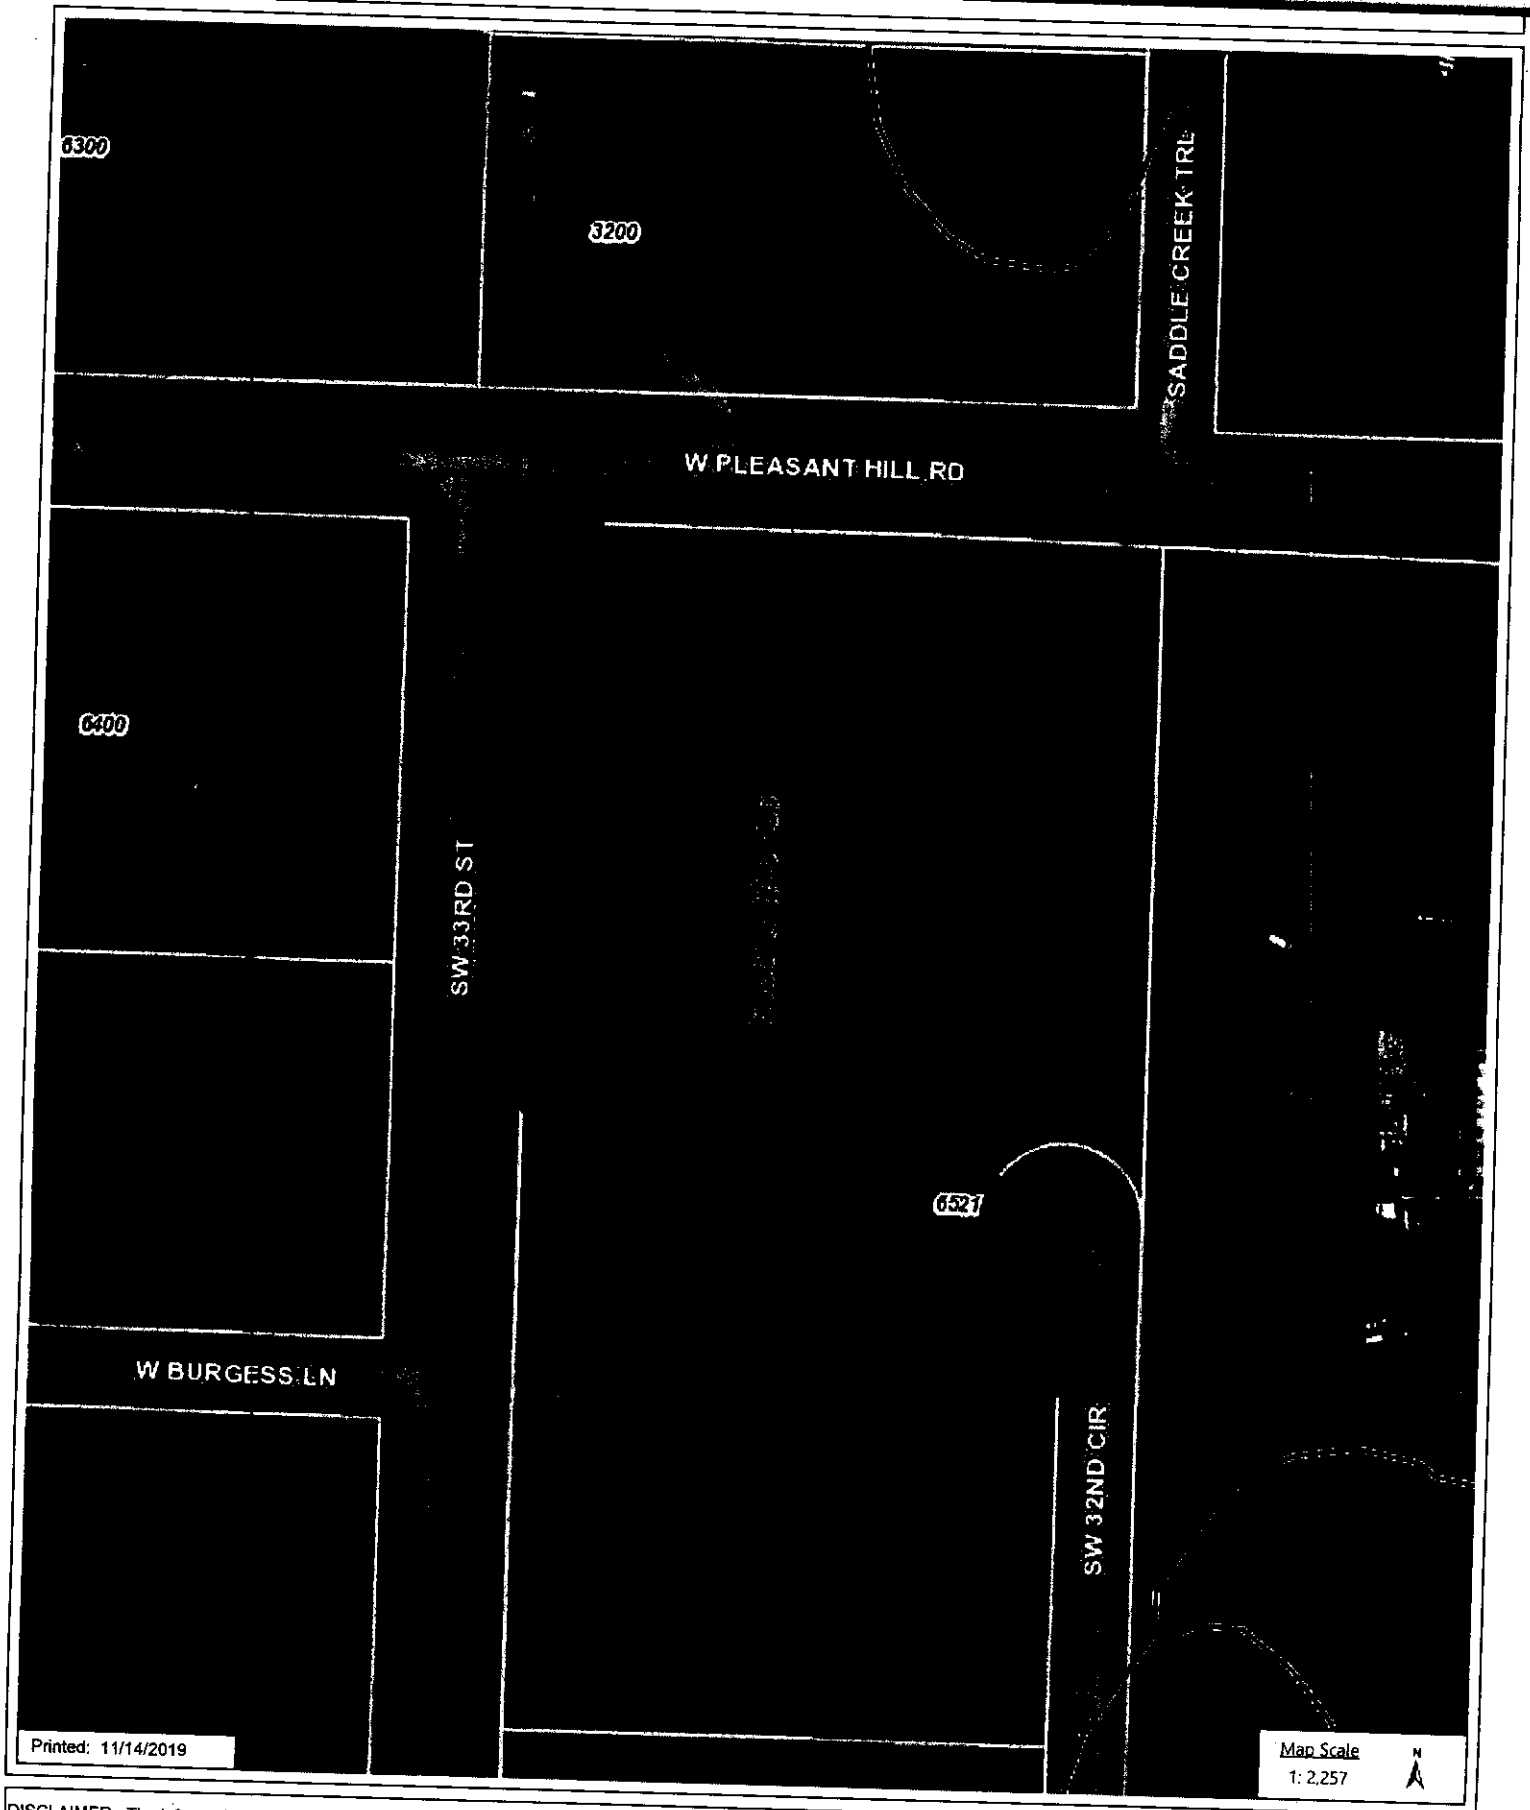

DISCLAIMER: The information is presented on a best-efforts basis, and should not be relied upon for making financial, survey, legal or other commitments. If you have questions or comments regarding the data displayed on this map, please email assessor@lancaster.ne.gov and you will be directed to the appropriate department.

Lincoln-Lancaster County Health Department
Environmental Public Health Division (402) 441-8027
3131 O Street Lincoln, Nebraska 68510-1514

ON-SITE WASTE WATER SYSTEM
CONSTRUCTION - INSTALLATION PERMIT
No. HS001931

System Type: Standard

Situs: 6521 SW 32 ST, LINCOLN, NE 68523

Issued: 11/15/2019

Expires: 11/15/2020

Description: TWIN PINES ADDITION, BLOCK 1, Lot 2

Owner: TYSHKOV, OLEH V & TYSHKOVA, NATALIYA P
909 W WELTER DR
LINCOLN, NE 68522

Patricia D. Lopez

Patricia D. Lopez, RN, MSN, Interim Health Director

Dear Applicant:

The above document is your permit to construct a new On-site Waste Water System at the location listed. Please contact this office once the sytem is complete in order to schedule a final inspection before use.

Patricia D. Lopez

Patricia D. Lopez, RN, MSN
Interim Health Director

HARRY MUHLBACH
14277 N 56TH ST
LINCOLN, NE 68514
