Lincoln-Lancaster County Health Department
Environmental Public Health Division
3140 N Street • Lincoln NE 68510-1514
Phone: 402-441-8643

A

Permit Number H5002137

Existing Building

Onsite Wastewater Treatment System
Request for Site Clearance and Permit

Include Form B and C. Submit correct fee with this Application

3 acres or more required for: ☑ Septic System ☐ Lagoon ☐ Other (Refer to Form C)

The undersigned hereby requests site clearance and permit to construct a Wastewater Treatment System in conformance with appropriate regulations.

PLEASE PRINT OR TYPE

A. Onsite System Location

Address 6300 Wittstruck Rd (no rural route) City Roca, NE Zip 68430

Legal Description SE (1/4) NW (1/4) 9 (Section) 8N (Township) 7E (Range) _____ (Subdivison) _____ (Addition) 13 (Block) _____ (Lot)

PID 15-09-200-008-000

B. Owner

Name Hausmann Development LLC Signature _____

Address 8885 Executive Woods Dr City/State/Zip Lincoln, NE 68512

Home Phone 402-580-2181 Work Phone _____

C. Certified Installer

Name: Lloyd Jakoubek, Raymond Contracting Inc Signature _____

Address 13800 NW 70th St City/State/Zip Raymond, NE 68428

Work Phone 402-890-6009 or 402-783-2663

D. Engineer

☐ Check and complete if engineer designed system P.E. License Number: _____

Designer Name _____ Firm _____ Work Phone _____

E. This system will serve a

☐ Residential Dwelling Number of Bedrooms _____ Whirlpool Bathtub? ☐ Yes ☐ No Total Acres 39.96

Garbage Grinder? ☐ Yes ☐ No

☑ Commercial Establishment/Other Facility Specify Private Hangar with Restrooms Design flow in gallons per day <200

Type of Wastewater ☑ Domestic ☐ Non-Domestic

DO NOT WRITE BELOW THIS LINE

Approval Process ☐ Municipal Code 24.38 ☐ County Resolution No. 02-30

1. Health Department ACTION ☐ Approved ☐ Disapproved

Site visits _____ Date rec'd _____ Signature _____

Date frwd _____

Comments _____

2. Supt. Bldg. Insp. or Village Clerk ACTION ☐ Approved ☐ Disapproved

Comments _____ Date rec'd _____ Signature _____

Date frwd _____

3. City or County Engineer ACTION ☐ Approved ☐ Disapproved

Comments _____ Date rec'd _____ Signature _____

Date frwd _____

Installation Final Written Approval

By _____

Date _____

Business Office Use Only
Date Received 1-13-20 Amount Paid $140.00
Received By JAC Cash/Check No. CC0287

White - Health Department Yellow - Engineer Pink - Building & Safety

Form A Updated: 1/13

Lincoln-Lancaster County Health Department (LLCHD)
Environmental Public Health Division
3140 "N" Street • Lincoln, NE 68510-1514
Phone: 402-441-8022

B

Permit Number:

Onsite Wastewater Treatment System

Soil Evaluation Report

PLEASE PRINT OR TYPE

Onsite System Location

Address 6300 Wittstruck Rd (no rural route) City Roca NE, Zip 68430

Owner Hausmann Development LLC Address 8885 Executive Woods Dr, Lincoln, NE 68512

Date of Tests 11/5/20 to 11/6/20 Weather: Precipitation 0 Temperature 60°

Percolation Test Data Table

A.	B.	C. D. E. F. Saturation/Swelling Time				G. H. I. J. K. Water Level Drop Last 30 mins of 4 hr or last 10 mins of 1 hr					L. M. N. Results		
		Start		End		Start		Initial	End				
Hole No.	Hole Depth (in)	Date (Mo/Da)	Time (Hr/Min)	Date (Mo/Da)	Time (Hr/Min)	Date (Mo/Da)	Time (Hr/Min)	Water Lev (in.)	Date (Mo/Da)	Time (Hr/Min)	Elapsed Time Interval	Water Level Drop (in)	Percolation Rates (Min/in = mpi)
1	21	11/5	9:30a	11/6	7:00a	11/6	10:30a	6	11/6	11:00a	30	1/2	60
2	32	"	"	"	"	"	"	6	"	"	"	1/2	60
3	24	"	"	"	"	"	"	6	"	"	"	5/8	48
								6					
								6					
								6					
								6					
								6					

Person Conducting Percolation Test

Name: Terri L Jakoubek, Raymond Contracting, Inc.

Phone: 402-783-2663 or 402-890-6009

Address 13800 NW 70th St

Raymond, NE 68428 Cert #1198

Soil type (NRCS Maps/Other) Mayberry SCL

Groundwater Depth >8'

Sum of Percolation Rates: 168

Average of Rates: 56

Rate Used for Calculation: 56

DO NOT WRITE BELOW THIS LINE

Reviewing Action

Comments (Soil type, groundwater, floodplain, etc.)

Signature of Reviewing Official Date

Lincoln-Lancaster County Health Department
Environmental Public Health Division
3140 "N" Street • Lincoln, NE 68510-1514
Phone: 402-441-8022


C

Permit Number:

Onsite Wastewater Treatment System

Preliminary Plan Specifications

Draw a plot plan showing onsite system sewer lines, drop of distribution boxes, tank, drainfields, percolation test holes, well, residence, direction of groundwater flow, property lines, and reserve area for replacement onsite system.

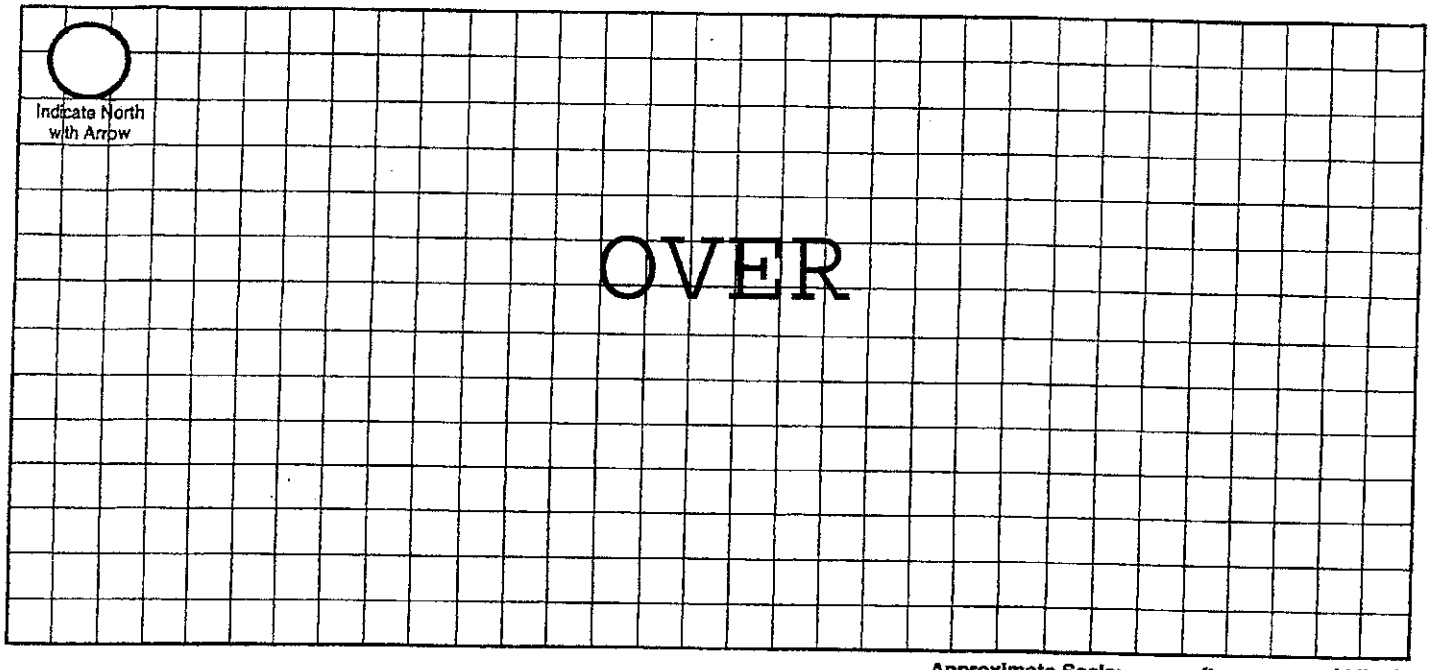

Approximate Scale: _____ft. = _____ grid line/s

A. Onsite System Location

Address (no rural route) 6300 Wittstruck Rd City Roca NE, Zip 68430

B. Proposed Septic Tank/s

Septic Tank Cap. 2000 gals Tank Material: ☒ Concrete ☐ Plastic ☐ Other_____ ☐ Lagoon(Max. seepage 1/8" per day)

C. Reserve Area for Replacement Onsite System

☐ Drainfield Absorption Area (percolation test required) ☒ Lagoon

D. Drainfield Absorption System

Percolation Rate 56 (min/inch = mpi) No. of Bedrooms N/A Soil Type Mayberry SCL Land Slope_____%

☒ Trench ☐ Bed ☐ Non-Standard (engineer designed and NDEQ approved Total Square feet of drainfield 450 sq.ft.

Total length of laterals 100 Type of distribution: ☐ Perforated pipe ☐ Half-Round ☐ Chamber ☒ Other EZFlow 1203H

No. of absorption trenches 1 Width 38" No. of drop boxes 1 Distrubtion Box_____

No. of absorption beds_____ Width_____ No of Distribution lines per bed_____

E. Setbacks Check the Boxes Below if the Required Setback has been Satisfied

Distance From	Private Well	Public Well	Surface Water	Gound Water	Pressure Water Lines	Property Lines	Foundations Yours	Foundations Neighbors	All Other Setbacks
Tank (ft)	50 ☒	500 ☒	50 ☒	NA ☒	25 ☒	20 ☒	15 ☒	25 ☒	☒
Field (ft)	100 ☒	500 ☒	50 ☒	4 ☒	30 ☒	20 ☒	30 ☒	40 ☒	☒
Lagoon (ft)	100 ☐	500 ☐	50 ☐	N/A ☐	30 ☐	50 ☐	100 ☐	200 ☐	☐

F. Required Signatures


Home Building Contractor Existing Building Date_____

Installer Kevin L. Wittstruck Date 11/11/20

Hausmann Development LLC 6300 Wittstruck Rd, Roca, NE 68430

GIS Viewer
CITY OF LINCOLN - LANCASTER COUNTY, NE

City of Lincoln\Lancaster County GIS Map

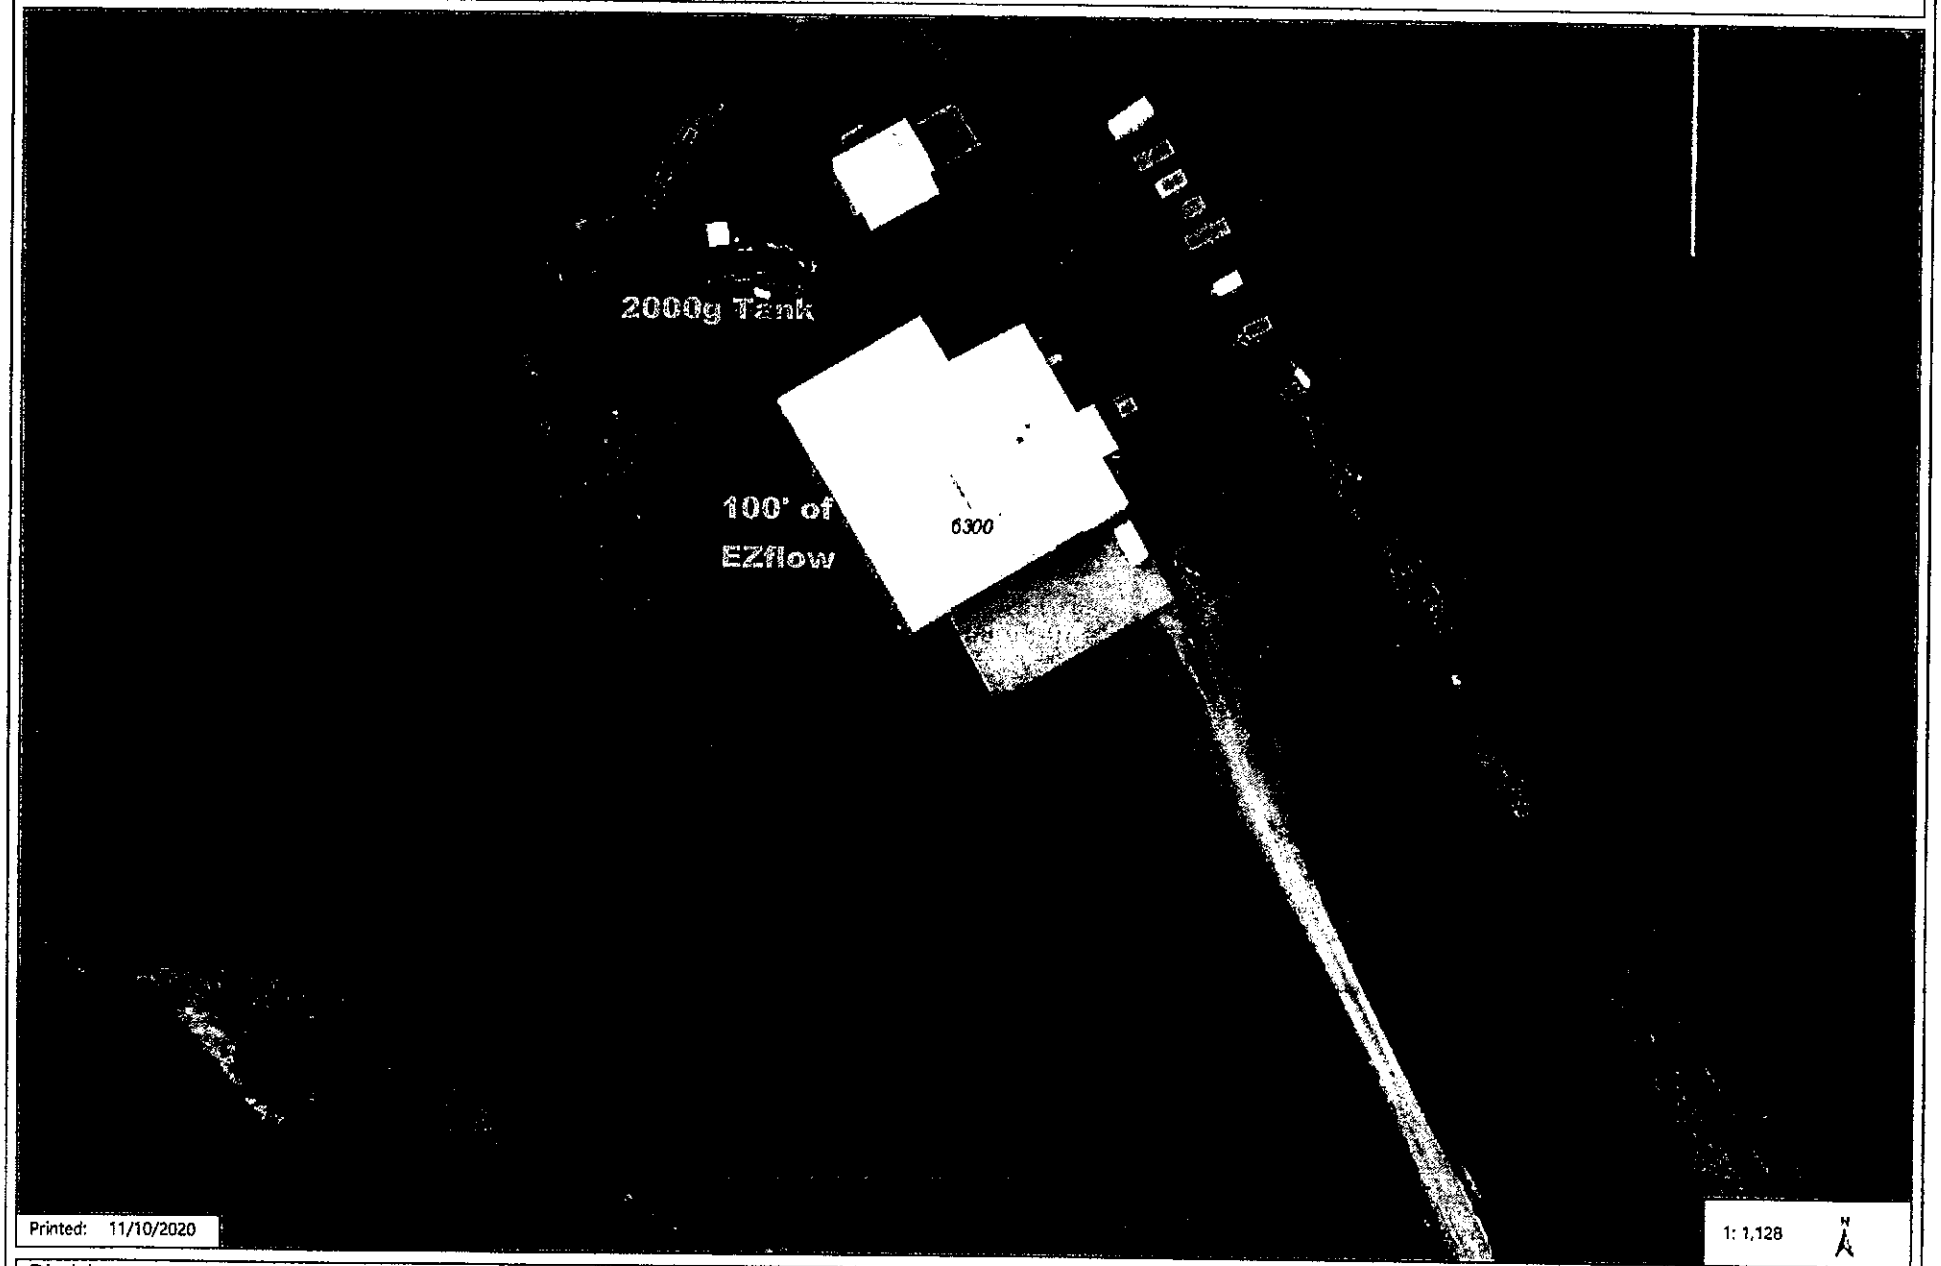

Printed: 11/10/2020

1: 1,128

N

Disclaimer: The information is presented on a best-efforts basis, and should not be relied upon for making financial, survey, legal or other commitments. If you have questions or comments regarding the data displayed on this map, please email assessor@lancaster.ne.gov and you will be directed to the appropriate department.

Lincoln-Lancaster County Health Department
Environmental Public Health Division (402) 441-8027
3131 O Street Lincoln, Nebraska 68510-1514

ON-SITE WASTE WATER SYSTEM
CONSTRUCTION - INSTALLATION PERMIT
No. HS002137

System Type: Standard

Situs: No Site Address Specified

Issued: 11/13/2020

Expires: 11/13/2021

Description: S9, T8, R7, 6th Principal Meridian, LOT 12 NE & LOT 13 NW

Owner: HAUSMANN DEVELOPMENT LLC
8885 EXECUTIVE WOODS DR
LINCOLN, NE 68512

Patricia D. Lopez

Patricia D. Lopez, RN, MSN, Interim Health Director

Dear Applicant:

The above document is your permit to construct a new On-site Waste Water System at the location listed. Please contact this office once the sytem is complete in order to schedule a final inspection before use.

Patricia D. Lopez

Patricia D. Lopez, RN, MSN
Health Director

RAYMOND CONTRACTING INC
13800 NW 70TH ST
RAYMOND, NE 68428
