HS002311

Application to Alter or Repair an Onsite Wastewater Treatment System

The applicant is applying for a permit to: ☑ALTER ☐REPAIR an existing Onsite Wastewater Treatment System, and agrees to comply with LMC 24.38 or County Resolution 02-0030.

1. **Street Address (No Rural Route):** 8800 Davey Rd.

   Legal Description of Property: Township: 12 Range: 7 Section: 23

   Block _____ Lot 1B SubDivsion _____ Add: _____

   *Parcel ID 19 . 23 . 300 . 604 . 000 (i.e. 99-99-999-999-999)

2. **Property use:** ☑ Residential ☐ Commercial ☐ Other use (Describe: _____)
   Number of bedrooms 4 Does the system have a: ☑Garbage Grinder ☐Large Capacity Tub

3. **Type of Present Individual Disposal System** ☑ septic system ☐ lagoon ☐ other

4. **Description of proposed alteration or repair:** Replace Lateral Field and add 1000 gal tank to bring system to Title 124 Requirements.

5. **Current Type of Lateral-** Plastic ½ Round **Current Linear Ft. Of Lateral -** 225

   Current Tank Gallonage- 1000

6. Print Name Steven C Lewis Address 3300 N 71st Street Phone: 402 432 1082

   Applicant Signature: _____

Please contact LLCHD for the current permit fee for this application
Fee must be included before the application will be processed. Incomplete information will delay processing.

HEALTH DEPARTMENT USE ONLY

☐Municipal Code 24.38 ☐County Resolution Number 02-30

Date received ___/___/___ REVIEW: ☐ Approved ☐ Disapproved By: _____

Comments (if any): _____

Site visits
Date ___/___/___ By _____
Date ___/___/___ By _____

Installation final written approval
Date ___/___/___ By _____

Return application to:

Lincoln-Lancaster County Health Department
Environmental Public Health Division
3140 "N" Street, Lincoln, NE 68510
Phone: (402) 441-8643

Business Office Use Only

Received: Date: ___/___/___ Amount _____ Check No. _____ Initials _____

Revised 4/8/13

Lincoln-Lancaster County Health Department
Environmental Public Health Division (402) 441-8027
3131 O Street Lincoln, Nebraska 68510-1514

ON-SITE WASTE WATER SYSTEM
ALTERATION PERMIT
No. HS002311

System Type: Standard

Situs: No Site Address Specified

Issued: 10/20/2021

Expires: 10/20/2022

Description: S23, T12, R7, 6th Principal Meridian, LOT 18 SW

Owner: JOHNSON, DUSTIN P
8800 DAVEY RD
LINCOLN, NE 68517

Patricia D. Lopez

Patricia D. Lopez, RN, MSN, Health Director

Dear Applicant:

The above document is your permit to alter an existing On-site Waste Water System at the location listed. Please contact this office once the alteration is complete to obtain final approval before use.

Patricia D. Lopez

Patricia D. Lopez, RN, MSN
Health Director

STEVEN LEWIS
3300 N 71 ST
LINCOLN, NE 68507

H5002311
SCANNED

Application to Alter or Repair an Onsite Wastewater Treatment System

The applicant is applying for a permit to: ☑ALTER ☐REPAIR an existing Onsite Wastewater Treatment System, and agrees to comply with LMC 24.38 or County Resolution 02-0030.

1. **Street Address (No Rural Route):** 8800 Davey Rd.

   Legal Description of Property: Township: 12 Range: 7 Section: 23

   Block _____ Lot 18 SubDivsion _____ Add: _____

   *Parcel ID 19 . 23 . 300 . 004 . 000 (i.e. 99-99-999-999-999)

2. **Property use:** ☑ Residential ☐ Commercial ☐ Other use (Describe: _____)
   Number of bedrooms 4 Does the system have a: ☑Garbage Grinder ☐Large Capacity Tub

3. **Type of Present Individual Disposal System** ☑ septic system ☐ lagoon ☐ other

4. **Description of proposed alteration or repair:** Replace Lateral Field and add 1000 gal tank to bring system to Title 124 Requirements. Installing 320 linear ft.

5. **Current Type of Lateral-** Plastic ½ Round **Current Linear Ft. Of Lateral -** 225

   Current Tank Gallonage- 1000

6. Print Name Steven C Lewis Address 3300 N 71st street Phone: 402 432 1082

   Applicant Signature: _____

60 mil

Please contact LLCHD for the current permit fee for this application
Fee must be included before the application will be processed. Incomplete information will delay processing.

HEALTH DEPARTMENT USE ONLY

☐Municipal Code 24.38 ☒County Resolution Number 02-30

Date received 10/20/21 REVIEW: ☒ Approved ☐ Disapproved By: _____

Comments (if any): _____

Site visits
Date 10/21/21 By DC
Date ___/___/___ By _____

Installation final written approval
Date 10/22/21 By DC

Return application to:
Lincoln-Lancaster County Health Department
Environmental Public Health Division
3140 "N" Street, Lincoln, NE 68510
Phone: (402) 441-8643

Business Office Use Only

Received: Date: 10/19/21 Amount 240.00 Check No. CC5909 Initials LC

Revised 4/8/13

Lincoln-Lancaster County HEALTH DEPARTMENT
Environmental Public Health Division
3140 N Street • Lincoln NE 68510-1514
Phone: 402-441-8643

Exhibit 5

Permit Number: HS002311

Onsite Wastewater Treatment System

Inspection Sheet

Date 10/22/21 Legal Description ____ ¼ ¼ Section/Township/Range

Onsite System Location

Address (no rural route) 8800 Davey Rd City ____

Owner ____ Address ____

Mark One: ☒ Dwelling ☐ Non-dwelling

~~☐ New System~~ ☒ Alteration [☐ Tank Only ☐ Trench Only] ☐ Lateral Only

☐ Temporary modification (Describe problem causing discharge and reason for temporary modification): ____

Drainfield Absorption System:

Two tank 1,000 existing used
New 1,000 installed in line

☐ Lateral ☐ Bed ☐ Non-standard (engineer-designed and NDEQ approved) ☐ Holding Tank ☐ Trench

Total square feet of drainfield 1,440 Sq. Ft. Tank Size 2,000 total gals

Total length of laterals 320' Type of Distribution: ☐ Chamber ☐ Perforated Pipe ☒ Other (describe) E2 flow

No. of Absorption Laterals 3 Width 4.5 facts No. of Drop Boxes ____ Distribution Box 1

Leveling Method Used Laser

Setbacks (Check the Boxes Below if the Required Setback has been Satisfied):

Distance From	Private Well	Public Well	Surface Water	Ground water	Pressure Water Lines	Property Lines
Tank (ft)	50 ☐	500 ☐	50 ☐	NA ☐	10 ☐	5 ☐
Field (ft)	100 ☐	500 ☐	50 ☐	4 ☐	25 ☐	5 ☐

Geographical Coordinates to 6 Decimals:

Tank ____ NA

Lateral #1 ____ Lateral #3 ____

Lateral #2 ____ Lateral #4 ____

Comments:

Inspections prior to Final Approval
Initial DS Date 10/22/21
Follow-Up ____ Date ____
Follow-Up ____ Date ____
Installation Final Written Approval By Doug Shaw
Date 10/22/21

Field Note Drawing (See Reverse Side):

Lincoln-Lancaster County Health Department
Environmental Public Health Division
3140 N Street • Lincoln NE 68510-1514
Phone: 402-441-8643

D Exhibit 4

Permit Number:

Onsite Wastewater Treatment System
As-Built Description and Drawing

Type of Onsite Wastewater System: ☐ Lagoon (Skip to Back Page ☑ Subsurface Septic ☐ Mound

Onsite Wastewater System Location

Address or Legal Description or Parcel Identification Number (PID) 19-23-300-004-000

Owner: Leigh Ann Johnson Address 8800 Davey Rd. Lincoln 68517

A. Wastewater Piping

1. Material: Sch 40 PVC Diameter: 4 in.
2. Distance between dwelling and septic tank: New 120 ft.

B. Septic Tank

1. Material Plastic
2. Capacity: 1000 + existing 1000
3. Depth to top of tank, below unfinished grade: 12 in.
4. Distance to:
   Well >100 ft.
   Pressure line NA ft
   Property Line >100 ft.
   Foundation 120 ft.

C Distribution Box or Drop Box

Distance **and** Direction from septic tank: 40 ft. W

D. Drainfield/Absorption Field

☑ Trench ☐ Bed

1. Type: ☐ Perforated Pipe ☐ Chamberless ☑ Other
   Material brand and inside width of Chamberless.
   EZ Flow
2. Number of Laterals: 3
3. Length of each lateral (linear): ft. 120 ft. 60 ft. 146 ft.
4. Drainfield size: 1440 sq. ft.
5. Distance to:
   Well >100' ft.
   Pressure line NA ft.
   Property line NA ft.
   Depth of Groundwater 132

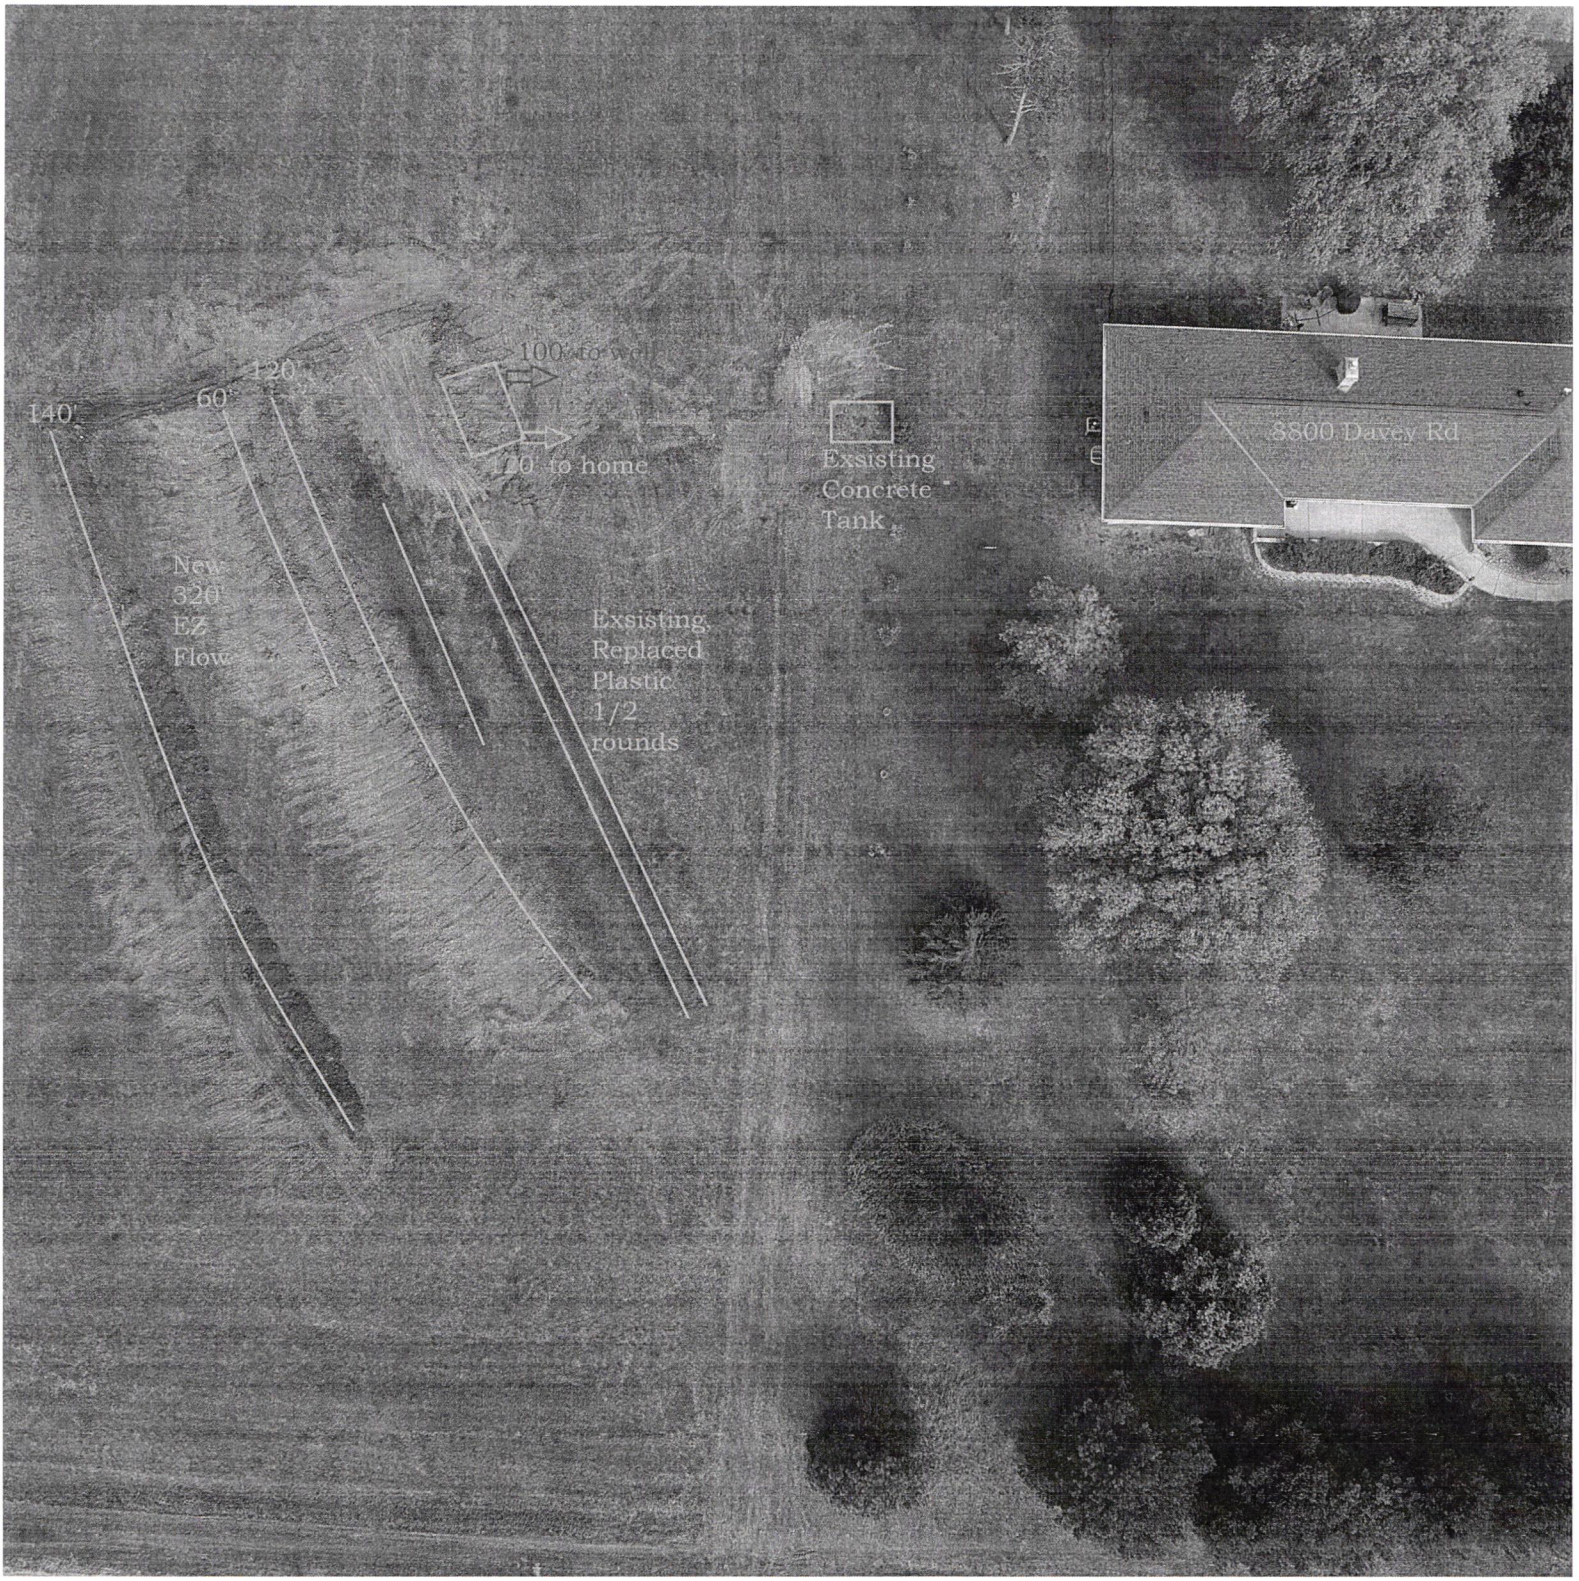
Was the Onsite Wastewater System covered prior to LLCHD inspection? ☑ Yes ☐ No

If Yes, the Certified Professional must sign below for final approval:

I swear and affirm that the system complies with Lincoln Municipal Code (LMC) 24.38 and/or County Resolution R-13-0062 requirements and that the information and documentation submitted are true and accurate.

Certified Professional Signature: _____ Date: 10-21-21

Complete As-Built drawing on the back of this form.


100' to well
120'
60'
140'
110' to home
Exsisting
Concrete
Tank
8800 Davey Rd
New
320
EZ
Flow
Exsisting
Replaced
Plastic
1/2
rounds
