FORM HD-40(73) REQUEST FOR SITE CLEARANCE FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM

City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 475-6221)

FILE NO. 466-C

TO: Division of Environmental Health
Lincoln-Lancaster County Health Dept.

DATE: 14 June 1974

The undersigned hereby requests SITE CLEARANCE to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 7N ; Range 7E ; Section 14
Block _____; Lot _____; Addition N 525' of E 565' of W½ NE¼
Street Address _____

2. Property Use: Residential ☒ ; Commercial ☐
No. of Bedrooms 3.
Describe: _____
Other Use ☐
Describe: _____

3. Type of Individual Sewage Disposal System: Septic Tank ☒ ; Other ☐

4. Distance to public sewer: _____ ft.

Garry Wernimont
by Vernon Wernimont
Signature of Applicant (Owner or Lessee)

Box, Neb 68324
Address

(Do not write below this double line)

REVIEWING ACTION

1. Health Department: Date Rec'd. 6/20/74. Date Frwd. 6/21/74.
ACTION: Approved ☒ Disapproved ☐
Signature: Jerrold C. Hoob

2. Supt. Bldg. Insp.: Date Rec'd. _____. Date Frwd. _____.
ACTION: Approved ☐ Disapproved ☐
Signature: _____

3. City or County Engineer: Date Rec'd. _____. Date Frwd. 6-21-74.
ACTION: Approved ☐ Disapproved ☐
Signature: Walter Hoppe

REMARKS OR REASONS FOR DISAPPROVAL _____

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

M Lipsky
6/21/74

FORM HD-42(73) APPLICATION FOR PERMIT TO CONSTRUCT INDIVIDUAL SEWAGE DISPOSAL SYSTEM

City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 475-6221)

FILE NO. 466-C

DATE: 14 June 1974

TO: Director of Health
Lincoln-Lancaster County Health Dept.

The undersigned hereby applies for a permit to construct an Individual Sewage Disposal System in conformance with appropriate Ordinance or Resolution, as described in this application and the annexed forms attached hereto.

1. Legal description of property: Twp. 7N ; Range 7E ; Section 14 ; Block ; Lot ; Addition N525' of E385' W½ NE¼.
Street Address .

2. Property Use: Residential ☐; Commercial ☐
No. of Bedrooms 3
Describe:
Other Use
Describe:

3. Type of Individual Sewage Disposal System: Septic Tank ☒; Other ☐

4. Plans and Specifications of Proposed System. (See FORM HD-45(73) PLANS & SPECIFICATIONS, SEWAGE DISPOSAL SYSTEM, attached hereto.)

5. Soil Absorption Properties. (See FORM HD-43(73) SOIL ABSORPTION TEST DATA REPORT, attached hereto).

Garry Wiesinle
by Vernon O'Rensike
Signature of Applicant (owner or lessee)

Burr, Nebr 68324
Address

(Do not write below double line)

REVIEWING ACTION

1. Date Rec'd;
Filing Fee: $ 30.00

2. Site Visits:
Date: 7-25-74 by: jw
Date: by:
Date: by:

3. Date: Approved ☐; Disapproved ☐ 6/20/74
by: Jerrold C. Wood

4. INSTALLATION FINAL WRITTEN APPROVAL
Date: 7-25-74 by: James Neverba

FORM HD- 45(73) PLANS & SPECIFICATIONS
SEWAGE DISPOSAL SYSTEM

(Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 475-6221)

FILE NO. 466-C

SPECIFICATIONS

DATE: 14 June


A. BUILDING SEWER:
1. Material Cast; Diameter 4 in.
2. Distance above basement floor ___ in.; or below basement floor 6 in.
3. Distance between dwelling and septic tank 100 ft.
4. Number of clean-outs 1.
5. Distances To:
Well or Suction Line 56 ft.;
Stream 200 ft.; Pressure Line 56 ft.;
Property Line 150 ft.

B. SEPTIC TANK (Provide construction drawings.)
1. Material Concrete; No. of compartments 1.
2. Capacity 1000 gals.; Liquid depth ___ in.
3. Factory Built: Yes ☒ (Company Precast) No ☐
4. Manholes: Over Inlet; diam. ___ in.
Over Outlet; diam. ___ in.
Below Grade ___ in.
5. Inlet: Baffle ☐; or Tee ☐
6. Outlet: Baffle ☐; or Tee ☑
Depth of outlet below inlet ___ in.
7. Depth of top of tank below finished grade 24 in.
8. Distances To:
Well or Suction Line 120 ft.;
Stream 200 ft.; Pressure Line 120 ft.;
Property Line 150 ft.

C. DISTRIBUTION BOX
1. Material Concrete No. available outlets 4.
2. Factory Built: Yes ☒, (Company Precast) No ☐
3. Dimension: Length ___ in.; Width ___ in. Depth ___ in.
4. Distance from Septic Tank 40 ft.
5. Serial Distribution: Yes ☐, No ☑ (If yes, show detailed plans.)

D. ABSORPTION FIELD: (Provide drawings.)
1. Type: HALF ROUND
2. Lateral Lines: Depth below grade 24 in. Number 2; Length of each line ___ ft Total length of Laterals 188 ft.; Slope 4 in/100 ft. Diameter of pipe ___ in.; Shape O
Material: concrete ☒; fiber asbestos ☐; clay ☐; other ___
Distance between lateral lines ___ ft.
3. Trench Dimensions: Depth 30 in.; Width 48 in.
4. Filter Material: Gravel.
Depth of material from trench bottom 24 in.
5. Distances To:
Well or Suction Line 130 ft.;
Stream 200 ft.; Pressure Line ___ ft.
Property Line 150 ft.
6. Percolation Rate: 30 minutes/inch

TYPICAL SKETCHES

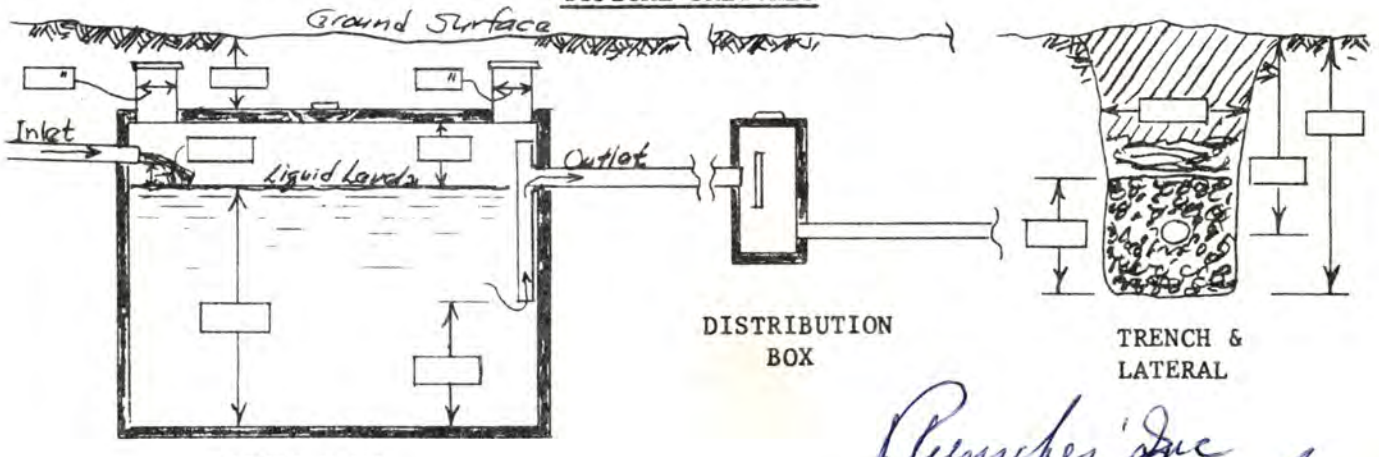

Clemens C. Reinecke Jr.
Clemens C. Reinecke Jr.
Signature of Applicant

FORM HD- 43(73) SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150 and County Resolution No. 2832)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone 475-6221)

FILE NO. 466-C

PROPERTY WHERE SOIL TESTED:
Location: Township 7N ; Range 7E
Section & ¼ Sect. W½ NE¼
Property Dimensions: 525 ft. x 585 ft.
Area: 7 acres. (Attach sketch of property showing hole location).
Soil Type: Silty Clay ☐; Silty Clay Loam ☐; Sandy Loam ☐
Silty Loam ☑; Clay Loam ☐; Sandy Clay ☐

Owner: _____
Address _____

Dates of Tests: June 19 to June 20. Weather: Precip. 0 Temp. 90°/100°F

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
		Pre-Saturation Period				Percolation Readings					Results		
		Start		End		Start			End				
Hole No.	Hole Depth (in.)	Date (Mo. Day)	Time (Hr. Min.)	Date (Mo. Day)	Time (Hr. Min.)	Date (Mo. Day)	Time (Hr. Min.)	Water Level (in.)	Time (Hr. Min.)	Water Level (in.)	Elapsed Time (Min.)	Water Level Drop (in.)	Percolation Rates (Min./inch)
1	24	June 19	3:40	June 20	10:15	June 20	10:15	9"	10:45	7¾"	30	1¼	
2	24	〃	〃	〃	〃	〃	〃	10¾"	〃	9½"	30	1	
3	24	〃	〃	〃	〃	〃	〃	10"	〃	8⅞"	30	1⅛	
4	24	〃	〃	〃	〃	〃	〃	10¾"	〃	9¼"	30	¾	

Sum of Percolation Rates _____
Average of Rates: _____
Mean of Rates: _____

Verne C Reinke
Signature of Person Conducting Test

Address _____
Phone: _____

(Do not write below this line)

REVIEWING ACTION

REMARKS: _____

Approved Percolation Rate(s)
A. 30 min./inch
B. _____ min./inch
C. _____ min./inch

DATE: June 20, 1974

Jerrold C. Hood
Signature of Reviewing Official

Vantage Pointe Homes
Advanced Building Systems

1000 W. Rokeby Rd.
Lincoln, NE 68523

Phone: (402) 423-8821
Fax: (402) 423-8661

DATE: December 14, 2006

TO: Nate
Lincoln Lancaster County Health
Fax: 441-3890


FROM: Cathy Luebe
Office Admin./Mgr.

RE: Septic System for 9105 Olive Creek Road, Hickman, NE 68372

Nate, per our conversation today, this is to confirm that we hooked up to the existing septic system when we built the new home for Garry and Darlene Wissink at 9105 Olive Creek Road. Their septic system was fairly new so we were allowed to do that.

Call with any questions.

Cathy

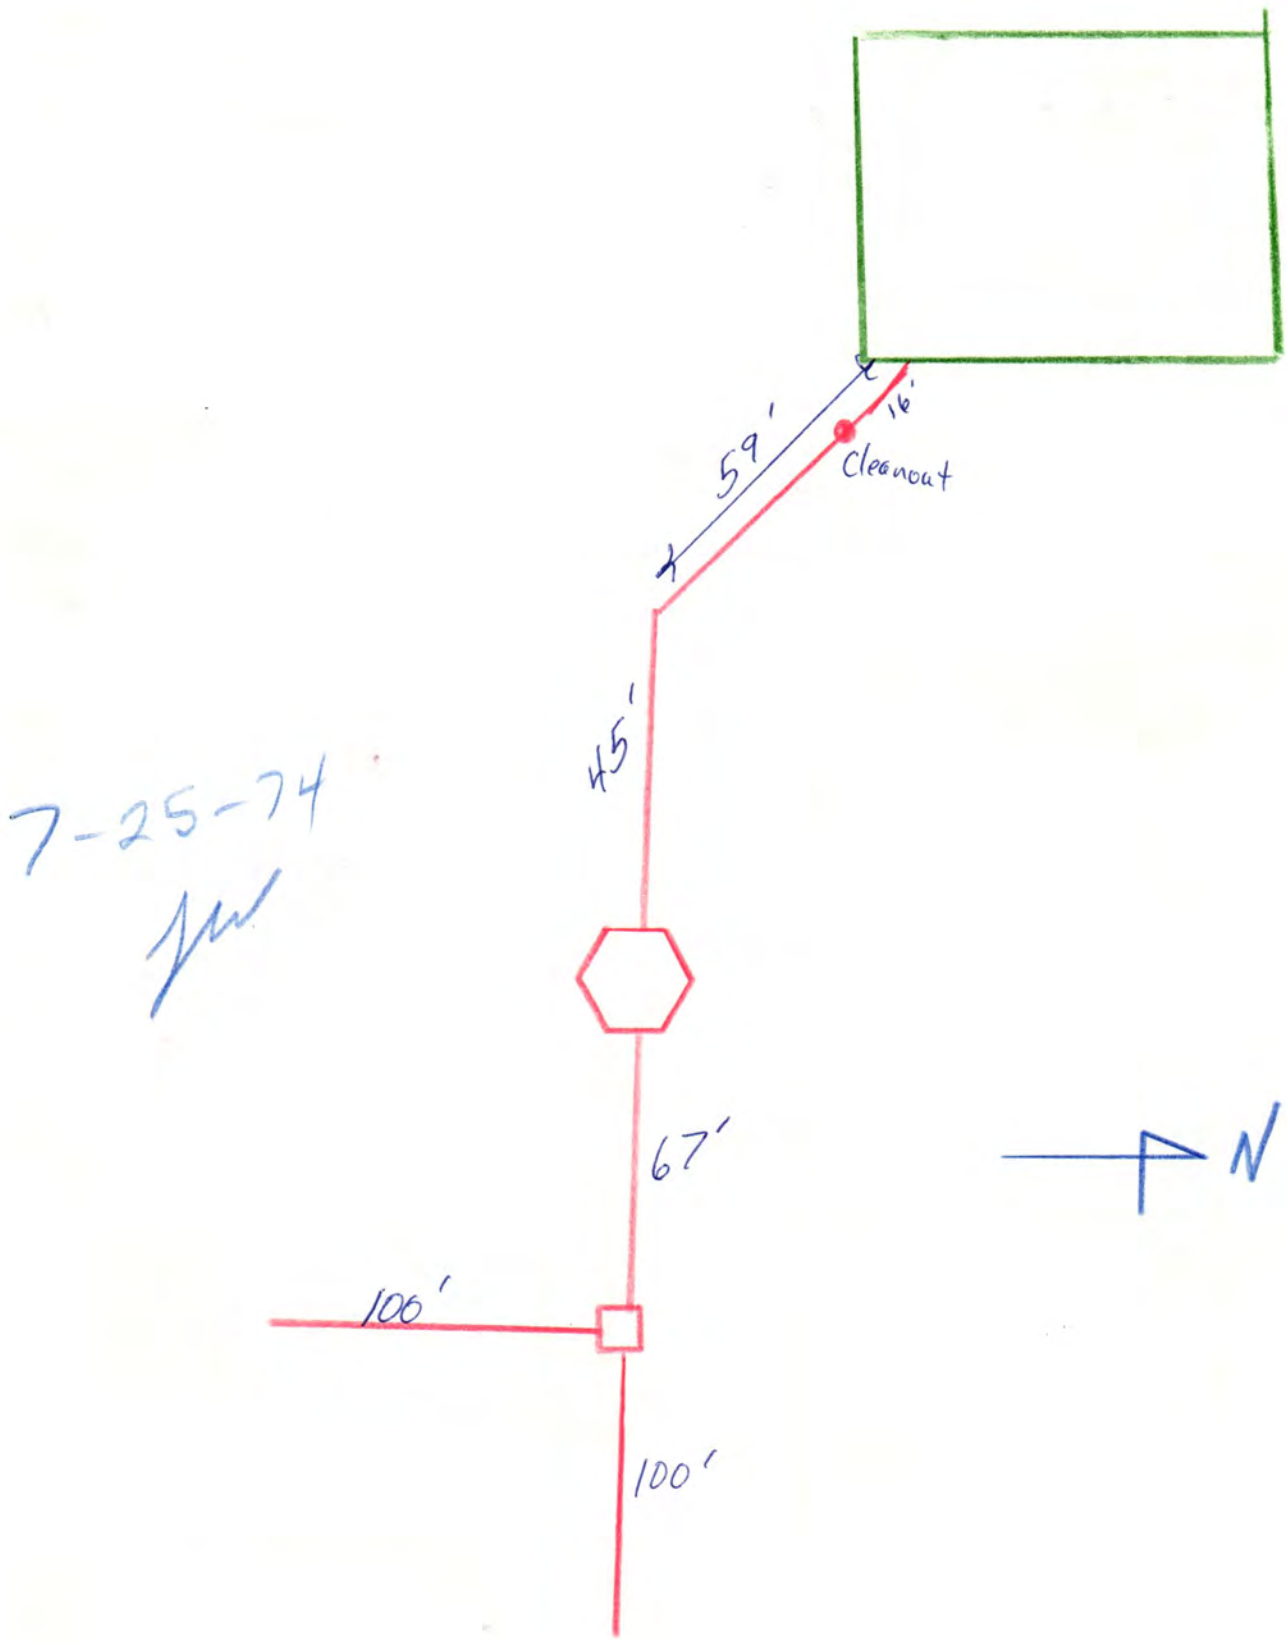

7-25-74
