LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

FILE NO. 560-C

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION — June 2, 1975

TYPE OF PERMIT — THIS PERMIT EXPIRES

George Vlasnik — Box 39; Panama

ISSUED TO — ADDRESS

T7N; R7E; Sec. 17; East 1/2; SW 1/4

LEGAL DESCRIPTION

REMARKS:

PERMIT	INSPECTION FEE	OCCUPATION TAX	TOTAL
$ 30.00	$	$	$ 30.00
ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE
6241535	110.16	148.14	6-2
RECEIPTED BY	DATE	AMOUNT	

VALID RECEIPT ONLY IF RECEIPTED IN THIS SPACE

ISSUING OFFICER

THIS PERMIT IS ISSUED AS PROVIDED BY COUNTY RESOLUTION NO. 2832

FORM HD-40(73) REQUEST FOR SITE CLEARANCE FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM

City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 475-6221)

FILE NO. 560-C

TO: Division of Environmental Health
Lincoln-Lancaster County Health Dept.

DATE: 11-29-74

The undersigned hereby requests SITE CLEARANCE to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 7N ; Range 7E ; Section 17 SW 4
   Block ____; Lot 21 IT ; Addition ____
   Street Address ____

2. Property Use: Residential ____ ☒ ; Commercial ____ ☐
   No. of Bedrooms 3 . Describe: ____
   Other Use ____ ☐
   Describe: ____

3. Type of Individual Sewage Disposal System: Septic Tank ☒ ; Other ☐

4. Distance to public sewer: NONE ft.

George Wasnik
Signature of Applicant (Owner or Lessee)

Box 39 Panama Nebr
Address

(Do not write below this double line)

REVIEWING ACTION

1. Health Department: Date Rec'd. 12/2/74 . Date Frwd. 12/2/74 . ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Hood
2. Supt. Bldg. Insp.: Date Rec'd. ____ . Date Frwd. ____ . ACTION: Approved ☐ Disapproved ☐ Signature: JWB
3. City or County Engineer: Date Rec'd. ____ . Date Frwd. 12-9-74 . ACTION: Approved ☑ Disapproved ☐ Signature: Walter Hoppe

REMARKS OR REASONS FOR DISAPPROVAL ____

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

INTER-DEPARTMENT COMMUNICATION

TO Charlie Seale

DEPARTMENT Building Inspections

ATTENTION

CARBONS TO

DATE December 2, 1974

FROM Jerrold C. Hood

DEPARTMENT Health

SUBJECT Individual Sewage System Construction - File No. 560-C

George Vlasnik
Box 39; Panama

The Application and plans have been reviewed and approved for the construction of an individual sewage disposal system on property legally described as:

T7N; R7E; Sec. 17; East 1/2; SW 1/4

Jerrold C. Hood, R.S., Supervisor
County Sanitation Section
Division of Environmental Health

JCH:sf

INTER-DEPARTMENT COMMUNICATION

TO Charlie Seale

DEPARTMENT Building Inspections

ATTENTION

CARBONS TO

DATE December 2, 1974

FROM Jerrold C. Hood

DEPARTMENT Health

SUBJECT Individual Sewage System Construction - File No. 560-C

George Vlasnik
Box 39; Panama

The Application and plans have been reviewed and approved for the construction of an individual sewage disposal system on property legally described as:

T7N; R7E; Sec. 17; East 1/2; SW 1/4

Jerrold C. Hood, R.S., Supervisor
County Sanitation Section
Division of Environmental Health

JCH:sf

INTER-DEPARTMENT COMMUNICATION

TO Charlie Seale

DEPARTMENT Building Inspections

ATTENTION

CARBONS TO

DATE December 2, 1974

FROM Jerrold C. Hood

DEPARTMENT Health

SUBJECT Individual Sewage System Construction - File No. 560-C

George Vlasnik
Box 39; Panama

The Application and plans have been reviewed and approved for the construction of an individual sewage disposal system on property legally described as:

T7N; R7E; Sec. 17: East 1/2; SW 1/4

Jerrold C. Hood, R.S., Supervisor
County Sanitation Section
Division of Environmental Health

JCH:sf

FORM HD-42(73) APPLICATION FOR PERMIT TO CONSTRUCT INDIVIDUAL SEWAGE DISPOSAL SYSTEM

City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 475-6221)

FILE NO. 560-C

DATE: 11-29-74

TO: Director of Health
Lincoln-Lancaster County Health Dept.

The undersigned hereby applies for a permit to construct an Individual Sewage Disposal System in conformance with appropriate Ordinance or Resolution, as described in this application and the annexed forms attached hereto.

1. Legal description of property: Twp. 7N ; Range 7E ; Section 17 ; Block ; Lot ; Addition .
Street Address .

2. Property Use: Residential ☒; Commercial ☐
No. of Bedrooms 3
Describe:

Other Use
Describe:

3. Type of Individual Sewage Disposal System: Septic Tank ☒; Other ☐

4. Plans and Specifications of Proposed System. (See FORM HD-45(73) PLANS & SPECIFICATIONS, SEWAGE DISPOSAL SYSTEM, attached hereto.)

5. Soil Absorption Properties. (See FORM HD-43(73) SOIL ABSORPTION TEST DATA REPORT, attached hereto).

George Vlasnik
Signature of Applicant (owner or lessee)

Box 39 Panama Nebr
Address

(Do not write below double line)

REVIEWING ACTION

1. Date Rec'd;
Filing Fee: $ 30.00

2. Site Visits:
Date: June 24-75 by: [illegible]
Date: June 25-75 by: [illegible]
Date: by:

3. Date: Approved ☒; Disapproved ☐ 12/2/74
by: Jerrold E. Wood

4. INSTALLATION FINAL WRITTEN APPROVAL
Date: June 25 75 by: Ronald Maynard

FORM HD- 43(73) SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150 and County Resolution No. 2832)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone 475-6221)

FILE NO. 392-C

PROPERTY WHERE SOIL TESTED:
Location: Township 7N; Range 7E of the 6 P.M.
Section & ¼ Sect. SW 1/4 sect. 17
Property Dimensions: 725 ft. x 321 ft.
Area: _____ acres. (Attach sketch of property showing hole location).
Owner: Billy J Egr
Address 4600 Brian Pk. Drive LINCOLN

Soil Type: Silty Clay ☐; Silty Clay Loam ☒; Sandy Loam ☐
Silty Loam ☐; Clay Loam ☐; Sandy Clay ☐

Dates of Tests: 2/16/74 to 2/17/74. Weather: Precip. 0 Temp. 55°F

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
		Pre-Saturation Period				Percolation Readings					Results		
		Start		End		Start			End				
Hole No.	Hole Depth (in.)	Date (Mo. Day)	Time (Hr. Min.)	Date (Mo. Day)	Time (Hr. Min.)	Date (Mo. Day)	Time (Hr. Min.)	Water Level (in.)	Time (Hr. Min.)	Water Level (in.)	Elapsed Time (Min.)	Water Level Drop (in.)	Percolation Rates (Min./inch)
1	38	2/16	11:00	2/17	2:30	2/17	4:00	8	4:30	7 1/4	30	3/4	
2	36	〃	〃	〃	〃	〃	4:10	6	4:40	5 3/8	30	5/8	
3	36	〃	11:15	〃	〃	〃	4:15	6 1/2	4:45	5 3/4	30	3/4	
4	36	〃	〃	〃	〃	〃	4:20	6	4:50	5 1/4	30	3/4	
5	37	〃	11:30	〃	5:00	〃	4:25	8	4:55	7 1/4	30	3/4	
6	36	〃	〃	〃	〃	〃	4:30	7 1/2	5:00	6 3/8	30	7/8	

Sum of Percolation Rates _____
Average of Rates: .75/30
Mean of Rates: _____

Billy J Egr
Signature of Person Conducting Test

Address 4600 Brian Pk Drive 3/4
Phone: 489-3009

(Do not write below this line)

REVIEWING ACTION

REMARKS: _____

Approved Percolation Rate(s)
A. 40 min./inch
B. _____ min./inch
C. _____ min./inch

DATE: 2-19-74

James Wiruba
Signature of Reviewing Official

FORM HD- 45(73) PLANS & SPECIFICATIONS
SEWAGE DISPOSAL SYSTEM
(Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 475-6221)

FILE NO. 560-C

SPECIFICATIONS

DATE: 11-29-74


A. BUILDING SEWER:
1. Material plastic; Diameter 4 in.
2. Distance above basement floor ___in.; or below basement floor ___in.
3. Distance between dwelling and septic tank ___ft.
4. Number of clean-outs ___.
5. Distances To:
Well or Suction Line 50 ft.;
Stream ___ft.; Pressure Line ___ft.;
Property Line ___ft.

B. SEPTIC TANK (Provide construction drawings.)
1. Material Concrete; No. of compartments 1.
2. Capacity 1000 gals.; Liquid depth ___in.
3. Factory Built: Yes ☒ (Company Pre Cast)
No ☐
4. Manholes: Over Inlet; diam. ___in.
Over Outlet; diam. ___in.
Below Grade ___in.
5. Inlet: Baffle ☐; or Tee ☐
6. Outlet: Baffle ☐; or Tee ☐
Depth of outlet below inlet ___in.
7. Depth of top of tank below finished grade 16 in.
8. Distances To:
Well or Suction Line ___ft.;
Stream ___ft.; Pressure Line ___ft.;
Property Line ___ft.

C. DISTRIBUTION BOX
1. Material Concrete; No. available outlets 6.
2. Factory Built: Yes ☒, (Company Pre Cast) No ☐
3. Dimension: Length ___in.; Width ___in. Depth ___in.
4. Distance from Septic Tank 11 ft.
5. Serial Distribution: Yes ☐, No ☐
(If yes, show detailed plans.)


D. ABSORPTION FIELD: (Provide drawings.)
1. Type: perforated pipe ~~Tile~~ ~~Half moons~~
2. Lateral Lines: Depth below grade ___in.
Number 3; Length of each line 100 ft
Total length of Laterals 300 ft.; 100 / 100
Slope ___in/100 ft. Diameter of pipe ___in.; Shape ∩
Material: concrete ☐; fiber asbestos ☐; clay ☐; other PVC
Distance between lateral lines ___ft.
3. Trench Dimensions: Depth ___in.; Width ~~48~~ in. 3' wide
4. Filter Material: gravel.
Depth of material from trench bottom 12 in.
5. Distances To:
Well or Suction Line 100+ ft.;
Stream ___ft.; Pressure Line ___ft.
Property Line ___ft.
6. Percolation Rate: ___minutes/inch

TYPICAL SKETCHES

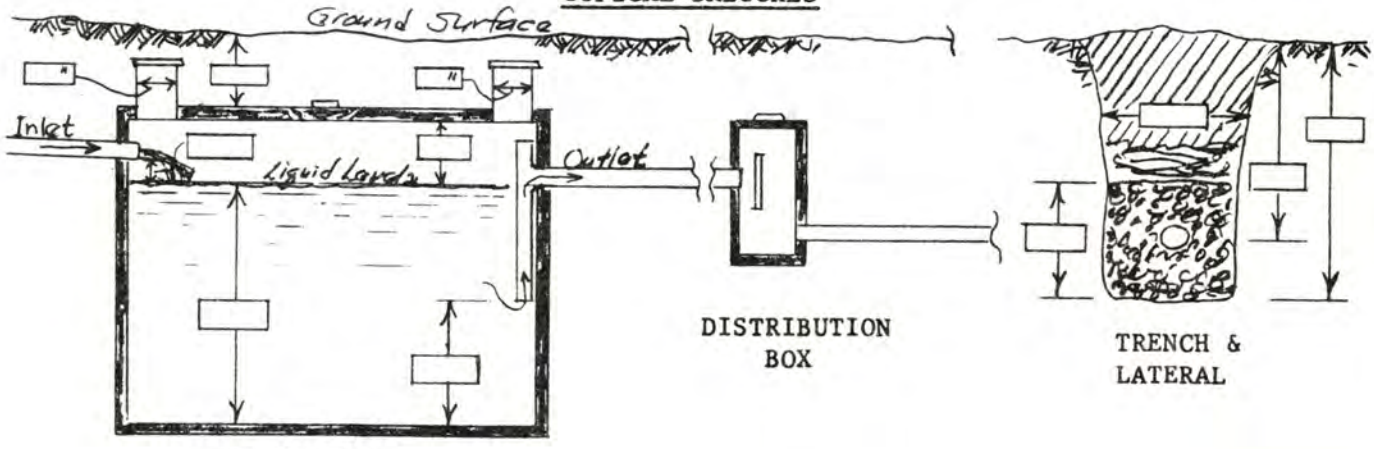

SEPTIC TANK

Signature of Applicant

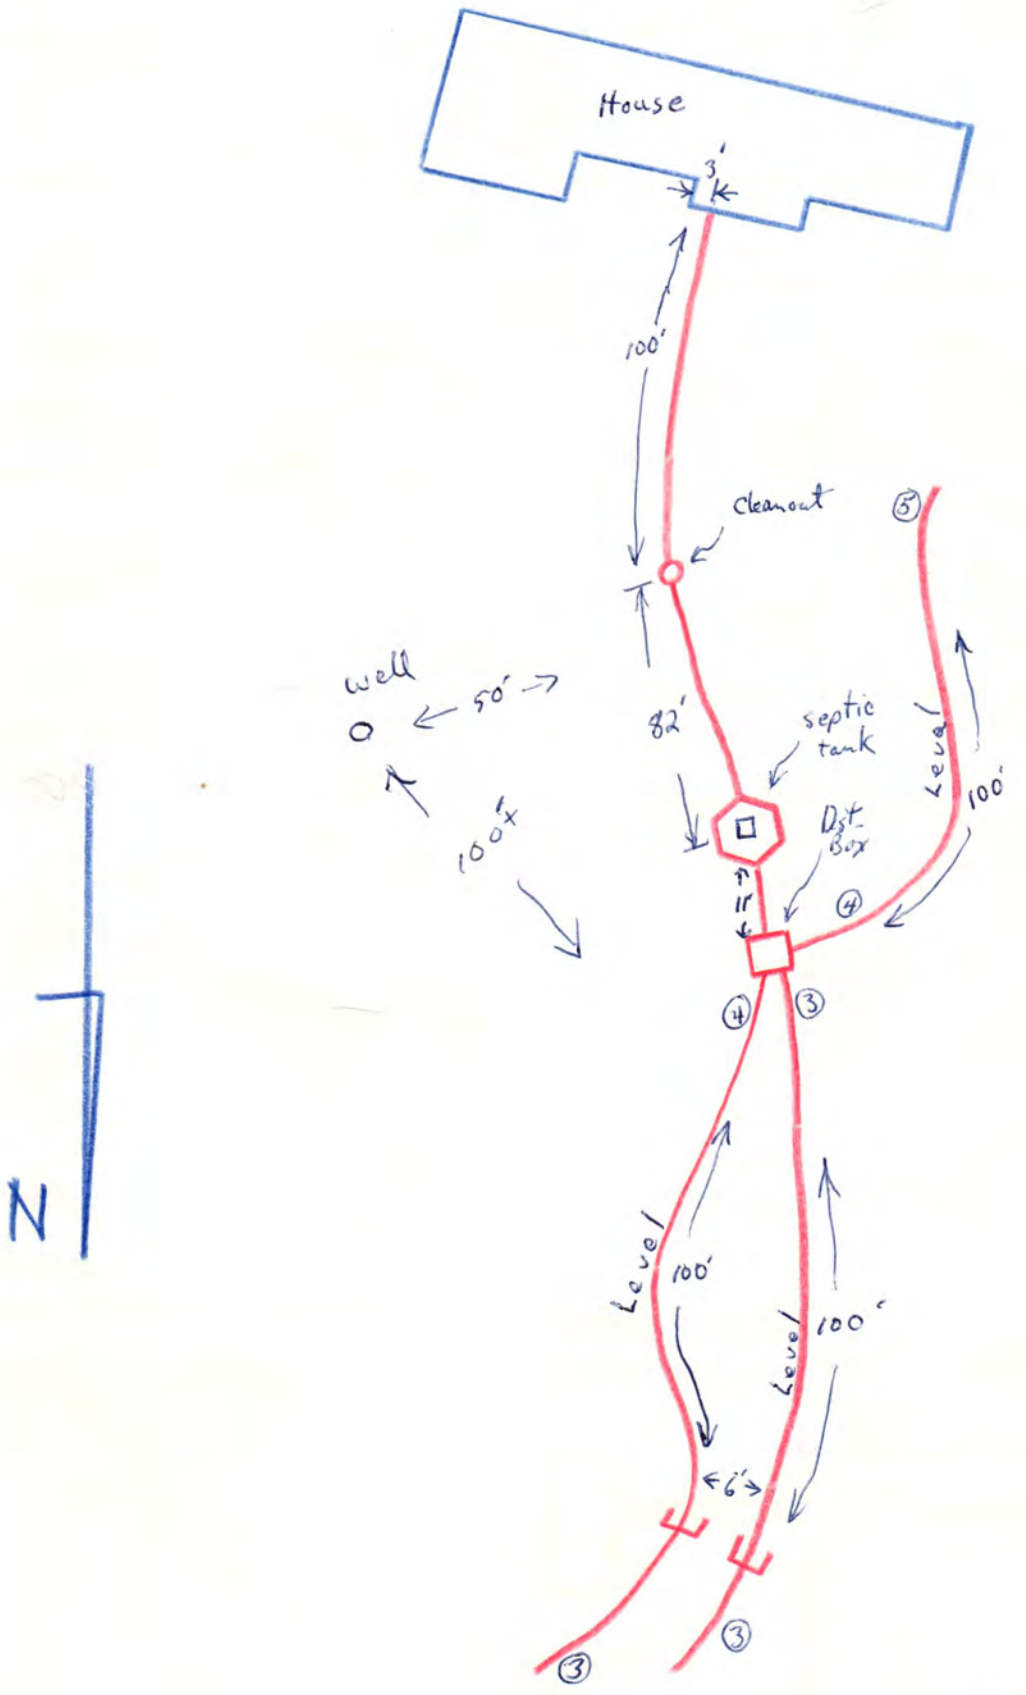
House
3'
100'
Cleanout
5
well
50'
100'
82'
septic tank
Dist. Box
Level
100'
11'
4
3
4
3
Level
100'
Level
100'
6'
3
3
N

June - 25 - 75

Jm
