LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

ENVIRONMENTAL HEALTH DIVISION

2200 St. Marys Ave Lincoln, NE 68502-3785 (402) 471-8000

NON TRANSFERABLE

PERMIT

Permit
SEWAGE SYSTEM REPAIR

No. 92390028701

Issued 07/21/92
Expires 01/21/93
Revenue Code 18754

Establishment
DAN CILLESSEN
T8N R5E SEC 1

FEES: $50.00

TOTAL $50.00

Permittee
DAN CILLESSEN
6200 W BENNET RD
DENTON NE 68339

Issued By M. Jane Ford
Health Director

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW
"POST IN A PROMINENT PLACE"

FORM HD-41(73) APPLICATION FOR PERMIT TO ALTER, EXTEND OR REPAIR INDIVIDUAL SEWAGE DISPOSAL SYSTEM

City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Ave.
Lincoln, Nebraska 68502 (Phone: 471-7800)

FILE NO. _____

TO: Division of Environmental Health
Lincoln-Lancaster County Health Dept.

DATE: 7-15-92

The undersigned hereby applies for a permit to ALTER ☒, EXTEND ☐, or REPAIR ☐ an existing Individual Sewage Disposal System, in conformance with appropriate Ordinance or Resolution, as described in this application and drawings attached hereto.

1. Legal description of property: Twp. 8N ; Range 5E ; Section 1 ;
Block _____ ; Lot _____ ; Addition _____
Street Address _____

2. Property Use: Residential ✓ ☐ ; Commercial _____ ☐
No. Bedrooms 3
Describe _____
Other Use ☐
Describe _____

3. Type of existing Individual Sewage Disposal System: Septic Tank ✓ ; Other ☐

4. Description of proposed alteration, extension or repair: install 1½ round Lagoon

5. Work to be done by: Owner ☐ ; or Contractor ☒ , Friesen Excavating
Contractor's Name

6. Estimated cost of project:

a. Materials	$
b. Labor	$
c. Other	$
TOTAL	$ 1952.00

DAN CILLESSEN
Signature of Applicant (owner or lessee)

6200 WEST BENNET ROAD
Address
DENTON, NEBRASKA

(Do not write below this line)


REVIEWING ACTION

1. Date Rec'd: _____
Filing Fee: $ 50.00

2. Site Visits:
Date: 7/15/92 by: J.C.H.
Date: _____ by: _____
Date: _____ by: _____

3. Date: Approved ☒ ; Disapproved ☐
by: Jerrold E. Hood

4. INSTALLATION FINAL WRITTEN APPROVAL
Date: _____ by: _____

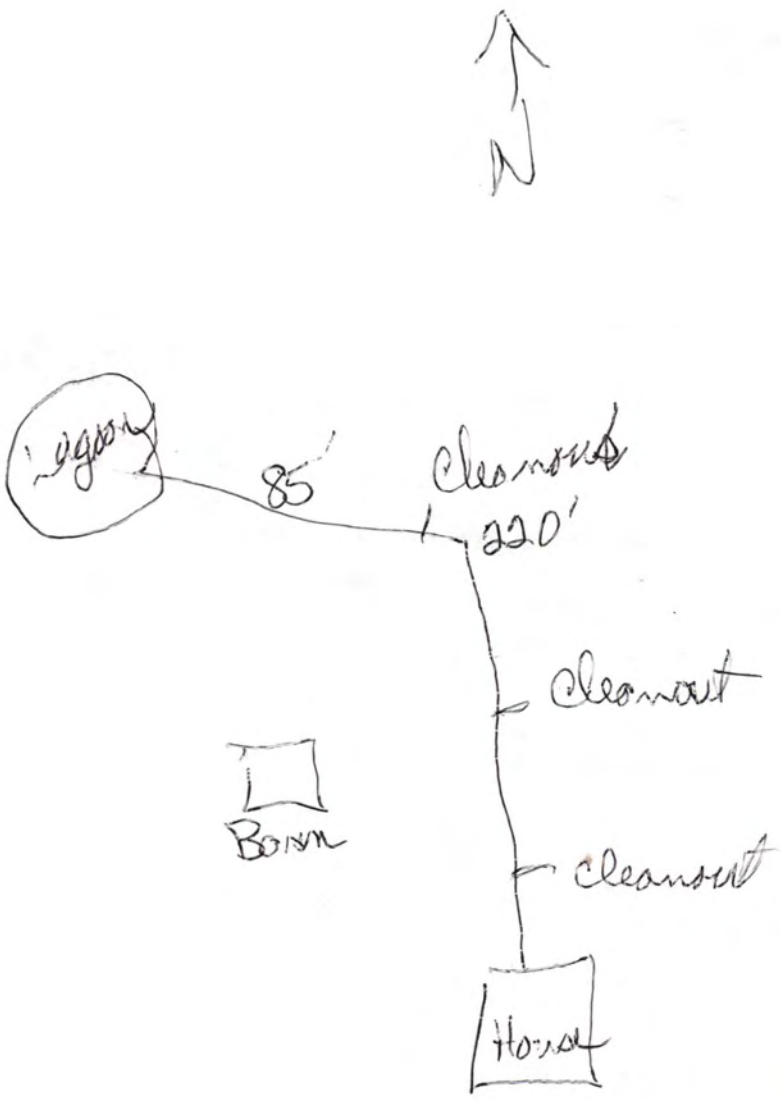
N
85'
220'
Barn

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

FILE NO. 1240-C

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION — TYPE OF PERMIT

JUNE 8, 1978 — THIS PERMIT EXPIRES

Larry Machiejewski — ISSUED TO

6901 Van Dorn, Lincoln, NE — ADDRESS

T8N, R6E, Section 1 — LEGAL DESCRIPTION

Lot 10

REMARKS: NON-TRANSFERABLE

PERMIT	INSPECTION FEE	OCCUPATION TAX	TOTAL
$ 30.00	$	$	$ 30.00
ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE
	110.16	148.14	6-2

RECEIPTED BY — DATE — AMOUNT

VALID RECEIPT ONLY IF RECEIPTED IN THIS SPACE

HEALTH — ISSUING OFFICER

THIS PERMIT IS ISSUED AS PROVIDED BY COUNTY RESOLUTION NO. 2832

20109-0977

FORM HD-40(73) REQUEST FOR SITE CLEARANCE FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM

City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 475-6221)

Lot 10

FILE NO. 1240-C

TO: Division of Environmental Health
Lincoln-Lancaster County Health Dept.

DATE: 12-7-77

The undersigned hereby requests SITE CLEARANCE to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

SEE ATTACHED

1. Legal description of property: Twp. 8N ; Range 5E ; Section 1
Block ____; Lot ____; Addition ____
Street Address ____

2. Property Use: Residential ____ ☒ ; Commercial ____ ☐
No. of Bedrooms 3 . Describe: ____
Other Use ____ ☐
Describe: ____

3. Type of Individual Sewage Disposal System: Septic Tank ☒ ; Other ☐

4. Distance to public sewer: ____ ft.

Larry Maciejewski
Signature of Applicant (Owner or Lessee)

6901 Van Dorn
Address

(Do not write below this double line)

REVIEWING ACTION

1. Health Department: Date Rec'd. 12/8/77 . ACTION: Approved ☒ Disapproved ☐
Date Frwd. 12/8/77 . Signature: Jerrold C. Wood

2. Supt. Bldg. Insp.: Date Rec'd. 12/8/77 . ACTION: Approved ☒ Disapproved ☐
Date Frwd. 12/8/77 . Signature: Glenn N. Sherwood

3. City or County Engineer : Date Rec'd. 12-8-77 . ACTION: Approved ☒ Disapproved ☐
Date Frwd. 12-8-77 . Signature: Henry Graff

REMARKS OR REASONS FOR DISAPPROVAL ____

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

FORM HD-42(73) APPLICATION FOR PERMIT TO CONSTRUCT INDIVIDUAL SEWAGE DISPOSAL SYSTEM

City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 475-6221)

Lot 10

FILE NO. 1240-C

DATE: 12-7-77

TO: Director of Health
Lincoln-Lancaster County Health Dept.

The undersigned hereby applies for a permit to construct an Individual Sewage Disposal System in conformance with appropriate Ordinance or Resolution, as described in this application and the annexed forms attached hereto. SEE ATTACHED

1. Legal description of property: Twp. 8N ; Range 5E ; Section 1 ; Block ____ ; Lot ____ ; Addition ____.
Street Address ____.

2. Property Use: Residential ____ ☒ ; Commercial ____ ☐
No. of Bedrooms 3
Describe: ____
Other Use ____
Describe: ____

3. Type of Individual Sewage Disposal System: Septic Tank ☒ ; Other ☐

4. Plans and Specifications of Proposed System. (See FORM HD-45(73) PLANS & SPECIFICATIONS, SEWAGE DISPOSAL SYSTEM, attached hereto.)

5. Soil Absorption Properties. (See FORM HD-43(73) SOIL ABSORPTION TEST DATA REPORT, attached hereto).

Larry Maciejewski
Signature of Applicant (owner or lessee)

6901 Van Dorn
Address

(Do not write below double line)

* It rained on the open laterals some silting was noted in laterals

REVIEWING ACTION

1. Date Rec'd; ____
Filing Fee: $ 30.00

2. Site Visits:
Date: 9-7-78 by: *
Date: 7-10-78 by: ~~***~~
Date: ____ by: ____

3. Date: Approved ☒ ; Disapproved ☐ 12/8/77
by: Jerrold C. Hood

4. INSTALLATION FINAL WRITTEN APPROVAL ** not yet
Date: 9-7-78 by: ~~Ron Hoppe~~

~~* plat map not what was to be approved~~
~~** laterals were installed in muddy soil conditions + peeling of the sidewall + packing of the trench bottom were noted~~

FORM HD- 45(73) PLANS & SPECIFICATIONS
SEWAGE DISPOSAL SYSTEM
(Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 475-6221)

FILE NO. 1240-C

Lot 10

SPECIFICATIONS

DATE: _____


A. BUILDING SEWER:
1. Material Pla; Diameter 4 in.
2. Distance above basement floor ___in.; or below basement floor 12 in.
3. Distance between dwelling and septic tank ___ft.
4. Number of clean-outs _____.
5. Distances To:
Well or Suction Line ___ft.;
Stream ___ft.; Pressure Line ___ft.;
Property Line ___ft.

B. SEPTIC TANK (Provide construction drawings.)
1. Material Conc; No. of compartments _____.
2. Capacity 1000 gals.; Liquid depth 53 in.
3. Factory Built: Yes ☒ (Company Smitek) No ☐
4. Manholes: Over Inlet; diam. 24 in.
Over Outlet; diam. ___in.
Below Grade 8 in.
5. Inlet: Baffle ☐; or Tee ☐
6. Outlet: Baffle ☐; or Tee ☒
Depth of outlet below inlet ___in.
7. Depth of top of tank below finished grade 8 in.
8. Distances To:
Well or Suction Line 100 ft.;
Stream ___ft.; Pressure Line 50 ft.;
Property Line ___ft.

C. DISTRIBUTION BOX
1. Material Pla; No. available outlets 7.
2. Factory Built: Yes ☒, (Company Home made) No ☐
3. Dimension: Length 18 in.; Width 12 in. Depth 12 in.
4. Distance from Septic Tank 10 ft.
5. Serial Distribution: Yes ☒, No ☐ (If yes, show detailed plans.)

D. ABSORPTION FIELD: (Provide drawings.)
1. Type: perforated
2. Lateral Lines: Depth below grade 18 in. Number 3; Length of each line ___ft. Total length of Laterals 318 ft.; Slope 6 in/100 ft. Diameter of pipe 4 in.; Shape round Material: concrete ☐; fiber asbestos ☐; clay ☐; other Pla Distance between lateral lines ___ft.
3. Trench Dimensions. Depth 18 in.; Width 36 in.
4. Filter Material: road Gravel. Depth of material from trench bottom 12 in.
5. Distances To:
Well or Suction Line 100 ft.;
Stream ___ft.; Pressure Line 50 ft.
Property Line ___ft.
6. Percolation Rate: _____minutes/inch

TYPICAL SKETCHES

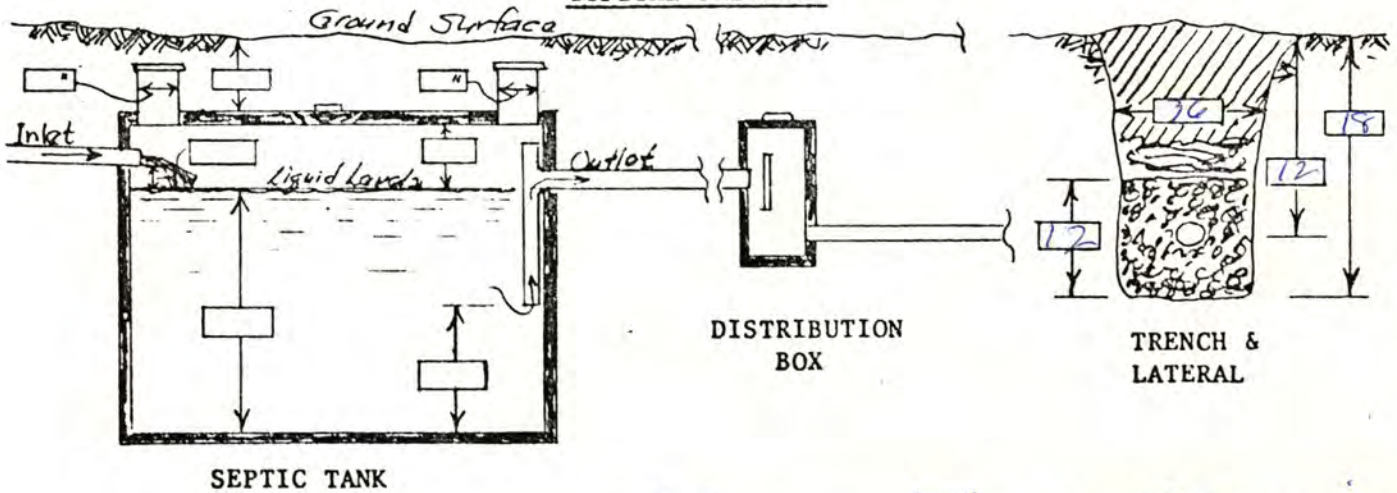

SEPTIC TANK

DISTRIBUTION BOX

TRENCH & LATERAL

2-19

Larry Maciejewski
Signature of Applicant

FORM HD- 45(73) PLANS & SPECIFICATIONS
SEWAGE DISPOSAL SYSTEM
(Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 475-6221)

FILE NO. 1240-C

SPECIFICATIONS

Lot 10

DATE: _____


A. BUILDING SEWER:
1. Material Pla; Diameter 4 in.
2. Distance above basement floor ___ in.; or below basement floor 12 in.
3. Distance between dwelling and septic tank ___ ft.
4. Number of clean-outs _____.
5. Distances To:
Well or Suction Line ___ ft.;
Stream ___ ft.; Pressure Line ___ ft.;
Property Line ___ ft.

B. SEPTIC TANK (Provide construction drawings.)
1. Material Conn; No. of compartments 1.
2. Capacity 1000 gals.; Liquid depth 53 in.
3. Factory Built: Yes ☒ (Company Smith) No ☐
4. Manholes: Over Inlet; diam. 21 in.
Over Outlet; diam. ___ in.
Below Grade 8 in.
5. Inlet: Baffle ☐; or Tee ☐
6. Outlet: Baffle ☐; or Tee ☒
Depth of outlet below inlet 4 in.
7. Depth of top of tank below finished grade 8 in.
8. Distances To:
Well or Suction Line ___ ft.;
Stream ___ ft.; Pressure Line ___ ft.;
Property Line ___ ft.

C. DISTRIBUTION BOX
1. Material Pla; No. available outlets 7.
2. Factory Built: Yes ☒, (Company Hand Core) No ☐
3. Dimension: Length 18 in.; Width 12 in. Depth 12 in.
4. Distance from Septic Tank 10 ft.
5. Serial Distribution: Yes ☒, No ☐ (If yes, show detailed plans.)

D. ABSORPTION FIELD: (Provide drawings.)
1. Type: perforated
2. Lateral Lines; Depth below grade 18 in. Number 3 4/shot; Length of each line ___ ft Total length of Laterals 318 ft.; Slope 4 in/100 ft. Diameter of pipe 4 in.; Shape round Material: concrete ☐; fiber asbestos ☐; clay ☐; other Pla Distance between lateral lines ___ ft.
3. Trench Dimensions. Depth 18 in.; Width 36 in.
4. Filter Material: road Gravel. Depth of material from trench bottom 12 in.
5. Distances To:
Well or Suction Line 100 ft.;
Stream ___ ft.; Pressure Line 50 ft.
Property Line ___ ft.
6. Percolation Rate: _____ minutes/inch

TYPICAL SKETCHES

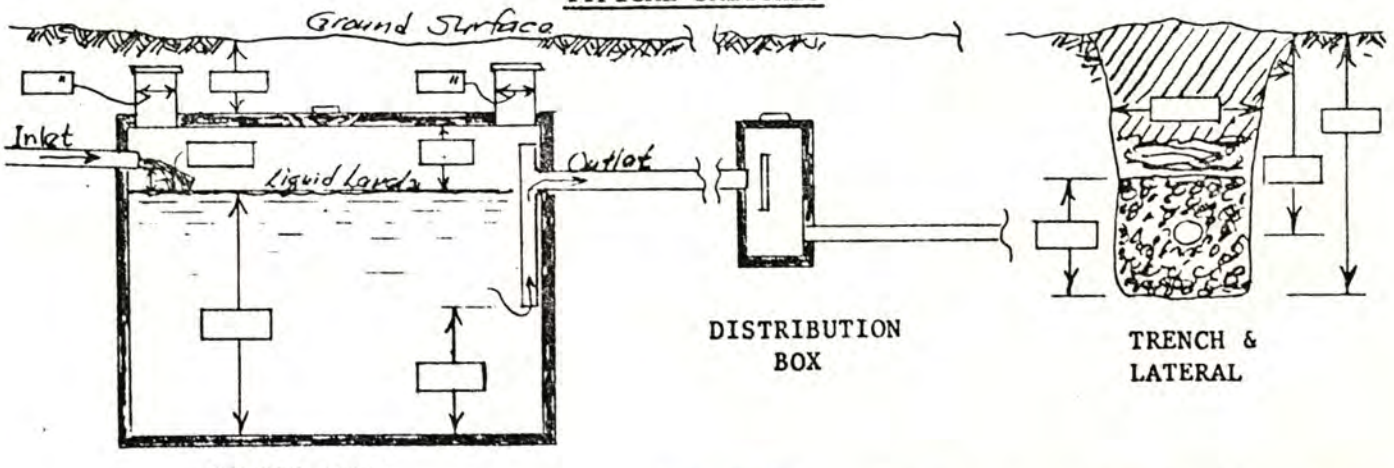

Lot 9 Larry Maciejewski
Signature of Applicant

FORM HD-43 (73) SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150 and County Resolution No. 2832)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone 474-1541)

Lot 10

FILE NO. 1240-C

PROPERTY WHERE SOIL TESTED:
Location: Township 8N : Range 5E
Section & ¼ Sect. 1 Lot 9
Property Dimensions: ____ft. x ____ft.
Area: 5.97 acres. (Attach sketch of property showing hole location).
Soil Type: Silty Clay ; Silty Clay Loam ; Sandy Loam
Silty Loam ; Clay Loam ; Sandy Clay

Owner: Larry Maciejewski
Address: 6901 Van Dorn

Dates of Tests: 12-6-77 to 12-7-77. Weather: Precip. No Temp. 31

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
		Pre-Saturation Period				Percolation Readings						Results	
		Start		End		Start			End				
Hold No.	Hole Depth (in.)	Date (Mo. Day)	Time (Hr. Min.)	Date (Mo. Day)	Time (Hr. Min.)	Date (Mo. Day)	Time (Hr. Min.)	Water Level (in.)	Time (Hr. Min.)	Water Level (in.)	Elapsed Time (Min.)	Water Level Drop (in.)	Percolation Rates (Min./inch)
1	18	12-6	10	12-6	2	12-7	11	6	12	4 7/8	60	1 1/8	
	↓	↓	↓	↓	↓	↓	↓	↓	↓		↓		
2										5		1	
3										5		1	
4										5		1	
5										4 15/16		1/16	
6										4 15/16		1/16	

Sum of Percolation Rates:
Average of Rates:
Mean of Rates:

SINTEK SERV. CO.
2425 SOUTH ST.
LINCOLN, NE 68502
475-1486

Signature of Person Conducting Test
Address
Phone

(Do not write below this line)

REVIEWING ACTION

REMARKS: Wymore Silty Clay Loam. (S.C.S.)
DATE: December 8, 1977

Approved Percolation Rate (a)
A. 56 min./inch
B. ____ min./inch
C. ____ min./inch

Verrold C. Hood
Signature of Reviewing Official

Corrected Deed

Official Survey Record

LANCASTER County, Nebraska

ALLIED SURVEYING AND MAPPING
LAND SURVEYORS
7116 Starr Street Lincoln, Nebraska 68505


Telephone 46

Sheet 1 of

Survey of the East One Hundred Ninety-Seven and No Tenths (197.0) feet of the West One Thou
Five Hundred Seventy-Six and No Tenths (1,576.0) feet of the South One-Half of the
Southeast Quarter of Section 1 T 8 N, R 7 E of the 6t
5E

Job No. 0276

Date September ,

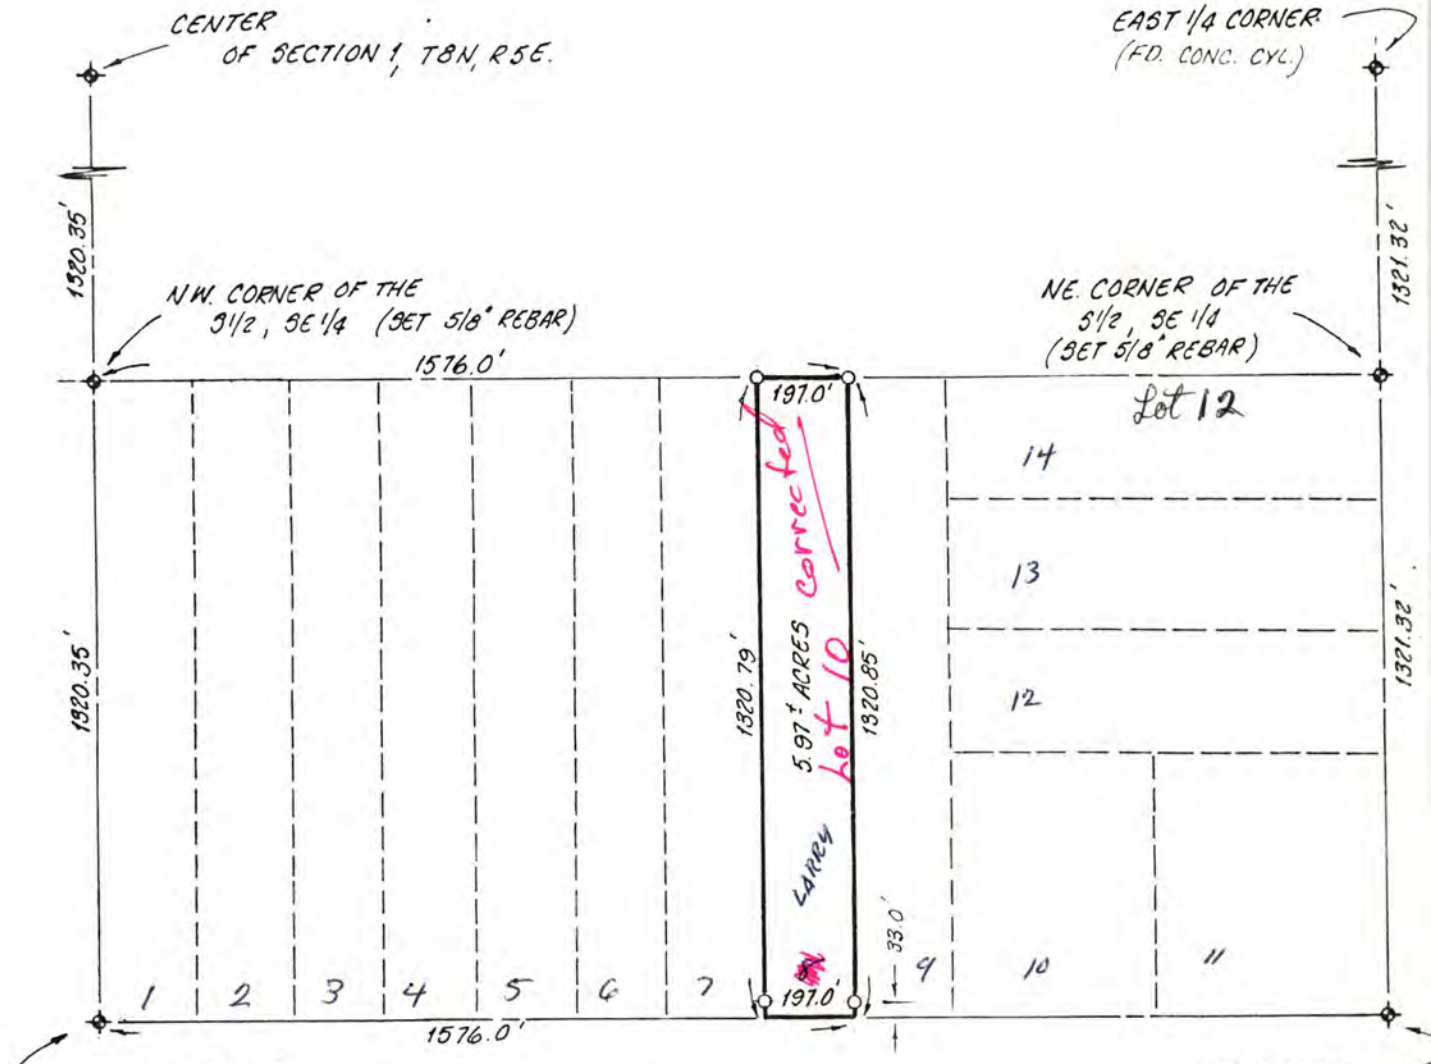

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

FILE NO. 1239-C

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION — TYPE OF PERMIT

JUNE 8, 1978 — THIS PERMIT EXPIRES

Larry Machiejewski — ISSUED TO

6901 Van Dorn, Lincoln, NE — ADDRESS

T8N# R5E, Section 1 — LEGAL DESCRIPTION

Lot #

REMARKS: NON-TRANSFERABLE

PERMIT	INSPECTION FEE	OCCUPATION TAX	TOTAL
$ 30.00	$	$	$ 30.00
ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE
	110.16	148.14	6-2

RECEIPTED BY — DATE — AMOUNT

VALID RECEIPT ONLY IF RECEIPTED IN THIS SPACE

HEALTH — ISSUING OFFICER

THIS PERMIT IS ISSUED AS PROVIDED BY COUNTY RESOLUTION NO. 2832

20109-0977

FORM HD-40(73) REQUEST FOR SITE CLEARANCE FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM

City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 475-6221)

Lot 11

FILE NO. 1239-C

TO: Division of Environmental Health
Lincoln-Lancaster County Health Dept.

DATE: 12-7-77

The undersigned hereby requests SITE CLEARANCE to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 8N ; Range 5E ; Section 1
   Block _____ ; Lot 11 ; Addition SEE ATTACHED
   Street Address _____

2. Property Use: Residential ☒ ; Commercial ☐
   No. of Bedrooms 3 . Describe: _____
   Other Use ☐
   Describe: _____

3. Type of Individual Sewage Disposal System: Septic Tank ☒ ; Other ☐

4. Distance to public sewer: _____ ft.

Larry Maciejewski
Signature of Applicant (Owner or Lessee)

6901 Van Dorn
Address

(Do not write below this double line)

REVIEWING ACTION

1. Health Department: Date Rec'd. 12/8/77 . Date Frwd. 12/8/77 . ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Rose

2. Supt. Bldg. Insp.: Date Rec'd. 12/8/77 . Date Frwd. 12/8/77 . ACTION: Approved ☒ Disapproved ☐ Signature: Harry M. Shemwell

3. City or County Engineer: Date Rec'd. 12-8-77 . Date Frwd. 12-8-77 . ACTION: Approved ☒ Disapproved ☐ Signature: Henry Graff

REMARKS OR REASONS FOR DISAPPROVAL _____

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

FORM HD-43 (73) SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150 and County Resolution No. 2832)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone 474-1541)

Lot 11

FILE NO. 1239-C

PROPERTY WHERE SOIL TESTED:
Location: Township 8 : Range 5
Section & ¼ Sect. 1
Property Dimensions: ____ ft. x ____ ft.
Area: 5.97 acres. (Attach sketch of property showing hole location).
Soil Type: Silty Clay ; (Silty Clay Loam) ; Sandy Loam
Silty Loam ; Clay Loam ; Sandy Clay

Owner: Larry Maciejewski
Address: 6901 Van Dorn Lot 8

Dates of Tests: 12-6-77 to 12-7-77 Weather: Precip. No Temp. 31

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
		Pre-Saturation Period				Percolation Readings						Results	
		Start		End		Start			End				
Hold No.	Hole Depth (in.)	Date (Mo. Day)	Time (Hr. Min.)	Date (Mo. Day)	Time (Hr. Min.)	Date (Mo. Day)	Time (Hr. Min.)	Water Level (in.)	Time (Hr. Min.)	Water Level (in.)	Elapsed Time (Min.)	Water Level Drop (in.)	Percolation Rates (Min./inch)
1	18	12-6	11	12-6	3	12-7	1	6	2	5	60	1	
2	↓	↓	↓	↓	↓	↓	↓	↓	↓	5	↓	1	
3										5		1	
4										4 7/8		1 1/8	
5										4 7/8		1 1/8	
6										5		1	

Sum of Percolation Rates:
Average of Rates:
Mean of Rates:

Signature of Person Conducting Test
SINTEK SERV. CO.
Address 2425 SOUTH ST.
LINCOLN, NE 68502
Phone 475-1486

(Do not write below this line)

REVIEWING ACTION

REMARKS: Wymore Silty Clay Loam. (L.C.L.D.)
DATE: December 8, 1977

Approved Percolation Rate (a)
A. 56 min./inch
B. ____ min./inch
C. ____ min./inch

Gerrold C. Hood
Signature of Reviewing Official

FORM HD-42(73) APPLICATION FOR PERMIT TO CONSTRUCT INDIVIDUAL SEWAGE DISPOSAL SYSTEM

City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 475-6221)

Lot 11

FILE NO. 1239-C

DATE: 12-7-77

TO: Director of Health
Lincoln-Lancaster County Health Dept.

The undersigned hereby applies for a permit to construct an Individual Sewage Disposal System in conformance with appropriate Ordinance or Resolution, as described in this application and the annexed forms attached hereto. SEE ATTACHED

1. Legal description of property: Twp. 8N ; Range 5E ; Section 1 ; Block ; Lot 8 ; Addition .
Street Address .

2. Property Use: Residential ☒; Commercial ☐
No. of Bedrooms 3
Describe:
Other Use
Describe:

3. Type of Individual Sewage Disposal System: Septic Tank ☒; Other ☐

4. Plans and Specifications of Proposed System. (See FORM HD-45(73) PLANS & SPECIFICATIONS, SEWAGE DISPOSAL SYSTEM, attached hereto.)

5. Soil Absorption Properties. (See FORM HD-43(73) SOIL ABSORPTION TEST DATA REPORT, attached hereto).

Larry Maciejewski
Signature of Applicant (owner or lessee)

6901 Van Dorn
Address

(Do not write below double line)

REVIEWING ACTION

1. Date Rec'd;
Filing Fee: $ 30.00

2. Site Visits:
Date: 7-7-78 by: pm
Date: by:
Date: by:

3. Date: Approved ☒; Disapproved ☐ 12/8/77
by: Jerrold C. Hood

4. INSTALLATION FINAL WRITTEN APPROVAL
Date: 7-7-78 by: Ron Maynard *

* Rain fell on the open laterals & silting was noted.

FORM HD- 45(73) PLANS & SPECIFICATIONS
SEWAGE DISPOSAL SYSTEM
(Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 475-6221)

FILE NO. 1239-C

Lot 11

SPECIFICATIONS

DATE: 12-7-77


A. BUILDING SEWER:
1. Material Pla ; Diameter 4 in.
2. Distance above basement floor ___ in.; or below basement floor 12 in.
3. Distance between dwelling and septic tank ___ ft.
4. Number of clean-outs ___.
5. Distances To:
Well or Suction Line 100 ft.;
Stream ___ ft.; Pressure Line 50 ft.;
Property Line ___ ft.

B. SEPTIC TANK (Provide construction drawings.)
1. Material Conc ; No. of compartments ___.
2. Capacity 1000 gals.; Liquid depth 53 in.
3. Factory Built: Yes ☐ (Company Smith)
No ☐
4. Manholes: Over Inlet; diam. 24 in.
Over Outlet; diam. 24 in.
Below Grade 8 in.
5. Inlet: Baffle ☐; or Tee ☐
6. Outlet: Baffle ☐; or Tee ☒
Depth of outlet below inlet 4 in.
7. Depth of top of tank below finished grade 6 in.
8. Distances To:
Well or Suction Line 100 ft.;
Stream ___ ft.; Pressure Line 50 ft.;
Property Line ___ ft.

C. DISTRIBUTION BOX
1. Material Pla ; No. available outlets 7.
2. Factory Built: Yes ☒, (Company Hand one) No ☐
3. Dimension: Length 18 in.; Width 12 in. Depth 12 in.
4. Distance from Septic Tank 10 ft.
5. Serial Distribution: Yes ☒, No ☐
(If yes, show detailed plans.)

D. ABSORPTION FIELD: (Provide drawings.)
1. Type: perforated
2. Lateral Lines: Depth below grade 18 in.
Number ___; Length of each line ___ ft
Total length of Laterals 318 ft.;
Slope 6 in/100 ft. Diameter of pipe 4 in.; Shape round
Material: concrete ☐; fiber asbestos ☐; clay ☐; other Pla
Distance between lateral lines ___ ft.
3. Trench Dimensions. Depth 18 in.; Width 36 in.
4. Filter Material: road Gravel
Depth of material from trench bottom 12 in.
5. Distances To:
Well or Suction Line 100 ft.;
Stream ___ ft.; Pressure Line 50 ft.
Property Line ___ ft.
6. Percolation Rate: ___ minutes/inch

TYPICAL SKETCHES

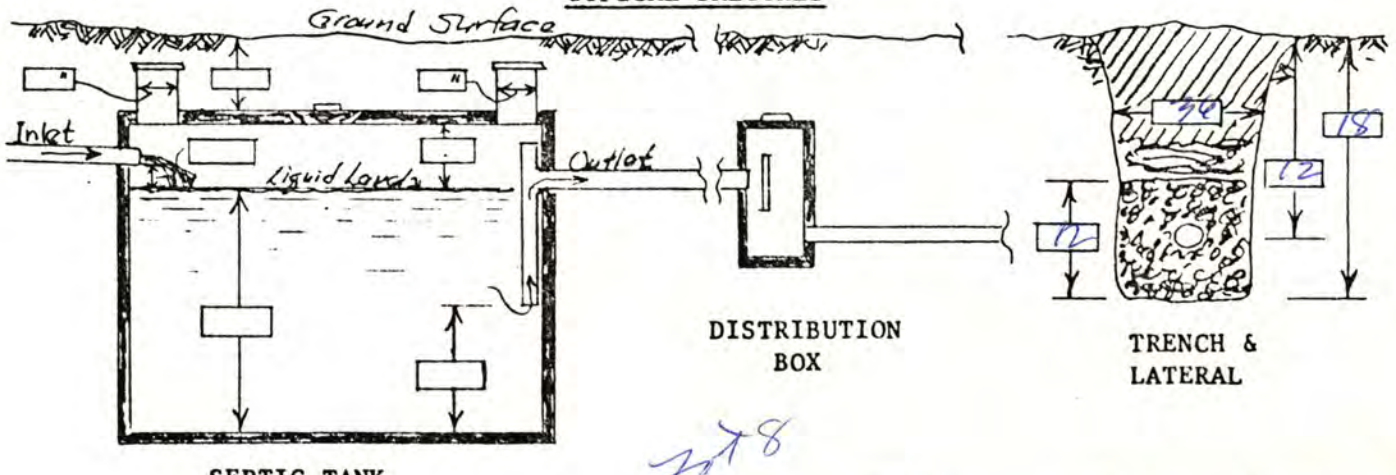

Jt 8

Larry Maciejewski
Signature of Applicant

FORM HD- 45(73) PLANS & SPECIFICATIONS
SEWAGE DISPOSAL SYSTEM
(Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 475-6221)

FILE NO. 1239-C

Lot 11

SPECIFICATIONS

DATE: 12-7-77


A. BUILDING SEWER:
1. Material Pla; Diameter 4 in.
2. Distance above basement floor ___in.; or below basement floor 12 in.
3. Distance between dwelling and septic tank ___ft.
4. Number of clean-outs _____.
5. Distances To:
Well or Suction Line 100 ft.;
Stream ___ft.; Pressure Line 50 ft.;
Property Line ___ft.

B. SEPTIC TANK (Provide construction drawings.)
1. Material Cm; No. of compartments 1.
2. Capacity 1000 gals.; Liquid depth 53 in.
3. Factory Built: Yes ☐ (Company Sintes)
No ☐
4. Manholes: Over Inlet; diam. 24 in.
Over Outlet; diam. ___in.
Below Grade _____in.
5. Inlet: Baffle ☐; or Tee ☐
6. Outlet: Baffle ☐; or Tee ☒
Depth of outlet below inlet 4 in.
7. Depth of top of tank below finished grade 8 in.
8. Distances To:
Well or Suction Line 100 ft.;
Stream ___ft.; Pressure Line 50 ft.;
Property Line ___ft.

C. DISTRIBUTION BOX
1. Material Pla; No. available outlets 7.
2. Factory Built: Yes ☒, (Company Hanel Core) No ☐
3. Dimension: Length 18 in.; Width 12 in Depth 12 in.
4. Distance from Septic Tank 16 ft.
5. Serial Distribution: Yes ☒, No ☐
(If yes, show detailed plans.)

D. ABSORPTION FIELD: (Provide drawings.)
1. Type: perforated
2. Lateral Lines: Depth below grade 18 in.
Number ___; Length of each line ___ft
Total length of Laterals 318 ft.;
Slope 6 in/100 ft. Diameter of pipe 4 in.; Shape round
Material: concrete ☐; fiber asbestos ☐; clay ☐; other Pla
Distance between lateral lines ___ft.
3. Trench Dimensions. Depth 18 in.; Width 36 in.
4. Filter Material: round Gravel
Depth of material from trench bottom 12 in.
5. Distances To:
Well or Suction Line 100 ft.;
Stream ___ft.; Pressure Line 50 ft.
Property Line ___ft.
6. Percolation Rate: _____minutes/inch

TYPICAL SKETCHES

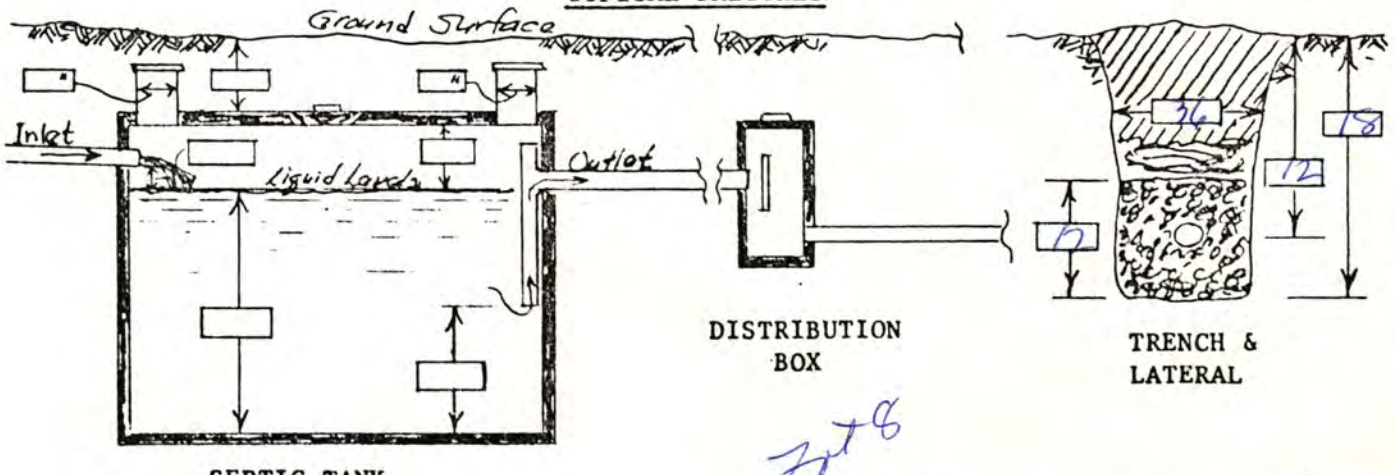

Jr + 8

Larry Maciejewski
Signature of Applicant

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

D

DATE: 7-7-78

FILE NO. _____

Lot 11


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material ~~C~~ PVC; Diameter 4 in.
2. Distance above basement floor _____ in., or below basement floor 12 in.
3. Distance between dwelling and septic tank ~~60~~ 12½ ft.
4. Number of clean-outs 2.
5. Distances to:
Well or Suction Line ~~100~~ + ft.; Stream _____ ft.; Pressure Line Above ft.; Property Line ~~80~~ ft.

B. SEPTIC TANK:
1. Material ~~C~~ Fiberglass; No. of compartments 1.
2. Capacity 1000 gals.;
3. Factory Built: Yes ☒ No ☐
(Company Mississippi)
4. Manholes: Over Inlet; diam. ~~24~~ in.
Over Outlet; diam. 24 in.
Riser Above ☒ Below ☐ Grade ~~24~~ in.
5. Inlet: Baffle ☒ ; or Tee ☐
6. Outlet: Baffle ☒ ; or Tee ☐
7. Depth of top of tank below finished grade 36 in.
8. Distances to:
Well or Suction Line _____ ft.; Stream _____ ft.; Pressure Line 200 + ft.; Property Line _____ ft.

C. DISTRIBUTION BOX:
1. Material Fiberglass; Number - available outlets 4.
2. Factory Built: Yes ☒ No ☐
(Company " ")
3. Distance from Septic Tank 12 ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☐ Perforated Pipe ☒
Diameter of Half Round _____ or Perforated Pipe 4" _____.
Material: fiberglass ☐ ; plastic ☒ ; concrete ☐ ; other _____.
2. Lateral Lines:
Number 4; Length of each line 100, 90, 60, 70, _____ ft.;
Total length of laterals 318 ft.;
Distance between lateral lines ~~30~~ 20 + ft.
3. Trench dimensions: Width 3 ft.;
Slope 4 in/100 ft.; Average Depth ~~36~~ 30 in.
4. Filter Material: Gravel
Depth of Material ~~12~~ 16 in.
5. Distances to:
Well or Suction Line ~~200 +~~ ft.; Stream _____ ft.; Pressure Line 200 + ft.; Property Line _____ ft.

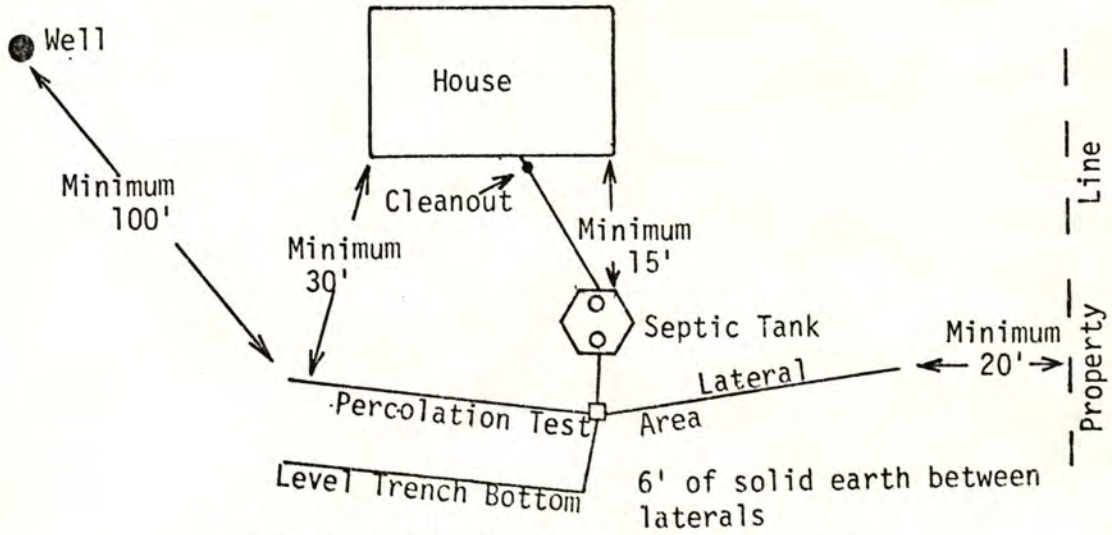

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

Official Survey Record

LANCASTER County, Nebraska


ALLIED SURVEYING AND MAPPING
LAND SURVEYORS
7116 Starr Street Lincoln, Nebraska 68505

Telephone 466-

Survey of the East One Hundred Ninety-Seven and No Tenths (197.0) feet of the West One Thous
Seven Hundred Seventy-Three and No Tenths (1,773.0) feet of the South One-Half of the
Southeast Quarter of Section 1 T 8 N, R 5 E of the 6th


Job No. 0276

Date September , 19

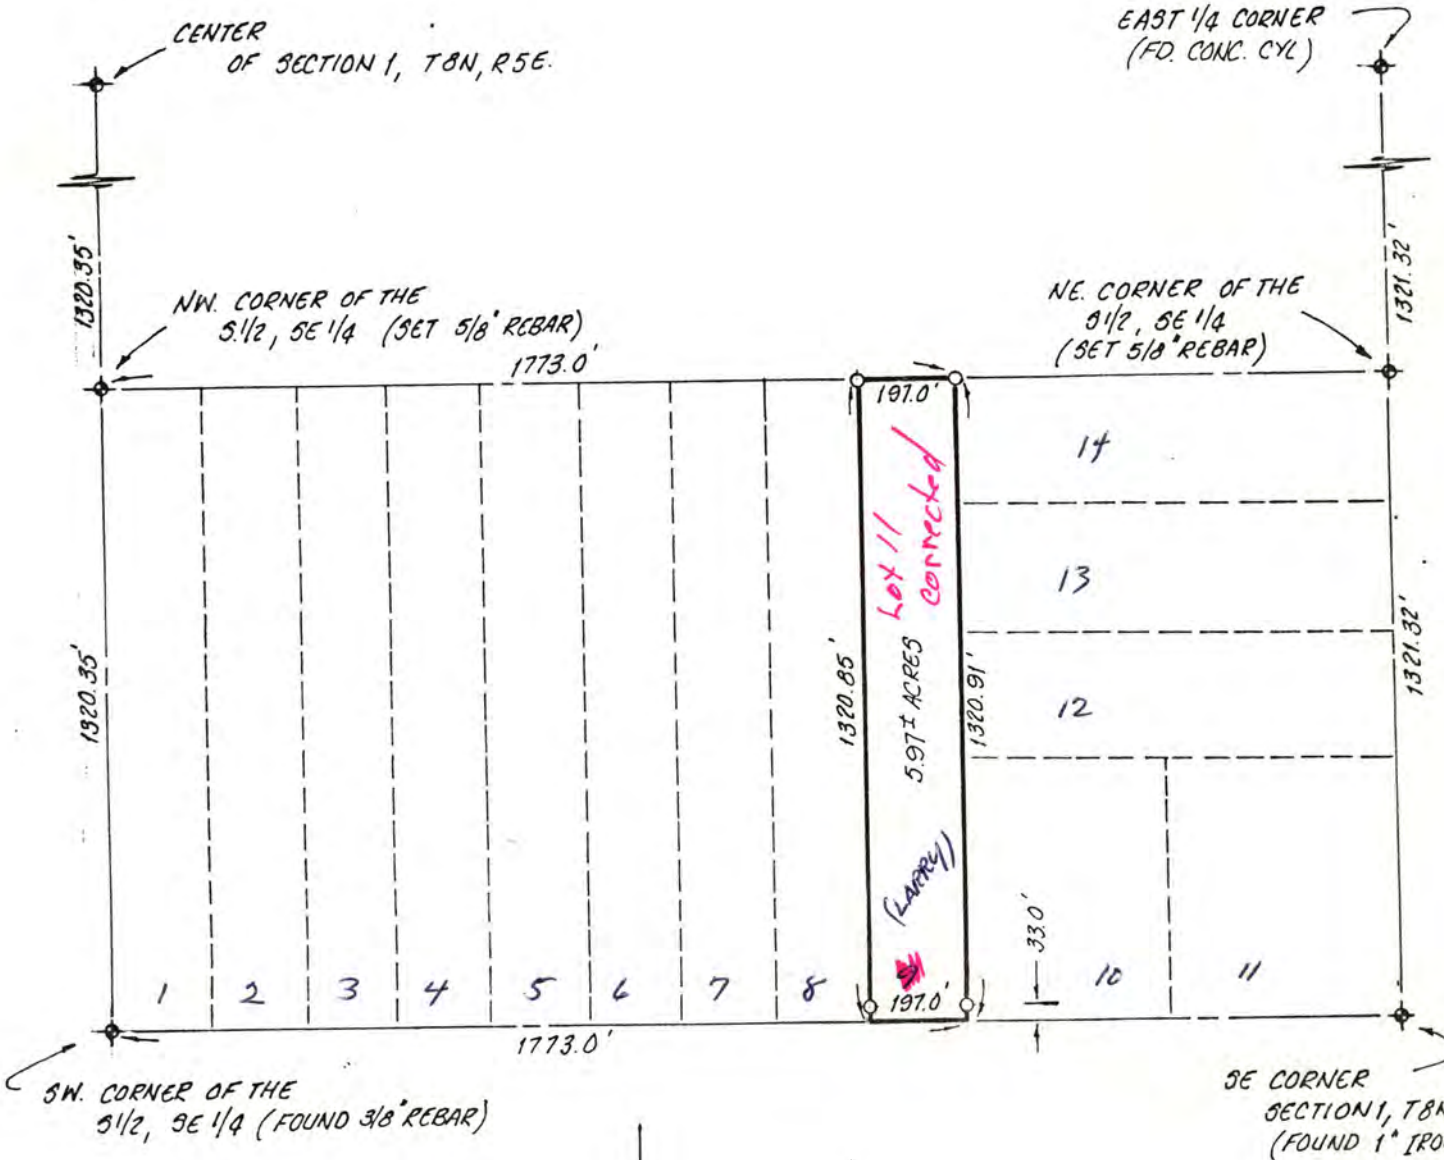

AS BUILT DRAWING OF SYSTEM

DATE 7-7-78 INSTALLER Pathyco Plumbing

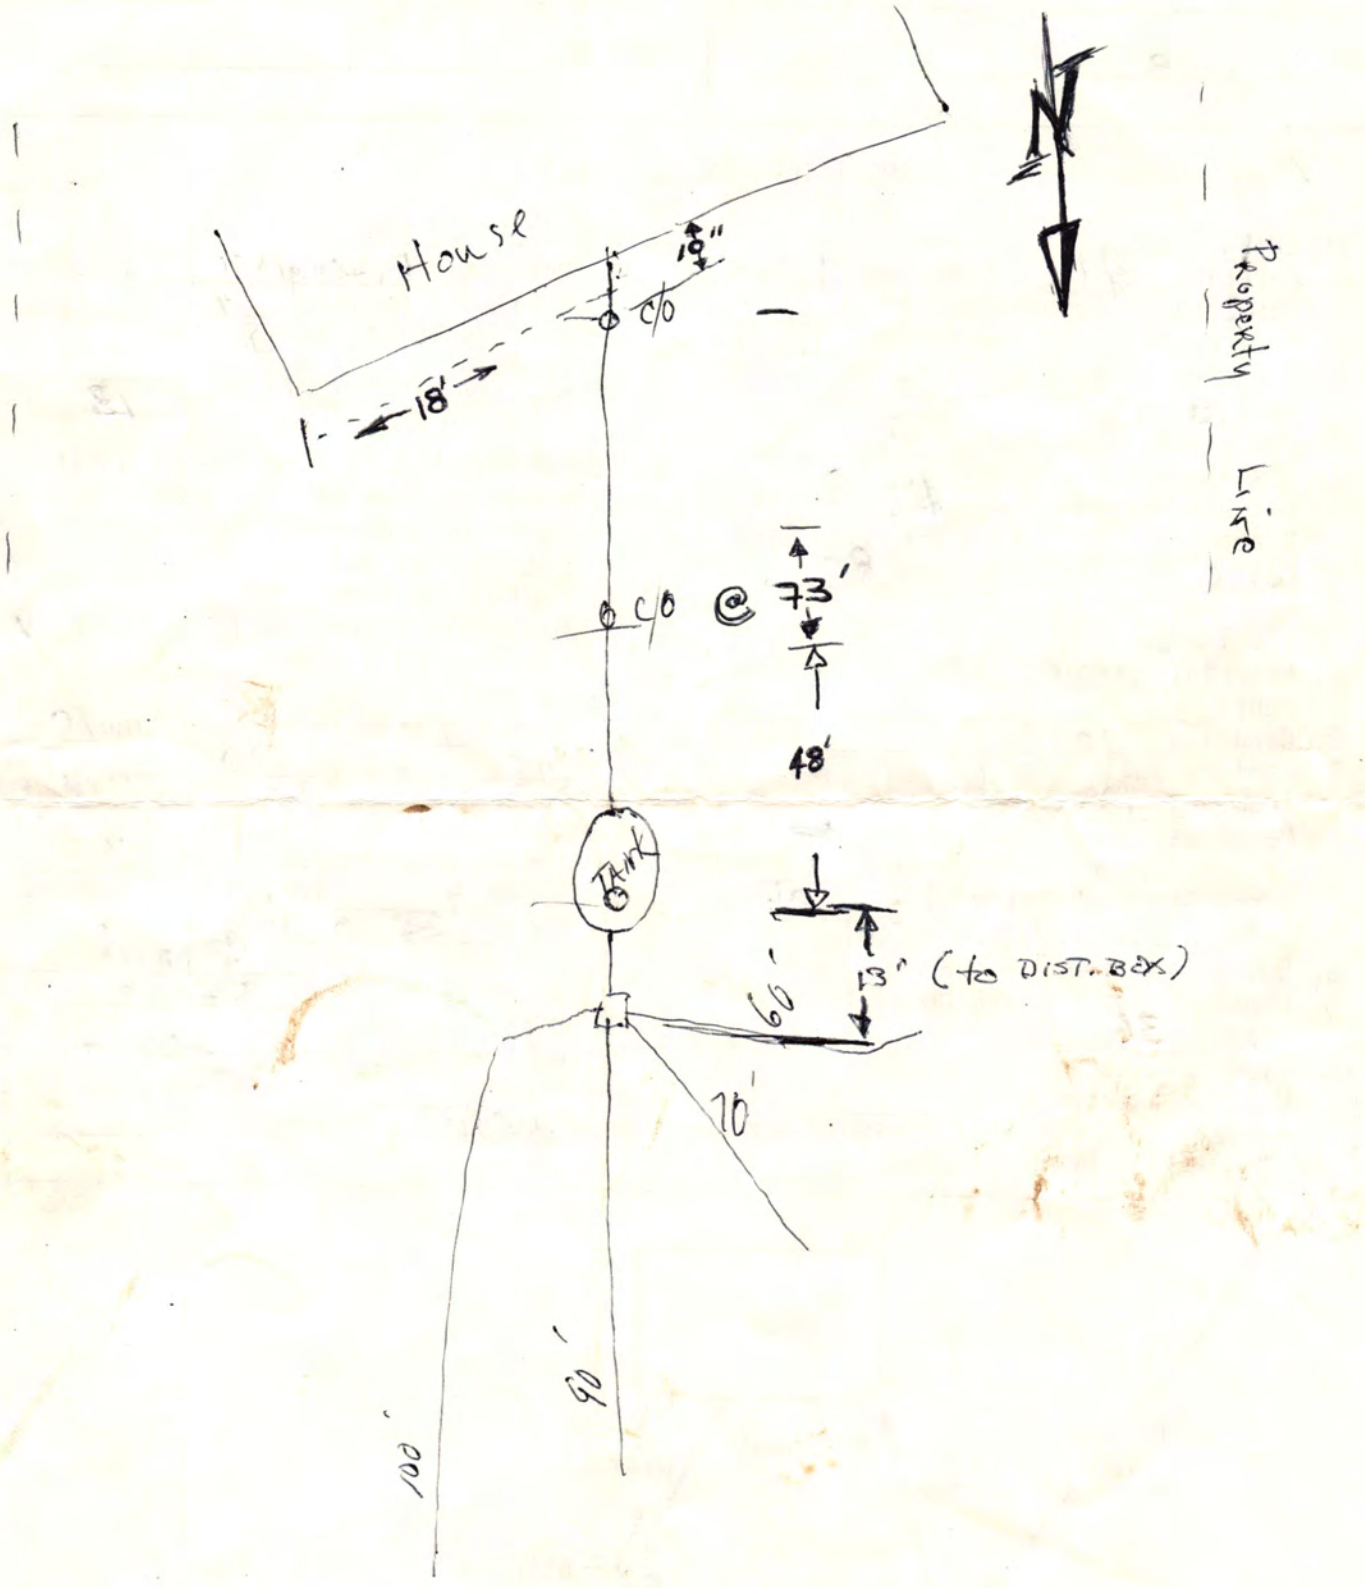

Lot 11
