LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

2200 ST. MARYS
LINCOLN, NEBRASKA 68502

FILE NO. 2176-C

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION — TYPE OF PERMIT

AUGUST 28, 1985 — THIS PERMIT EXPIRES

GERALD ROACH — ISSUED TO

RT #1 LINCOLN, NE 68502 — ADDRESS

T8N; R6E; Sec 3; 1101 WEST SALTILLO — LEGAL DESCRIPTION

REMARKS: NON-TRANSFERABLE NEW CONSTRUCTION

PERMIT	INSPECTION FEE	OCCUPATION TAX	TOTAL
$ 60.00	$	$	$ 60.00
ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE
	110.16	148.14	6-2

RECEIPTED BY — DATE — AMOUNT

VALID RECEIPT ONLY IF RECEIPTED IN THIS SPACE

HEALTH
ISSUING OFFICER

THIS PERMIT IS ISSUED AS PROVIDED BY COUNTY RESOLUTION NO. 2832

20109-0977

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

A

FILING FEE: $ 60.00

FILE NO. 2176-C

DATE: _____

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 8 N ; Range 6 E ; Section 3 ;
   Block _____ : Lot _____ : Addition _____
   Street Address Hot West Saltillo

2. Property Use: Residential ☐ ; Commercial ☐ Other Use ☒
   No. of Bedrooms _____. Describe Trailer Court

3. Type of Individual Sewage Disposal System: Septic Tank ☐ ; Other ☒

4. Distance to public sewer: None ft.

Gerald Rook
Signature of Applicant (Owner or Lessee)

Route 1 Lincoln Ne 68502
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. 2/28/85. Date Frwd. 3/1/85. ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Hood

2. Supt. Bldg. Insp.: or Village Clerk: Date Rec'd. 3-1-85. Date Frwd. 3-1-85. ACTION: Approved ☒ Disapproved ☐ Signature: Paul Bauer

3. City or County Engineer: Date Rec'd. 3/1/85. Date Frwd. 11. ACTION: Approved ☑ Disapproved ☐ Signature: Don Thomas

REMARKS OR REASONS FOR DISAPPROVAL _____

Site Visits:
Date: _____ by: _____
Date: _____ by: _____
Date: _____ by: _____

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

INSTALLATION FINAL WRITTEN APPROVAL
Date: _____ By: _____

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

3140 "N" STREET
ENVIRONMENTAL HEALTH DIVISION
LINCOLN NE 68510-1514
(402) 441-8000

NON TRANSFERABLE

Permit

SEWAGE SYSTEM REPAIR
ADDING A RISER TO EXISTING TANK;
INLET PIPE TO ATTACH TO DWELLING

Establishment

GERALD D ROACH
T8N R6E SEC 3 QTR NW
1101 W SALTILLO RD--ROCA

Permittee

GERALD D ROACH
201 W OLD CHENEY RD
LINCOLN NE 68523-9209

008134

No. 98390059401

Issued 09/15/98
Expires 03/15/99
Revenue Code 3157

FEES:

PAID

TOTAL $0.00

Issued By Health Director
Lincoln-Lancaster County Health Department

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW "POST IN A PROMINENT PLACE"

SEP 9 1998

Individual Sewage Disposal System
Application to Alter, Extend or Repair

☐ Municipal Code 24.38 ☒ County Resolution Number 2832

Date: 9. 8. 98	File No.:

The undersigned hereby applies for a permit to: ☐ **ALTER** ☐ **EXTEND** ☒ **REPAIR** an existing Individual Sewage Disposal System, in conformance with appropriate Ordinance or Resolution, as described in this application and drawings attached hereto.

1. **Legal description of property:**
   Township 8N Range 6E Section 3T 1/4 Section NW
   Block _____ Lot _____ Addition _____
   Street Address 1101 W Saltillo Rt 1 Roca Ne 68430

2. **Property use:** ☒ residential ☐ commercial ☐ other use
   Number of bedrooms 3 Describe Ranch Type.

3. **Type of Present Individual Disposal System:** ☒ septic tank ☐ lagoon ☐ other

4. **Description of proposed alteration, extension or repair:** adding a riser to existing 1000 gal Tank and extending inlet pipe to attach to dwelling

5. **Work to be done by:** ☒ owner ☐ contractor's name _____

6. **Estimated project:** a. Repair, replace or minor extension with a cost of less than $400.00 (no fee required).
   b. Total cost is greater than $400.00 (Return fee with this application).
   c. A "construction permit" is required if the use, operation, location, or type of the system is being changed.

Print Name GERALD ROACH Address 20 W old Cheney Rd Lincoln NE 68523 Phone 423-5366
Applicant Signature (owner or lessee) Gerald D Roach

Please include the permit fee ($50.00) with this application

(Please do not write below this line)

Date rec'd 9/10/98 REVIEW: ☒ approved ☐ disapproved By: Jerrold C. Hood

Site visits:
Date 6/6/99 By J. C. Hood Basement finally built
Date _____ By _____
Date _____ By _____

Installation final written approval
Date 10/6/99 By Jerrold C. Hood

Return to: Lincoln-Lancaster County Health Department - Environmental Health Division
3140 "N" Street, Lincoln, NE. 68510
441-8022

White - EH Pink - Business Office Revised 1/98

OCT 5 1999

D

Lincoln-Lancaster County Health Department
Environmental Health Division
3140 "N" Street • Lincoln, NE 68510-1514
Phone: 402-441-8022

Permit Number: 983900594

Sewage Disposal System

As Built Plans & Specifications

Date 10-4-99

System Location (Indicate correct number and street)

Address 1101 W. SALTILLO RD. City ROCA NE, Zip 68430
(no rural route)

A. Building Sewer

1. Material: PVC
   Diameter: 4" in.
2. Distance above basement floor: 72" in.
   or distance below basement floor: ~~72~~ in.
3. Distance between dwelling and septic tank: 25' ft.
4. Number of clean-outs: 1
5. Distances to: well or suction line 300 ft.
   stream NONE ft.
   pressure line 20 ft.
   property line 105 ft.

B. Septic Tank

1. Material: CONCRETE
   Number of compartments: 1
2. Capacity: 1500 gal.
3. Factory built: ☒ Yes ☐ No
4. Manholes: Over inlet, diameter 28 in.
   Over outlet, diameter 18" in.
   Riser: ☒ above ☒ below grade 2 in.
5. Inlet: ☒ baffle ☐ tee
6. Outlet: ☒ baffle ☐ tee
7. Depth to top of tank, below unfinished grade: 30 in.
8. Distances to: Well or suction line 325 ft.
   Stream NONE ft.
   Pressure line ~~350~~ ft.
   Property line ~~110~~ 90 ft.

C. Distribution Box

1. Material: CONCRETE
   Number available outlets: 3
2. Factory built: ☒ Yes ☐ No
3. Distance from septic tank: 20' ft.

D. Absorption Field


(Provide as-built drawings on back of this form)

1. Type: ☒ Half rounds ☐ Perforated pipe
   Diameter of half round:
   or perforated pipe: 18"
   Material: ☐ fiberglass ☐ plastic ☒ concrete
   ☐ other
2. Lateral lines: Number 3
   Length of each line: ~~350~~ ft. 75 ft.
   75 ft. ft., ft.
3. Trench dimensions: Width 4' ft.
   Slope 1" in/100 ft.
   Average depth 18" in
4. Filter material: GRAVEL
   Depth of material 1' in.
5. Distances to: Well or suction line 400' ft.
   Stream NONE ft.
   Pressure line 100' ft.
   Property line 25' ft.


Complete "As Built" drawing on back of this form.

Indicate North with Arrow


Individual Sewage System Design (Example)

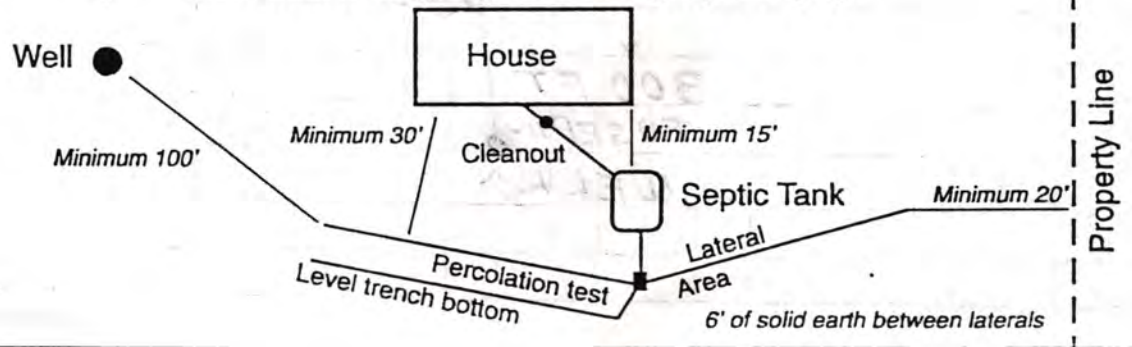

FORM 23-103 10-96

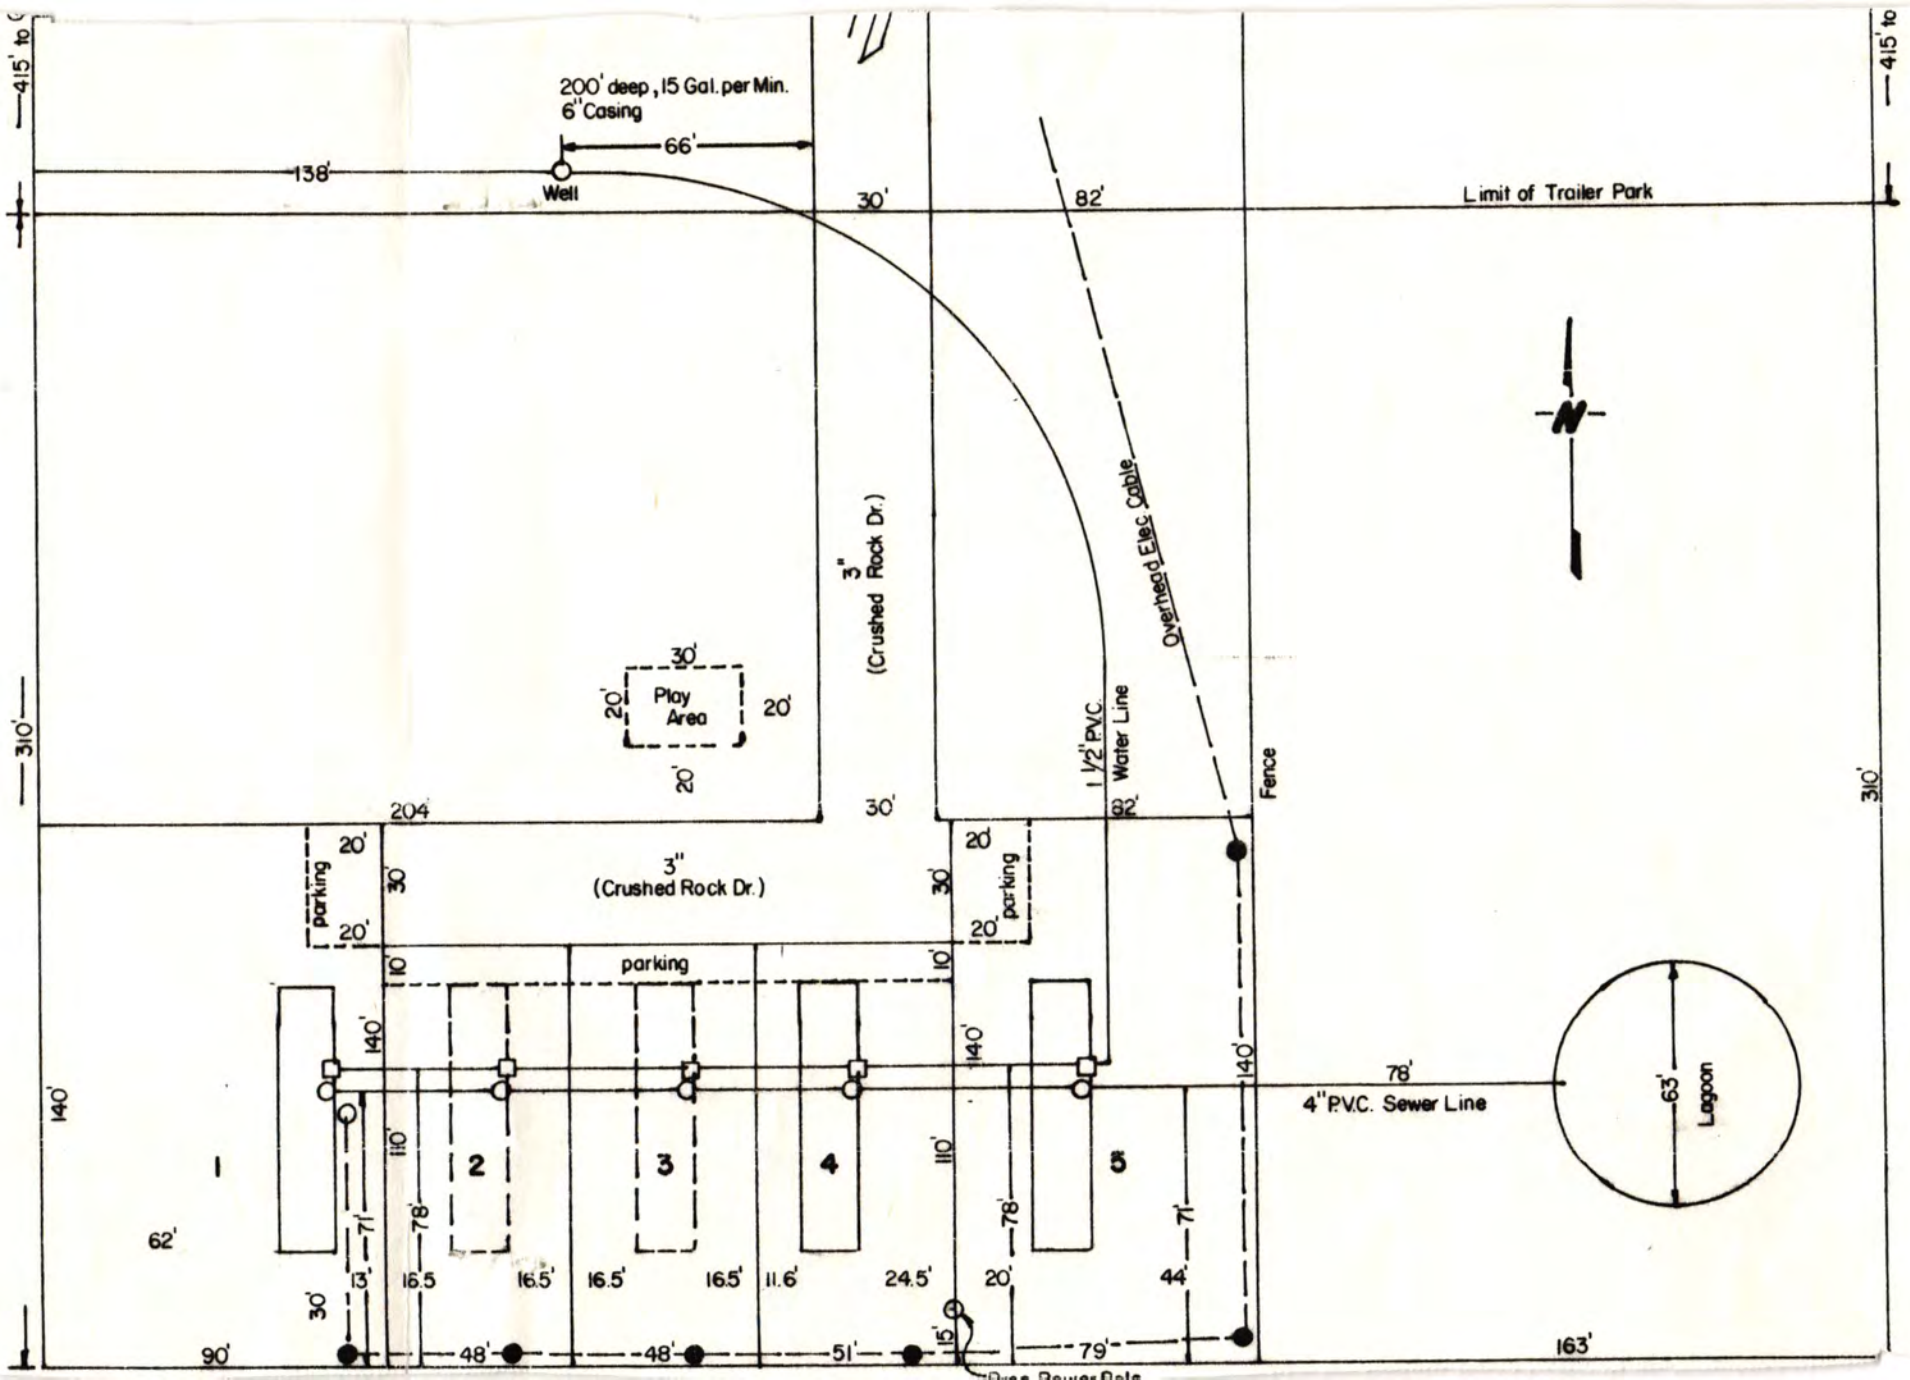
415' to ℄
200' deep, 15 Gal. per Min.
6" Casing
66'
138'
Well
30'
82'
Limit of Trailer Park
415' to ℄
310'
3"
(Crushed Rock Dr.)
Overhead Elec. Cable
30'
20'
Play
Area
20'
20'
1 1/2" P.V.C.
Water Line
82'
Fence
310'
204'
30'
20'
parking
20'
30'
3"
(Crushed Rock Dr.)
30'
20'
parking
20'
10'
parking
10'
140'
140'
140'
140'
78'
4" P.V.C. Sewer Line
63'
Lagoon
1
2
3
4
5
110'
110'
62'
78'
78'
71'
71'
30'
13'
16.5'
16.5'
16.5'
16.5'
11.6'
24.5'
20'
44'
90'
48'
48'
51'
15'
79'
163'
Pipe Power Pole

As Built Drawing

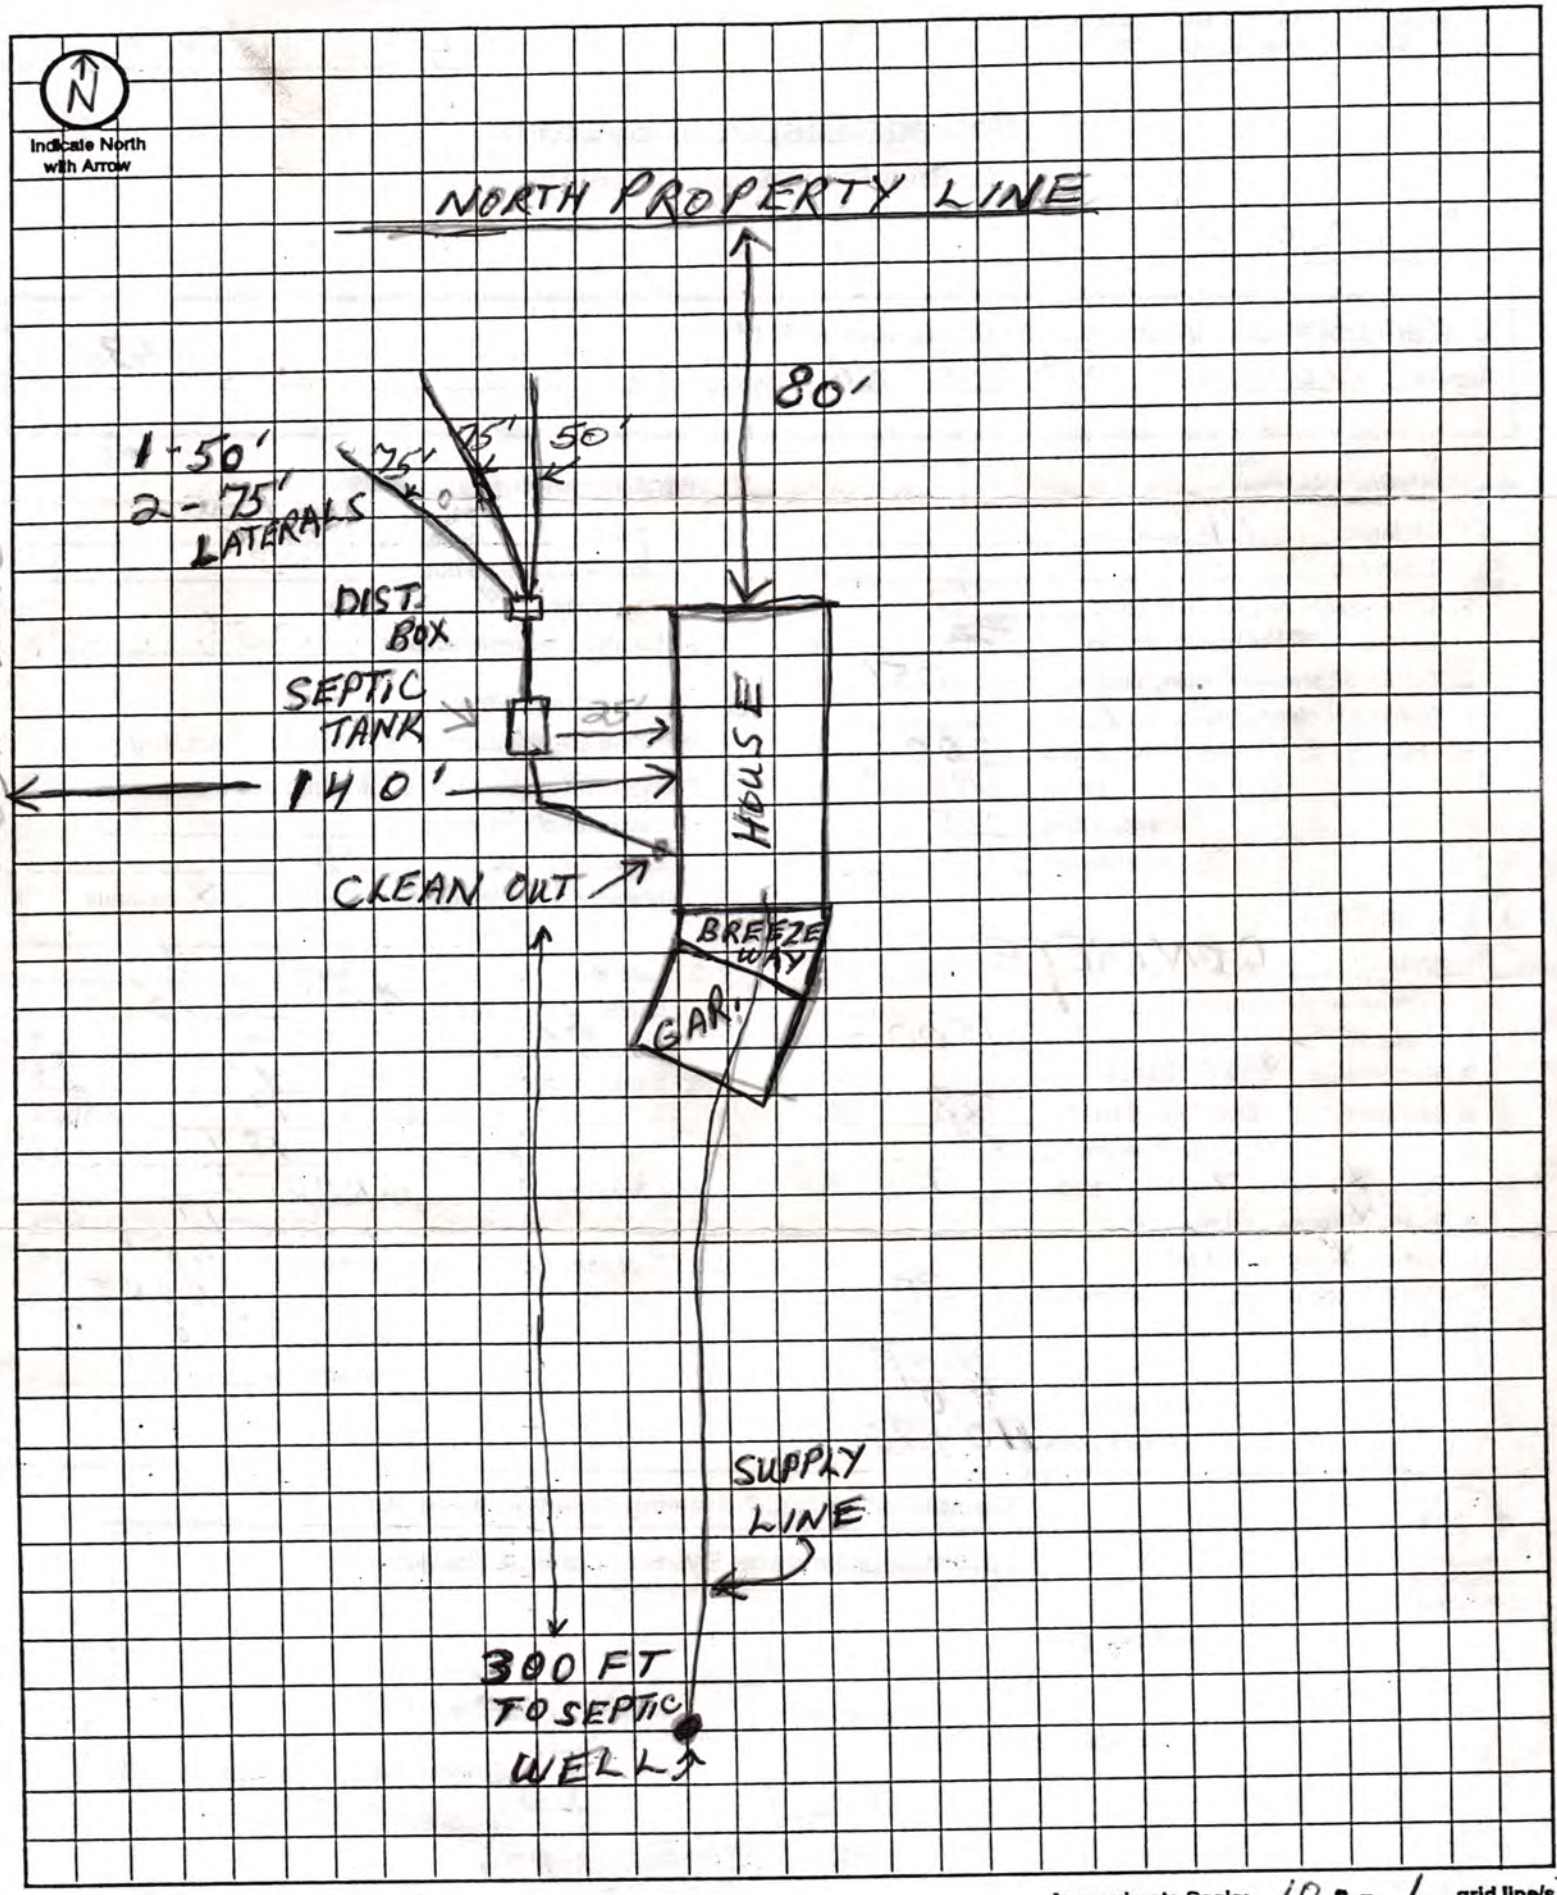

Approximate Scale: 10 ft. = 1 grid line/s
