Lincoln-Lancaster County Health Department

ENVIRONMENTAL HEALTH DIVISION
3140 N STREET · LINCOLN, NE 68510-1514 (402) 441-8000

Permit

SEWAGE SYSTEM REPAIR
SEWAGE REPAIR

Permit # 02390073301

Issued 10/11/02
Expires 04/11/03
Revenue Code 3157

FEES: $100.00

TOTAL: $100.00

Establishment

MARK LIDOLPH
T8N R6E SEC 11
LOT 21IT
13605 S 12 ST-ROCA

Permittee

MARK LIDOLPH
13605 S 12 ST
ROCA NE 68430

Bruce D. Dart

Bruce D. Dart, Health Director

• POST IN A PROMINENT PLACE • NOT TRANSFERABLE

003001

#02390073

Application to Alter, Extend or Repair an Individual Sewage Disposal System

☐ Municipal Code 24.38 ☐ County Resolution Number 2832

The undersigned hereby applies for a permit to: ☐ **ALTER** ☒ **EXTEND** ☐ **REPAIR** an existing Individual Sewage Disposal System, in conformance with appropriate Ordinance or Resolution, as described in this application and drawings attached hereto.

1. **Legal description of property:**
   Township 8N Range 6E Section 11 1/4 Section _____
   Block _____ Lot 21 I.T. Addition _____
   Parcel ID ____-____-_____-_____-_____ (i.e. 99-99-999-999-999)
   Street Address 13605 S 12 Roca, Ne 68430

2. **Property use:** ☒ residential ☐ commercial ☐ other use
   Number of bedrooms 3 Describe _____

3. **Type of Present Individual Disposal System** ☒ septic tank ☐ lagoon ☐ other

4. **Description of proposed alteration, extension or repair** add drop box & 100' of Infiltrator style lateral

5. **Work to be done by:** ☐ owner ☒ contractor's name Southwick Sewer Drain

6. **Estimated project:**
   a. Repair, replace or minor extension with a cost less than $400 (no fee required).
   b. Total cost is greater than $400 (Return fee with this application)
   c. A "construction permit" is required if the use, operation, location, or type of the system is being change.

Print Name Mark Lidolph Address 13605 So 12 Roca Phone 421-9088
Applicant Signature (owner or lessee) _____

Please include the permit fee ($100) with this application
Fee must be included before the application will be processed. Incomplete information will delay processing

---

HEALTH DEPARTMENT USE ONLY

Date received 10/11/02 REVIEW: ☒ Approved ☐ Disapproved By: Jerrold C. Hood

Site visits
Date ____/____/____ By _____
Date ____/____/____ By _____
Date ____/____/____ By _____

Installation final written approval
Date 11/4/02 By Doug Smith
Field note on reverse side

Return application to: Lincoln-Lancaster County Health Department - Environmental Health Division
3140 "N" Street, Lincoln, NE 68510
Phone: 441-8022

Business Office Use Only
Received: Date: 10/11/02 Amount 100.00 Check No. 4833 Initials ls

White - Division Copy Pink - Business Office Revised 9/00

8-6-11 Lot 21

Lincoln-Lancaster County Health Department
Environmental Health Division
3140 "N" Street • Lincoln, NE 68510-1514
Phone: 402-441-8022

D

Permit Number:

Sewage Disposal System

As Built Plans & Specifications

Date 11-1-02 ← 100' Extention to System Southside Sewer & Drain

System Location (Indicate correct number and street)

Address 13605 S. 12 (no rural route) City Roca NE, Zip 68430

A. Building Sewer

1. Material: _____
   Diameter: _____ in.
2. Distance above basement floor: _____ in.
   or distance below basement floor: _____ in.
3. Distance between dwelling and septic tank: _____ ft.
4. Number of clean-outs: _____
5. Distances to: well or suction line _____ ft.
   stream _____ ft.
   pressure line _____ ft.
   property line _____ ft.

B. Septic Tank

1. Material: Concrete
   Number of compartments: 1
2. Capacity: 1,000 gal.
3. Factory built: ☒ Yes ☐ No
4. Manholes: Over inlet, diameter _____ in.
   Over outlet, diameter _____ in.
   Riser: ☐ above ☐ below grade _____ in.
5. Inlet: ☐ baffle ☐ tee
6. Outlet: ☐ baffle ☒ tee
7. Depth to top of tank, below unfinished grade: 12 in.
8. Distances to: Well or suction line _____ ft.
   Stream _____ ft.
   Pressure line _____ ft.
   Property line _____ ft.

C. Distribution Box

1. Material: Concrete
   Number available outlets: 5
2. Factory built: ☒ Yes ☐ No
3. Distance from septic tank: 20' ft.

D. Absorption Field


(Provide as-built drawings on back of this form)

1. Type: ☒ Half rounds ☐ Perforated pipe
   Diameter of half round: 16" Concrete
   or perforated pipe: _____
   Material: ☐ fiberglass ☒ plastic ☐ concrete
   ☐ other Infiltrator 100' 11-1-02
2. Lateral lines: Number _____
   Length of each line: 100 ft. 100 ft.
   100 ft. _____ ft., _____ ft.
3. Trench dimensions: Width 4' ft.
   Slope _____ in/100 ft.
   Average depth 36 in
4. Filter material: Road Gravel
   Depth of material 16 in.
5. Distances to: Well or suction line _____ ft.
   Stream _____ ft.
   Pressure line _____ ft.
   Property line _____ ft.


Indicate North with Arrow

Complete "As Built" drawing on back of this form.

Individual Sewage System Design (Example)

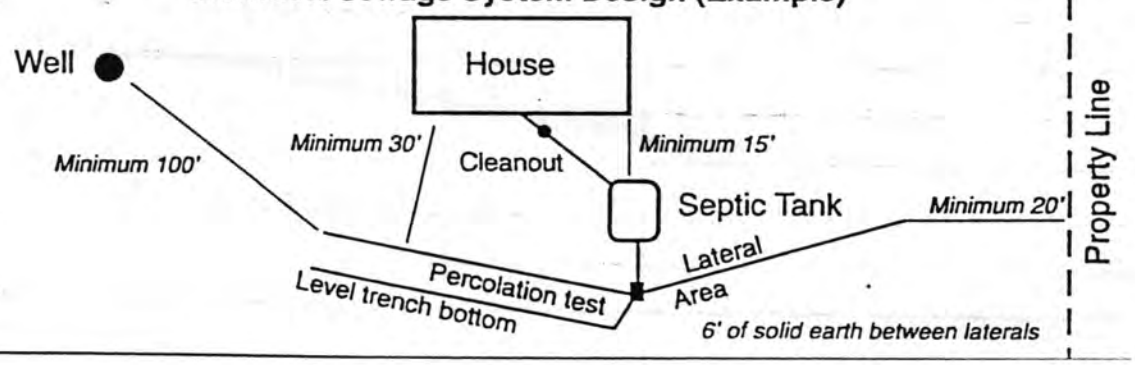

FORM 23-103 10-96

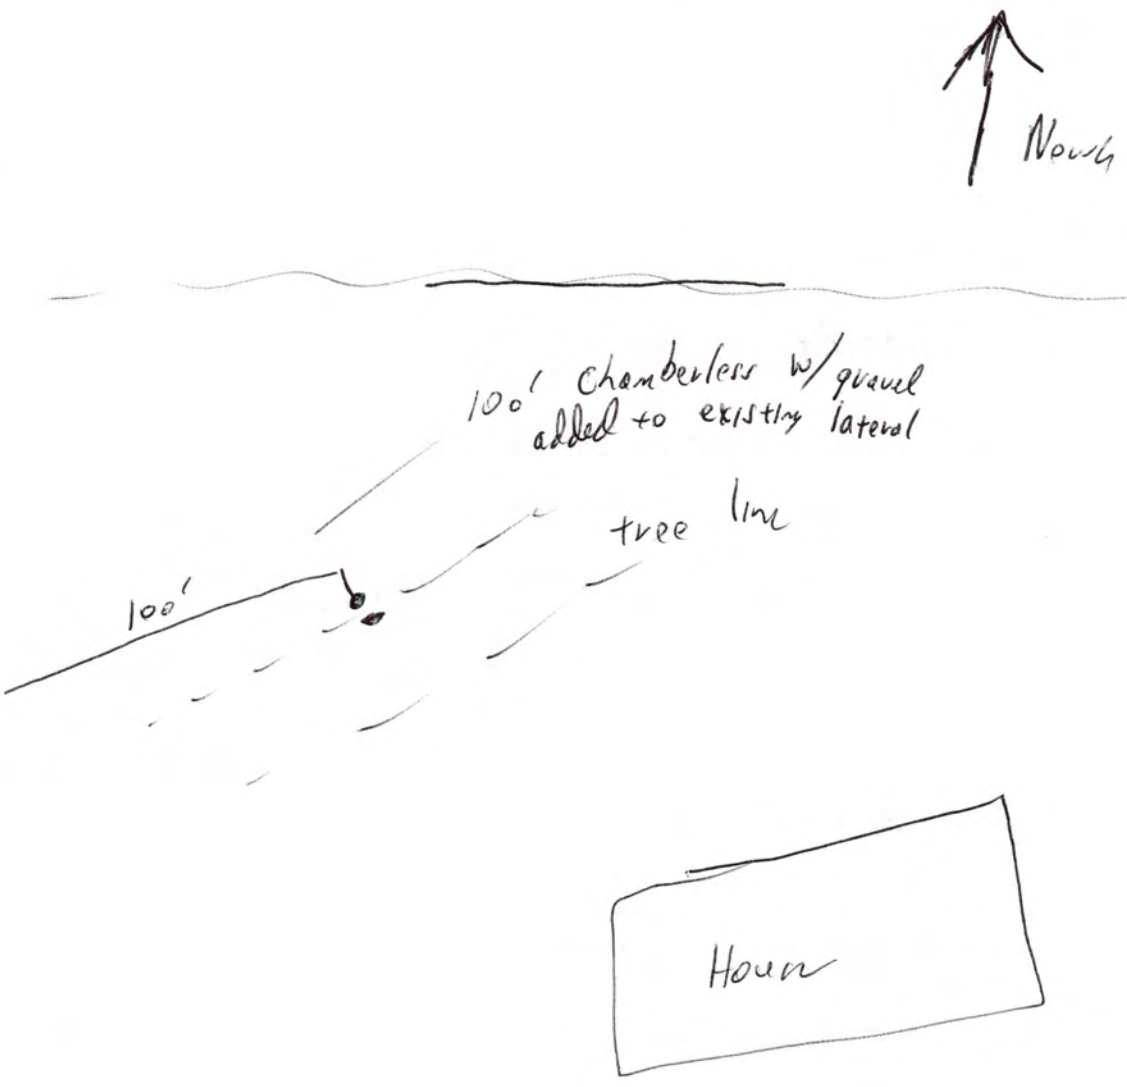
North
100' Chamberless w/ gravel added to existing lateral
tree line
100'
House

As Built Drawing

