LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

ENVIRONMENTAL HEALTH DIVISION

2200 St. Marys Ave Lincoln, NE 68502-3785 (402) 441-8000

NON TRANSFERABLE

P E R M I T

Permit

SEWAGE INSTALLATION

No. 94380113301

Issued 03/21/94
Expires 09/21/94
Revenue Code 18754

Establishment

RICHARD J YOUNG
T8N R6E SEC 13
10501 WITTSTRUCK ROAD

FEES: $150.00

TOTAL $150.00

Permittee

RICHARD J YOUNG
12200 S 162 ST
BENNET NE 68317

Issued By M. Jane Ford
Health Director

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW
"POST IN A PROMINENT PLACE"

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

A

FILING FEE: $_____

FILE NO._____

DATE:_____

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 8N ; Range ~~6~~ 6E ; Section 13 ; W½ NE¼
   Block_____: Lot_____: Addition_____
   Street Address 10501 Wittstruck Rd
2. Property Use: Residential ☒ ; Commercial ☐ Other Use ☐
   No. of Bedrooms 3 . Describe_____
3. Type of Individual Sewage Disposal System: Septic Tank ☐ ; Other ☒ (Lagoon)
4. Distance to public sewer: _____ft.

Richard J Young Young's Mfg. Co.
Signature of Applicant (Owner or Lessee)

12200 So 162nd Bennet Ne 68317
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. 3/21/94. Date Frwd. 3/21/94. ACTION: Approved ☒ Disapproved ☐ Signature: Jerold C. Wood
2. Supt. Bldg. Insp.: or Village Clerk: Date Rec'd. 3/21/94. Date Frwd. 3/21/94. ACTION: Approved ☒ Disapproved ☐ Signature: Ray Spain
3. City or County Engineer: Date Rec'd. 3-21-94. Date Frwd. 3-21-94. ACTION: Approved ☒ Disapproved ☐ Signature: Larry V. Worrell


REMARKS OR REASONS FOR DISAPPROVAL_____

Site Visits:
Date: 4-18-94 by: P.D Need fence etc
Date: 5/17/94 by: J.C.H.
Date: 5/18/94 by: J.C.H.

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

INSTALLATION FINAL WRITTEN APPROVAL
Date: 5/18/94 By: Jerold C. Wood

FORM 23-43

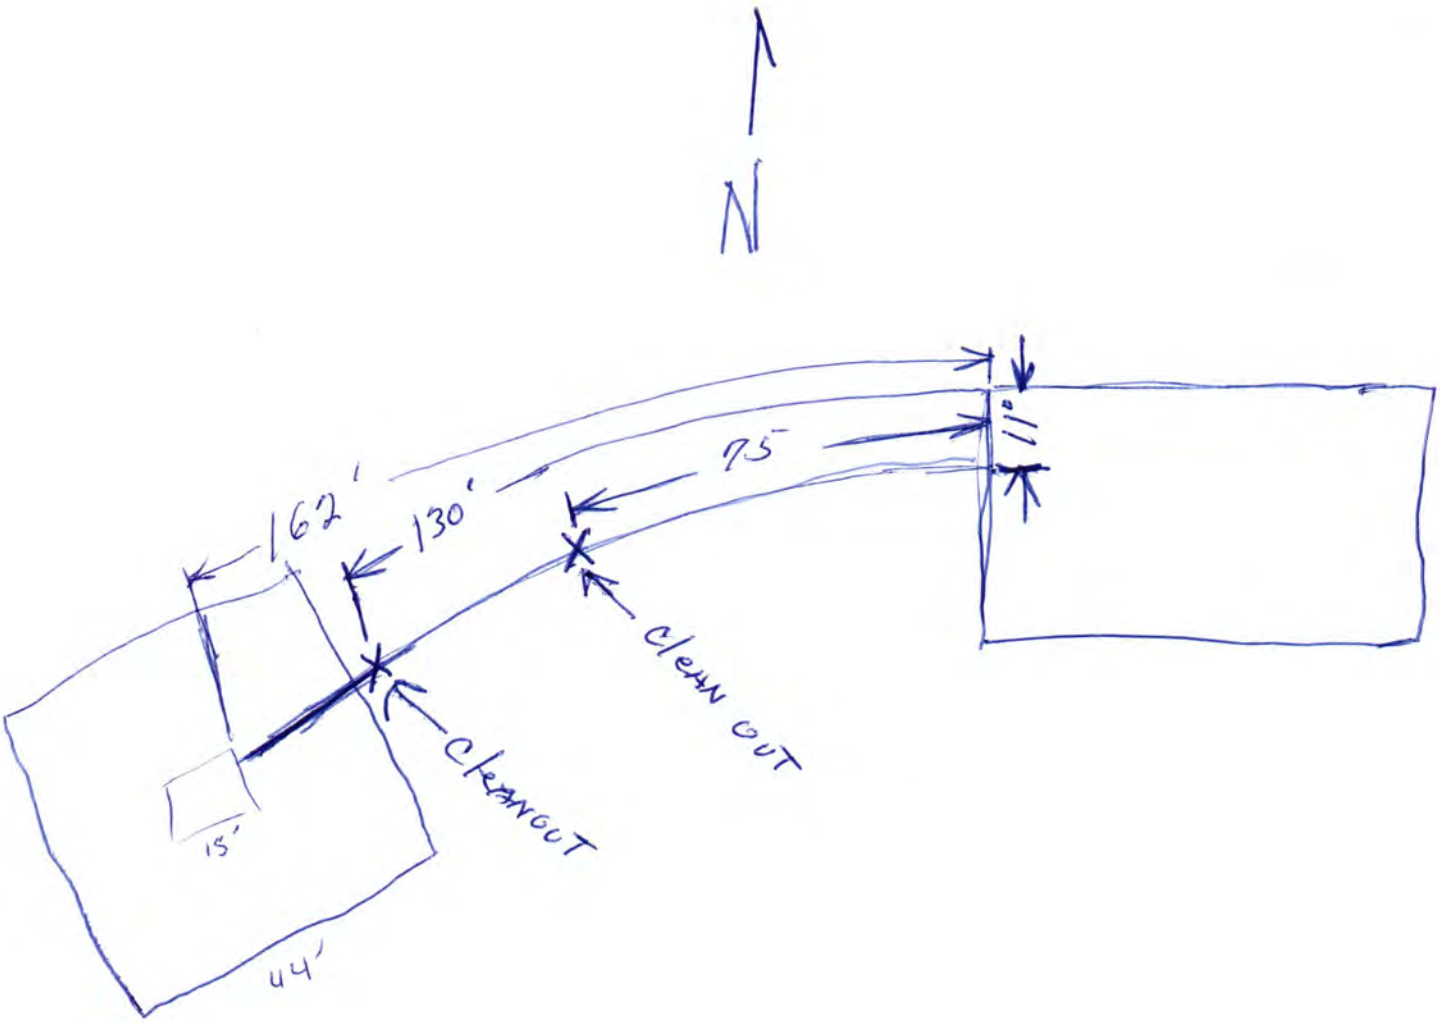

Capital City Trenching
4-18-94

FORM 20105-0477
SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150 and County Resolution No. 2832)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

B

FILE NO. (10501 Wittstruck Rd)

PROPERTY WHERE SOIL TESTED:

Location: Township 8N ; Range 7E ; Section & ¼ Section W½ NE¼ 13.
Property Dimensions: _____ ft. x _____ ft. Area: 60 acres. (Attach Sheet C with sketch of property).
Soil Type: Silty Clay ☐ ; Silty Clay Loam ☐ ; Sandy Loam ☐ ; Silt Loam ☐ ; Clay Loam ■ .
Dates of Tests: 3-16-94 to 3-17-94 . Weather: Precip. 0 Temp. 50°.

Test Location 110th + Wittstruck Rd. So. side.

OWNER: Young's Plumbing
Address: Bennet NE. 68317
782-6600

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
		Pre-Saturation Period				Percolation Readings						Results	
		Start		End		Start			End				
Hold No.	Hole Depth (in.)	Date (Mo./Day)	Time (Hr./Min.)	Date (Mo./Day)	Time (Hr./Min.)	Date (Mo./Day)	Time (Hr./Min.)	Water Level (in.)	Time (Hr./Day)	Water Level (in.)	Elapsed Time (Min.)	Water Level Drop (in.)	Percolation Rates (Min./in.)
1	36	3-16	6:00 pm	3-17	5:00 pm	3-17	5:00 pm	6"	9:00 pm	4¾"	30m	1¼"	
2	36	3-16	6:00 pm	3-17	5:00 pm	3-17	5:00 pm	6"	9:00 pm	5"	30m	1"	
3	36	3-16	6:00 pm	3-17	5:00 pm	3-17	5:00 pm	6"	9:00 pm	5"	30m	1"	
4	36	3-16	6:00 pm	3-17	5:00 pm	3-17	5:00 pm	6"	9:00 pm	5¾"	30m	¼"	
5	36	3-16	6:00 pm	3-17	5:00 pm	3-17	5:00 pm	6"	9:00 pm	5⅞"	30m	⅛"	
6	36	3-16	6:00 pm	3-17	5:00 pm	3-17	5:00 pm	6"	9:00 pm	5"	30m	1"	

Sum of Percolation Rates: _____
Average of Rates: _____
Mean of Rates: _____

Mike Haugland
Signature of Person Conducting Test
Address 2700 Dan Ave. Lincoln NE. Phone 464-0638
Precast Products Inc.

(Do not write below this line)

REVIEWING ACTION

Remarks: _____
Soil Type (SCS): Wymore Silty Clay Loam
Date: March 21, 1994

Approved Percolation Rate (a)
A. 40 min./inch
B. _____ min./inch
C. _____ min./inch

Jerrold C. Hood
Signature of Reviewing Official

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

RECEIVED FEB 1 0 1994
LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

D

DATE: 4-18-94

FILE NO. _____


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material PVC ; Diameter 4 in.
2. Distance above basement floor ____ in., or below basement floor 18 in.
3. Distance between dwelling and septic tank _____ ft.
4. Number of clean-outs _____.
5. Distances to:
Well or Suction Line _____ ft.;
Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

B. SEPTIC TANK:
1. Material _____; No. of compartments _____.
2. Capacity _____ gals.;
3. Factory Built: Yes ☐ No ☐
(Company _____)
4. Manholes: Over Inlet; diam. _____ in.
Over Outlet; diam. _____ in.
Riser Above ☐ Below ☐ Grade ____ in.
5. Inlet: Baffle ☐ ; or Tee ☐
6. Outlet: Baffle ☐ ; or Tee ☐
7. Depth of top of tank below finished grade _____ in.
8. Distances to:
Well or Suction Line _____ ft.;
Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

C. DISTRIBUTION BOX:
1. Material _____; Number - available outlets _____.
2. Factory Built: Yes ☐ No ☐
(Company _____)
3. Distance from Septic Tank _____ ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☐ Perforated Pipe ☐
Diameter of Half Round _____ or
Perforated Pipe _____.
Material: fiberglass ☐ ; plastic ☐ ; concrete ☐ ; other _____.
2. Lateral Lines:
Number ___ ; Length of each line _____, _____, _____, _____, _____ ft.;
Total length of laterals _____ ft.;
Distance between lateral lines ____ ft.
3. Trench dimensions: Width _____ ft.;
Slope _____ in/100 ft.; Average Depth _____ in.
4. Filter Material: _____
Depth of Material _____ in.
5. Distances to:
Well or Suction Line _____ ft.;
Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

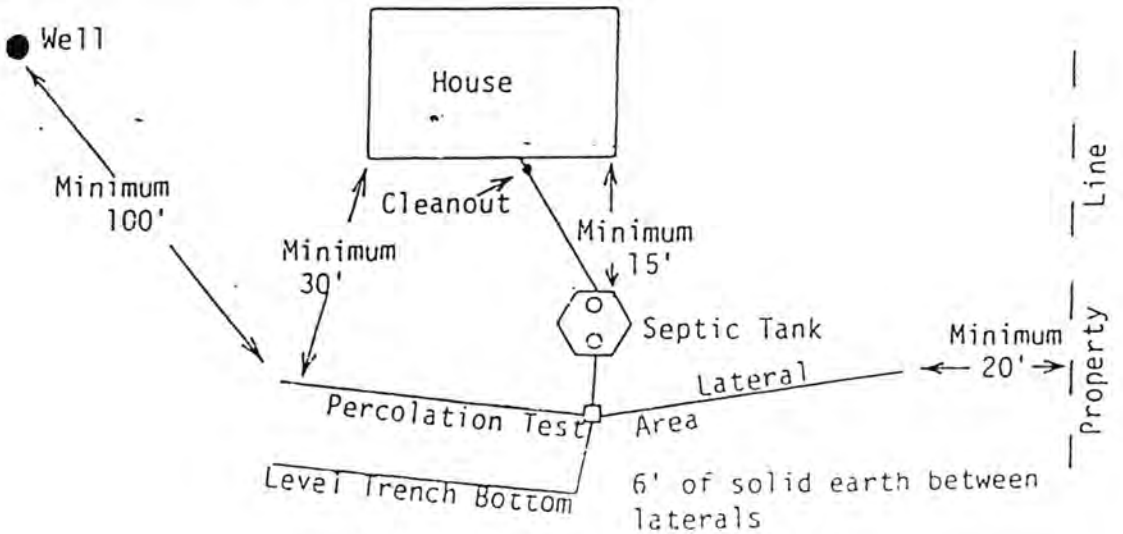

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN
