LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

FILE NO. 737-C

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION — TYPE OF PERMIT

May 20, 1976 — THIS PERMIT EXPIRES

Clayton Etmund — ISSUED TO

Roca, Nebraska — ADDRESS

T8N; R7E; Sec. 3-SW¼; — LEGAL DESCRIPTION

REMARKS: NON-TRANSFERABLE

PERMIT	INSPECTION FEE	OCCUPATION TAX	TOTAL
$ 30.00	$	$	$ 30.00
ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE
	110.16	148.14	6-2

RECEIPTED BY — DATE — AMOUNT

VALID RECEIPT ONLY IF RECEIPTED IN THIS SPACE

ISSUING OFFICER

THIS PERMIT IS ISSUED AS PROVIDED BY COUNTY RESOLUTION NO. 2832

FORM HD-42(73) APPLICATION FOR PERMIT TO CONSTRUCT INDIVIDUAL SEWAGE DISPOSAL SYSTEM

City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 475-6221)

FILE NO. 737-C

DATE: _____

TO: Director of Health
Lincoln-Lancaster County Health Dept.

The undersigned hereby applies for a permit to construct an Individual Sewage Disposal System in conformance with appropriate Ordinance or Resolution, as described in this application and the annexed forms attached hereto.

1. Legal description of property: Twp. 8 Nalthila ; Range 7E ; Section SW¼ of Sec 3 ; Block _____ ; Lot _____ ; Addition _____.
Street Address _____.

2. Property Use: Residential _____ ☒; Commercial _____ ☐
No. of Bedrooms 3
Describe: _____
Other Use _____
Describe: _____

3. Type of Individual Sewage Disposal System: Septic Tank ☒; Other ☐

4. Plans and Specifications of Proposed System. (See FORM HD-45(73) PLANS & SPECIFICATIONS, SEWAGE DISPOSAL SYSTEM, attached hereto.)

5. Soil Absorption Properties. (See FORM HD-43(73) SOIL ABSORPTION TEST DATA REPORT, attached hereto).

Clayton Edmund
Signature of Applicant (owner or lessee)

Roca Neb.
Address

(Do not write below double line)

REVIEWING ACTION

1. Date Rec'd; _____
Filing Fee: $ 30.00

2. Site Visits:
Date: [redacted] by: [redacted]
Date: 12/11/75 by: J.C.N.
Date: _____ by: _____

3. Date: Approved ☒; Disapproved ☐ 11/20/75
by: Jerrold C. Hood

4. INSTALLATION FINAL WRITTEN APPROVAL
Date: [redacted] by: [redacted]
12/11/75 Jerrold C. Hood

FORM HD- 45(73) PLANS & SPECIFICATIONS
SEWAGE DISPOSAL SYSTEM
(Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 475-6221)

FILE NO. 737-C

SPECIFICATIONS

DATE: _____


A. BUILDING SEWER:
1. Material PLASTIC; Diameter 4 in.
2. Distance above basement floor ___in.; or below basement floor ___in.
3. Distance between dwelling and septic tank 97 ft.
4. Number of clean-outs 1.
5. Distances To:
Well or Suction Line 100+ ft.;
Stream 100+ ft.; Pressure Line ___ft.;
Property Line 100+ ft.

B. SEPTIC TANK (Provide construction drawings.)
1. Material CON; No. of compartments 1.
2. Capacity 1000 gals.; Liquid depth ___in.
3. Factory Built: Yes ☒ (Company PRE-CAST
No ☐
4. Manholes: Over Inlet; diam. 6 in.
Over Outlet; diam. 6 in.
Below Grade _____in.
5. Inlet: Baffle ☐; or Tee ☐
6. Outlet: Baffle ☒; or Tee ☐
Depth of outlet below inlet ___in.
7. Depth of top of tank below finished grade ___in.
8. Distances To:
Well or Suction Line 100+ ft.;
Stream 100+ ft.; Pressure Line ___ft.;
Property Line 100+ ft.

C. DISTRICTION BOX
1. Material CON; No. available outlets 5.
2. Factory Built: Yes ☒, (Company PRE-CAST STEP No ☐
3. Dimension: Length ___in.; Width ___in. Depth ___in.
4. Distance from Septic Tank 8'7" ft.
5. Serial Distribution: Yes ☐, No ☒ (If yes, show detailed plans.)

D. ABSORPTION FIELD: (Provide drawings.)
1. Type: HALF ROUND
2. Lateral Lines: Depth below grade ___in. Number 2; Length of each line 100 ft Total length of Laterals 180 ft.; +80
Slope 6 in/100 ft. Diameter of pipe 24 in.; Shape ∩
Material: concrete ☒; fiber asbestos ☐; clay ☐; other ___
Distance between lateral lines 18 ft.
3. Trench Dimensions: Depth 30 in.; Width 36 in.
4. Filter Material: GRAVEL.
Depth of material from trench bottom ___in.
5. Distances To:
Well or Suction Line 100+ ft.;
Stream 100+ ft.; Pressure Line ___ft.
Property Line 100+ ft.
6. Percolation Rate: _____minutes/inch

TYPICAL SKETCHES

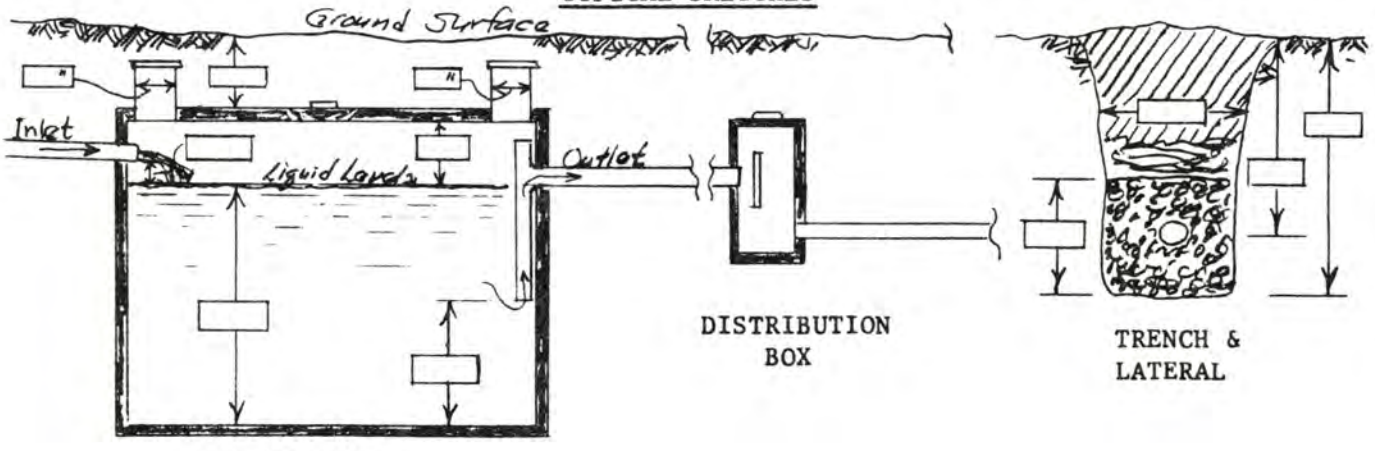

_____
Signature of Applicant

FORM HD-40(73) REQUEST FOR SITE CLEARANCE FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM

City Ordinance No. 9150 ☐

County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 475-6221)

FILE NO. 737-C

TO: Division of Environmental Health
Lincoln-Lancaster County Health Dept.

DATE: _____

The undersigned hereby requests SITE CLEARANCE to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 8N Saltillo ; Range 7E ; Section SW 1/4 Sec. 3
Block _____; Lot _____; Addition _____ 159.33 ac ±
Street Address _____

2. Property Use: Residential _____ ☒ ; Commercial _____ ☐
No. of Bedrooms 3 . Describe: _____
Other Use _____ ☐
Describe: _____

3. Type of Individual Sewage Disposal System: Septic Tank ☒ ; Other ☐

4. Distance to public sewer: None ft.

Clayton Etmund
Signature of Applicant (Owner or Lessee)

Roca ~~Nebraska~~, Nebr.
Address

(Do not write below this double line)

REVIEWING ACTION

1. Health Department: Date Rec'd. 11/20/75 . Date Frwd. 11/21/75 . ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Hood

2. Supt. Bldg. Insp.: Date Rec'd. 11/21/75 MX Date Frwd. _____ . ACTION: Approved ☐ Disapproved ☐ Signature: _____

3. City or County Engineer: Date Rec'd. 11/21/75 . Date Frwd. 11/24/75 . ACTION: Approved ☒ Disapproved ☐ Signature: Melvin Heidenreich

REMARKS OR REASONS FOR DISAPPROVAL _____

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

FORM HD- 43(73) SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150 and County Resolution No. 2832)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone 475-6221)

FILE NO. 737-C

PROPERTY WHERE SOIL TESTED: Salt Valley
Location: Township 7; Range 8
Section & ¼ Sect. SW ¼ Sec 3
Property Dimensions: ____ ft. x ____ ft.
Area: _____ acres. (Attach sketch of property showing hole location).

Owner: Clayton Etzmuller
Address Roca Nebr

Soil Type: Silty Clay [X]; Silty Clay Loam [ ]; Sandy Loam [ ]
Silty Loam [ ]; Clay Loam [ ]; Sandy Clay [ ]

Dates of Tests: 11-10 to 11-11. Weather: Precip. 0 Temp. 60° F.

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
		Pre-Saturation Period				Percolation Readings					Results		
		Start		End		Start			End				
Hole No.	Hole Depth (in.)	Date (Mo. Day)	Time (Hr. Min.)	Date (Mo. Day)	Time (Hr. Min.)	Date (Mo. Day)	Time (Hr. Min.)	Water Level (in.)	Time (Hr. Min.)	Water Level (in.)	Elapsed Time (Min.)	Water Level Drop (in.)	Percolation Rates (Min./inch)
1	36"	11-10	1:00	11-11	2:30	11-11	3:00	20	3:30	18½	30	1½	30/1½
2	36"	11/10			2:30					18	30	2	30/2
3	36"	11/10								18¼	30	1¾	30/1¾
4	36"	11/10								18¾	30	¼	30/¼
5	36"	11/10								19	30	1	30/1
6	36"	11/10	1:00	11-11	2:40		3:06	20	3:36	18¾	30	1¾	30/1¾

Sum of Percolation Rates 9¾
Average of Rates: 1.54
Mean of Rates: 30 min/1½ in.

Signature of Person Conducting Test

Address _____
Phone: _____

(Do not write below this line)


REVIEWING ACTION

REMARKS: _____

Approved Percolation Rate(s)
A. 13 min./inch
B. _____ min./inch
C. _____ min./inch

DATE: November 20, 1975

Gerrold C. Hood
Signature of Reviewing Official

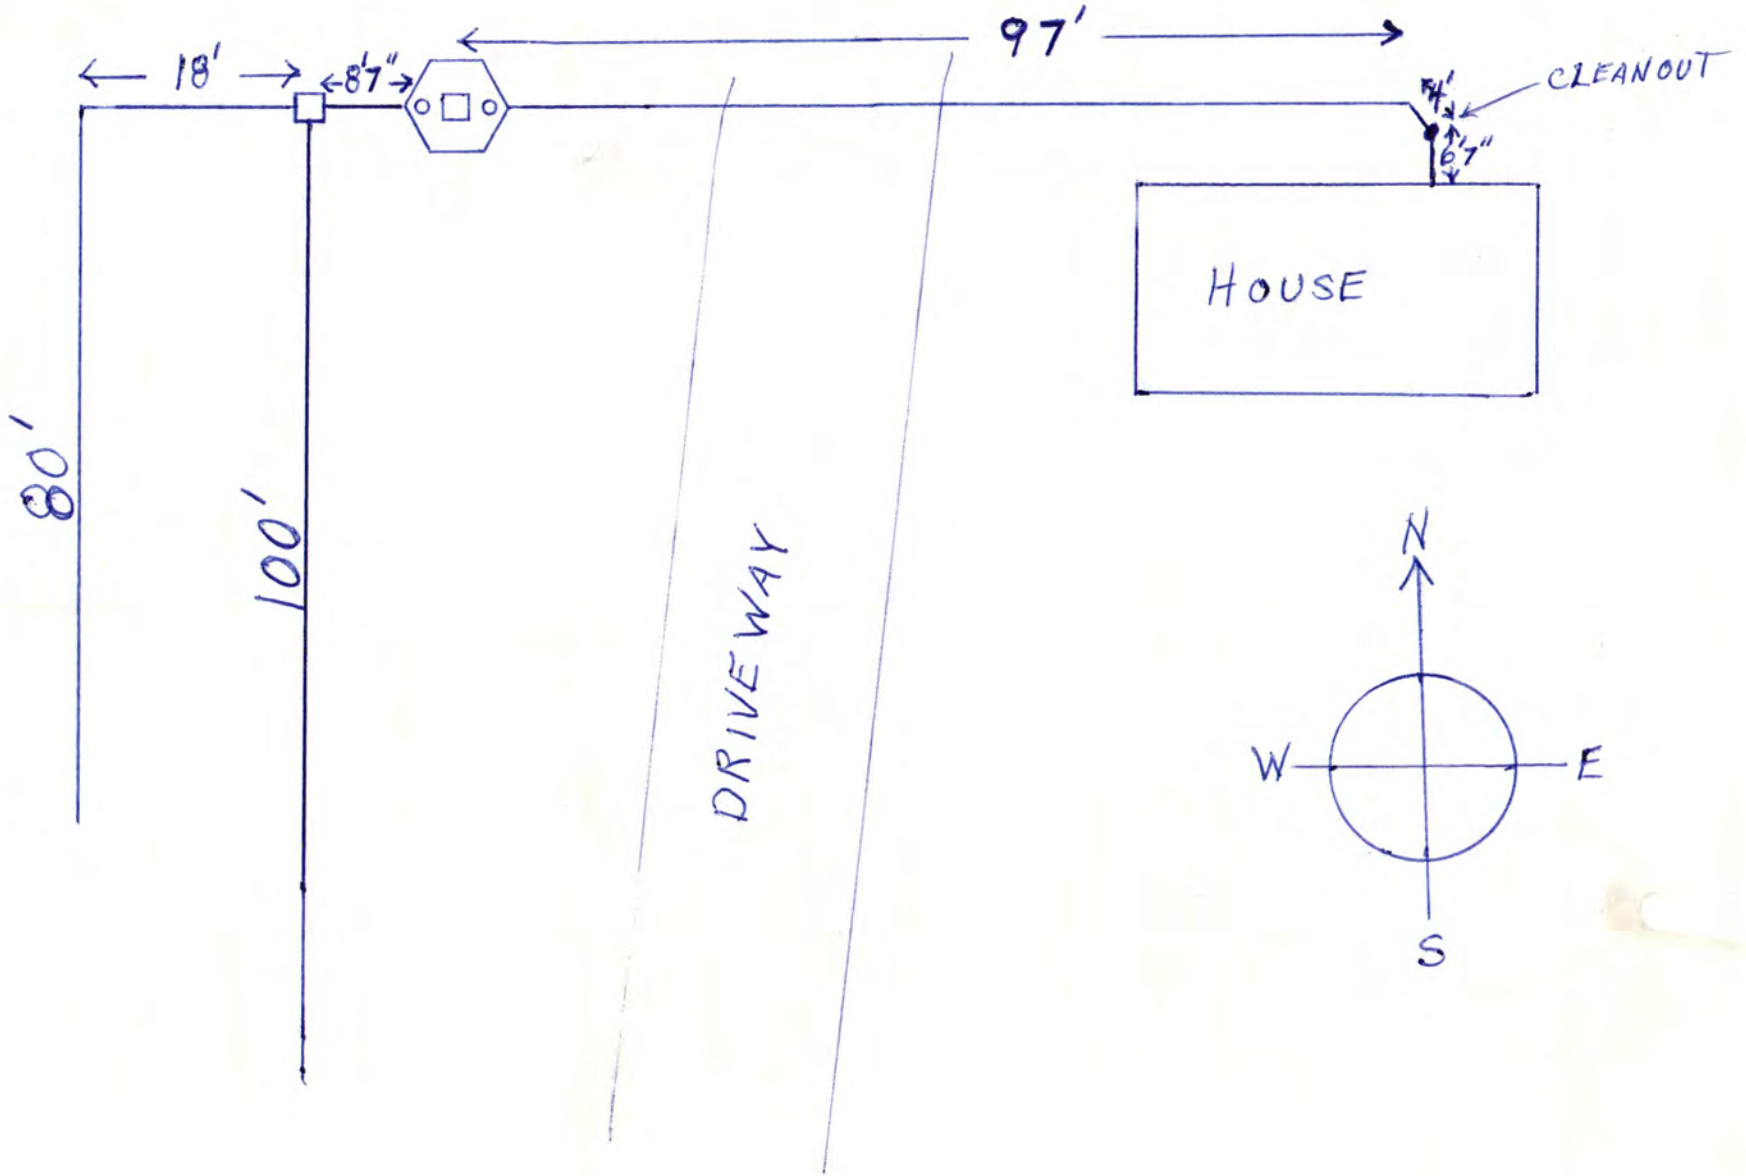
97'
18'
8'7"
4'
CLEANOUT
6'7"
HOUSE
80'
100'
DRIVEWAY
N
W
E
S

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

FILE NO. 737-C

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION — TYPE OF PERMIT

May 20, 1976 — THIS PERMIT EXPIRES

Clayton Etmund — ISSUED TO

Roca, Nebraska — ADDRESS

T8N; R7E; Sec. 3-SW¼; — LEGAL DESCRIPTION

REMARKS: NON-TRANSFERABLE

PERMIT	INSPECTION FEE	OCCUPATION TAX	TOTAL
$ 30.00	$	$	$ 30.00
ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE
	110.16	148.14	6-2

RECEIPTED BY — DATE — AMOUNT

VALID RECEIPT ONLY IF RECEIPTED IN THIS SPACE

ISSUING OFFICER

THIS PERMIT IS ISSUED AS PROVIDED BY COUNTY RESOLUTION NO. 2832

FORM HD-42(73) APPLICATION FOR PERMIT TO CONSTRUCT INDIVIDUAL SEWAGE DISPOSAL SYSTEM

City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 475-6221)

FILE NO. 737-C

DATE: _____

TO: Director of Health
Lincoln-Lancaster County Health Dept.

The undersigned hereby applies for a permit to construct an Individual Sewage Disposal System in conformance with appropriate Ordinance or Resolution, as described in this application and the annexed forms attached hereto.

1. Legal description of property: Twp. 8 Nalthila ; Range 7E ; Section SW¼ of Sec 3 ; Block _____ ; Lot _____ ; Addition _____.
Street Address _____.

2. Property Use: Residential _____ ☒; Commercial _____ ☐
No. of Bedrooms 3
Describe: _____
Other Use _____
Describe: _____

3. Type of Individual Sewage Disposal System: Septic Tank ☒; Other ☐

4. Plans and Specifications of Proposed System. (See FORM HD-45(73) PLANS & SPECIFICATIONS, SEWAGE DISPOSAL SYSTEM, attached hereto.)

5. Soil Absorption Properties. (See FORM HD-43(73) SOIL ABSORPTION TEST DATA REPORT, attached hereto).

Clayton Edmund
Signature of Applicant (owner or lessee)

Roca Neb.
Address

(Do not write below double line)

REVIEWING ACTION

1. Date Rec'd; _____
Filing Fee: $ 30.00

2. Site Visits:
Date: [redacted] by: [redacted]
Date: 12/11/75 by: J.C.N.
Date: _____ by: _____

3. Date: Approved ☒; Disapproved ☐ 11/20/75
by: Jerrold C. Hood

4. INSTALLATION FINAL WRITTEN APPROVAL
Date: [redacted] by: [redacted]
12/11/75 Jerrold C. Hood

FORM HD- 45(73) PLANS & SPECIFICATIONS
SEWAGE DISPOSAL SYSTEM
(Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 475-6221)

FILE NO. 737-C

SPECIFICATIONS

DATE: _____


A. BUILDING SEWER:
1. Material PLASTIC; Diameter 4 in.
2. Distance above basement floor ___in.; or below basement floor ___in.
3. Distance between dwelling and septic tank 97 ft.
4. Number of clean-outs 1.
5. Distances To:
Well or Suction Line 100+ ft.;
Stream 100+ ft.; Pressure Line ___ft.;
Property Line 100+ ft.

B. SEPTIC TANK (Provide construction drawings.)
1. Material CON; No. of compartments 1.
2. Capacity 1000 gals.; Liquid depth ___in.
3. Factory Built: Yes ☒ (Company PRE-CAST
No ☐
4. Manholes: Over Inlet; diam. 6 in.
Over Outlet; diam. 6 in.
Below Grade _____in.
5. Inlet: Baffle ☐; or Tee ☐
6. Outlet: Baffle ☒; or Tee ☐
Depth of outlet below inlet ___in.
7. Depth of top of tank below finished grade ___in.
8. Distances To:
Well or Suction Line 100+ ft.;
Stream 100+ ft.; Pressure Line ___ft.;
Property Line 100+ ft.

C. DISTRICTION BOX
1. Material CON; No. available outlets 5.
2. Factory Built: Yes ☒, (Company PRE-CAST STEP No ☐
3. Dimension: Length ___in.; Width ___in. Depth ___in.
4. Distance from Septic Tank 8'7" ft.
5. Serial Distribution: Yes ☐, No ☒ (If yes, show detailed plans.)

D. ABSORPTION FIELD: (Provide drawings.)
1. Type: HALF ROUND
2. Lateral Lines: Depth below grade ___in. Number 2; Length of each line 100 ft Total length of Laterals 180 ft.; +80
Slope 6 in/100 ft. Diameter of pipe 24 in.; Shape ∩
Material: concrete ☒; fiber asbestos ☐; clay ☐; other ___
Distance between lateral lines 18 ft.
3. Trench Dimensions: Depth 30 in.; Width 36 in.
4. Filter Material: GRAVEL.
Depth of material from trench bottom ___in.
5. Distances To:
Well or Suction Line 100+ ft.;
Stream 100+ ft.; Pressure Line ___ft.
Property Line 100+ ft.
6. Percolation Rate: _____minutes/inch

TYPICAL SKETCHES

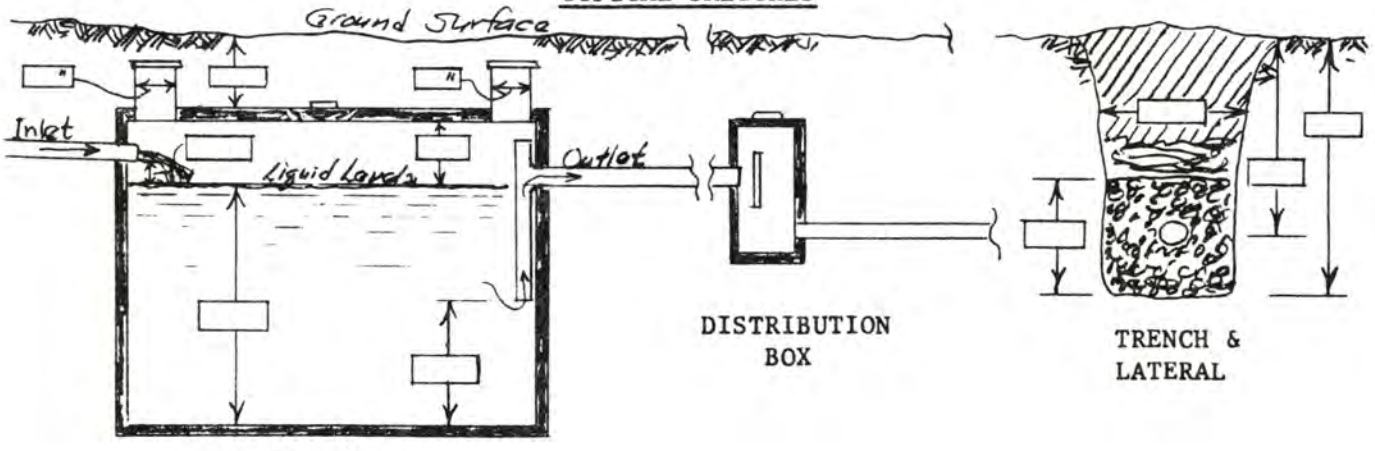

_____
Signature of Applicant

FORM HD-40(73) REQUEST FOR SITE CLEARANCE FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM

City Ordinance No. 9150 ☐

County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 475-6221)

FILE NO. 737-C

TO: Division of Environmental Health
Lincoln-Lancaster County Health Dept.

DATE: _____

The undersigned hereby requests SITE CLEARANCE to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 8N Saltillo ; Range 7E ; Section SW 1/4 Sec. 3
Block _____; Lot _____; Addition _____ 159.33 ac ±
Street Address _____

2. Property Use: Residential _____ ☒ ; Commercial _____ ☐
No. of Bedrooms 3 . Describe: _____
Other Use _____ ☐
Describe: _____

3. Type of Individual Sewage Disposal System: Septic Tank ☒ ; Other ☐

4. Distance to public sewer: None ft.

Clayton Etmund
Signature of Applicant (Owner or Lessee)

Roca ~~Nebraska~~, Nebr.
Address

(Do not write below this double line)

REVIEWING ACTION

1. Health Department: Date Rec'd. 11/20/75 . Date Frwd. 11/21/75 . ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Hood

2. Supt. Bldg. Insp.: Date Rec'd. 11/21/75 MX Date Frwd. _____ . ACTION: Approved ☐ Disapproved ☐ Signature: _____

3. City or County Engineer: Date Rec'd. 11/21/75 . Date Frwd. 11/24/75 . ACTION: Approved ☒ Disapproved ☐ Signature: Melvin Heidenreich

REMARKS OR REASONS FOR DISAPPROVAL _____

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

FORM HD- 43(73) SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150 and County Resolution No. 2832)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone 475-6221)

FILE NO. 737-C

PROPERTY WHERE SOIL TESTED: Salt Valley
Location: Township 7; Range 8
Section & ¼ Sect. SW ¼ Sec 3
Property Dimensions: ____ ft. x ____ ft.
Area: _____ acres. (Attach sketch of property showing hole location).

Owner: Clayton Etzmuller
Address Roca Nebr

Soil Type: Silty Clay [X]; Silty Clay Loam [ ]; Sandy Loam [ ]
Silty Loam [ ]; Clay Loam [ ]; Sandy Clay [ ]

Dates of Tests: 11-10 to 11-11. Weather: Precip. 0 Temp. 60° F.

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
		Pre-Saturation Period				Percolation Readings					Results		
		Start		End		Start			End				
Hole No.	Hole Depth (in.)	Date (Mo. Day)	Time (Hr. Min.)	Date (Mo. Day)	Time (Hr. Min.)	Date (Mo. Day)	Time (Hr. Min.)	Water Level (in.)	Time (Hr. Min.)	Water Level (in.)	Elapsed Time (Min.)	Water Level Drop (in.)	Percolation Rates (Min./inch)
1	36"	11-10	1:00	11-11	2:30	11-11	3:00	20	3:30	18½	30	1½	30/1½
2	36"	11/10			2:30					18	30	2	30/2
3	36"	11/10								18¼	30	1¾	30/1¾
4	36"	11/10								18¾	30	¼	30/¼
5	36"	11/10								19	30	1	30/1
6	36"	11/10	1:00	11-11	2:40		3:06	20	3:36	18¾	30	1¾	30/1¾

Sum of Percolation Rates 9¾
Average of Rates: 1.54
Mean of Rates: 30 min/1½ in.

Signature of Person Conducting Test

Address _____
Phone: _____

(Do not write below this line)


REVIEWING ACTION

REMARKS: _____

Approved Percolation Rate(s)
A. 13 min./inch
B. _____ min./inch
C. _____ min./inch

DATE: November 20, 1975

Gerrold C. Hood
Signature of Reviewing Official

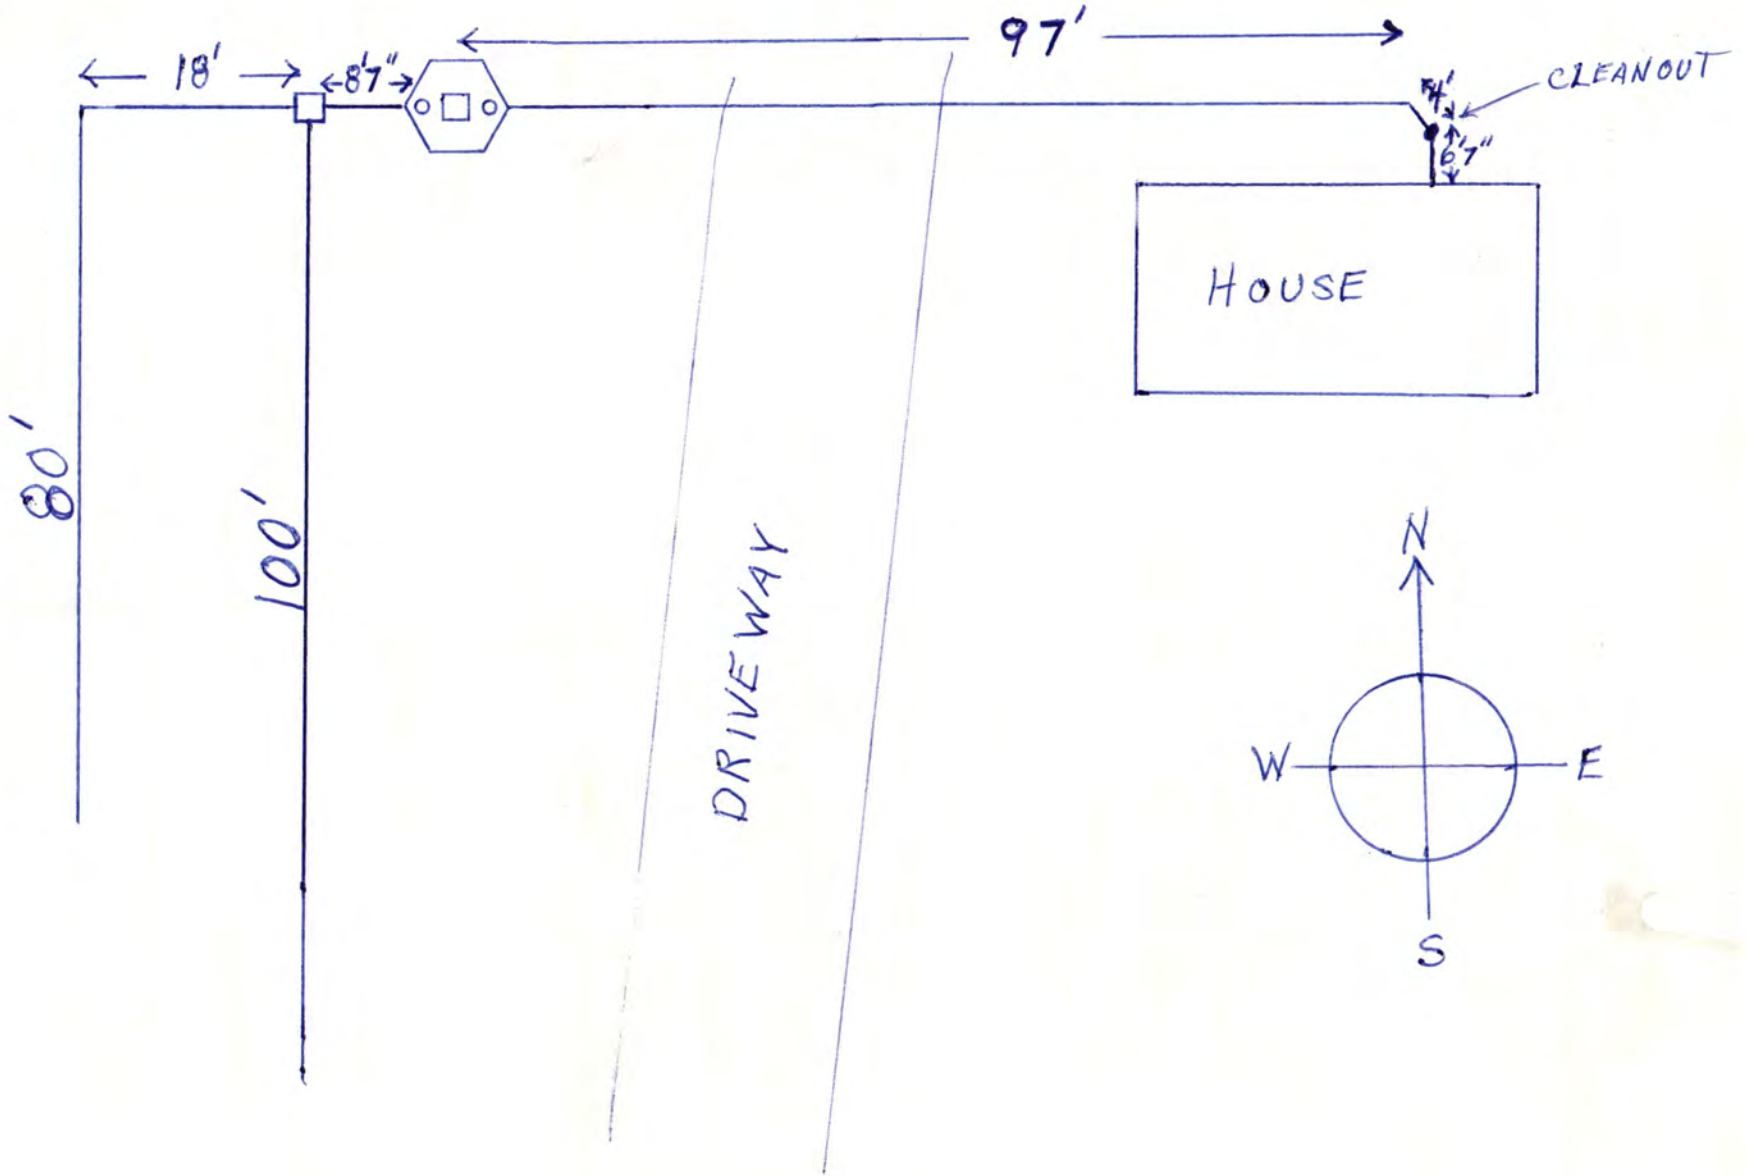
97'
18'
8'7"
4'
CLEANOUT
6'7"
HOUSE
80'
100'
DRIVEWAY
N
W
E
S
