LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

ENVIRONMENTAL HEALTH DIVISION

2200 St. Marys Ave Lincoln, NE 68502-3785 (402) 471-8000

NON TRANSFERABLE

PERMIT

Permit
SEWAGE INSTALLATION

No. 92380090001

Issued 08/20/92
Expires 02/20/93
Revenue Code 18754

Establishment
DAN MEYER
T8N R7E SEC 8
LOT 27

FEES: $150.00

TOTAL $150.00

Permittee
DAN MEYER
BOX 0185A
ROCA NE 68430

Issued By M. Jane Ford
Health Director

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW
"POST IN A PROMINENT PLACE"

923800900

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

A

FILING FEE: $_____

FILE NO._____

DATE: 8/19/92

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 8N ; Range 7E ; Section 8 ; S.W 1/4
   Block _____ : Lot 27 I.T. : Addition _____
   Street Address _____ So. 46th

2. Property Use: Residential ☑ ; Commercial ☐ Other Use ☐
   No. of Bedrooms 3 . Describe _____

3. Type of Individual Sewage Disposal System: Septic Tank ☑ ; Other ☐ EXPERIMENTAL SYSTEM

4. Distance to public sewer: _____ ft.

Additional land
Lot 30

DAN MEYER Dan Meyer
Signature of Applicant (Owner or Lessee)

BOX 185A, ROCA, NEBRASKA 68430
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. 8/20/92. Date Frwd. _____. ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Hood

2. Supt. Bldg. Insp.: or Village Clerk Date Rec'd. _____. Date Frwd. _____. ACTION: Approved ☐ Disapproved ☐ Signature: _____

3. City or County Engineer : Date Rec'd. _____. Date Frwd. _____. ACTION: Approved ☐ Disapproved ☐ Signature: _____

REMARKS OR REASONS FOR DISAPPROVAL _____

Site Visits:
Date: 8/20/92 by: J.C.H.
Date: _____ by: _____
Date: _____ by: _____

INSTALLATION FINAL WRITTEN APPROVAL *
Date: 8/24/92 By: Jerrold C. Hood

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

* EXPERIMENTAL SYSTEM PROVISIONAL APPROVAL

FORM 23-43

FORM 20105-0477
SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150 and County Resolution No. 2832)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

B

FILE NO. _____

PROPERTY WHERE SOIL TESTED:

Location: Township 8 ; Range 7 ; Section & ¼ Section SW ¼ 8 .
Property Dimensions: _____ ft. x _____ ft. Area: 1 acres. (Attach Sheet C with sketch of property).
Soil Type: Silty Clay ☒, Silty Clay Loam ☐ ; Sandy Loam ☐ ; Silt Loam ☐ ; Clay Loam ☐ .
Dates of Tests: 6/4/92 to 6/5/92 . Weather: Precip. _____ Temp. 80° .

OWNER: Dan Meyer

Address: _____

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
		Pre-Saturation Period				Percolation Readings						Results	
		Start		End		Start			End				
Hold No.	Hole Depth (in.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Water Level (in.)	Time (Hr./ Day)	Water Level (in.)	Elapsed Time (Min.)	Water Level Drop (in.)	Percolation Rates (Min./in.)
1												1½	
2												1	
3												1¾	
4												1¼	
5												¾	
6												1	

John Stuhmer
Signature of Person Conducting Test

Address 9811 N.W. 40th LNK Phone 474-9811

Sum of Percolation Rates: _____
Average of Rates: _____
Mean of Rates: _____

(Do not write below this line)

REVIEWING ACTION

Remarks: _____
Soil Type (SCS): Wymore Silty Clay Loam
Date: August 20, 1992

Approved Percolation Rate (a)
A. _____ min./inch
B. _____ min./inch
C. _____ min./inch

_____
Signature of Reviewing Official

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

D

DATE: 8/19/92

FILE NO: _____


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material PVC; Diameter 4 in.
2. Distance above basement floor ~~5~~ in., or below basement floor 18" in.
3. Distance between dwelling and septic tank 113 ft.
4. Number of clean-outs 2.
5. Distances to:
Well or Suction Line Road Wt. ft.; Stream 100' + ft.; Pressure Line _____ ft.; Property Line _____ ft.


B. SEPTIC TANK:
1. Material Concrete; No. of compartments 1.
2. Capacity 1000 gals.;
3. Factory Built: Yes ☑ No ☐
(Company Pre-cast)
4. Manholes: Over Inlet; diam. _____ in.
Over Outlet; diam. _____ in.
Riser Above ☑ Below ☐ Grade ___ in.
5. Inlet: Baffle ☑; or Tee ☐
6. Outlet: Baffle ☑; or Tee ☐
7. Depth of top of tank below finished grade 12 in.
8. Distances to:
Well or Suction Line NA ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

C. DISTRIBUTION BOX:
1. Material Concrete; Number available outlets 10.
2. Factory Built: Yes ☑ No ☐
(Company Pre-cast)
3. Distance from Septic Tank 18 ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☐ Perforated Pipe ☑
Diameter of Half Round 15" or Perforated Pipe 4".
Material: fiberglass ☐; plastic ☐; concrete ☑; other PVC.
2. Lateral Lines:
Number 2; Length of each line 100, _____, _____, _____, _____ ft.;
Total length of laterals 200 ft.;
Distance between lateral lines 20 ft.
3. Trench dimensions: Width 5.5 ft.;
Slope 3-5 in/100 ft.; Average Depth 24" in.
4. Filter Material: Road Gravel
Depth of Material 18 in.
5. Distances to:
Well or Suction Line NA ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

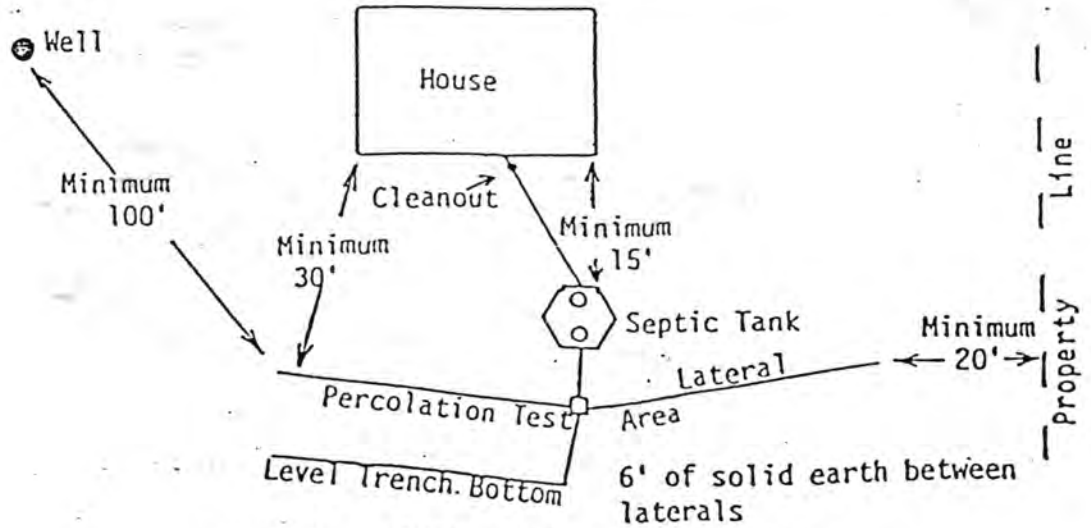

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

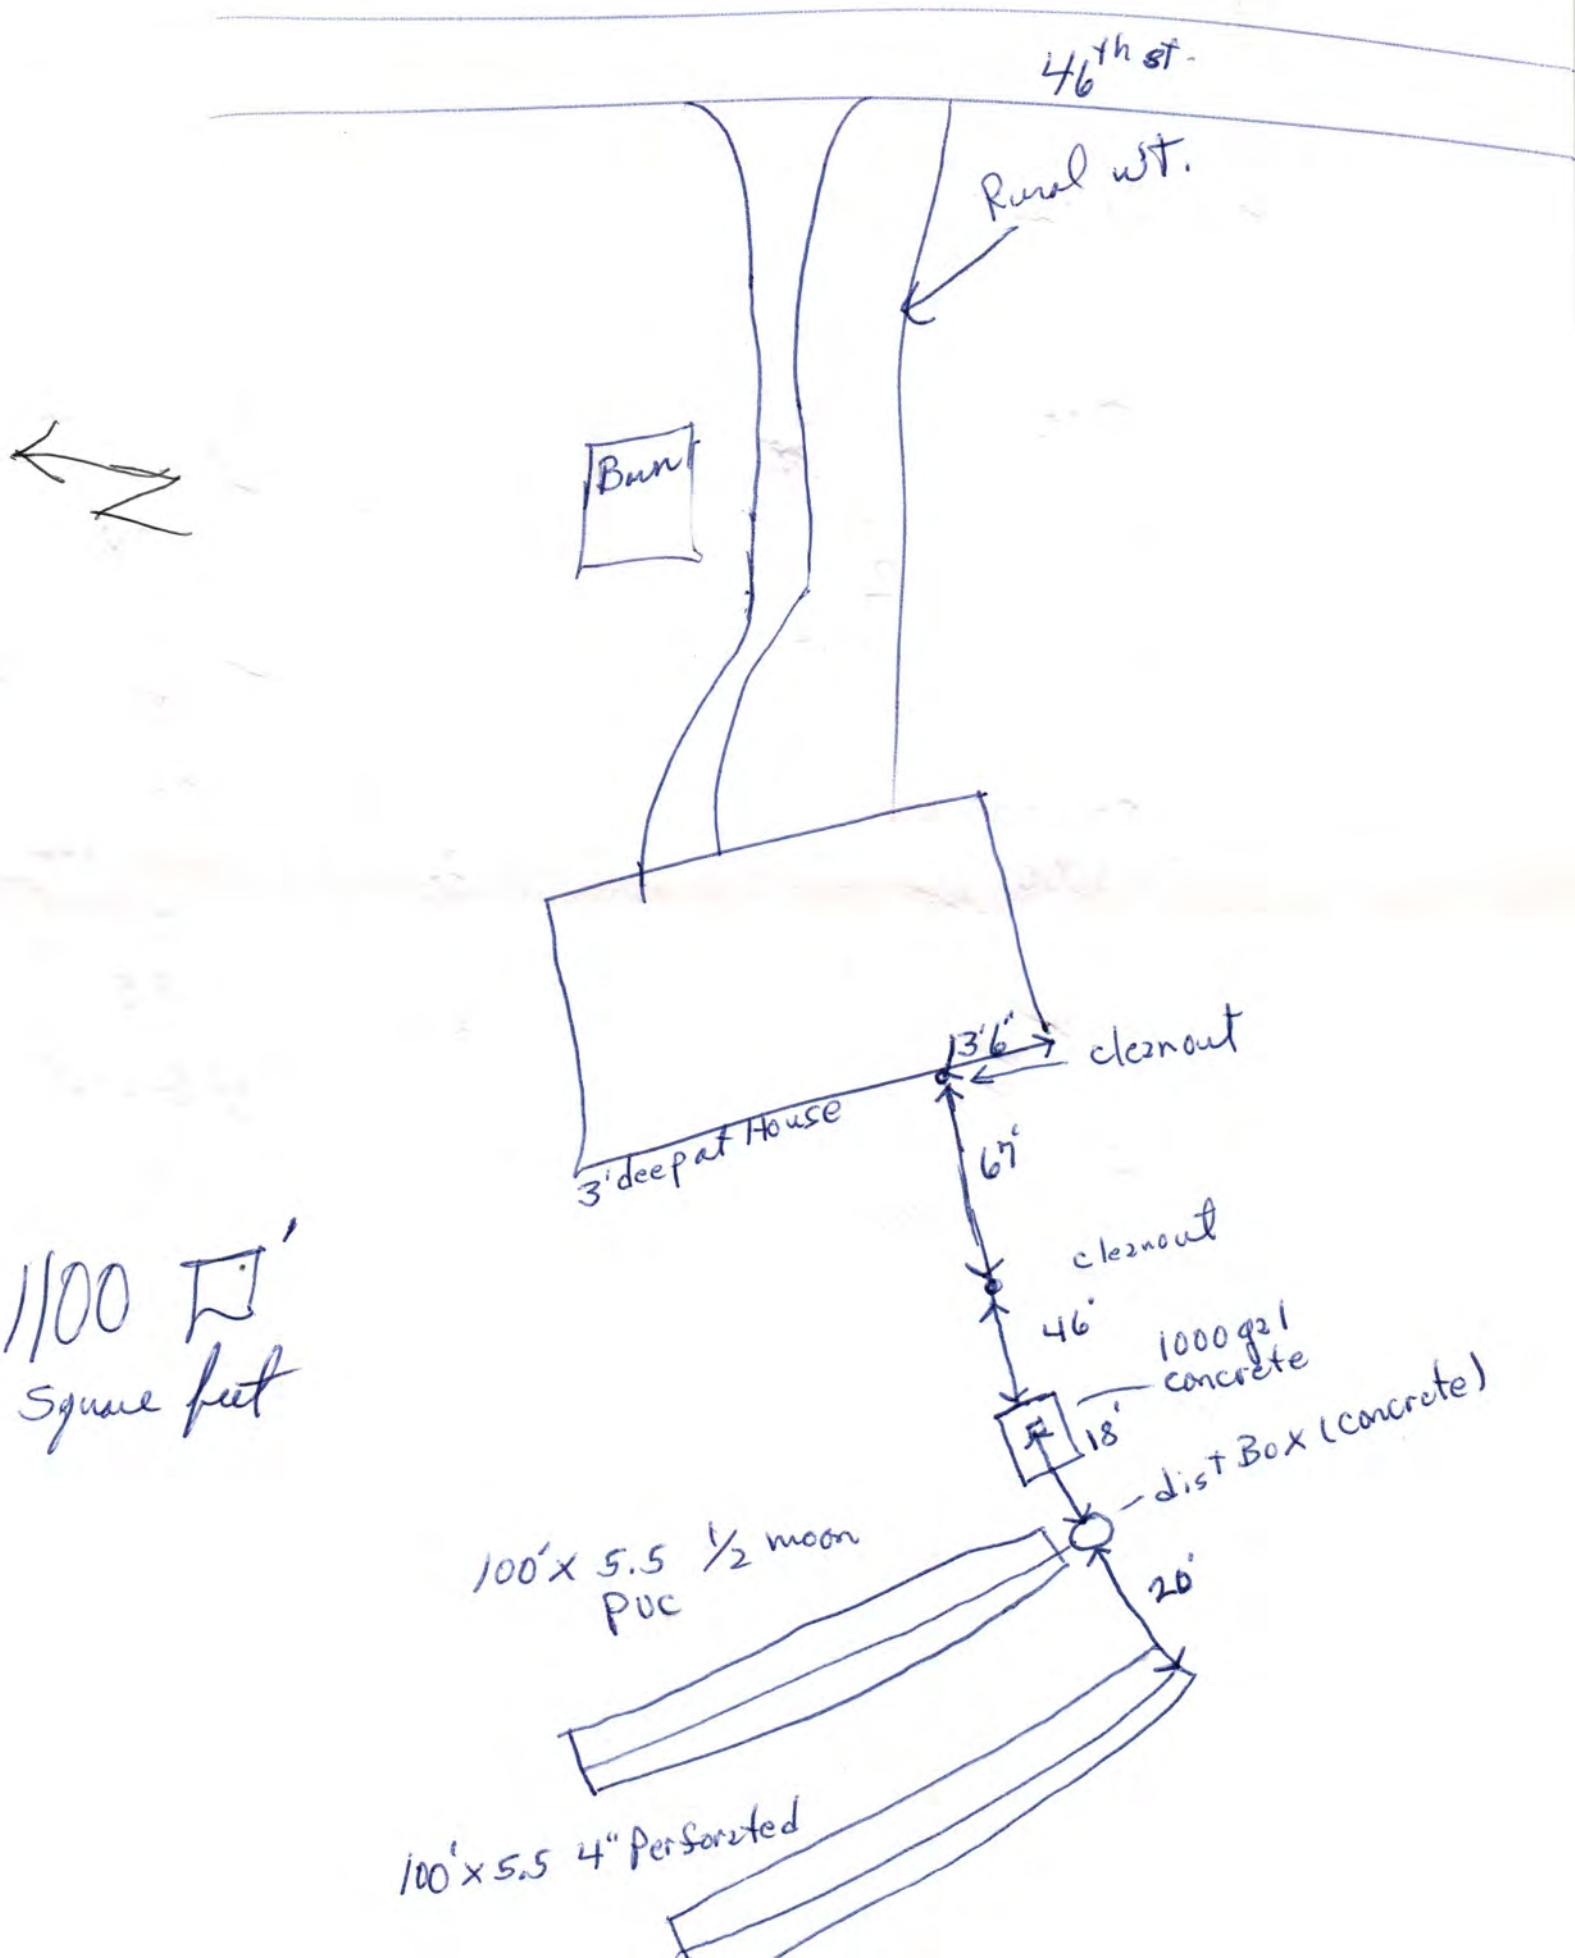

1100 Square feet

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

ENVIRONMENTAL HEALTH DIVISION

2200 St. Marys Ave Lincoln, NE 68502-3785 (402) 471-8000

NON TRANSFERABLE

PERMIT

Permit
SEWAGE INSTALLATION

No. 92380090001

Issued 08/20/92
Expires 02/20/93
Revenue Code 18754

Establishment
DAN MEYER
T8N R7E SEC 8
LOT 27

FEES: $150.00

TOTAL $150.00

Permittee
DAN MEYER
BOX 0185A
ROCA NE 68430

Issued By M. Jane Ford
Health Director

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW
"POST IN A PROMINENT PLACE"

923800900

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

A

FILING FEE: $_____

FILE NO._____

DATE: 8/19/92

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 8N ; Range 7E ; Section 8 ; S.W 1/4
   Block _____ : Lot 27 I.T. : Addition _____
   Street Address _____ So. 46th

2. Property Use: Residential ☑ ; Commercial ☐ Other Use ☐
   No. of Bedrooms 3 . Describe _____

3. Type of Individual Sewage Disposal System: Septic Tank ☑ ; Other ☐ EXPERIMENTAL SYSTEM

4. Distance to public sewer: _____ ft.

Additional land
Lot 30

DAN MEYER Dan Meyer
Signature of Applicant (Owner or Lessee)

BOX 185A, ROCA, NEBRASKA 68430
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. 8/20/92. Date Frwd. _____. ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Hood

2. Supt. Bldg. Insp.: or Village Clerk Date Rec'd. _____. Date Frwd. _____. ACTION: Approved ☐ Disapproved ☐ Signature: _____

3. City or County Engineer : Date Rec'd. _____. Date Frwd. _____. ACTION: Approved ☐ Disapproved ☐ Signature: _____

REMARKS OR REASONS FOR DISAPPROVAL _____

Site Visits:
Date: 8/20/92 by: J.C.H.
Date: _____ by: _____
Date: _____ by: _____

INSTALLATION FINAL WRITTEN APPROVAL *
Date: 8/24/92 By: Jerrold C. Hood

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

* EXPERIMENTAL SYSTEM PROVISIONAL APPROVAL

FORM 23-43

FORM 20105-0477
SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150 and County Resolution No. 2832)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

B

FILE NO. _____

PROPERTY WHERE SOIL TESTED:

Location: Township 8 ; Range 7 ; Section & ¼ Section SW ¼ 8 .
Property Dimensions: _____ ft. x _____ ft. Area: 1 acres. (Attach Sheet C with sketch of property).
Soil Type: Silty Clay ☒, Silty Clay Loam ☐ ; Sandy Loam ☐ ; Silt Loam ☐ ; Clay Loam ☐ .
Dates of Tests: 6/4/92 to 6/5/92 . Weather: Precip. _____ Temp. 80° .

OWNER: Dan Meyer

Address: _____

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
		Pre-Saturation Period				Percolation Readings						Results	
		Start		End		Start			End				
Hold No.	Hole Depth (in.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Water Level (in.)	Time (Hr./ Day)	Water Level (in.)	Elapsed Time (Min.)	Water Level Drop (in.)	Percolation Rates (Min./in.)
1												1½	
2												1	
3												1¾	
4												1¼	
5												¾	
6												1	

John Stuhmer
Signature of Person Conducting Test

Address 9811 N.W. 40th LNK Phone 474-9811

Sum of Percolation Rates: _____
Average of Rates: _____
Mean of Rates: _____

(Do not write below this line)

REVIEWING ACTION

Remarks: _____
Soil Type (SCS): Wymore Silty Clay Loam
Date: August 20, 1992

Approved Percolation Rate (a)
A. _____ min./inch
B. _____ min./inch
C. _____ min./inch

_____
Signature of Reviewing Official

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

D

DATE: 8/19/92

FILE NO: _____


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material PVC; Diameter 4 in.
2. Distance above basement floor ~~5~~ in., or below basement floor 18" in.
3. Distance between dwelling and septic tank 113 ft.
4. Number of clean-outs 2.
5. Distances to:
Well or Suction Line Road Wt. ft.; Stream 100' + ft.; Pressure Line _____ ft.; Property Line _____ ft.


B. SEPTIC TANK:
1. Material Concrete; No. of compartments 1.
2. Capacity 1000 gals.;
3. Factory Built: Yes ☑ No ☐
(Company Pre-cast)
4. Manholes: Over Inlet; diam. _____ in.
Over Outlet; diam. _____ in.
Riser Above ☑ Below ☐ Grade ___ in.
5. Inlet: Baffle ☑; or Tee ☐
6. Outlet: Baffle ☑; or Tee ☐
7. Depth of top of tank below finished grade 12 in.
8. Distances to:
Well or Suction Line NA ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

C. DISTRIBUTION BOX:
1. Material Concrete; Number available outlets 10.
2. Factory Built: Yes ☑ No ☐
(Company Pre-cast)
3. Distance from Septic Tank 18 ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☐ Perforated Pipe ☑
Diameter of Half Round 15" or Perforated Pipe 4".
Material: fiberglass ☐; plastic ☐; concrete ☑; other PVC.
2. Lateral Lines:
Number 2; Length of each line 100, _____, _____, _____, _____ ft.;
Total length of laterals 200 ft.;
Distance between lateral lines 20 ft.
3. Trench dimensions: Width 5.5 ft.;
Slope 3-5 in/100 ft.; Average Depth 24" in.
4. Filter Material: Road Gravel
Depth of Material 18 in.
5. Distances to:
Well or Suction Line NA ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

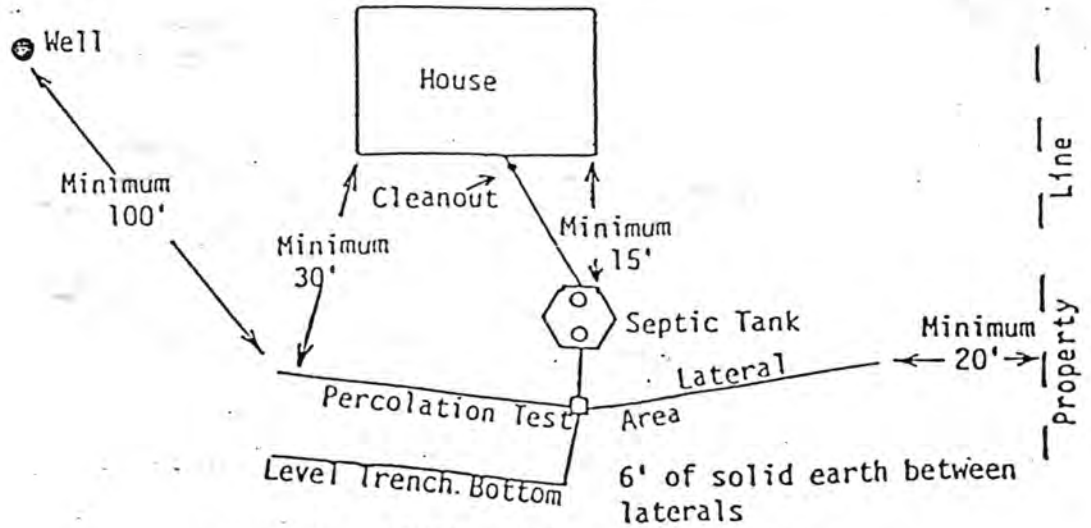

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

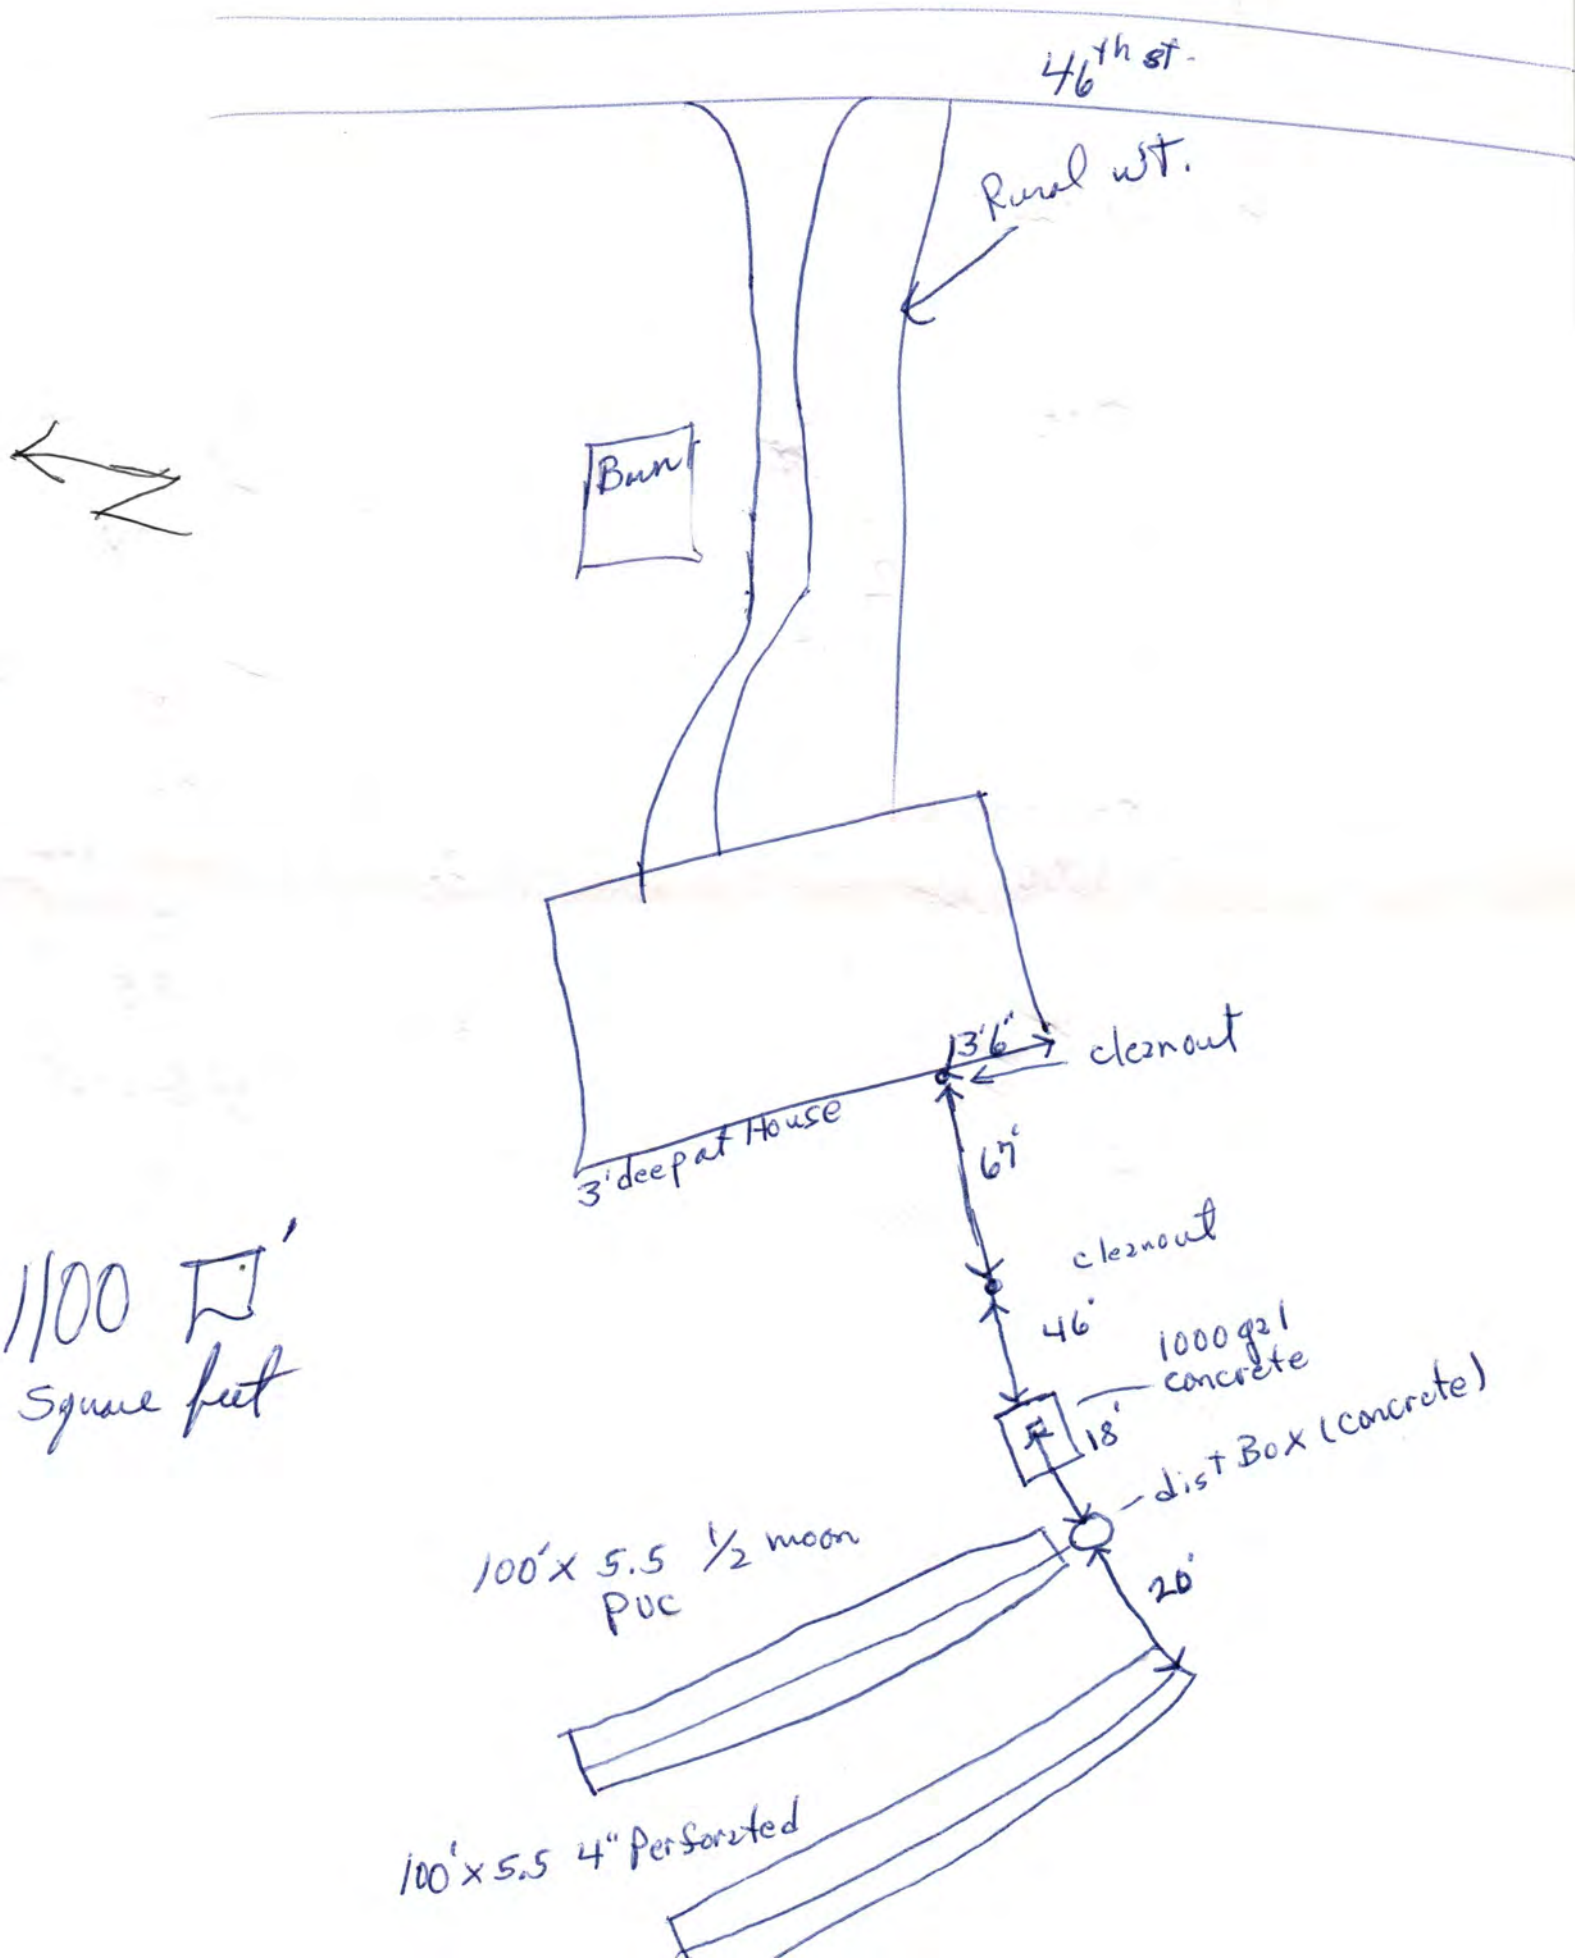

1100 Square feet
