LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

FILE NO. 991-C

INDIVIDUAL SEWAGE SYSTEM PERMIT — June 29, 1977

TYPE OF PERMIT — THIS PERMIT EXPIRES

J. D. Schwarck — Roca, Nebraska 68430

ISSUED TO — ADDRESS

T8N; R7E; Section 9 S½ of W½ of NW¼ — Replace Tank and lateral

LEGAL DESCRIPTION

REMARKS: NON-TRANSFERABLE

PERMIT	INSPECTION FEE	OCCUPATION TAX	TOTAL
$ 15.00	$	$	$ 15.00
ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE
624-1535	110.16	148.14	6-2

RECEIPTED BY — DATE — AMOUNT

VALID RECEIPT ONLY IF RECEIPTED IN THIS SPACE

Health

ISSUING OFFICER

THIS PERMIT IS ISSUED AS PROVIDED BY COUNTY RESOLUTION NO. 2832

FORM HD-41(73) APPLICATION FOR PERMIT TO ALTER, EXTEND OR REPAIR INDIVIDUAL SEWAGE DISPOSAL SYSTEM

City Ordinance No. 9150 ☐

County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Ave.
Lincoln, Nebraska 68502 (Phone: 475-6221)

FILE NO. 991-C

TO: Division of Environmental Health
Lincoln-Lancaster County Health Dept.

DATE: _____

The undersigned hereby applies for a permit to ALTER ☐, EXTEND ☒, or REPAIR ☒ an existing Individual Sewage Disposal System, in conformance with appropriate Ordinance or Resolution, as described in this application and drawings attached hereto.

1. Legal description of property: Twp. 8N ; Range 7E ; Section S½ OF W½ OF NW¼ 9 ;
Block _____ ; Lot _____ ; Addition _____
Street Address _____

2. Property Use: Residential _____ ☐; Commercial _____ ☐
No. Bedrooms _____ Describe _____
Other Use ☒
Describe TRAILER COURT

3. Type of existing Individual Sewage Disposal System: Septic Tank ☒; Other ☐

4. Description of proposed alteration, extension or repair: REPLACE TANK AND LATERAL

5. Work to be done by: Owner ☒ ; or Contractor ☐ , J. D. SCHWARCK
Contractor's Name

6. Estimated cost of project:

a. Materials	$	over $200.00
b. Labor	$	
c. Other	$	
TOTAL	$	

J. D. Schwarck
Signature of Applicant (owner or lessee)

Roca, Nebraska
Address

(Do not write below this line)

REVIEWING ACTION

1. Date Rec'd: _____
Filing Fee: $ 15.00

2. Site Visits:
Date: _____ by: _____
Date: _____ by: _____
Date: _____ by: _____

3. Date: Approved ☒; Disapproved ☐
by: Jerold C. Hood

4. INSTALLATION FINAL WRITTEN APPROVAL
Date: _____ by: _____

Post-it™ brand fax transmittal memo 7671	# of pages ▸ 3
To Doug Smith	From Linda
Co. Leaf'd	Co. Gagner Const.
Dept. Dept.	Phone # 402-432-5698
Fax # 402-444-3890	Fax # 797-7475

Nov 26-12

T8, R7, S9 Lot 22

Hi Doug. Here's drawing for 13400 So. 54th St. Roca, NE 68430

Thanks!
Linda

Lincoln-Lancaster County Health Department
Environmental Health Division
3140 "N" Street • Lincoln, NE 68510-1514
Phone: 402-441-8022

D

Permit Number:

Sewage Disposal System
As Built Plans & Specifications

GPS
N40° 40.755'
W096° 38.858'

Date 11/21/2012

System Location (Indicate correct number and street)
Address 13400 So 54th St. (no rural route) City ROCA NE Zip 68430

A. Building Sewer

1. Material: PVC
   Diameter: 4 in.
2. Distance above basement floor: NA in.
   or distance below basement floor: ____ in.
3. Distance between dwelling and septic tank: 20 ft.
4. Number of clean-outs: 1
5. Distances to: well or suction line NA ft.
   stream NA ft.
   pressure line 50 ft.
   property line OVER 30 ft.

B. Septic Tank

1. Material: CONCRET
   Number of compartments: 1
2. Capacity: 1500 gal.
3. Factory built: ☒ Yes ☐ No
4. Manholes: Over inlet, diameter ____ in.
   Over outlet, diameter ____ in.
   Riser: ☒ above ☐ below grade 4 in.
5. Inlet: ☒ baffle ☐ tee
6. Outlet: ☒ baffle ☐ tee
7. Depth to top of tank, below unfinished grade: 40 in.
8. Distances to: Well or suction line NA ft.
   Stream NA ft.
   Pressure line 50 ft.
   Property line OVER 30 ft.

C. Distribution Box

1. Material: ____
   Number available outlets: ____
2. Factory built: ☐ Yes ☐ No
3. Distance from septic tank: 107 ft.

D. Absorption Field


(Provide as-built drawings on back of this form)

1. Type: ☐ Half rounds ☐ Perforated pipe
   Diameter of half round: ____
   or perforated pipe: ____
   Material: ☐ fiberglass ☐ plastic ☐ concrete
   ☐ other INFILTRATORS
2. Lateral lines: Number 6
   Length of each line: 58 ft. 76 ft.
   76 ft. 76 ft. 76/76 ft.
3. Trench dimensions: Width 4 ft.
   Slope 0 in/100 ft.
   Average depth 30 in
4. Filter material: NA
   Depth of material NA in.
5. Distances to: Well or suction line NA ft.
   Stream NA ft.
   Pressure line OVER 100 ft.
   Property line OVER 25 ft.

Complete "As Built" drawing on back of this form.

Indicate North with Arrow

Individual Sewage System Design (Example)

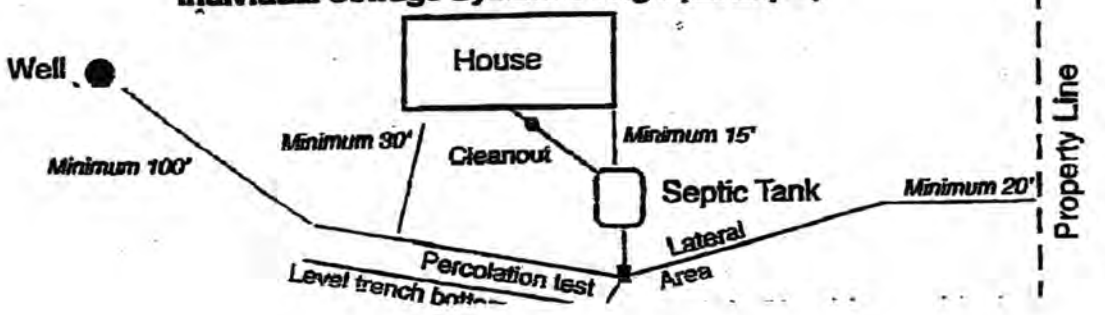

As Built Drawing

