Lincoln-Lancaster County Health Department

ENVIRONMENTAL HEALTH DIVISION

3140 N STREET · LINCOLN, NE 68510-1514 (402) 441-8000

Permit

SEWAGE SYSTEM REPAIR
SEWAGE REPAIR

Permit # 03390074301

Issued 01/06/03
Expires 07/06/03
Revenue Code 3157

Establishment

KUBR CONSTRUCTION
T8N R7E SEC 16 QTR SE
N 1/2
15105 S 68 ST-ROCA

FEES: $100.00

TOTAL: $100.00

Permittee

KUBR CONSTRUCTION
9901 SALTILLO RD
ROCA NE 68430

Bruce D. Dart

Bruce D. Dart, Health Director

• POST IN A PROMINENT PLACE • NOT TRANSFERABLE

003189

#033900743

Application to Alter, Extend or Repair an Individual Sewage Disposal System

☐ Municipal Code 24.38 ☒ County Resolution Number 2832

The undersigned hereby applies for a permit to: ☐ **ALTER** ☒ **EXTEND** ☒ **REPAIR** an existing Individual Sewage Disposal System, in conformance with appropriate Ordinance or Resolution, as described in this application and drawings attached hereto.

1. **Legal description of property:**
   Township 8N Range 7E Section 16 1/4 Section N/2 of SE/4
   Block _____ Lot _____ Addition _____
   Parcel ID ____-____-_____-_____-_____ (i.e. 99-99-999-999-999)
   Street Address 15105 So 68 Roca, Ne 68430

2. **Property use:** ☒ residential ☐ commercial ☐ other use
   Number of bedrooms 2 Describe _____

3. **Type of Present Individual Disposal System** ☒ septic tank ☐ lagoon ☐ other

4. **Description of proposed alteration, extension or repair** R+R orangeburg Sewer Line w/ Sch 40 PVC & extend lateral field 100'x4" with Infiltrator

5. **Work to be done by:** ☐ owner ☒ contractor's name Southwick Sewer & Drain

6. **Estimated project:**
   a. Repair, replace or minor extension with a cost less than $400 (no fee required).
   b. Total cost is greater than $400 (Return fee with this application)
   c. A "construction permit" is required if the use, operation, location, or type of the system is being change.

Print Name Kuhr Const. Address 9901 Saltillo Rd. Roca Phone 423-3045
Applicant Signature (owner or lessee) _____

Please include the permit fee ($100) with this application
Fee must be included before the application will be processed. Incomplete information will delay processing

---

HEALTH DEPARTMENT USE ONLY

Date received 1/6/03 REVIEW: ☒ Approved ☐ Disapproved By: Jerrold C. Hood

Site visits
Date 1/6/03 By Jerrold Hood
Date ____/____/____ By _____
Date ____/____/____ By _____

Installation final written approval
Date 6/23/03 By Jerrold Hood

Return application to: Lincoln-Lancaster County Health Department - Environmental Health Division
3140 "N" Street, Lincoln, NE 68510
Phone: 441-8022

Business Office Use Only
Received: Date: 01/06/03 Amount 100.00 Check No. 4943 Initials LO

White - Division Copy Pink - Business Office Revised 9/00

Lincoln-Lancaster County Health Department
Environmental Health Division
3140 "N" Street • Lincoln, NE 68510-1514
Phone: 402-441-8022

D

Permit Number:

Sewage Disposal System

As Built Plans & Specifications

Date 1-7-03

Don Kuhr

System Location (Indicate correct number and street)

Address 15105 So 68 (no rural route) City ROCA NE, Zip 68430

A. Building Sewer

1. Material: Sch 40 PVC
   Diameter: 4 in.
2. Distance above basement floor: _____ in.
   or distance below basement floor: 10 in.
3. Distance between dwelling and septic tank: 25 ft.
4. Number of clean-outs: 4
5. Distances to: well or suction line > 50 ft.
   stream NA ft.
   pressure line NA ft.
   property line NA ft.

B. Septic Tank

1. Material: Concrete
   Number of compartments: 1
2. Capacity: 1,000 gal.
3. Factory built: ☐ Yes ☐ No
4. Manholes: Over inlet, diameter 8 in.
   Over outlet, diameter 8 in.
   Riser: ☐ above ☐ below grade 6 in.
5. Inlet: ☐ baffle ☐ tee NONE
6. Outlet: ☒ baffle ☐ tee
7. Depth to top of tank, below unfinished grade: 30 in.
8. Distances to: Well or suction line > 50 ft.
   Stream NA ft.
   Pressure line NA ft.
   Property line NA ft.

C. Distribution Box

1. Material: PVC
   Number available outlets: 5
2. Factory built: ☒ Yes ☐ No
3. Distance from septic tank: 1 ft.

D. Absorption Field


(Provide as-built drawings on back of this form)

1. Type: ☒ Half rounds ☐ Perforated pipe
   Diameter of half round: 16
   or perforated pipe: _____
   Material: ☐ fiberglass ☒ plastic ☐ concrete
   ☐ other _____
2. Lateral lines: Number 2
   Length of each line: 100 ft. 100 ft.
   _____ ft. _____ ft., _____ ft.
3. Trench dimensions: Width _____ ft.
   Slope _____ in/100 ft.
   Average depth 6 in
4. Filter material: Road Gravel
   Depth of material 14 in.
5. Distances to: Well or suction line > 100 ft.
   Stream NA ft.
   Pressure line NA ft.
   Property line NA ft.

Indicate North with Arrow


Complete "As Built" drawing on back of this form.

Individual Sewage System Design (Example)

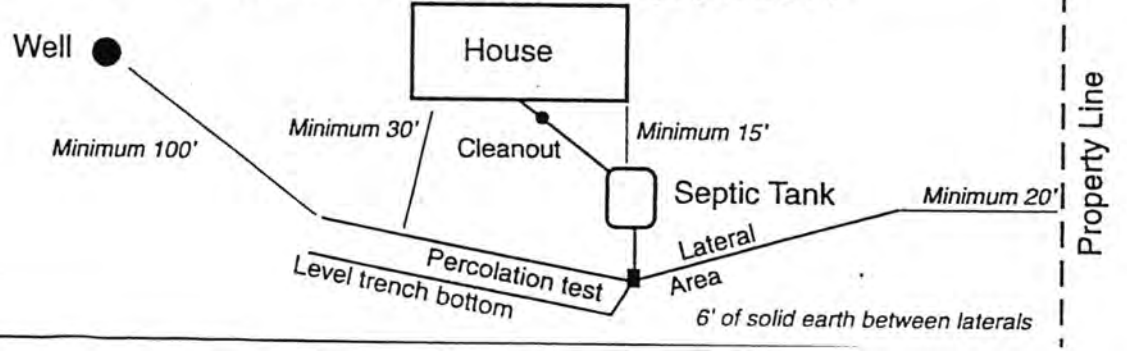

FORM 23-103 10-96

As Built Drawing

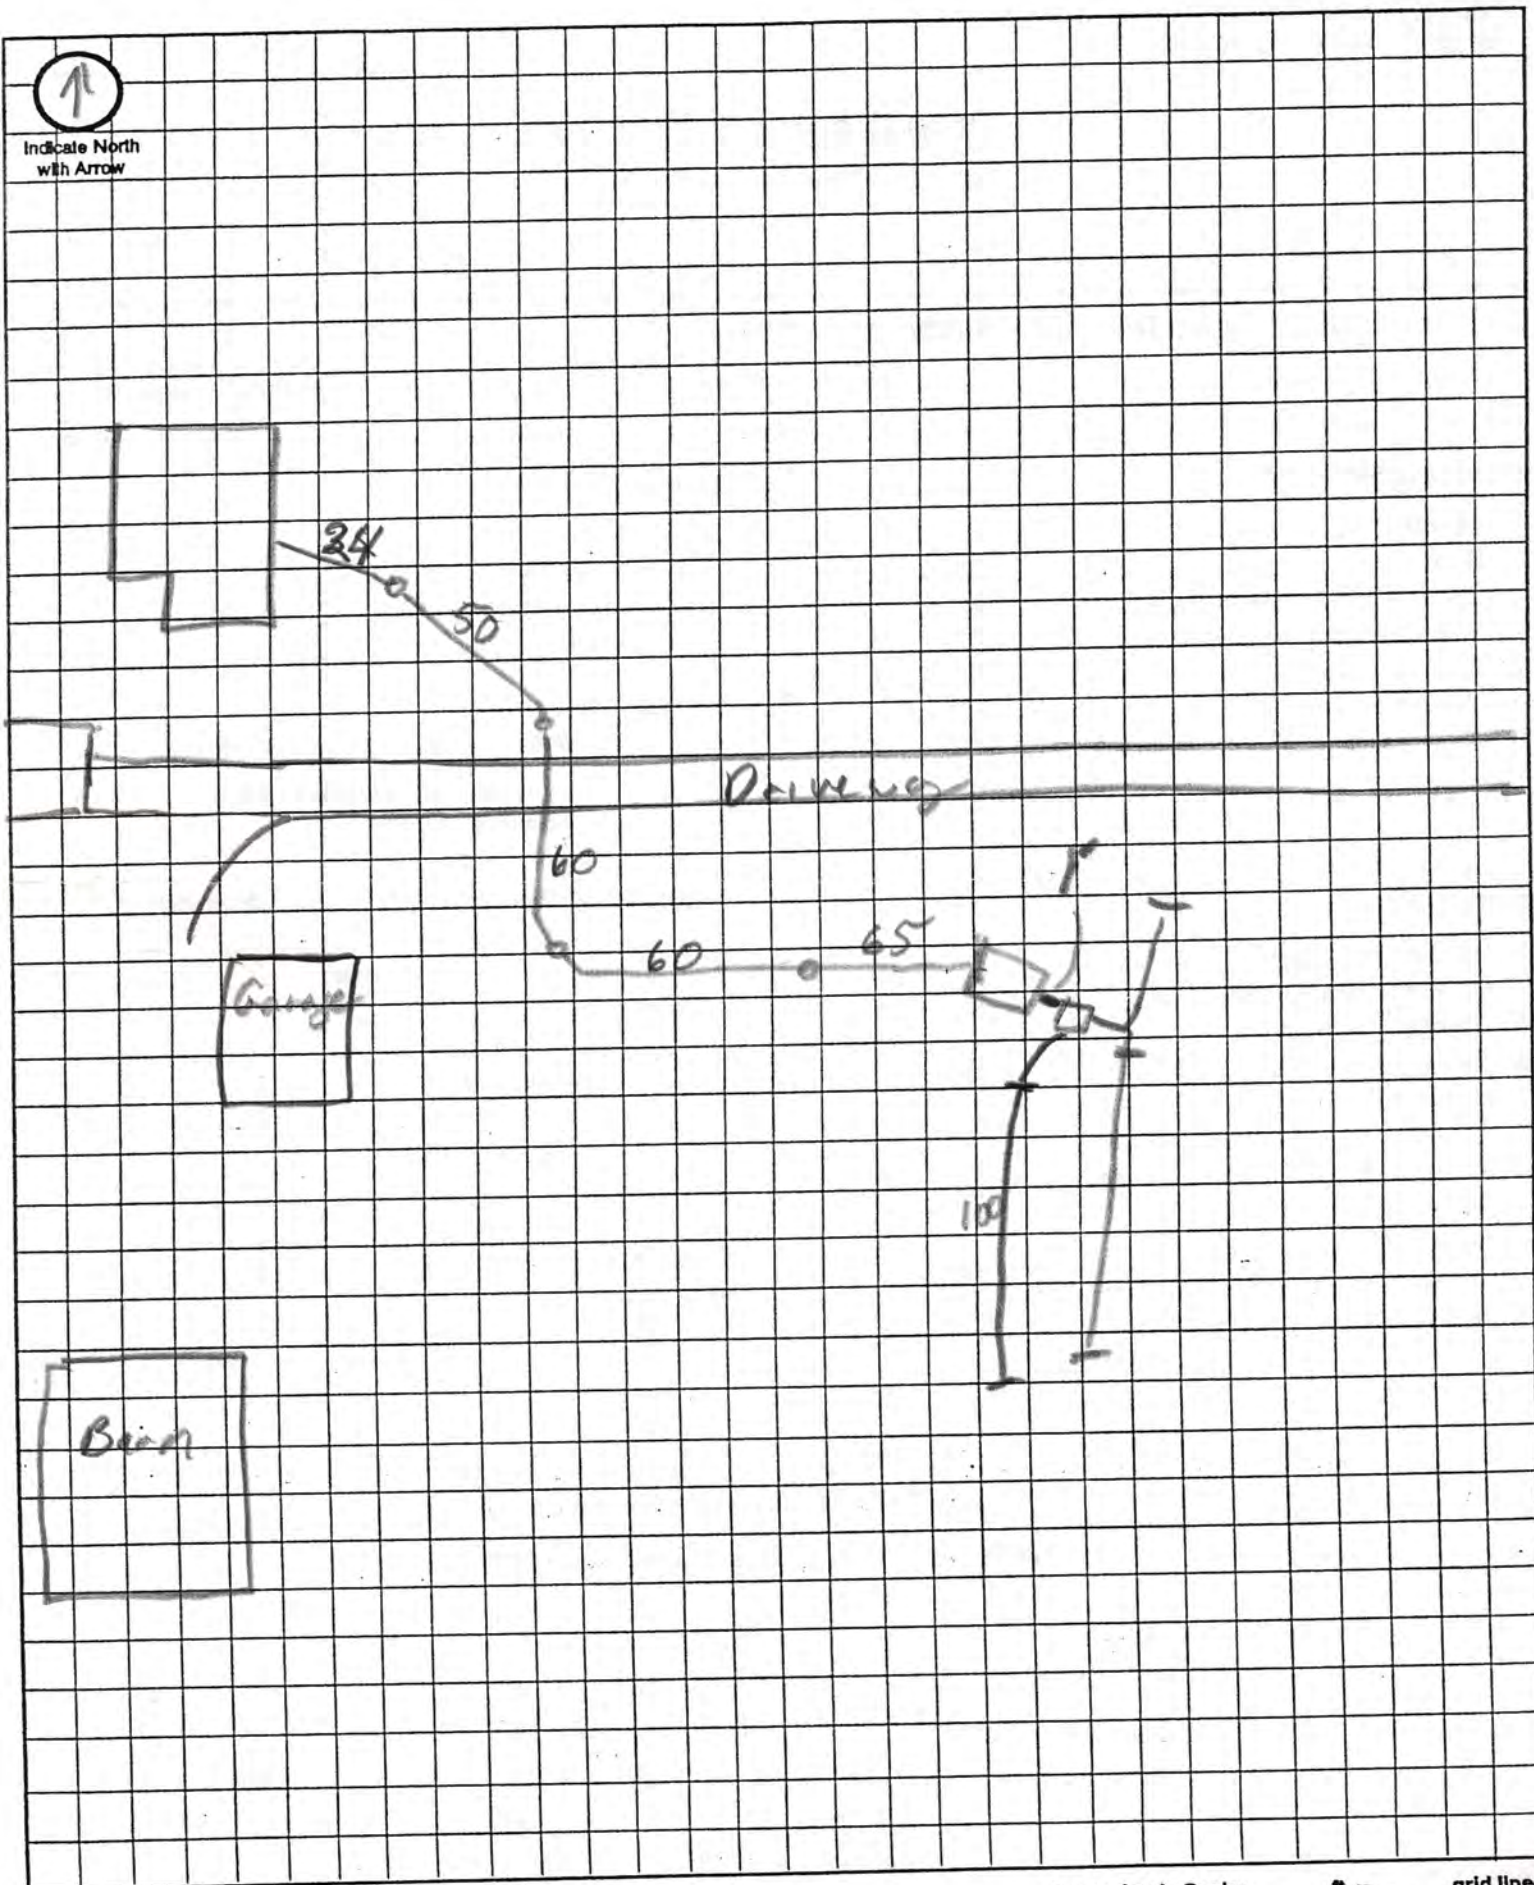

Approximate Scale: _____ ft. = _____ grid line/s
