LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

3140 "N" STREET
ENVIRONMENTAL HEALTH DIVISION
Lincoln, NE 68510-1514
(402) 441-8000

NON TRANSFERABLE

PERMIT

Permit
SEWAGE INSTALLATION

No. 95380136401

Issued 10/26/95
Expires 04/26/96
Revenue Code 18754

Establishment
BEVERLY SCHAEFER
T8N R7E SEC 19
LOT 194

FEES: $150.00

TOTAL $150.00

Permittee
BEVERLY SCHAEFER
RR0001
BOX 00001
ROCA NE 68430

Issued By M. Jane Ford
Health Director

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW "POST IN A PROMINENT PLACE"

FORM 20103-0477

REQUEST FOR SITE CLEARANCE AND PERMIT FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM

City Ordinance No. 9150 ☐

County Resolution No. 2832 ☐

Lincoln-Lancaster County
HEALTH DEPARTMENT
3140 "N" STREET LINCOLN, NE 68510-1514

OCT 25 1995

A

FILING FEE: $ 150.00

FILE NO. _____

DATE: 9-15-95

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 8N ; Range ~~8~~ 7E ; Section 19 ;
   Block _____ : Lot 194 IT ; Addition _____
   Street Address _____

2. Property Use: Residential ☐ ; Commercial ☒ Other Use ☐
   No. of Bedrooms _____. Describe _____

3. Type of Individual Sewage Disposal System: Septic Tank ☑ ; Other ☐

4. Distance to public sewer: _____ ft.

DBA: ROCA BERRY FARM

Beverly Schaefer
Signature of Applicant (Owner or Lessee)

RR 1 Box 1 Roca NE 68430
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. 10/25/95. Date Frwd. 10/26/95. ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Hood

2. Supt. Bldg. Insp.: or Village Clerk Date Rec'd. _____. Date Frwd. _____. ACTION: Approved ☒ Disapproved ☐ Signature: Mike Olschlager

3. City or County Engineer: Date Rec'd. 10-26-95. Date Frwd. 10-26-95. ACTION: Approved ☑ Disapproved ☐ Signature: Larry V. Worrell

REMARKS OR REASONS FOR DISAPPROVAL _____

Site Visits:
Date: 9-15-95 by: P.D.
Date: ~~9-15-95~~ by: ~~Mike Olschlager~~
Date: _____ by: _____

INSTALLATION FINAL WRITTEN APPROVAL
Date: 11-2-95 By: Paul Waggoner

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

FORM 22.43

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

D

DATE: _____

FILE NO. _____


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material Sch 40 PVC; Diameter 4 in.
2. Distance above basement floor _____ in., or below basement floor _____ in.
3. Distance between ~~dwelling~~ and septic tank 20 ft. Bldg.
4. Number of clean-outs 1.
5. Distances to:
Well or Suction Line >100 ft.; Stream NA ft.; Pressure Line NA ft.; Property Line NA ft.


B. SEPTIC TANK:
1. Material Concrete; No. of compartments _____.
2. Capacity 600 gals.;
3. Factory Built: Yes ☒ No ☐
(Company Pre Cast Products)
4. Manholes: Over Inlet; diam. 6 in.
Over Outlet; diam. 10 in.
Riser Above ☐ Below ☐ Grade ____ in.
5. Inlet: Baffle ☒ ; or Tee ☐
6. Outlet: Baffle ☒ ; or Tee ☐
7. Depth of top of tank below finished grade 14 in.
8. Distances to:
Well or Suction Line >100 ft.; Stream NA ft.; Pressure Line >25 ft.; Property Line >20 ft.

C. DISTRIBUTION BOX:
1. Material _____; Number - available outlets _____.
2. Factory Built: Yes ☐ No ☐
(Company _____)
3. Distance from Septic Tank _____ ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☐ Perforated Pipe ☐
Diameter of Half Round _____ or Perforated Pipe _____.
Material: fiberglass ☐ ; plastic ☐ ; concrete ☐ ; other _____.
2. Lateral Lines:
Number 1 ; Length of each line 45, _____, _____, _____, _____ ft.;
Total length of laterals 45 ft.;
Distance between lateral lines ____ ft.
3. Trench dimensions: Width 3 ft.;
Slope 3 in/100 ft.; Average Depth _____ in.
4. Filter Material: Road Gravel
Depth of Material 12 in.
5. Distances to:
Well or Suction Line >100 ft.; Stream NA ft.; Pressure Line >50 ft.; Property Line >20 ft.

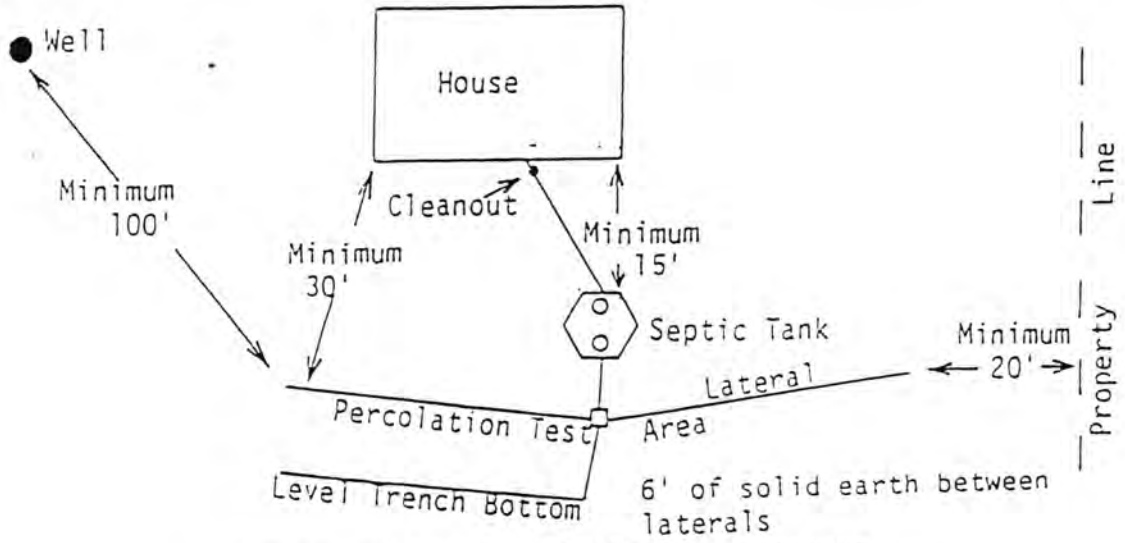

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

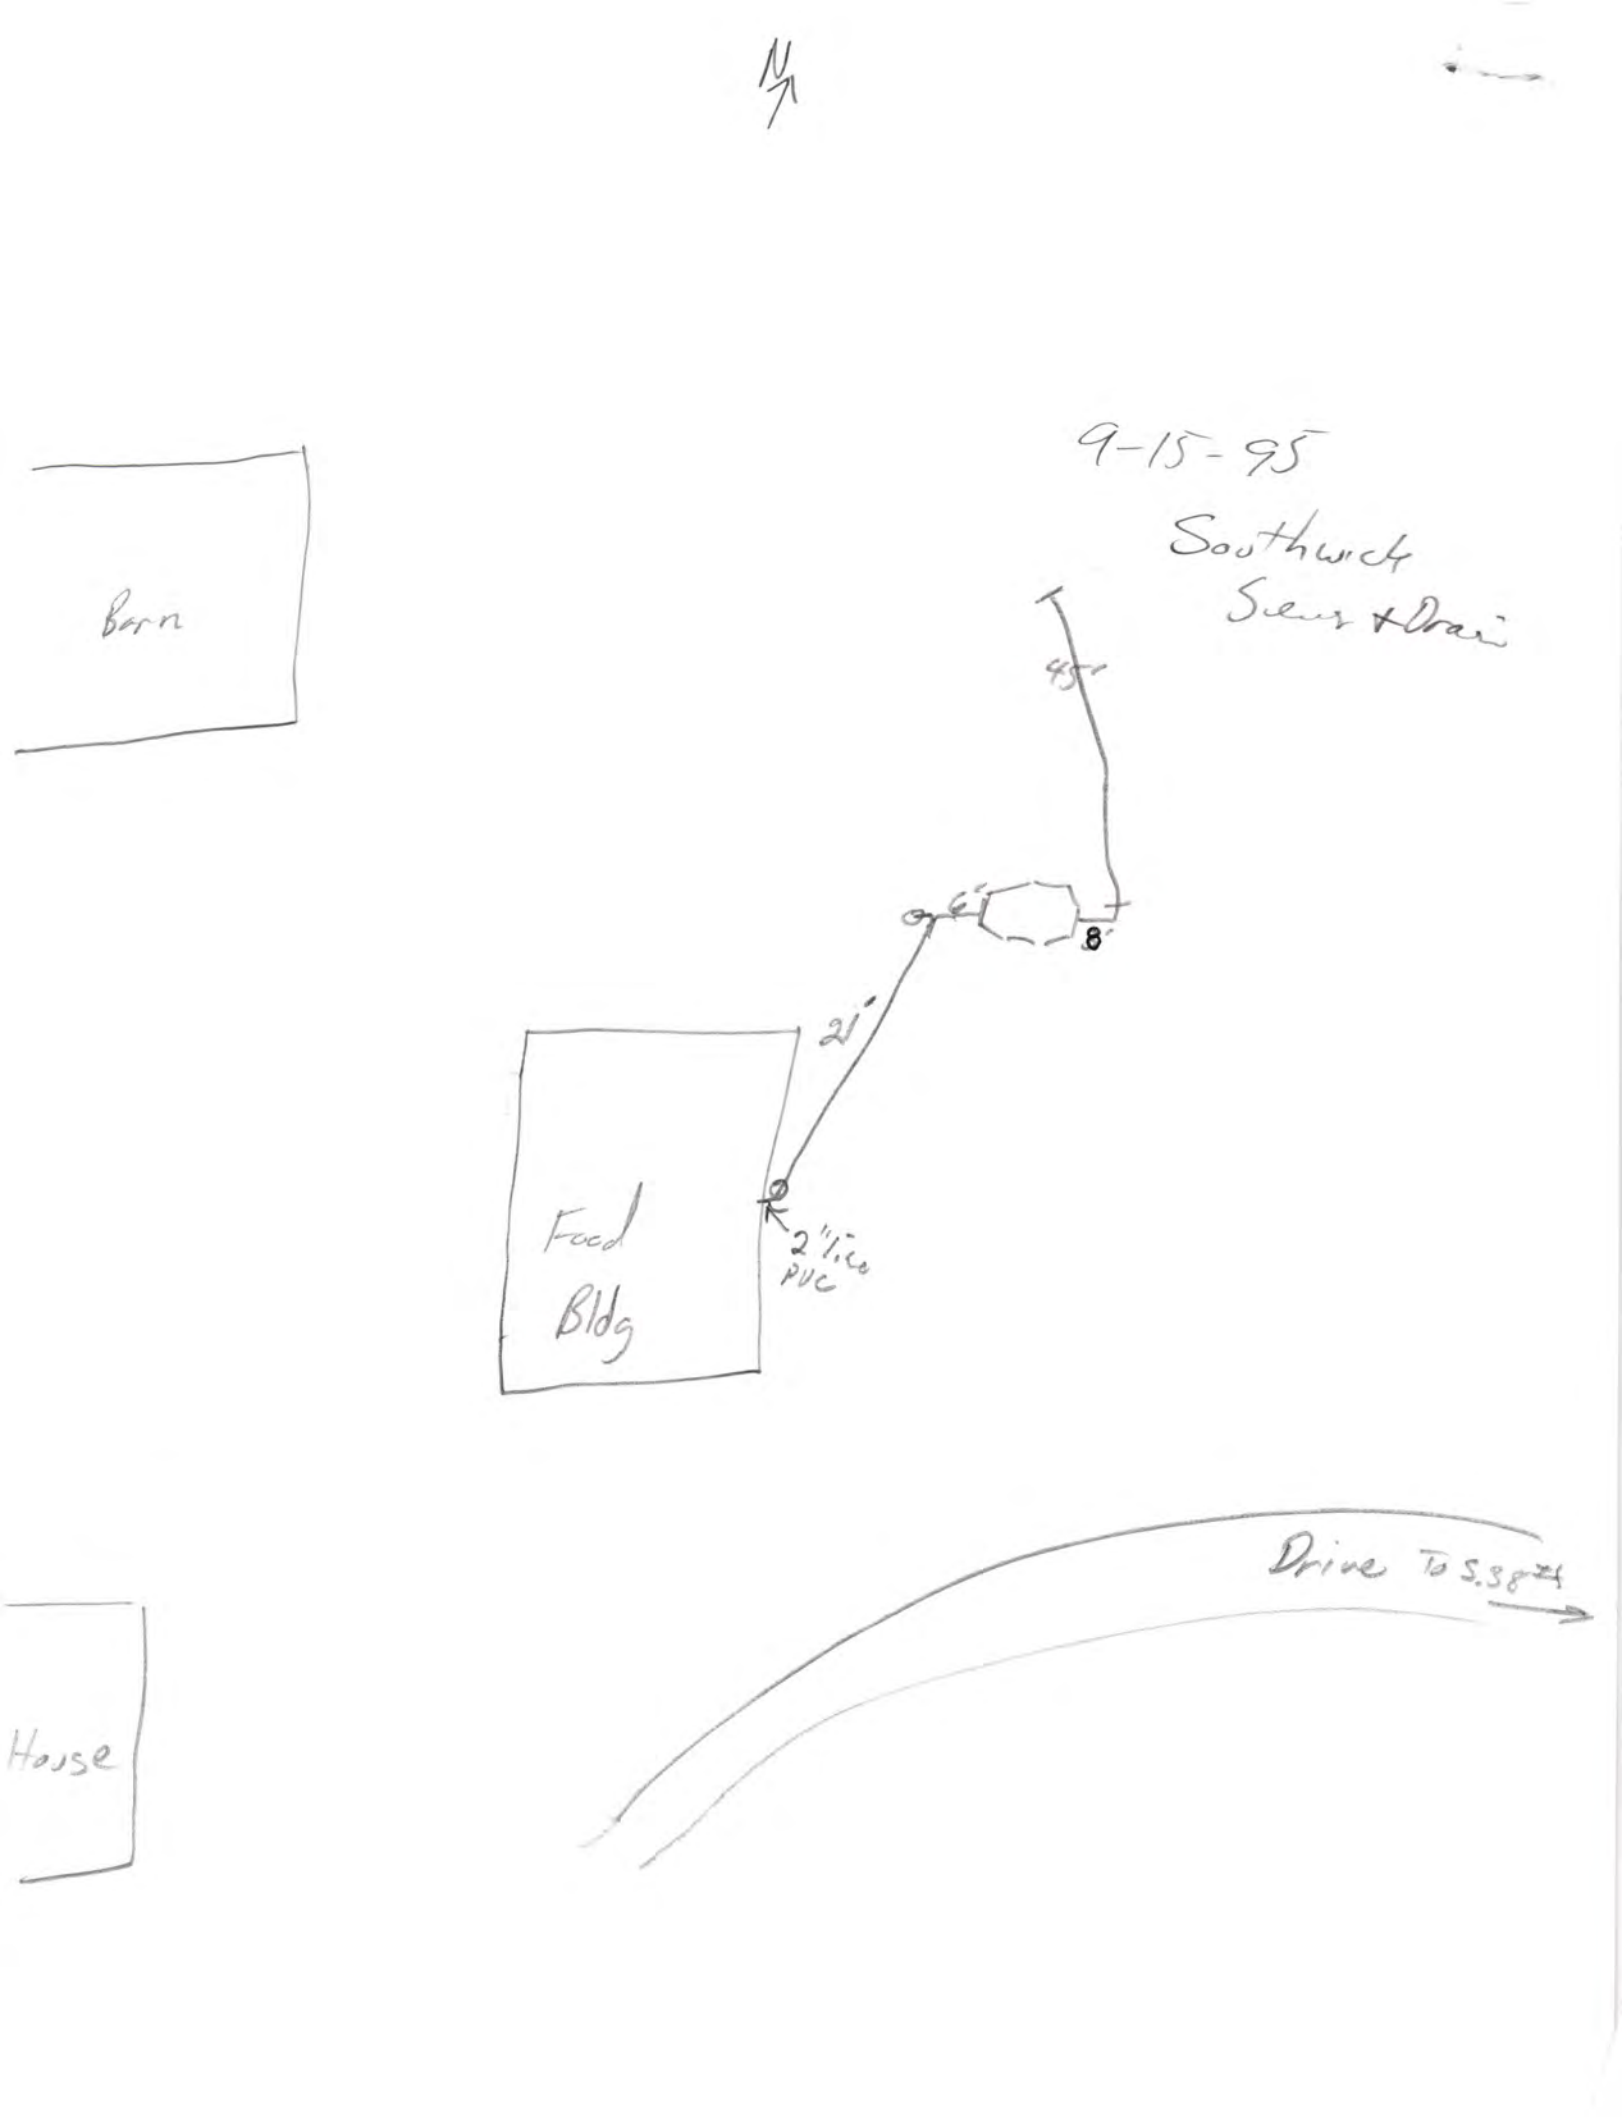
N
9-15-95
Southwick
Sewer + Drain
Barn
45°
6'
8'
21'
Feed
Bldg
2" I.D.
PVC
Drive To S.S.
House
