LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

2200 ST. MARYS
LINCOLN, NEBRASKA 68502

FILE NO. 1842-C

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION — TYPE OF PERMIT

May 12, 1982 — THIS PERMIT EXPIRES

Vic Schmuttee — ISSUED TO

RFD Roca, NE — ADDRESS

T8N; R7F; Sec 24; West ½ of NE ¼ — LEGAL DESCRIPTION

REMARKS: NONTRANSFERABLE

PERMIT	INSPECTION FEE	OCCUPATION TAX	TOTAL
$ 60.00	$	$	$ 60.00
ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE
	110.16	148.14	6-2

RECEIPTED BY — DATE — AMOUNT

VALID RECEIPT ONLY IF RECEIPTED IN THIS SPACE

HEALTH
ISSUING OFFICER

THIS PERMIT IS ISSUED AS PROVIDED BY COUNTY RESOLUTION NO. 2832

20109-0977

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

A

FILING FEE: $ 60.00

FILE NO. _____

DATE: Nov 11, 1981

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 8N ; Range 7E ; Section 24 ; west 1/2 of NE 1/4
   Block _____ : Lot _____ : Addition _____
   Street Address _____

2. Property Use: Residential ☑ ; Commercial ☐ Other Use ☐
   No. of Bedrooms 3 . Describe _____

3. Type of Individual Sewage Disposal System: Septic Tank ☐ ; Other ☐

4. Distance to public sewer: _____ ft.

Vic Schmutte
Signature of Applicant (Owner or Lessee)

RFD Roca
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. 11/12/81. Date Frwd. 11/12/81. ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Nodd
2. Supt. Bldg. Insp.: or Village Clerk Date Rec'd. 11-10-81. Date Frwd. 11-10-81. ACTION: Approved ☒ Disapproved ☐ Signature: Paul Bouma
3. City or County Engineer: Date Rec'd. _____. Date Frwd. _____. ACTION: Approved ☒ Disapproved ☐ Signature: Don R. Thomas

REMARKS OR REASONS FOR DISAPPROVAL _____

Site Visits:
Date: 11-24-81 by: JMA
Date: _____ by: _____
Date: _____ by: _____

INSTALLATION FINAL WRITTEN APPROVAL
Date: 12-2-81 By: Ron Marquardt

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

FORM 20105-0477
SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150 and County Resolution No. 2832)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

B

FILE NO. _____

PROPERTY WHERE SOIL TESTED:

Location: Township 8 ; Range 7E ; Section & ¼ Section West ½ NE 1/4 24 .
Property Dimensions: _____ ft. x _____ ft. Area: _____ acres. (Attach Sheet C with sketch of property).
Soil Type: Silty Clay ☐ ; Silty Clay Loam ☐ ; Sandy Loam ☐ ; Silt Loam ☐ ; Clay Loam ☐ .
Dates of Tests: Nov 9 to Nov 10 1981. Weather: Precip. _____ Temp. _____.

OWNER: Vic Schmuttee

Address: R.F.D. Roca

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
		Pre-Saturation Period				Percolation Readings						Results	
		Start		End		Start			End				
Hold No.	Hole Depth (in.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Water Level (in.)	Time (Hr./ Day)	Water Level (in.)	Elapsed Time (Min.)	Water Level Drop (in.)	Percolation Rates (Min./in.)
1	30"	11/9	10 AM	11/10	10 AM	11/10	11:00	6"	11:30	4	30	2	
2	"	"	"	"	"	"	"	"	"	4 3/4	"	1 1/4	
3	"	"	"	"	"	"	"	"	"	5	"	1	
4	"	"	"	"	"	"	"	"	"	4 3/4	"	1 1/4	
5	"	"	"	"	"	"	"	"	"	5 1/2	"	1/2	
6	"	"	"	"	"	"	"	"	"	5	"	1	

John L Strohmyer
Signature of Person Conducting Test

Sum of Percolation Rates: _____
Average of Rates: _____
Mean of Rates: _____

Address 4401 No. 27th Lincoln 68521 Phone 467-1627

(Do not write below this line)

REVIEWING ACTION

Remarks: Seems a little fast for Wymore
Soil Type (SCS): Wymore Silty Clay Loam
Date: November 12, 1981

Approved Percolation Rate (a)
A. 25 min./inch
B. _____ min./inch
C. _____ min./inch

Jerrold C. Hood
Signature of Reviewing Official

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

D

DATE: 11/24/81
Vic Schmutte

FILE NO. _____


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material Plastic ; Diameter 4" in.
2. Distance above basement floor _____ in., or below basement floor 20" in.
3. Distance between dwelling and septic tank 80' ft.
4. Number of clean-outs 1 .
5. Distances to:
Well or Suction Line N.A. ft.;
Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

B. SEPTIC TANK:
1. Material concrete ; No. of compartments _____ .
2. Capacity _____ gals.;
3. Factory Built: Yes ☑ No ☐
(Company Pre-cast)
4. Manholes: Over Inlet; diam. _____ in.
Over Outlet; diam. _____ in.
Riser Above ☑ Below ☐ Grade 2" in.
5. Inlet: Baffle ☐ ; or Tee ☐
6. Outlet: Baffle ☐ ; or Tee ☐
7. Depth of top of tank below finished grade 24" in.
8. Distances to:
Well or Suction Line _____ ft.;
Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

C. DISTRIBUTION BOX:
1. Material concrete ; Number - available outlets _____ .
2. Factory Built: Yes ☑ No ☐
(Company Precast)
3. Distance from Septic Tank 4' 6" ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☑ Perforated Pipe ☐
Diameter of Half Round 18" or
Perforated Pipe _____ .
Material: fiberglass ☐ ; plastic ☐ ;
concrete ☑ ; other _____ .
2. Lateral Lines:
Number 2 ; Length of each line 92' , 80' , _____ , _____ , _____ ft.;
Total length of laterals 172' ft.;
Distance between lateral lines 12' ft.
3. Trench dimensions: Width 4' ft.;
Slope 1" in/100 ft.; Average Depth 36" in.
4. Filter Material: Road Gravel
Depth of Material _____ in.
5. Distances to:
Well or Suction Line Rural water ft.;
Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

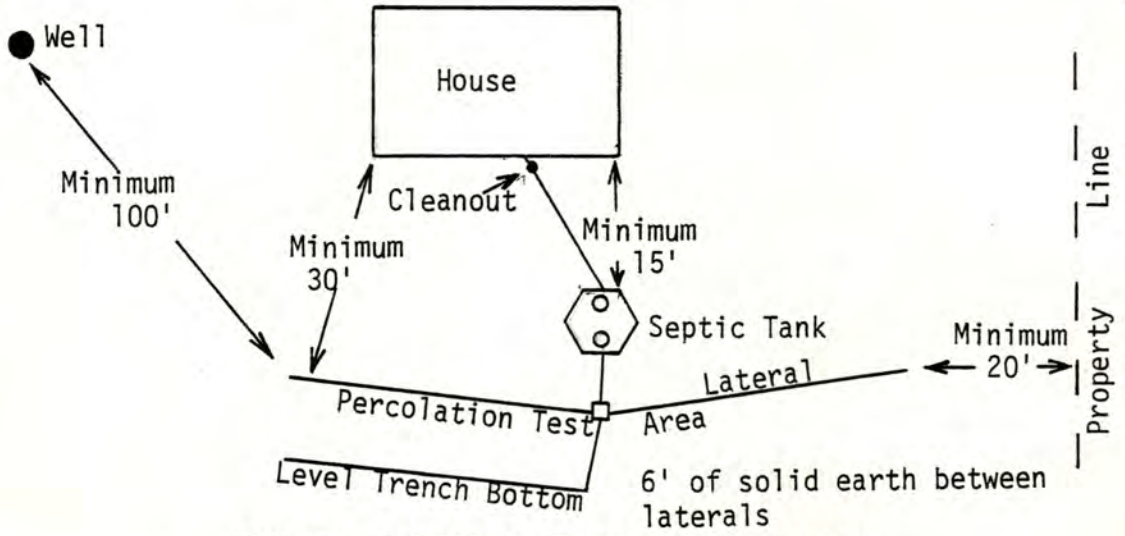

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

AS BUILT DRAWING OF SYSTEM

DATE 11/24/81 INSTALLER Strahmyer

