LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

ENVIRONMENTAL HEALTH DIVISION

3140 "N" STREET Lincoln, NE 68510-1514 (402) 441-8000

NON TRANSFERABLE

PERMIT

Permit No. 94380124301

SEWAGE INSTALLATION

Issued 10/31/94
Expires 05/01/95
Revenue Code 18754

Establishment

MELVIN GAGNER
T8N R8E SEC 10
LOT 77
15015 GARDEN

FEES: $150.00

TOTAL $150.00

Permittee

MELVIN GAGNER
RR0001
BOX 00342
LINCOLN NE 68502

Issued By M. Jane Ford
Health Director

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW "POST IN A PROMINENT PLACE"

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

A

FILING FEE: $_____

FILE NO._____

DATE: 26 OCT

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp: T8N ; Range R8E ; Section 10 ;
   Block _____ : Lot NE 77 : Addition _____
   Street Address 15015 GARDEN.
2. Property Use: Residential ☒ ; Commercial ☐ Other Use ☐
   No. of Bedrooms 4 . Describe _____
3. Type of Individual Sewage Disposal System: Septic Tank ☒ ; Other ☐
4. Distance to public sewer: 2500 ft. EXPERIMENTAL SYSTEM

Melvin F Dagner
Signature of Applicant (Owner or Lessee)
FOR MARTIN FICKEN
15015 GARDEN, WEST BENNET, NE
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. 10/31/94. Date Frwd. 10/31/94. ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Nool
2. Supt. Bldg. Insp.: or Village Clerk Date Rec'd. 10-26-95. Date Frwd. 10-26-95. ACTION: Approved ☒ Disapproved ☐ Signature: _____
3. City or County Engineer: Date Rec'd. _____. Date Frwd. ~~10/31/94~~ 10/31/94 ACTION: Approved ☒ Disapproved ☐ Signature: _____

REMARKS OR REASONS FOR DISAPPROVAL _____

Site Visits:
Date: 10/31/94 by: J. C. H.
Date: _____ by: _____
Date: _____ by: _____

INSTALLATION FINAL WRITTEN APPROVAL
Date: _____ By: _____

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

FORM 23-43

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

D

DATE: 31 OCT 1994

FILE NO. _____

SPECIFICATIONS AS BUILT


A. BUILDING SEWER:
1. Material C ; Diameter ____ in.
2. Distance above basement floor ____ in., or below basement floor ____ in.
3. Distance between dwelling and septic tank 120 ft.
4. Number of clean-outs 3.
5. Distances to:
Well or Suction Line ____ ft.; Stream ____ ft.; Pressure Line 100 ft.; Property Line 400 ft.

B. SEPTIC TANK:
1. Material CEMENT ; No. of compartments ____.
2. Capacity 1250 gals.;
3. Factory Built: Yes ☒ No ☐ (Company Pre-CAST)
4. Manholes: Over Inlet; diam. ____ in.
Over Outlet; diam. ____ in.
Riser Above ☒ Below ☐ Grade 3 in.
5. Inlet: Baffle ☒ ; or Tee ☐
6. Outlet: Baffle ☒ ; or Tee ☐
7. Depth of top of tank below finished grade 24 in.
8. Distances to:
Well or Suction Line ____ ft.; Stream ____ ft.; Pressure Line 30 ft.; Property Line 400 ft.

C. DISTRIBUTION BOX:
1. Material PLASTIC ; Number available outlets ____.
2. Factory Built: Yes ☒ No ☐ (Company ____)
3. Distance from Septic Tank 28 ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☐ Perforated Pipe ☒
Diameter of Half Round ____ or Perforated Pipe 4" .
Material: fiberglass ☐ ; plastic ☒ ; concrete ☐ ; other ____.
2. Lateral Lines:
Number 3 ; Length of each line 100, 100, 60, ____, ____ ft.;
Total length of laterals ____ ft.;
Distance between lateral lines 10 ft.
3. Trench dimensions: Width 7½-8 ft.; Slope 3 in/100 ft.; Average Depth 2-3 in.
4. Filter Material: GRAVEL
Depth of Material 12 in.
5. Distances to:
Well or Suction Line ____ ft.; Stream ____ ft.; Pressure Line 40 ft.; Property Line 400 ft.

15015 LARDEN

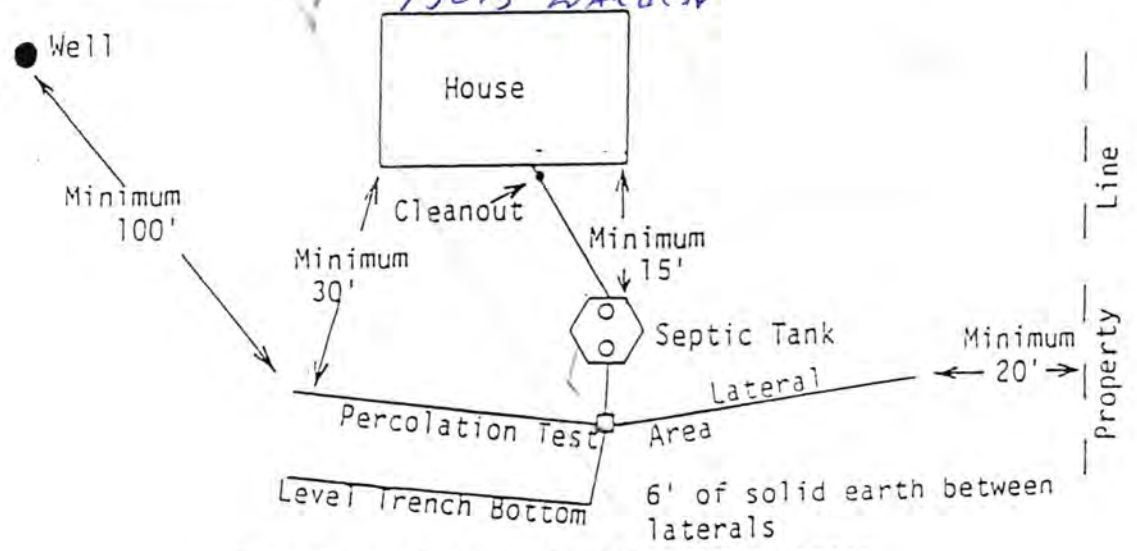

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

NORTH
24'
18'
15'
CLEAN OUTS
13'
19'
71'
62'
86'
120'
34'
CLEAN OUT
61'
28'
30'
100 FT
100 FT
60'
6 OUT
