LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

2200 ST. MARYS
LINCOLN, NEBRASKA 68502

FILE NO. 1893-C

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION
TYPE OF PERMIT

DEC. 25, 1982
THIS PERMIT EXPIRES

PAUL VON GILLERN 3308 NORTH COTNER LINCOLN NE
ISSUED TO ADDRESS

T8N, R8E, SECTION 17, LOT 12 I.T., ADDITION IRREGULAR SW QUARTER OF 6PM
LEGAL DESCRIPTION
LANCASTER

REMARKS: NONTRANSFERABLE NEW

PERMIT	INSPECTION FEE	OCCUPATION TAX	TOTAL
$ 60.00	$	$	$ 60.00
ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE
	110.16	148.14	6-2

RECEIPTED BY: ED
DATE: 6/25/82
AMOUNT:
VALID RECEIPT ONLY IF RECEIPTED IN THIS SPACE

ISSUING OFFICER

THIS PERMIT IS ISSUED AS PROVIDED BY COUNTY RESOLUTION NO. _____

20109-0977

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

A

FILING FEE: $60.00

FILE NO. 1893-C

DATE: 6-24

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 8N ; Range 8E ; Section 17 ; Block _____ : Lot 12 I.T. : Addition IRREGULAR SW QUARTER OF 6PM LANCASTER
   Street Address ~~12200 Rock Rd~~

2. Property Use: Residential ☒ ; Commercial ☐ Other Use ☐
   No. of Bedrooms 2 . Describe _____

3. Type of Individual Sewage Disposal System: Septic Tank ☒ ; Other ☐

4. Distance to public sewer: _____ ft.

ROBERT TERPSTRA
% Paul Von Gillern
Signature of Applicant (Owner or Lessee)

3308 No Cotner
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. 6/25/82. Date Frwd. 6/25/82. ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Wood

2. Supt. Bldg. Insp.: or Village Clerk: Date Rec'd. 6/25/82. Date Frwd. _____. ACTION: Approved ☒ Disapproved ☐ Signature: Gary Thomas

3. City or County Engineer: Date Rec'd. 6-25-82. Date Frwd. 6-25-82. ACTION: Approved ☒ Disapproved ☐ Signature: Harold E. Sothan

REMARKS OR REASONS FOR DISAPPROVAL _____

Site Visits:
Date: _____ by: _____
Date: _____ by: _____
Date: _____ by: _____

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

INSTALLATION FINAL WRITTEN APPROVAL
Date: _____ By: _____

FORM 20105-0477
SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150 and County Resolution No. 2832)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

B

FILE NO. _____

PROPERTY WHERE SOIL TESTED:

Location: Township 8N ; Range 8E ; Section & ¼ Section 17.
Property Dimensions: _____ ft. x _____ ft. Area: 13.40 acres. (Attach Sheet C with sketch of property).
Soil Type: Silty Clay ☐ ; Silty Clay Loam ☒ ; Sandy Loam ☐ ; Silt Loam ☐ ; Clay Loam ☐ .
Dates of Tests: _____ to _____. Weather: Precip. _____ Temp. _____.

OWNER: _____

Address: _____

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
		Pre-Saturation Period				Percolation Readings						Results	
		Start		End		Start			End				
Hold No.	Hole Depth (in.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Water Level (in.)	Time (Hr./ Day)	Water Level (in.)	Elapsed Time (Min.)	Water Level Drop (in.)	Percolation Rates (Min./in.)
1	20"	6/22	4 pm	6/23	11:30A	6/23	2 15/P	20"	3 00/P	14 5/8	45	5 3/8	
2	"	"	"	"	"	"	"	"	"	17 1/2	"	2 1/2	
3	"	"	"	"	"	"	"	"	"	17 5/8	"	2 3/8	
4	"	"	"	"	"	"	"	"	"	17	"	2	
5	"	"	"	"	"	"	"	"	"	18 1/4	"	1 3/4	
6	"	"	"	"	"	"	"	"	"	18 1/4	"	1 3/4	
7	"	"	"	"	"	"	"	"	"	19 1/4	"	3/4	
8	"	"	"	"	"	"	"	"	"	19 1/2	"	1/2	

Sum of Percolation Rates: _____
Average of Rates: _____
Mean of Rates: _____

Dale F Woodside
Signature of Person Conducting Test

Address 5729 Ballard Phone 464-3405

(Do not write below this line)

Watch and stay out of Colo. REVIEWING ACTION

Remarks: Seems too fast for Wymore
Soil Type (SCS): Wymore Silty Clay Loam
Date: June 25, 1982

Approved Percolation Rate (a)
A. 22 min./inch
B. _____ min./inch
C. _____ min./inch

Jerrold C. Hood
Signature of Reviewing Official

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

October 28, 1983

2200 ST. MARYS
LINCOLN, NEBRASKA 68502

FILE NO. 2053-C

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION
TYPE OF PERMIT

APRIL 28, 1984
THIS PERMIT EXPIRES

CHRISTO CONSTRUCTION CO. 641 SO. 21
ISSUED TO

LINCOLN, NE 68510
ADDRESS

T8N; R8E; Sec. 17; Lot 12 I.T.; 12200 Rosa Dr.
LEGAL DESCRIPTION

REMARKS: NONTRANSFERABLE NEW CONSTRUCTION

PERMIT	INSPECTION FEE	OCCUPATION TAX	TOTAL
$ 60.00	$	$	$ 60.00
ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE
	110.16	148.14	6-2

RECEIPTED BY	DATE	AMOUNT
SS	10-28-83	60.00

VALID RECEIPT ONLY IF RECEIPTED IN THIS SPACE

HEALTH
ISSUING OFFICER

THIS PERMIT IS ISSUED AS PROVIDED BY COUNTY RESOLUTION NO. 2832

20109-0977

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

A

FILING FEE: $ 60.00

FILE NO. 2053-C

DATE: _____

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 8N ; Range 8E ; Section 17 ;
   Block ' : Lot 12 I.T. : Addition _____
   Street Address 12200 Rosa Rd.

2. Property Use: Residential ☒ ; Commercial ☐ Other Use ☐
   No. of Bedrooms 2 . Describe _____

3. Type of Individual Sewage Disposal System: Septic Tank ☒ ; Other ☐

4. Distance to public sewer: _____ ft.

Jim Christo
Signature of Applicant (Owner or Lessee)

641 So. 21st
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. 10/28/83 . Date Frwd. 10/28/83 . ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Hoag

2. Supt. Bldg. Insp.: or Village Clerk: Date Rec'd. 10/28/83 . Date Frwd. 10/28/83 . ACTION: Approved ☐ Disapproved ☐ Signature: _____

3. City or County Engineer: Date Rec'd. 10/28/83 . Date Frwd. 10/28/83 . ACTION: Approved ☐ Disapproved ☐ Signature: Larry McDowell

REMARKS OR REASONS FOR DISAPPROVAL RURAL WATER DISTRICT WATER SUPPLY

Site Visits:
Date: 4-16-84 by: mm
Date: _____ by: _____
Date: _____ by: _____

INSTALLATION FINAL WRITTEN APPROVAL
Date: 4-16-84 By: Ron Maynard

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

FORM 20105-0477
SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150 and County Resolution No. 2832)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

B

FILE NO. 2053-C

PROPERTY WHERE SOIL TESTED:

Location: Township 8N ; Range 8E ; Section & ¼ Section 17.
Property Dimensions: _____ ft. x _____ ft. Area: 13.40 acres. (Attach Sheet C with sketch of property).
Soil Type: Silty Clay ☐ ; Silty Clay Loam ☒ ; Sandy Loam ☐ ; Silt Loam ☐ ; Clay Loam ☐ .
Dates of Tests: _____ to _____. Weather: Precip. _____ Temp. _____.

OWNER: _____

Address: _____

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
		Pre-Saturation Period				Percolation Readings						Results	
		Start		End		Start			End				
Hold No.	Hole Depth (in.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Water Level (in.)	Time (Hr./ Day)	Water Level (in.)	Elapsed Time (Min.)	Water Level Drop (in.)	Percolation Rates (Min./in.)
1	20"	6/22	1 pm	6/23	11 am	2"	2 1/2	20"	3 1/2	14 5/8	45	5 3/8	
2	"	"	"	"	"	"	"	"	"	17 1/2	"	2 1/2	
3	"	"	"	"	"	"	"	"	"	15 1/2	"	2 1/8	
4	"	"	"	"	"	"	"	"	"	17	"	2	
5	"	"	"	"	"	"	"	"	"	18 1/4	"	1 3/4	
6	"	"	"	"	"	"	"	"	"	18 1/4	"	1 3/4	
7	"	"	"	"	"	"	"	"	"	19 1/4	"	3/4	
8	"	"	"	"	"	"	"	"	"	19 1/2	"	1/2	

[illegible]
Signature of Person Conducting Test

Address [illegible] Phone [illegible]

Sum of Percolation Rates: _____
Average of Rates: _____
Mean of Rates: _____

(Do not write below this line)

REVIEWING ACTION

Remarks: Watch and stay out of Colo. Seems too fast for Wymore
Soil Type (SCS): Wymore Silty Clay Loam
Date: June 25, 1982

Approved Percolation Rate (a)
A. 22 min./inch
B. _____ min./inch
C. _____ min./inch

Jerrold C. Hood
Signature of Reviewing Official

FORM 20102-0477
PRELIMINARY PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

C

Sketch of property showing Percolation Test hole locations, well, residence, direction and property line.

FILE NO. 2053-C

Indicate on sketch if residence and well are exisiting or proposed.

REVIEWING ACTION

Remarks: _____

_____

Date: _____

Minimum Design Requirement
1. Capacity of Septic Tank 1000 gals.
2. Total Length of Laterals _____ ft.
3. With a Trench Width of _____ in.
4. Total Area of Lateral needed ~~1400~~ H35 sq.ft.

Jerrold C. Wood
Signature of Reviewing Official

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

D

DATE: 4-16-84

FILE NO. _____


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material Plastic; Diameter 4 in.
2. Distance above basement floor _____ in., or below basement floor 20 in.
3. Distance between dwelling and septic tank 62'6" ft.
4. Number of clean-outs one.
5. Distances to:
Well or Suction Line over 100 ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

B. SEPTIC TANK:
1. Material Fiber Glass No. of compartments one.
2. Capacity 1000 gals.;
3. Factory Built: Yes ☒ No ☐
(Company Corn-A-Glass)
4. Manholes: Over Inlet; diam. 18 in.
Over Outlet; diam. 18 in.
Riser Above ☐ Below ☒ Grade 12 in.
5. Inlet: Baffle ☒ ; or Tee ☐
6. Outlet: Baffle ☐ ; or Tee ☒
7. Depth of top of tank below finished grade 12 in.
8. Distances to:
Well or Suction Line over 100' ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line 40' ft.

C. DISTRIBUTION BOX:
1. Material Plastic; Number - available outlets Seven.
2. Factory Built: Yes ☒ No ☐
(Company _____)
3. Distance from Septic Tank 5 ft.


D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☒ Perforated Pipe ☐
Diameter of Half Round 12" or Perforated Pipe _____.
Material: fiberglass ☒ ; plastic ☐ ; concrete ☐ ; other _____.
2. Lateral Lines:
Number 2 ; Length of each line 60', 60', _____, _____, _____ ft.;
Total length of laterals 120' ft.;
Distance between lateral lines 10' ft.
3. Trench dimensions: Width 4' ft.;
Slope 0 in/100 ft.; Average Depth 18 in.
4. Filter Material: Road Gravel
Depth of Material 18 to 20" in.
5. Distances to:
Well or Suction Line _____ ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line 25 ft.

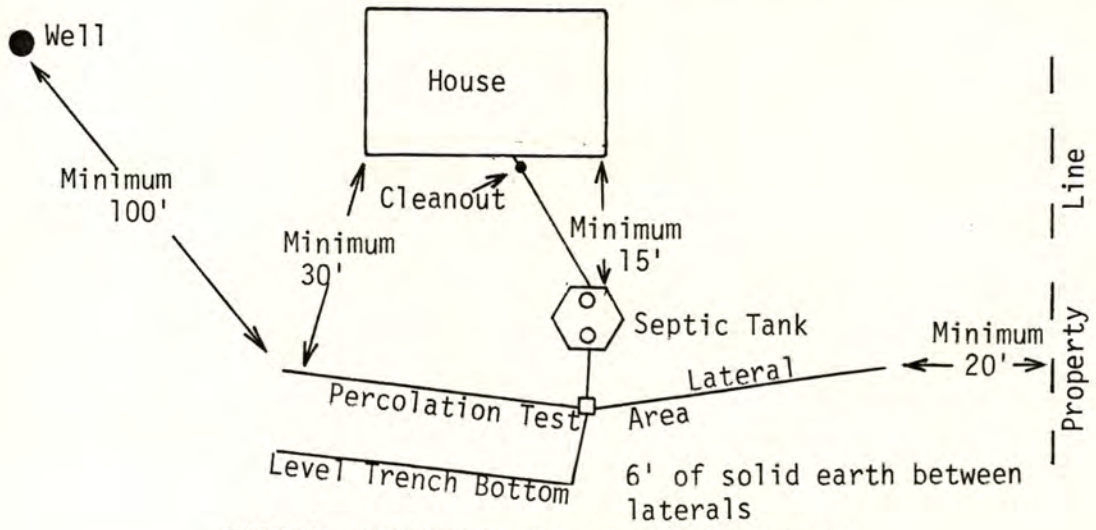

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

AS BUILT DRAWING OF SYSTEM

DATE 4-16-84 INSTALLER [illegible]

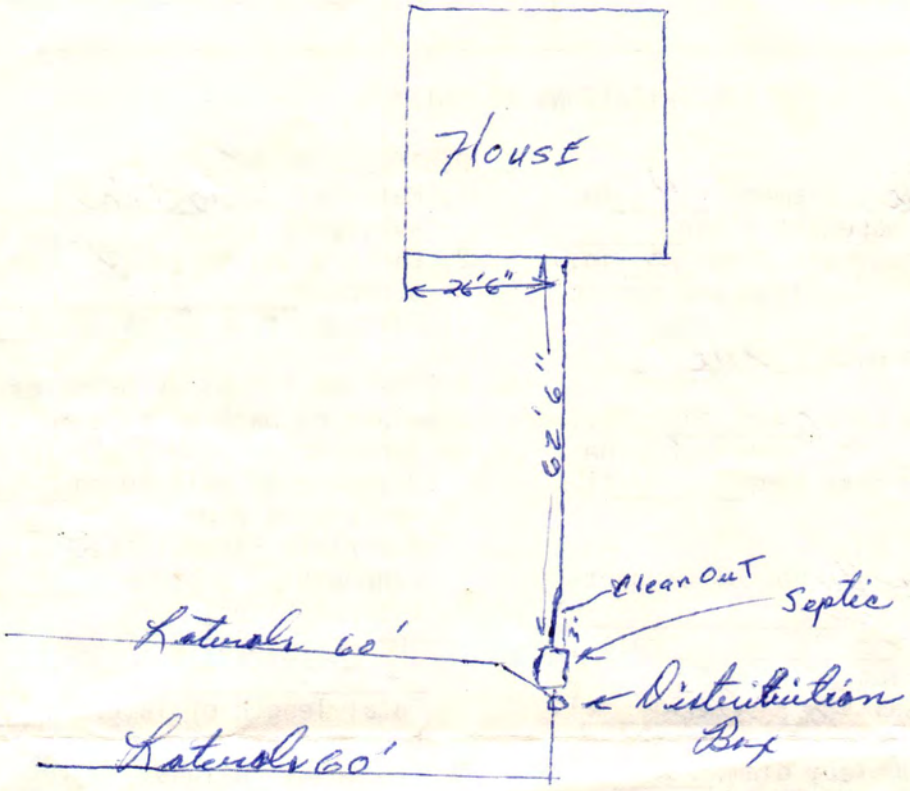

W
S N
E
