LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

FILE NO. 1484-C

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION — TYPE OF PERMIT

June 18, 1979 — THIS PERMIT EXPIRES

Rudolph Schroeder — ISSUED TO

Denton, NE 68339 — ADDRESS

T9N; R5E; Section 10 - east 1/2 of the NE 1/4 — LEGAL DESCRIPTION

REMARKS: NON-TRANSFERABLE

PERMIT	INSPECTION FEE	OCCUPATION TAX	TOTAL
$ 30.00	$	$	$ 30.00
ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE
	110.16	148.14	6-2

RECEIPTED BY	DATE	AMOUNT
Grand Golden Corp.	1.9.	

VALID RECEIPT ONLY IF RECEIPTED IN THIS SPACE

Health — ISSUING OFFICER

THIS PERMIT IS ISSUED AS PROVIDED BY COUNTY RESOLUTION NO. 2832

20109-0977

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

FILING FEE: $ 30.00

FILE NO. 1484-C

DATE: _____

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: SEE ATTACHED Twp. 9N ; Range 5E ; Section 10 ;
   Block _____ : Lot _____ : Addition _____
   Street Address _____

2. Property Use: Residential ☒ ; Commercial ☐ Other Use ☐
   No. of Bedrooms 3 . Describe _____

3. Type of Individual Sewage Disposal System: Septic Tank ☐ ; Other ☒ LAGOON

4. Distance to public sewer: _____ ft.

Rudolph Lahrsen
Signature of Applicant (Owner or Lessee)

Denton Nebr., 68339
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. 12/18/78. Date Frwd. 12/18/78. ACTION: Approved ☒ Disapproved ☐ Signature: Gerald C. Reed

2. Supt. Bldg. Insp.: or Village Clerk: Date Rec'd. _____. Date Frwd. 12-18-78. ACTION: Approved ☐ Disapproved ☐ Signature: _____

3. City or County Engineer: Date Rec'd. 12-18-78. Date Frwd. 12-18-78. ACTION: Approved ☒ Disapproved ☐ Signature: Henry Graff

REMARKS OR REASONS FOR DISAPPROVAL _____

Site Visits:
Date: 1-18-79 by: jpw
Date: 1-22-79 by: jpw
Date: _____ by: _____

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

INSTALLATION FINAL WRITTEN APPROVAL
Date: 2-1-79 By: Jim Woerth

FORM 20105-0477
SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150 and County Resolution No. 2832)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

B

FILE NO. 1484-C

PROPERTY WHERE SOIL TESTED:

Location: Township 9 ; Range 5 ; Section & ¼ Section NE ¼ 10
Property Dimensions: _____ ft. x _____ ft. Area: 3.24 acres. (Attach Sheet C with sketch of property).
Soil Type: Silty Clay ☐ ; Silty Clay Loam ☐ ; Sandy Loam ☐ ; Silt Loam ☐ ; Clay Loam ☐ .
Dates of Tests: 12/15/78 to 12/16/78 . Weather: Precip. 0 Temp. 40 .

OWNER: Rudolph Schroeder
Address: Denton, Neb. 68339

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
		Pre-Saturation Period				Percolation Readings						Results	
		Start		End		Start			End				
Hold No.	Hole Depth (in.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Water Level (in.)	Time (Hr./ Day)	Water Level (in.)	Elapsed Time (Min.)	Water Level Drop (in.)	Percolation Rates (Min./in.)
—	—	12/15/78	12:30	12/16/78	12:30	12/16/78	12:30		4:30				
1	34¾							12½		11½	30	1	
2	36							13½		12¼	30	1¼	
3	34¼							13¼		12	30	1¼	
4	36½							14		12¼	30	1¾	
5	35							14		12¾	30	1¼	
6	33"							14½		13¼	30	1¼	

Sum of Percolation Rates: _____
Average of Rates: _____
Mean of Rates: _____

James H Schroeder
Signature of Person Conducting Test
Address Rt 6 Lincoln, Nebr Phone 795-3095

(Do not write below this line)

REVIEWING ACTION

Remarks: Lagoon has been sealed
Soil Type (SCS): Zook Silt Loam
Date: December 18, 1978

Approved Percolation Rate (a)
A. 24 min./inch
B. _____ min./inch
C. _____ min./inch

Gerrold C. Hood
Signature of Reviewing Official

FORM 20102-0477
PRELIMINARY PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541


C

Sketch of property showing Percolation Test hole locations, well, residence, direction and property line.

FILE NO. 1484-C

Indicate on sketch if residence and well are exisiting or proposed.

Drive way continues

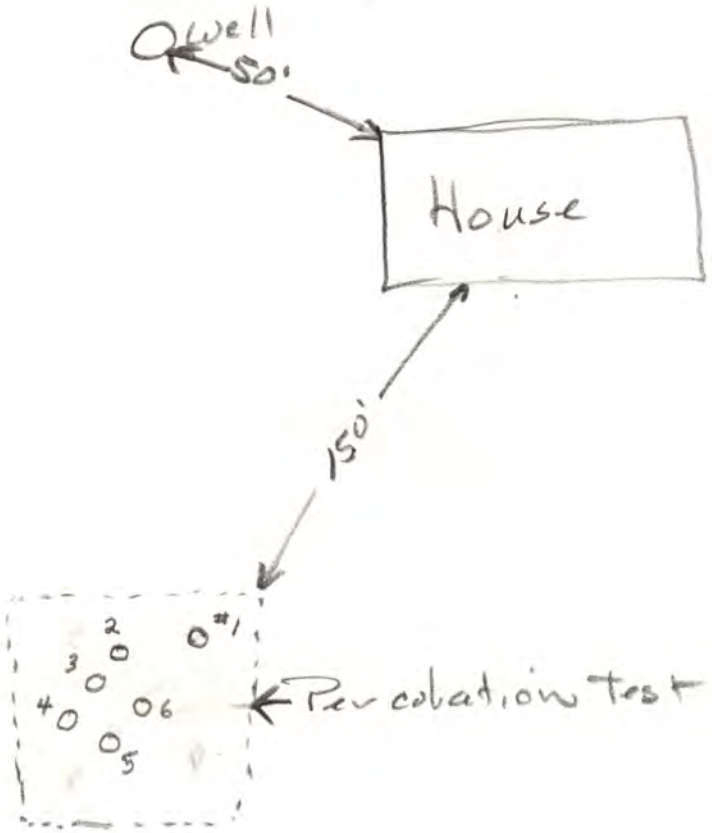

South-West 84th

REVIEWING ACTION

Remarks: _____

Date: December 18, 1978

Minimum Design Requirement
1. Capacity of Septic Tank _____ gals.
2. Total Length of Laterals _____ ft.
3. With a Trench Width of _____ in.
4. Total Area of Lateral needed _____ sq.ft.

Jerrold C. Hood
Signature of Reviewing Official

EXHIBIT "A"

LEGAL DESCRIPTION OF PROPERTY

An irregular tract of land situated in the east ½ of the NE ¼ of Section 10, T9N, R5E of the 6th P.M., Lancaster County, Nebraska, (a part of Lot 10 I.T.) more particularly described as follows: Referring to the east ¼ corner of the said section thence north along the east line of the northeast ¼, a distance of 1244.0 feet, thence west perpendicular to the east line of the NE ¼, a distance of 62.24 feet to the point of beginning, the said point being on the west right-of-way line of the state highway, thence continuing west along the last described line, a distance of 292.76 feet, thence southwesterly a distance of 434.52 feet to a point that is 430.0 feet west of the east line of the NE ¼, thence east perpendicular to the east line of the NE ¼, a distance of 367.19 feet to a point on the west right-of-way line of the state highway, thence north along the said right-of-way line, a distance of 428.0 feet to the point of beginning, the said tract containing 3.24 acres more or less.

DESCRIPTION OF PARCELS CREATED

PARCEL 1

An irregular tract of land situated in the east ½ of the NE ¼ of Section 10, T9N, R5E of the 6th P.M., Lancaster County, Nebraska, (a part of Lot 10 I.T.) more particularly described as follows: Referring to the east ¼ corner of the said section, thence north along the east line of the northeast ¼, a distance of 1244.0 feet, thence west perpendicular to the east line of the NE ¼, a distance of 62.24 feet to the point of beginning, the said point being on the west right-of-way line of the state highway, thence continuing west along the last described line, a distance of 292.76 feet, thence southwesterly a distance of 434.52 feet to a point that is 430.0 feet west of the east line of the NE ¼, thence east perpendicular to the east line of the NE ¼, a distance of367.19 feet to a point on the west right-of-way line of the state highway, thence north along the said right-of-way line, a distance of 428.0 feet to the point of beginning, the said tract containing 3.24 acres more or less.

INDEXED
MICRO-FILED
GENERAL

5-323.
misc.

LANCASTER COUNTY
REGISTER OF DEEDS
1978 DEC 12 PM 2:15
FILED FOR RECORD AS

$6.25

INST. NO. 78- 32995

Rudolph Schramadeu
Lincoln, Neb.

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

D

DATE: 22 JAN 79

FILE NO. _____


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material _____; Diameter _____ in.
2. Distance above basement floor _____ in., or below basement floor _____ in.
3. Distance between dwelling and septic tank _____ ft.
4. Number of clean-outs 2.
5. Distances to:
Well or Suction Line 110 ft.;
Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

B. SEPTIC TANK:
1. Material _____; No. of compartments _____.
2. Capacity _____ gals.;
3. Factory Built: Yes ☐ No ☐
(Company _____)
4. Manholes: Over Inlet; diam. _____ in.
Over Outlet; diam. _____ in.
Riser Above ☐ Below ☐ Grade _____ in.
5. Inlet: Baffle ☐ ; or Tee ☐
6. Outlet: Baffle ☐ ; or Tee ☐
7. Depth of top of tank below finished grade _____ in.
8. Distances to:
Well or Suction Line _____ ft.;
Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

C. DISTRIBUTION BOX:
1. Material _____; Number - available outlets _____.
2. Factory Built: Yes ☐ No ☐
(Company _____)
3. Distance from Septic Tank _____ ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☐ Perforated Pipe ☐
Diameter of Half Round _____ or
Perforated Pipe _____.
Material: fiberglass ☐ ; plastic ☐ ; concrete ☐ ; other _____.
2. Lateral Lines:
Number ___ ; Length of each line _____, _____, _____, _____, _____ ft.;
Total length of laterals _____ ft.;
Distance between lateral lines ____ ft.
3. Trench dimensions: Width _____ ft.;
Slope _____ in/100 ft.; Average Depth _____ in.
4. Filter Material: _____
Depth of Material _____ in.
5. Distances to:
Well or Suction Line _____ ft.;
Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

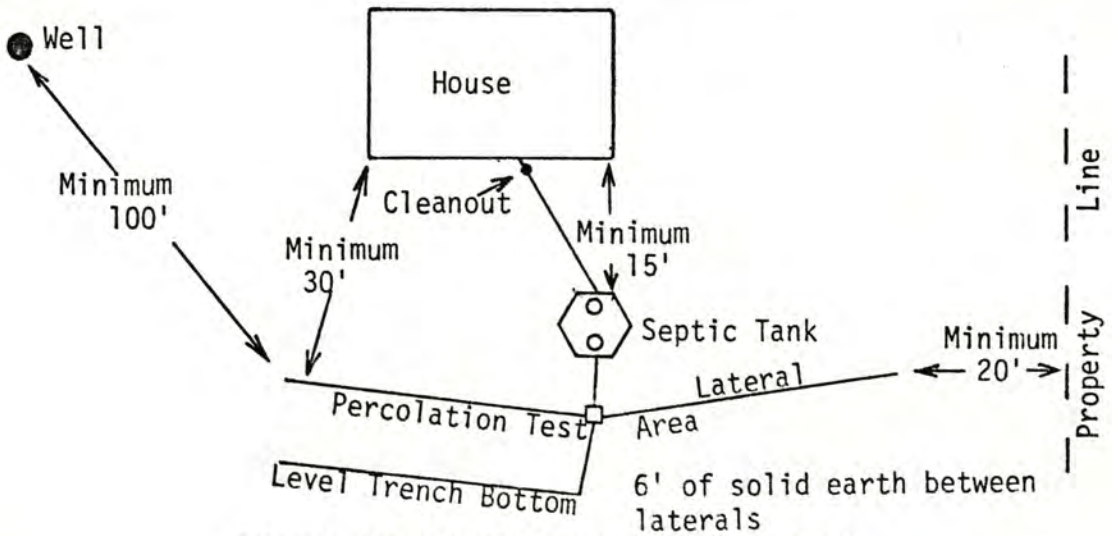

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

AS BUILT DRAWING OF SYSTEM

DATE 22 JAN 79 INSTALLER Melvin Wagner

