FILE NO. 1707

CITY OF LINCOLN NEBRASKA

DEPARTMENT OF LICENSES AND PERMITS

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION
TYPE OF LICENSE OR PERMIT

MARCH 26, 1981
THIS LICENSE OR PERMIT EXPIRES

WOBIG CONSTRUCTION CO. INC. BY R.C. WOBIG, 1143 Sumner, Lincoln, NE 68502
LICENSEE OR PERMITTEE — ADDRESS

T9N, R6E, Section 9
NAME OF ESTABLISHMENT, IF ANY — ADDRESS

REMARKS:

PERMIT	INSPECTION FEE	OCCUPATION TAX	LICENSE	TOTAL
$ 60.00	$	$	$	$ 60.00
ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE	
018754	110.16	148.14	6-2	

SERIAL NO.	DATE	AMOUNT
55891	3/26	60.00

VALID RECEIPT ONLY IF MACHINE RECEIPTED IN THIS SPACE

HEALTH APPLICATION

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☒
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

A

FILING FEE: $ 60.00

FILE NO. 1707

DATE: 9-24-80

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 9N; Range 6E; Section 9; Block _____: Lot _____: Addition SEE ATTACHED
   Street Address _____

2. Property Use: Residential ☒ ; Commercial ☐ Other Use ☐
   No. of Bedrooms 3. Describe S.F.R.

3. Type of Individual Sewage Disposal System: Septic Tank ☒ ; Other ☐

4. Distance to public sewer: _____ ft.

Wehrig Const. Co. Inc
by R.C. Wehrig Pres
Signature of Applicant (Owner or Lessee)

1143 Sumner
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. 9/26/80. Date Frwd. 9/26/80. ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Hood
2. Supt. Bldg. Insp.: or Village Clerk Date Rec'd. 9/26/80. Date Frwd. 9/26/80. ACTION: Approved ☒ Disapproved ☐ Signature: Walt Ludwig
3. City ~~or County~~ Engineer: Date Rec'd. 9-26-80. Date Frwd. 9-26-80. ACTION: Approved ☒ Disapproved ☐ Signature: [illegible]

REMARKS OR REASONS FOR DISAPPROVAL _____

Site Visits:
Date: 11/25/80 by: J.C.H.
Date: _____ by: _____
Date: _____ by: _____

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

INSTALLATION FINAL WRITTEN APPROVAL
Date: 11/25/80 By: Jerrold C. Hood

FORM 20105-0477
SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150 and County Resolution No. 2832)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

B

FILE NO. 1707

PROPERTY WHERE SOIL TESTED:

Location: Township 9N ; Range 6E ; Section & ~~¼ Section~~ 9 .
Property Dimensions: 360' ft. x 1244 ft. Area: 10.01 acres. (Attach Sheet C with sketch of property).
Soil Type: Silty Clay ☐ ; Silty Clay Loam ☐ ; Sandy Loam ☐ ; Silt Loam ☐ ; Clay Loam ☐ .
Dates of Tests: 9-22-80 to 9-23-80 . Weather: Precip. 0 Temp. 90° .

OWNER: Leon & Mary Johnson

Address: 1233 Clearview

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
		Pre-Saturation Period				Percolation Readings						Results	
		Start		End		Start			End				
Hold No.	Hole Depth (in.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Water Level (in.)	Time (Hr./ Day)	Water Level (in.)	Elapsed Time (Min.)	Water Level Drop (in.)	Percolation Rates (Min./in.)
1	32	~~9-22~~	1:00pm	9-23	2:PM	9-23	6 AM	18½"	6:30	19¼"	30	¾"	
2	34							22¼"		24¼"	30	2"	
3	32							21"		23"	30	2"	
4	32							23¼"		25-¼"	30	1¾"	
5	33							19⅛"		20⅓"	30	1⅜"	
6	34							20¼"		21¼"	30	1"	

R. C. Wolbig
Signature of Person Conducting Test

Sum of Percolation Rates: 8.87
Average of Rates: 1.48
Mean of Rates:

Address 1143 Sumner Phone 475-3288

(Do not write below this line)

REVIEWING ACTION

Remarks:
Soil Type (SCS): Wymore Silty Clay Loam
Date: September 26, 1980 for Sharpsburg Silty Clay Loam
Looks like Sharpsburg 11/25/80

Approved Percolation Rate (a)
A. 20 min./inch
B. min./inch
C. min./inch

Gerald C. Hood
Signature of Reviewing Official

FORM 20102-0477
PRELIMINARY PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541


C

Sketch of property showing Percolation Test hole locations, well, residence, direction and property line.

FILE NO. 1707

Indicate on sketch if residence and well are exisiting or proposed.

N

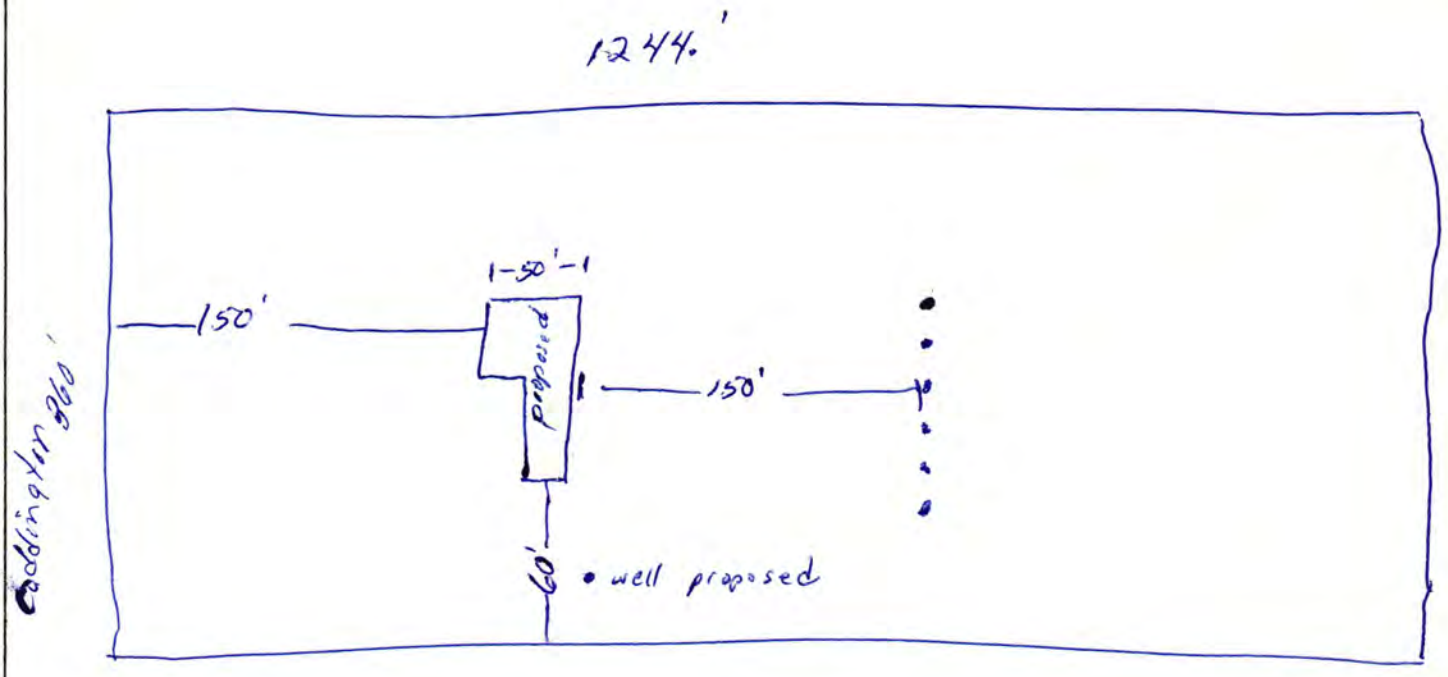

REVIEWING ACTION

Remarks: _____

Date: September 26, 1980

Minimum Design Requirement
1. Capacity of Septic Tank 1000 gals.
2. Total Length of Laterals 157 ft.
3. With a Trench Width of 48 in.
4. Total Area of Lateral needed 630 sq.ft.

Jerrold C. Hood
Signature of Reviewing Official

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

D

DATE: _____

FILE NO. _____


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material PVC ; Diameter 4 in.
2. Distance above basement floor _____ in., or below basement floor 8 in.
3. Distance between dwelling and septic tank 165 ft.
4. Number of clean-outs 2 .
5. Distances to:
Well or Suction Line 100' ft.;
Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

B. SEPTIC TANK:
1. Material Concrete; No. of compartments _____ .
2. Capacity 1500 gals.;
3. Factory Built: Yes ☒ No ☐
(Company Pre Cast)
4. Manholes: Over Inlet; diam. _____ in.
Over Outlet; diam. _____ in.
Riser Above ☐ Below ☐ Grade ____ in.
5. Inlet: Baffle ☐ ; or Tee ☐
6. Outlet: Baffle ☐ ; or Tee ☐
7. Depth of top of tank below finished grade _____ in.
8. Distances to:
Well or Suction Line 150' ft.;
Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

C. DISTRIBUTION BOX:
1. Material Concrete ; Number - available outlets 5 .
2. Factory Built: Yes ☒ No ☐
(Company Pre Cast)
3. Distance from Septic Tank 6' ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☒ Perforated Pipe ☐
Diameter of Half Round 24" or
Perforated Pipe _____ .
Material: fiberglass ☐ ; plastic ☐ ; concrete ☒ ; other _____ .
2. Lateral Lines:
Number 2 ; Length of each line 100 , 80' , _____ , _____ , _____ ft.;
Total length of laterals _____ ft.;
Distance between lateral lines ____ ft.
3. Trench dimensions: Width 4 ft.;
Slope 6 in/100 ft.; Average Depth 36 in.
4. Filter Material: Road Gravel ,
Depth of Material 20 in.
5. Distances to:
Well or Suction Line 200 ft.;
Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

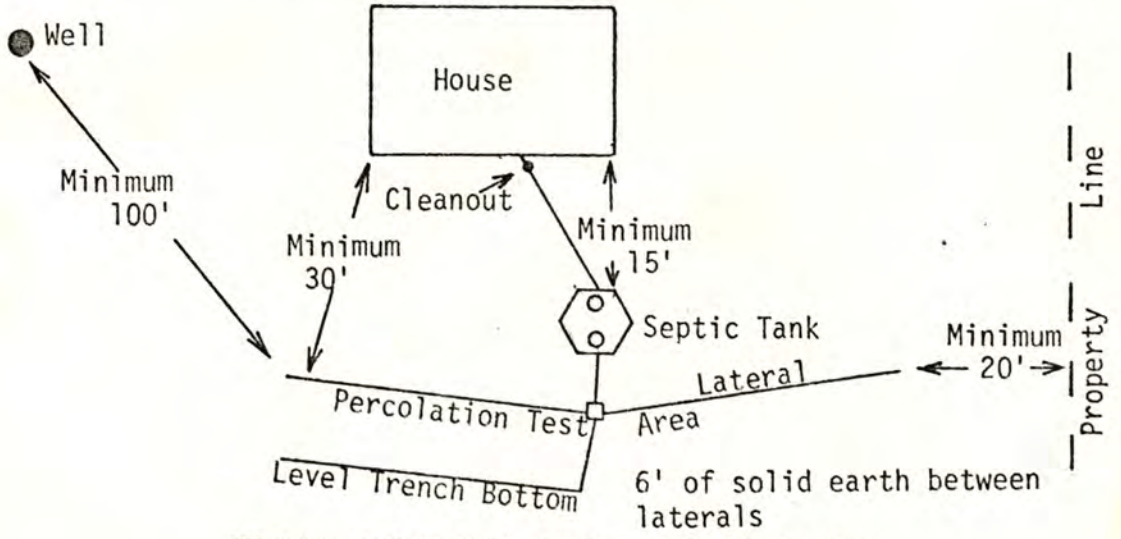

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

AS BUILT DRAWING OF SYSTEM

DATE Nov. 25, 80 INSTALLER Larry Schwarck

