CITY OF LINCOLN NEBRASKA

DEPARTMENT OF LICENSES AND PERMITS

FILE NO. 60

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION — TYPE OF LICENSE OR PERMIT

January 12, 1969 — THIS LICENSE OR PERMIT EXPIRES

Wayne J. Pauley — LICENSEE OR PERMITTEE

Rt. 1, No. 6 Lazy Acres, Lincoln, Nebr — ADDRESS

T 9N; R 6E; Sec. 14; Blk. 2; Lot 6; Lazy Acres Addition — NAME OF ESTABLISHMENT, IF ANY

ADDRESS

REMARKS: Non-Transferable

PERMIT	INSPECTION FEE	OCCUPATION TAX	LICENSE	TOTAL
$ 30.00	$	$	$	$ 30.00

ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE
143-1535	10.0116	24.0114	6-2

SERIAL NO.	DATE	AMOUNT
13961	JL12 68	30.00 Ck

VALID RECEIPT ONLY IF MACHINE RECEIPTED IN THIS SPACE

APPLICATION

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW

FORM HD-31(67) APPLICATION FOR PERMIT TO ALTER, EXTEND OR REPAIR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance 9150

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone 432-7611)

FILE NO. 60

TO: Division of Environmental Health
Lincoln-Lancaster County Health Dept.

DATE: 7-9-68

The undersigned hereby applies for a permit to ALTER [✓], EXTEND [ ], or REPAIR [ ] an existing Individual Sewage Disposal System, in conformance with Lincoln City Ordinance No. 9150, as described in this application and drawings attached hereto.

1. Legal description of property: Twp. 9N; Range 6E 6PM; Section 14;
Block 2; Lot 6; Addition Hazy acres
Street Address R1

2. Property Use: Residential Yes [✓]; Commercial [ ]
No. Bedrooms 3 Describe

Other Use [ ]
Describe

3. Type of existing Individual Sewage Disposal System: Septic Tank [✓]; Other [ ]

4. Description of proposed alteration, extension or repair: 100 ft
Cement Semoon 3ft Wide 3½ft deep

5. Work to be done by: Owner [ ]; or Contractor [✓], Sintek Pumping
Contractor's Name

6. Estimated cost of project:

a. Materials	$	
b. Labor	$	
c. Other	$	
TOTAL	$	400 00

Signature of Applicant (owner or lessee)

Address

(Do not write below this line)

REVIEWING ACTION

1. Date Rec'd:
Filing Fee: $

2. Date Site Clearance:

3. Site Visits:
Date: 7/10/68 by: L.C.H.
Date: by:
Date: by:

4. Date: 7/10/68 Approved [✓]; Disapproved [ ]
by: Jerrold C. Hood

5. BUREAU OF LICENSES & PERMITS
Date Notified:
Date Issued: Serial

6. INSTALLATION FINAL WRITTEN APPROVAL
Date: 7/10/68 by: L.C. Hood

FORM HD-32a(67) PLANS & SPECIFICATIONS
SEWAGE DISPOSAL SYSTEM
(Annex to Application)
Ordinance No. 9150

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 432-7611)

FILE NO. 60

SPECIFICATIONS

DATE: JULY 10, 1968


A. BUILDING SEWER:
1. Material _____; Diameter ____ in.
2. Distance above basement floor ____in.; or below basement floor ____in.
3. Distance between dwelling and septic tank ____ft.
4. Number of clean-outs _____.
5. Distances To:
Well or Suction Line ____ft.;
Stream ____ft.; Pressure Line ____ft.;
Property Line ____ft.

B. SEPTIC TANK (Provide construction drawings.)
1. Material CON; No. of compartments 1.
2. Capacity 1000 gals.; Liquid depth ____in.
3. Factory Built: Yes ☐ (Company _____)
No ☒
4. Manholes: Over Inlet; diam. ____in.
Over Outlet; diam. ___in.
Below Grade _____in.
5. Inlet: Baffle ☐; or Tee ☐
6. Outlet: Baffle ☐; or Tee ☐
Depth of outlet below inlet ___in.
7. Depth of top of tank below finished grade ____in.
8. Distances To:
Well or Suction Line ____ft.;
Stream ____ft.; Pressure Line ____ft.;
Property Line ____ft.


C. DISTRIBUTION BOX ADDED
1. Material CON; No. available outlets 5.
2. Factory Built: Yes ☒, (Company PRE-CAST STED No ☐
3. Dimension: Length ____in.; Width ___in. Depth ____in.
4. Distance from Septic Tank 5½ ft.
5. Serial Distribution: Yes ☒, No ☐
(If yes, show detailed plans.)

100' ADDED
D. ABSORPTION FIELD: (Provide drawings.)
1. Type: CONCRETE HALF MOON
2. Lateral Lines: Depth below grade ___in.
Number 2; Length of each line 100 ft
Total length of Laterals 200 ft.;
Slope 4 in/100 ft. Diameter of pipe 24 in.; Shape ∩
Material: concrete ☒; fiber asbestos ☐; clay ☐; other _____
Distance between lateral lines — ft.
3. Trench Dimensions: Depth 48 in.; Width 36 in.
4. Filter Material: GRAVEL.
Depth of material from trench bottom _____in.
5. Distances To:
Well or Suction Line ____ft.;
Stream _____ft.; Pressure Line ____ft.
Property Line ____ft.
6. Percolation Rate: _____minutes/inch

TYPICAL SKETCHES

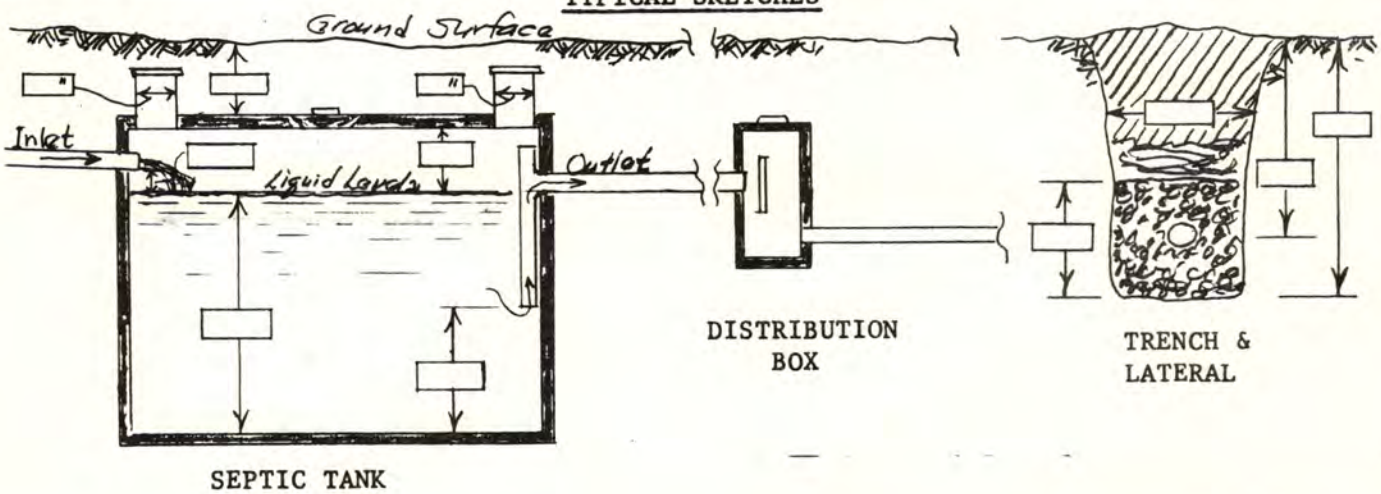

Signature of Applicant

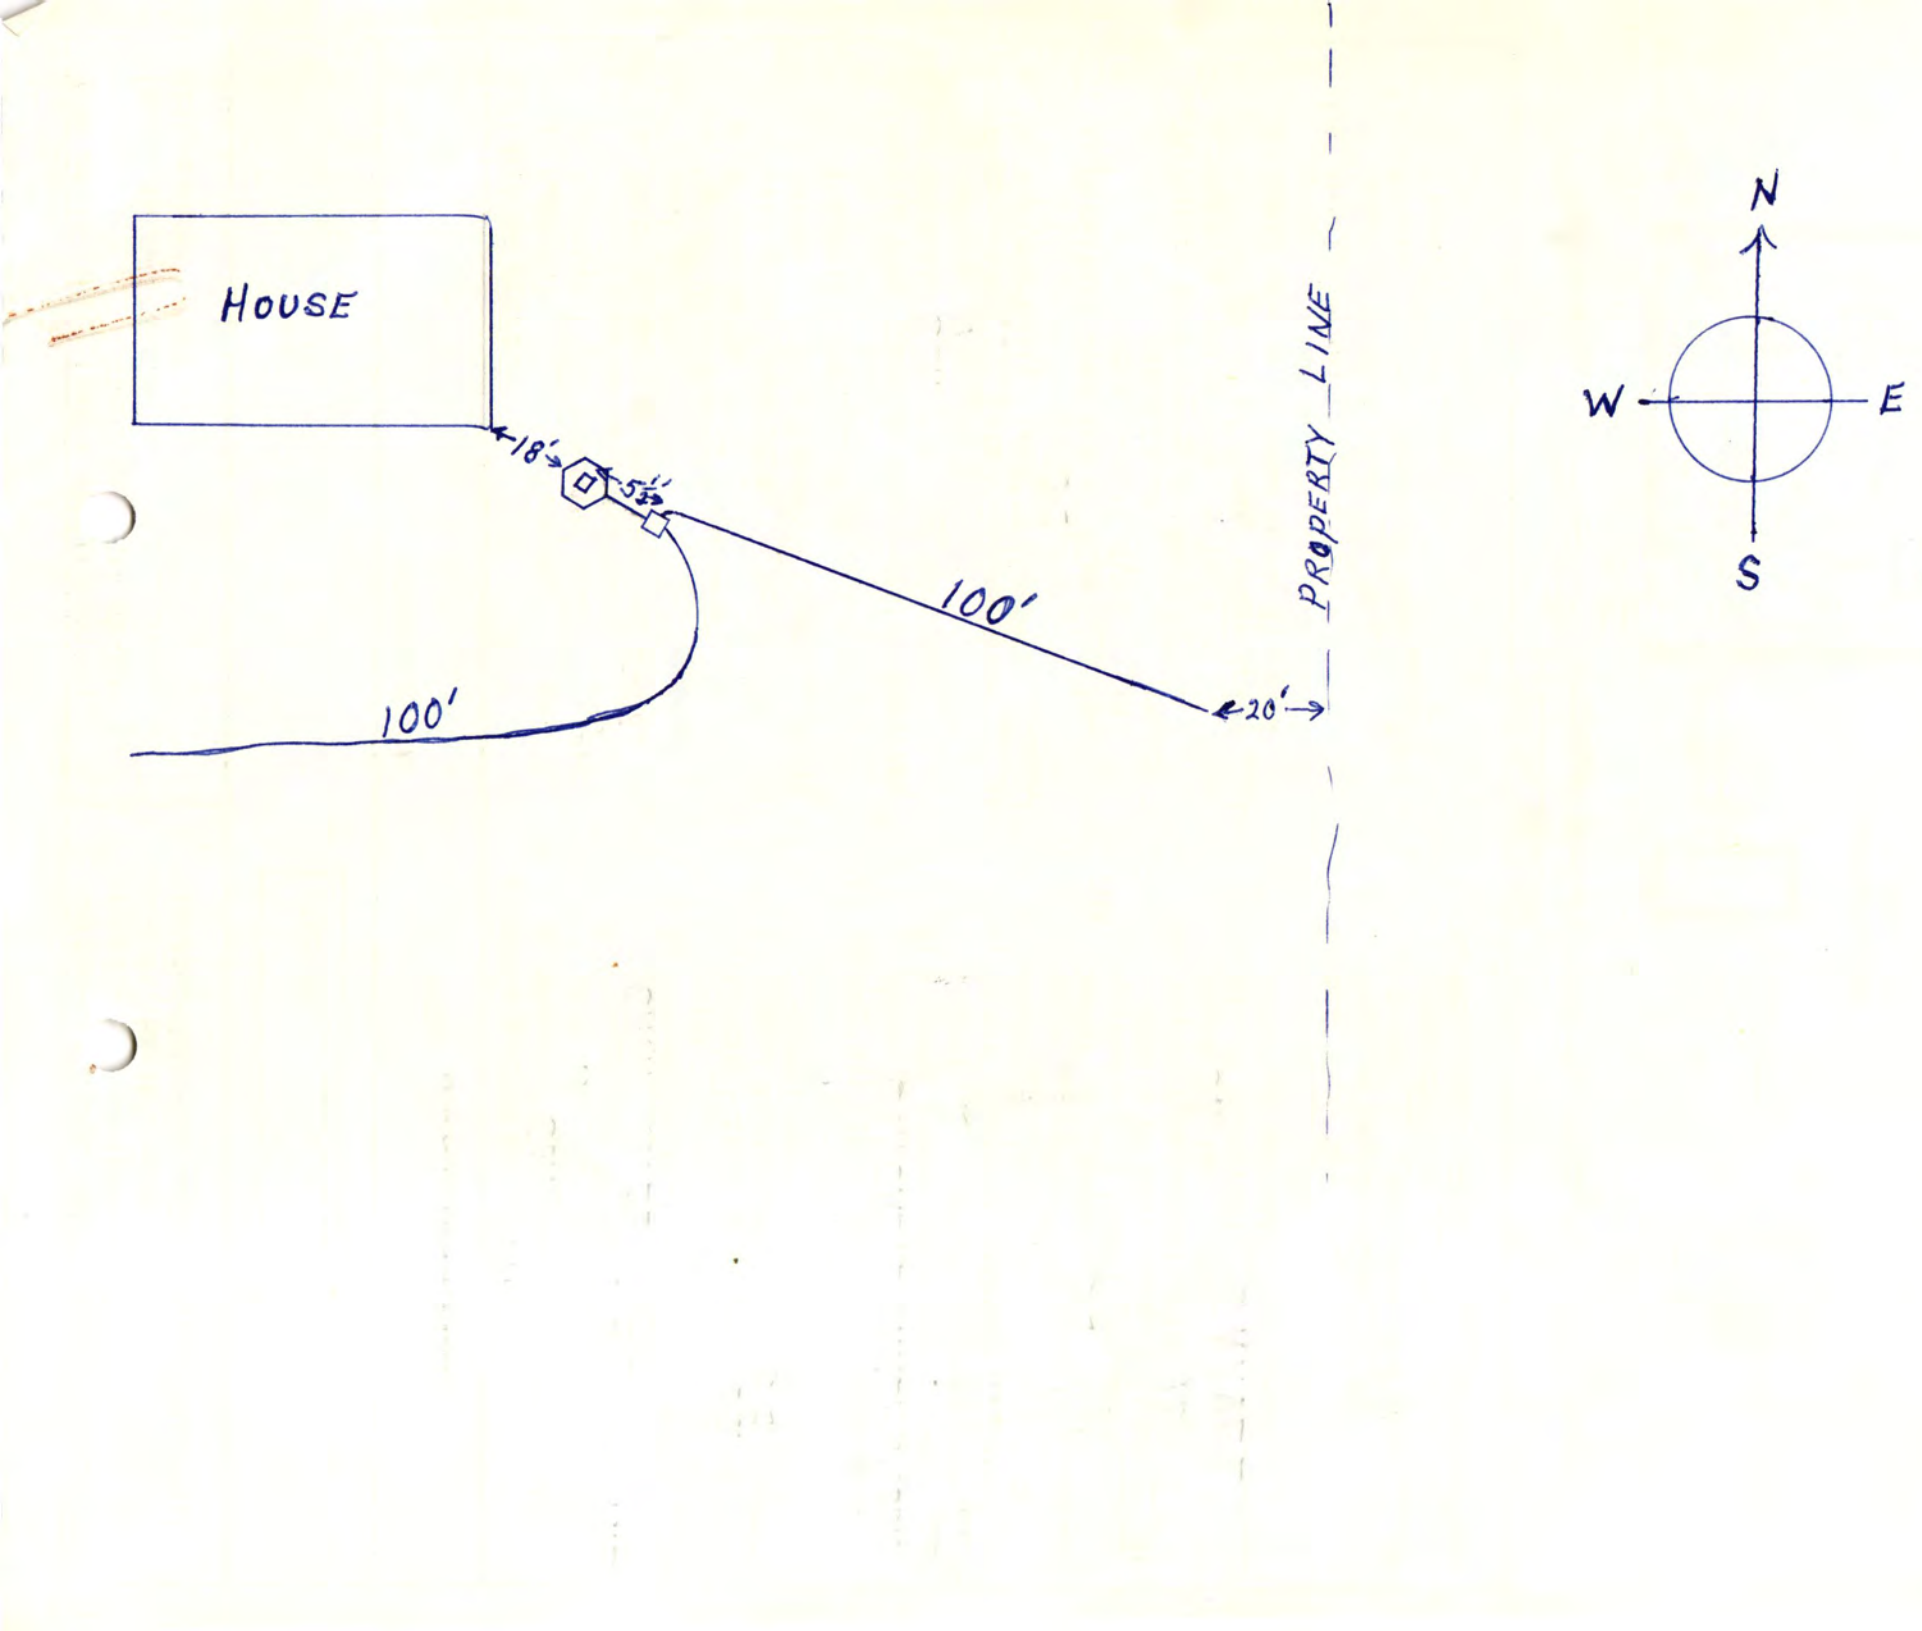
HOUSE
18'
5'
100'
100'
20'
PROPERTY LINE
N
W
E
S
