FILE NO. 1163

CITY OF LINCOLN NEBRASKA

DEPARTMENT OF LICENSES AND PERMITS

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION — TYPE OF LICENSE OR PERMIT

March 12, 1978 — THIS LICENSE OR PERMIT EXPIRES

Charles Kiner — LICENSEE OR PERMITTEE

3024 North 63, Street, Lincoln, NE — ADDRESS

T9N, R6E, Section 14, Block 1, Lot 6, Addition Lazy Acres — NAME OF ESTABLISHMENT, IF ANY

ADDRESS

REMARKS: NON-TRANSFERABLE

PERMIT	INSPECTION FEE	OCCUPATION TAX	LICENSE	TOTAL
$ 30.00	$	$	$	$ 30.00

ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE
624-1535	110.16	148.14	6-2

SERIAL NO.	DATE	AMOUNT
46923	3-13-78	30.00

VALID RECEIPT ONLY IF MACHINE RECEIPTED IN THIS SPACE

HEALTH APPLICATION

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW

FORM HD-40(73) REQUEST FOR SITE CLEARANCE FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM

City Ordinance No. 9150 ☒
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 475-6221)

FILE NO. 1163

TO: Division of Environmental Health
Lincoln-Lancaster County Health Dept.

DATE: 9-12-1977

The undersigned hereby requests SITE CLEARANCE to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 9N ; Range 6E ; Section 14
Block 1 ; Lot 6 ; Addition LAZY ACRES
Street Address _____

2. Property Use: Residential ☒ ; Commercial ☐
No. of Bedrooms 3 . Describe: _____
Other Use ☐
Describe: _____

3. Type of Individual Sewage Disposal System: Septic Tank ☒ ; Other ☐

4. Distance to public sewer: _____ ft.

Charles K Kunier
Signature of Applicant (Owner or Lessee)

3024 No. 63 Lincoln Nebr 68507
Address

(Do not write below this double line)

REVIEWING ACTION

1. Health Department: Date Rec'd. 9/12/77. Date Frwd. 9/13/77. ACTION: Approved ☐ Disapproved ☒ Signature: Jerrold C. Hoof

2. Supt. Bldg. Insp.: Date Rec'd. 9-13-77. Date Frwd. 9-13-77. ACTION: Approved ☐ Disapproved ☒ Signature: Williamson

3. City or County Engineer: Date Rec'd. 9/13/77. Date Frwd. 9/13/77. ACTION: Approved ☒ Disapproved ☐ Signature: Joel Hy

REMARKS OR REASONS FOR DISAPPROVAL _____

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

FORM HD-42(73) APPLICATION FOR PERMIT TO CONSTRUCT INDIVIDUAL SEWAGE DISPOSAL SYSTEM

City Ordinance No. 9150 ☒
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 475-6221)

FILE NO. 1163

DATE: 9-12-77

TO: Director of Health
Lincoln-Lancaster County Health Dept.

The undersigned hereby applies for a permit to construct an Individual Sewage Disposal System in conformance with appropriate Ordinance or Resolution, as described in this application and the annexed forms attached hereto.

1. Legal description of property: Twp. 9N ; Range 6E ; Section 14 ; Block 1 ; Lot 6 ; Addition Lazy acres.
Street Address _____.

2. Property Use: Residential _____ ☒; Commercial _____ ☐
No. of Bedrooms 3
Describe: _____
Other Use _____
Describe: _____

3. Type of Individual Sewage Disposal System: Septic Tank ☒; Other ☐

4. Plans and Specifications of Proposed System. (See FORM HD-45(73) PLANS & SPECIFICATIONS, SEWAGE DISPOSAL SYSTEM, attached hereto.)

5. Soil Absorption Properties. (See FORM HD-43(73) SOIL ABSORPTION TEST DATA REPORT, attached hereto).

Charles K. Kiner
Signature of Applicant (owner or lessee)

3024 1163 Lincoln
Address

(Do not write below double line)

REVIEWING ACTION

1. Date Rec'd; _____
Filing Fee: $ 30.00

2. Site Visits:
Date: 11/29/77 by: L. C. H.
Date: ___ ___ by: _____
Date: _____ by: _____

3. Date: Approved ☒; Disapproved ☐ 9/12/77
by: Jerrold E. Hood

4. INSTALLATION FINAL WRITTEN APPROVAL
Date: 11/29/77 by: Jerrold E. Hood

FORM HD-43 (73) SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150 and County Resolution No. 2832)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone 474-1541)

FILE NO. 1163

PROPERTY WHERE SOIL TESTED:
Location: Township _____ : Range _____
Section & ¼ Sect. _____
Property Dimensions: 200 ft. x 220 ft.
Area: 1 acres. (Attach sketch of property showing hole location).
Soil Type: Silty Clay ; Silty Clay Loam ; Sandy Loam
Silty Loam ; Clay Loam ; Sandy Clay

Owner: CHARLES & LOUISE KINER
Address: LAZY ACRES LOT 6 BLOCK 1 LINCOLN, NEBRASKA

Dates of Tests: 7-29-77 to 7-29-77. Weather: Precip. 0 Temp. 90

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
		Pre-Saturation Period				Percolation Readings						Results	
		Start		End		Start Last 10 min.			End				
Hold No.	Hole Depth (in.)	Date (Mo. Day) 1977	Time (Hr. Min.)	Date (Mo. Day)	Time (Hr. Min.)	Date (Mo. Day)	Time (Hr. Min.)	Water Level (in.)	Time (Hr. Min.)	Water Level (in.)	Elapsed Time (Min.)	Water Level Drop (in.)	Percolation Rates (Min./inch)
1	36"	7-29	9:00	7-29	10:00	7-29	11:20	6"	11:30	"0"	10 min	6"	
2	36"									Water completely seeps away after every 10 min. Test in one hour			
3	36"												
4	36"												
5	36"												
6	36"		9:00		10:00								

Charles K. Kiner
Signature of Person Conducting Test

Address 3024 M63
Phone 466-6767

Sum of Percolation Rates: _____
Average of Rates: _____
Mean of Rates: _____

(Do not write below this line)

REVIEWING ACTION

REMARKS: Dickinson fine sandy loam (L.C.L.) Confirmed 11/29/77 bottom of trench just into sand.

DATE: September 12, 1977

Approved Percolation Rate (a)
A. 2 min./inch
B. _____ min./inch
C. _____ min./inch

Gerald C. Hood
Signature of Reviewing Official

FORM HD- 45(73) PLANS & SPECIFICATIONS
SEWAGE DIS AL SYSTEM
(Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 475-6221)

FILE NO. 1163

SPECIFICATIONS

DATE: _____


A. BUILDING SEWER:
1. Material _____; Diameter ____ in.
2. Distance above basement floor ____in.; or below basement floor ____in.
3. Distance between dwelling and septic tank ____ft.
4. Number of clean-outs _____.
5. Distances To:
Well or Suction Line ____ft.;
Stream ____ft.; Pressure Line ____ft.;
Property Line ____ft.

B. SEPTIC TANK (Provide construction drawings.)
1. Material _____; No. of compartments _____.
2. Capacity 1000 gals.; Liquid depth ____in.
3. Factory Built: Yes ☐ (Company _____)
No ☐
4. Manholes: Over Inlet; diam. ____in.
Over Outlet; diam. ___in.
Below Grade _____in.
5. Inlet: Baffle ☐; or Tee ☐
6. Outlet: Baffle ☐; or Tee ☐
Depth of outlet below inlet ___in.
7. Depth of top of tank below finished grade ____in.
8. Distances To:
Well or Suction Line ____ft.;
Stream ____ft.; Pressure Line ____ft.;
Property Line ____ft.

C. DISTRIBUTION BOX
1. Material _____; No. available outlets _____.
2. Factory Built: Yes ☐, (Company _____) No ☐
3. Dimension: Length ____in.; Width ___in. Depth ____in.
4. Distance from Septic Tank ____ft.
5. Serial Distribution: Yes ☐, No ☐ (If yes, show detailed plans.)

D. ABSORPTION FIELD: (Provide drawings.)
1. Type: _____
2. Lateral Lines: Depth below grade ___in. Number ____; Length of each line ___ft Total length of Laterals 850 864 ft.; Slope ____in/100 ft. Diameter of pipe ____ in.; Shape _____
Material: concrete ☐; fiber asbestos ☐; clay ☐; other _____
Distance between lateral lines ____ft.
3. Trench Dimensions Depth ___in.; Width 36 48 in.
4. Filter Material: _____.
Depth of material from trench bottom _____in.
5. Distances To:
Well or Suction Line ____ft.;
Stream _____ft.; Pressure Line ____ft.
Property Line ____ft.
6. Percolation Rate: _____minutes/inch

TYPICAL SKETCHES

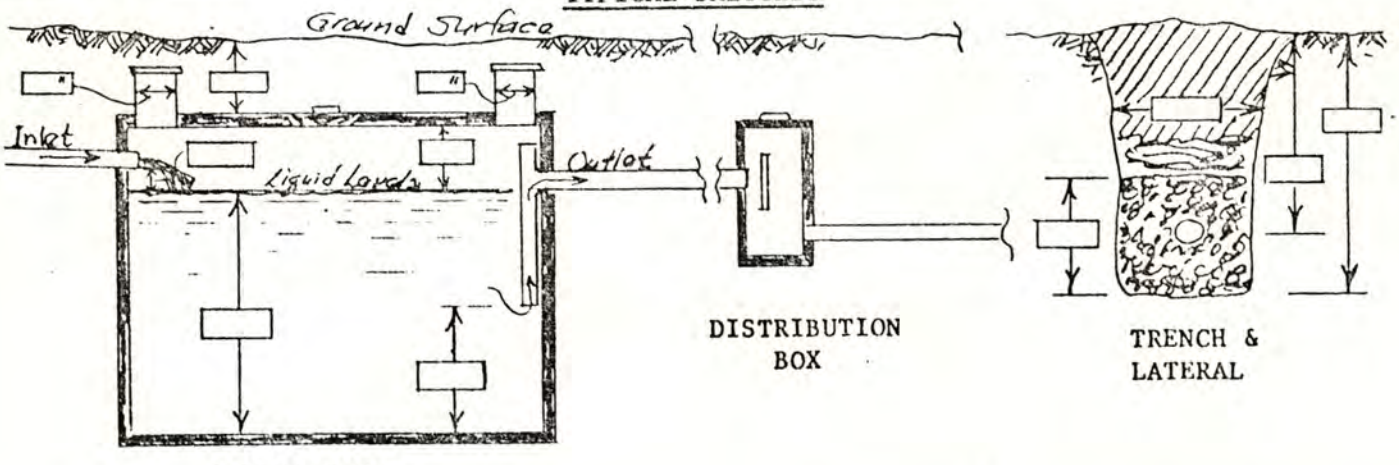

_____
Signature of Applicant

FORM HD- 45(73) PLANS & SPECIFICATIONS
SEWAGE DISPOSAL SYSTEM
(Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 475-6221)

FILE NO. _____

SPECIFICATIONS

DATE: _____


A. BUILDING SEWER:
1. Material PVC; Diameter 4 in.
2. Distance above basement floor ____in.; or below basement floor 24 in.
3. Distance between dwelling and septic tank 46 ft.
4. Number of clean-outs —.
5. Distances To:
Well or Suction Line ____ft.;
Stream ____ft.; Pressure Line ____ft.;
Property Line ____ft.

B. SEPTIC TANK (Provide construction drawings.)
1. Material CON; No. of compartments 1.
2. Capacity 1000 gals.; Liquid depth ____in.
3. Factory Built: Yes ☑ (Company Pre CAST)
No ☐
4. Manholes: Over Inlet; diam. ____in.
Over Outlet; diam. ____in.
Below Grade ____in.
5. Inlet: Baffle ☐; or Tee ☐
6. Outlet: Baffle ☑; or Tee ☐
Depth of outlet below inlet ____in.
7. Depth of top of tank below finished grade 12 in.
8. Distances To:
Well or Suction Line ____ft.;
Stream ____ft.; Pressure Line ____ft.;
Property Line ____ft.

C. DISTRIBUTION BOX
1. Material CON; No. available outlets 5.
2. Factory Built: Yes ☑, (Company Pre CAST) No ☐
3. Dimension: Length 24 in.; Width 12 in. Depth 12 in.
4. Distance from Septic Tank 4 ft.
5. Serial Distribution: Yes ☐, No ☐ (If yes, show detailed plans.)


D. ABSORPTION FIELD: (Provide drawings.)
1. Type: Half round
2. Lateral Lines: Depth below grade 42 in. Number 2; Length of each line 48 ft Total length of Laterals 100 ft.; Slope — in/100 ft. Diameter of pipe 24 in.; Shape Half round Material: concrete ☑; fiber asbestos ☐; clay ☐; other ____ Distance between lateral lines ____ft.
3. Trench Dimensions: Depth 42 in.; Width 48 in.
4. Filter Material: GRAVEL. Depth of material from trench bottom 28 in.
5. Distances To:
Well or Suction Line ____ft.;
Stream ____ft.; Pressure Line ____ft.
Property Line ____ft.
6. Percolation Rate: ____minutes/inch

TYPICAL SKETCHES

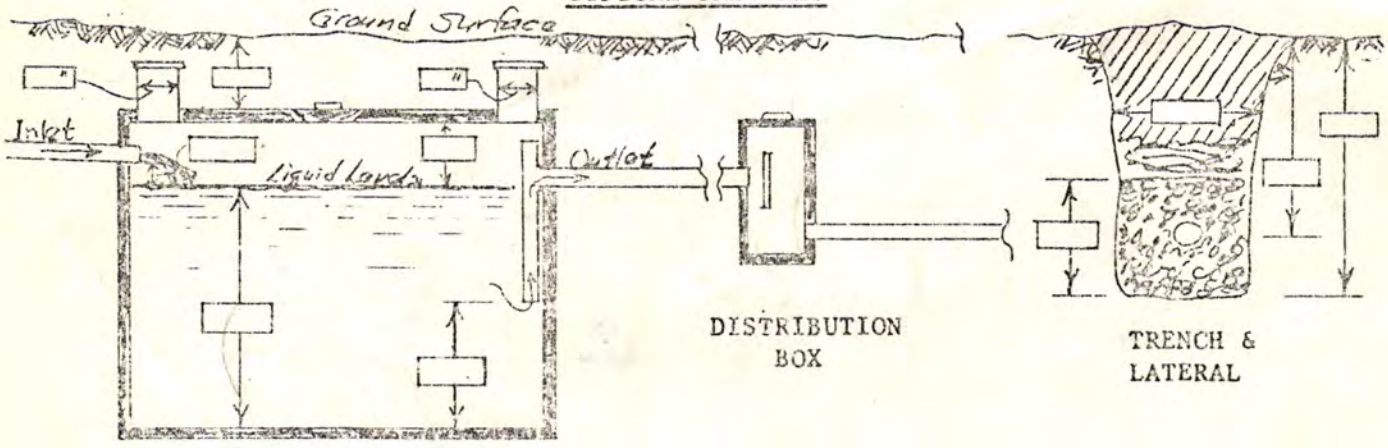

_____
Signature of Applicant

N

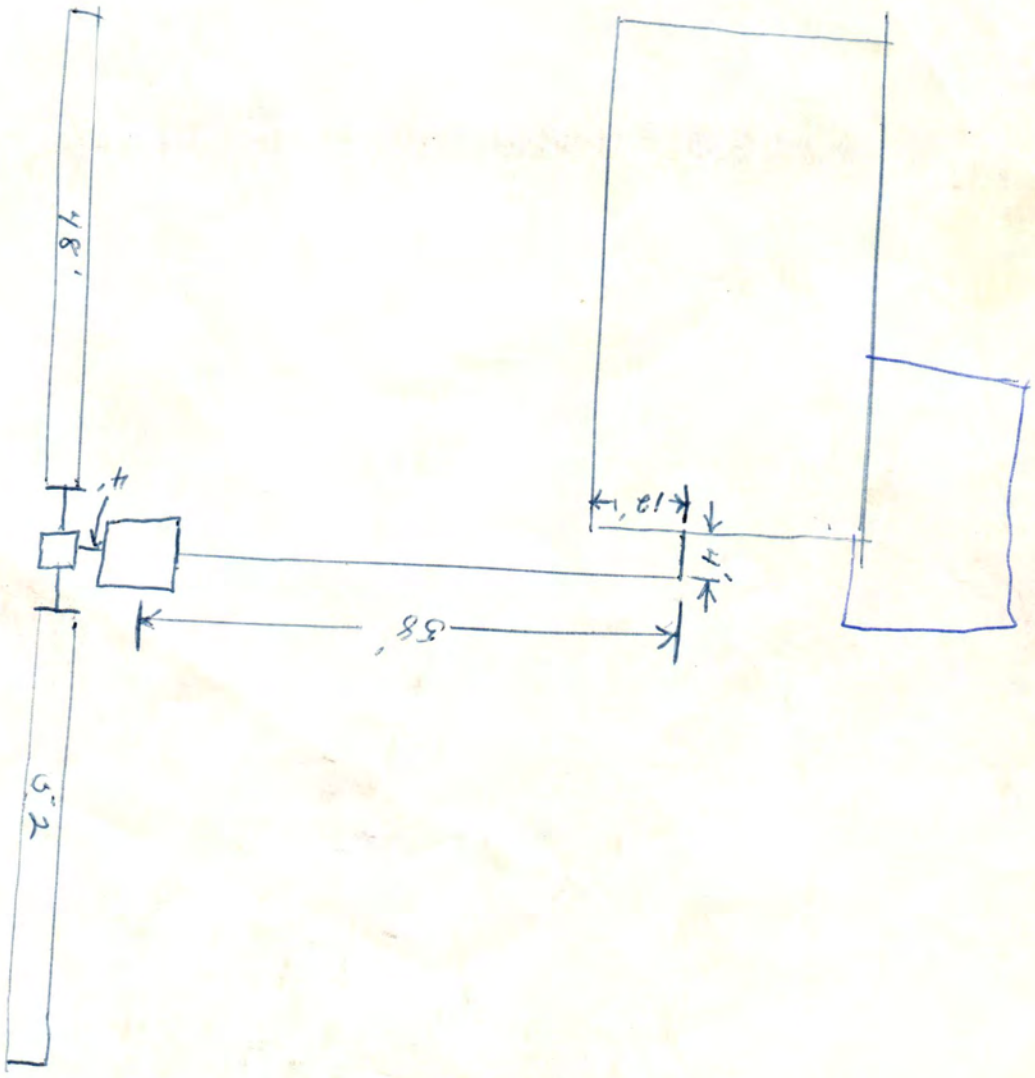

Capital City Trenching
Road Easement
11-29-77
