FILE #2529

CITY OF LINCOLN NEBRASKA

DEPARTMENT OF LICENSES AND PERMITS

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION — TYPE OF LICENSE OR PERMIT

JANUARY 22, 1988 — THIS LICENSE OR PERMIT EXPIRES

FRANK E. ANDELT — LICENSEE OR PERMITTEE

526 W. SAUNDERS — ADDRESS

LINCOLN, NE 68521

T9N; R6E; Sec 17; Bk 2; Lot 2; Hitching Post Hills, 2nd Addition — NAME OF ESTABLISHMENT, IF ANY

ADDRESS

REMARKS: NON TRANSFERABLE NEW CONSTRUCTION

PERMIT	ACCOUNTING NUMBER	TOTAL
$ 60.00	018754	$ 60.00

Valid Receipt Only if Machine Receipted In This Space

Serial No. — Date and Amount

APPLICATION

HEALTH

ISSUING OFFICER OR DEPARTMENT

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW

JUL 2 2 1987

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☒
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

A

FILING FEE: $ 60.00

FILE NO. 2529

DATE: 7-21-87

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 9 N ; Range 6 E ; Section 17 ; Block 2 : Lot 2 : Addition Hitching Post Hills Second Addition
   Street Address _____

2. Property Use: Residential ☒ ; Commercial ☐ Other Use ☐
   No. of Bedrooms 3 . Describe _____

3. Type of Individual Sewage Disposal System: Septic Tank ☒ ; Other ☐ or sewage lagoon

4. Distance to public sewer: N/A ft. depending on percolation test

Frank E. Andelt
Signature of Applicant (Owner or Lessee)

526 W. Saunders, Lincoln, NE 68521
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. 7/22/87. Date Frwd. 7/22/87. ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Hood

2. Supt. Bldg. Insp.: or Village Clerk Date Rec'd. 7-22-87. Date Frwd. 7-22-87. ACTION: Approved ☒ Disapproved ☐ Signature: Emma

3. City or County Engineer: Date Rec'd. 7-22-87. Date Frwd. 7-22-87. ACTION: Approved ☒ Disapproved ☐ Signature: Dennis Bartels

REMARKS OR REASONS FOR DISAPPROVAL WELL PERMIT STILL COMING

Site Visits:
Date: 9/21/87 by: J. C. H.
Date: / / by:
Date: / / by:

INSTALLATION FINAL WRITTEN APPROVAL
Date: 9/21/87 By: J. C. Hood

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

FORM 23-43

AUG 2 5 1987

FORM 20102-0477
PRELIMINARY PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐


LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

C

Sketch of property showing Percolation Test hole locations, well, residence, direction and property line.

FILE NO._____

Indicate on sketch if residence and well are exisiting or proposed.

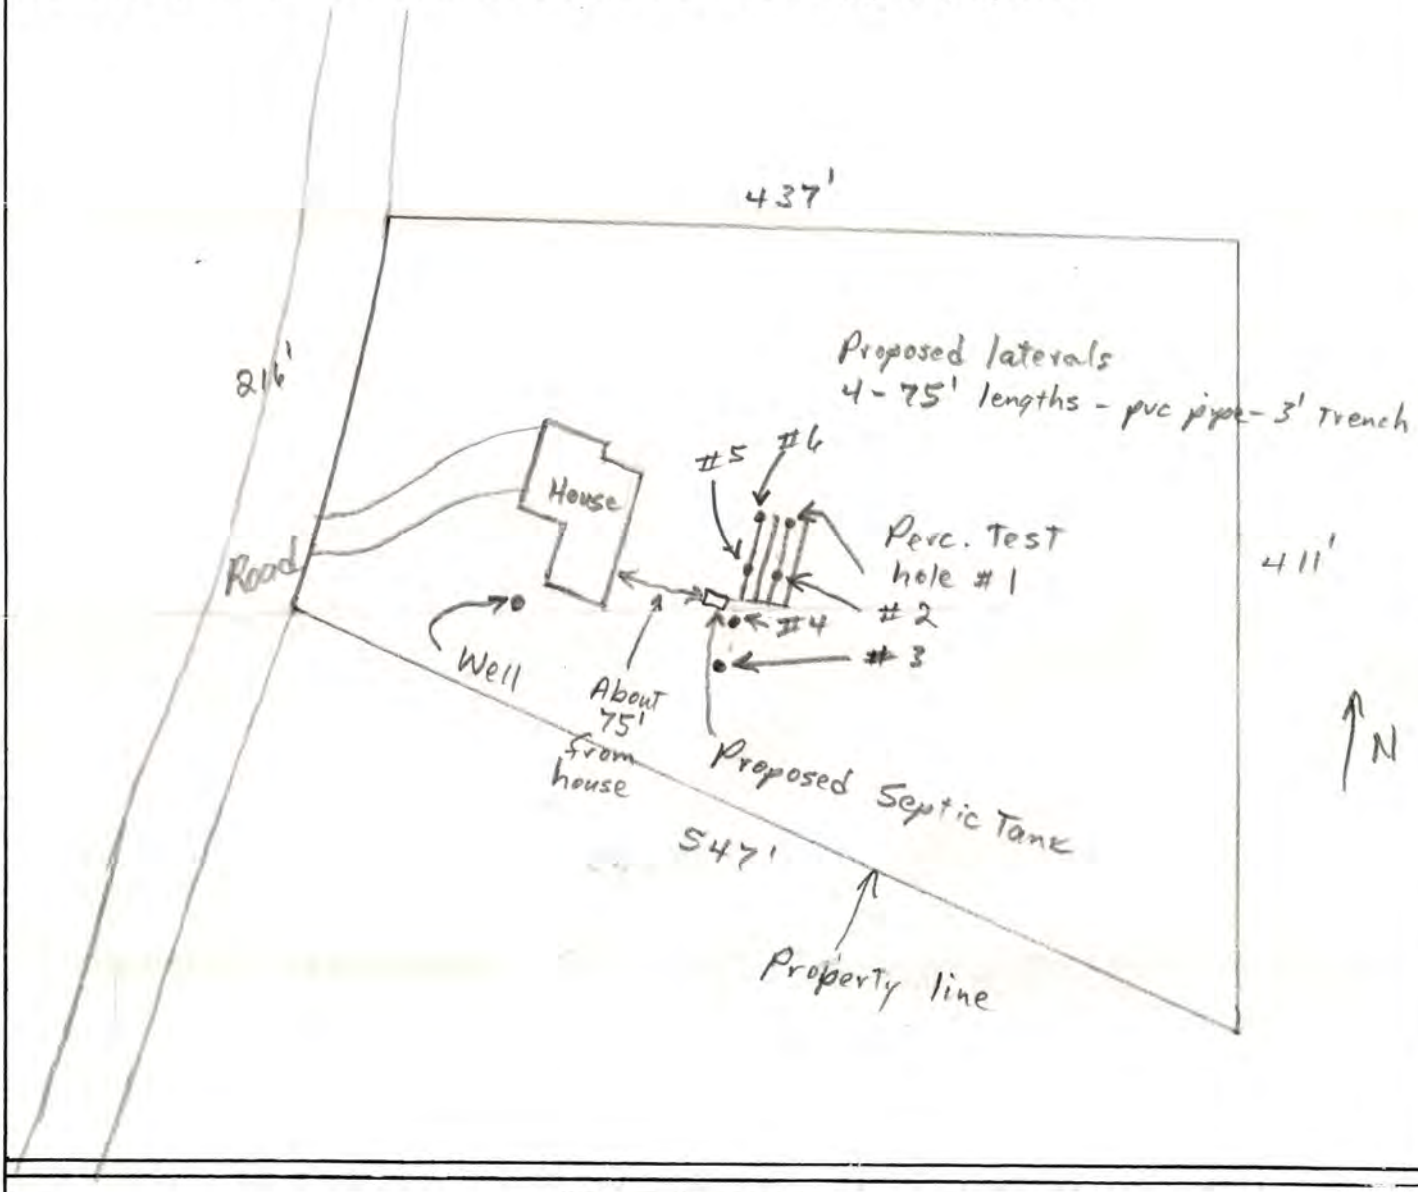

REVIEWING ACTION

Remarks:_____

Date: AUGUST 25, 1987

Minimum Design Requirement
1. Capacity of Septic Tank 1000 gals.
2. Total Length of Laterals_____ ft.
3. With a Trench Width of_____ in.
4. Total Area of Lateral needed 862 sq.ft.

Jerrold C. Hood
Signature of Reviewing Official

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

D

DATE: _____

FILE NO. _____


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material SDR 40 ; Diameter 4 in.
2. Distance above basement floor _____ in., or below basement floor _____ in.
3. Distance between dwelling and septic tank 110 ft.
4. Number of clean-outs 2 .
5. Distances to:
Well or Suction Line _____ ft.;
Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

B. SEPTIC TANK:
1. Material Pre Cast ; No. of compartments _____.
2. Capacity 1000 gals.;
3. Factory Built: Yes ☒ No ☐
(Company _____)
4. Manholes: Over Inlet; diam. _____ in.
Over Outlet; diam. _____ in.
Riser Above ☒ Below ☒ Grade 3" in.
5. Inlet: Baffle ☐ ; or Tee ☐
6. Outlet: Baffle ☐ ; or Tee ☐
7. Depth of top of tank below finished grade 17" in.
8. Distances to:
Well or Suction Line _____ ft.;
Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

C. DISTRIBUTION BOX:
1. Material Pre Cast ; Number - available outlets _____.
2. Factory Built: Yes ☒ No ☐
(Company _____)
3. Distance from Septic Tank _____ ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☐ Perforated Pipe ☒
Diameter of Half Round _____ or
Perforated Pipe 4" .
Material: fiberglass ☐ ; plastic ☒ ; concrete ☐ ; other _____.
2. Lateral Lines:
Number 3 ; Length of each line 100 , 100 , 100 , _____ , _____ ft.;
Total length of laterals 300 ft.;
Distance between lateral lines 10' ft.
3. Trench dimensions: Width 3 ft.;
Slope 3 in/100 ft.; Average Depth 32 in.
4. Filter Material: Road Gravel
Depth of Material 14 in.
5. Distances to:
Well or Suction Line — ft.;
Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

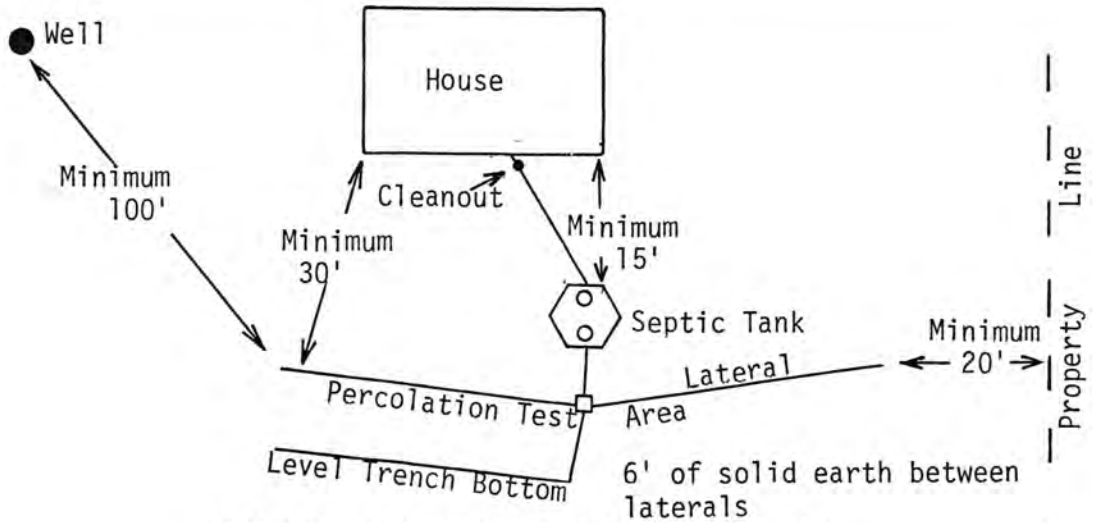

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

9-21-87 Larry Schabarick

