LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

ENVIRONMENTAL HEALTH DIVISION

2200 St. Marys Ave Lincoln, NE 68502-3785 (402) 471-8000

NON TRANSFERABLE

PERMIT

Permit
SEWAGE INSTALLATION

No. 92380092101

Issued 10/08/92
Expires 04/08/93
Revenue Code 18754

Establishment
MIKE REZAC
T9N R6E SEC 19
YANKEE HILL LAKE 1ST BLK 1 LOT 8

FEES: $150.00

TOTAL $150.00

Permittee
MIKE REZAC
1830 W BURNHAM
LINCOLN NE 68522

Issued By M. Jane Ford
Health Director

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW
"POST IN A PROMINENT PLACE"

923800921

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

A

FILING FEE: $_____

FILE NO._____

DATE: 10/8/92

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 9N ; Range 6E ; Section 19 ;
   Block 1 : Lot 8 : Addition Yankee Hill Lake 1ST ADD.
   Street Address _____

2. Property Use: Residential ☑ ; Commercial ☐ ; Other Use ☐
   No. of Bedrooms 3 . Describe _____

3. Type of Individual Sewage Disposal System: Septic Tank ☑ ; Other ☐

4. Distance to public sewer: _____ ft.

WILL INSTALL WHATEVER SOIL PERCOLATION TEST INDICATES

M Rezac
Signature of Applicant (Owner or Lessee)

1830 WEST. Burlington
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. 10/8/92 . Date Frwd. 10/12/92 . ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Nood

2. Supt. Bldg. Insp.: or Village Clerk: Date Rec'd. _____ . Date Frwd. _____ . ACTION: Approved ☐ Disapproved ☐ Signature: Norm Dwyer

3. City or County Engineer: Date Rec'd. 10/12/92 . Date Frwd. _____ . ACTION: Approved ☒ Disapproved ☐ Signature: [signature]

REMARKS OR REASONS FOR DISAPPROVAL _____

Site Visits:
Date: 6/25/93 by: L.C.H.
Date: _____ by: _____
Date: _____ by: _____

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

INSTALLATION FINAL WRITTEN APPROVAL *
Date: 7/6/93 By: Jerrold C. Nood

* EXPERIMENTAL SYSTEM HENCE APPROVAL IS PROVISIONAL

FORM 23-43

RECEIVED JUL 06 1993

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

D

DATE: 6-30-93

FILE NO: _____


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material PVC ; Diameter 4 in.
2. Distance above basement floor — in., or below basement floor 18 in.
3. Distance between dwelling and septic tank 150 ft.
4. Number of clean-outs 2 .
5. Distances to:
Well or Suction Line NA ft.; Stream NA ft.; Pressure Line 50+ ft.; Property Line 50+ ft.

B. SEPTIC TANK:
1. Material Concrete ; No. of compartments 1 .
2. Capacity 1000 gals.;
3. Factory Built: Yes ☒ No ☐
(Company American Concrete)
4. Manholes: Over Inlet; diam. 18 in.
Over Outlet; diam. 8 in.
Riser Above ☒ Below ☐ Grade 12 in.
5. Inlet: Baffle ☒ ; or Tee ☐
6. Outlet: Baffle ☒ ; or Tee ☐
7. Depth of top of tank below finished grade 12 in.
8. Distances to:
Well or Suction Line 100+ ft.; Stream 100+ ft.; Pressure Line 100+ ft.; Property Line 100+ ft.

C. DISTRIBUTION BOX:
1. Material Concrete ; Number - available outlets 5 .
2. Factory Built: Yes ☒ No ☐
(Company American Concrete)
3. Distance from Septic Tank 10 ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☒ Perforated Pipe ☐
Diameter of Half Round 22" or Perforated Pipe _____.
Material: fiberglass ☐ ; plastic ☐ ; concrete ☒ ; other _____.
2. Lateral Lines:
Number 2 ; Length of each line 100+, 100+, _____, _____, _____ ft.;
Total length of laterals 200 ft.;
Distance between lateral lines 13 ft.
3. Trench dimensions: Width 5 ft.;
Slope 4 in/100 ft.; Average Depth 36 in.
4. Filter Material: Gravel
Depth of Material 30 in.
5. Distances to:
Well or Suction Line 100+ ft.; Stream 100+ ft.; Pressure Line 100+ ft.; Property Line 100+ ft.

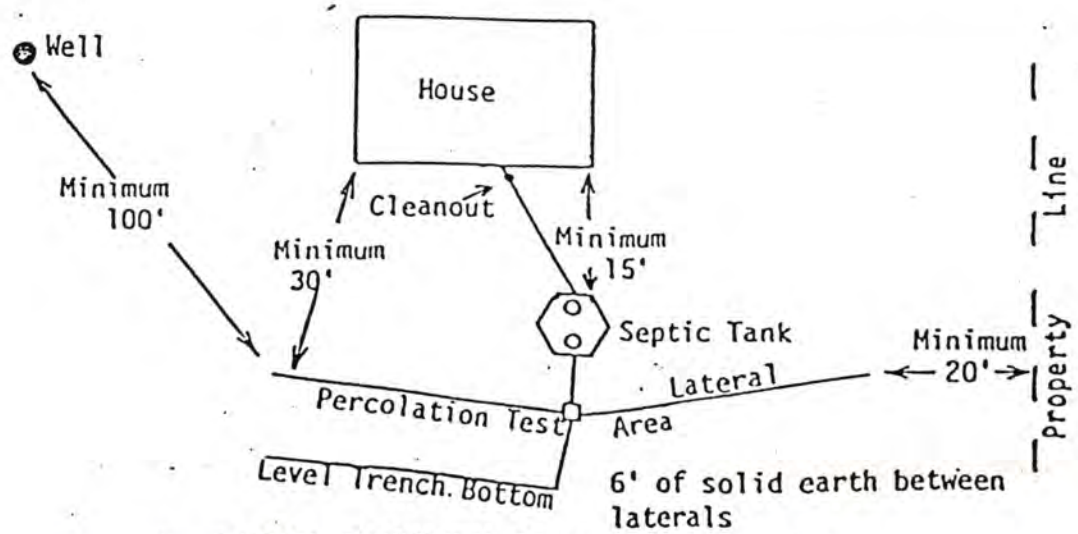

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

Reega Const.

Installed By Vogt Tor Excavating
6-24-93

