LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

Division of Environmental Health
2200 St. Marys Ave Lincoln, NE 68502 (402) 471-8000

NON TRANSFERABLE

PERMIT

SEWAGE INSTALLATION

No. 92380082501

Issued 04/20/92
Expires 10/20/92

ESTABLISHMENT

MIKE REZAC
T9N R6E SEC 19
YANKEE HILL LAKE BLK 1 LOT 10

FEES: Permit 018754 $150.00

Total $150.00

PERMITTEE

MIKE REZAC
1830 W BURNHAM
LINCOLN NE 68522

Issued By COUNTY HEALTH

VALID RECEIPT ONLY IF RECEIPTED IN THIS SPACE	
DATE	AMOUNT
4/20/92	PAID

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

A

FILING FEE: $ 150.00

FILE NO. _____

DATE: 4/17/92

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 9N ; Range 6E ; Section 19 ;
   Block 1 : Lot 10 : Addition Yankee Hill Lake
   Street Address _____

2. Property Use: Residential ☑ ; Commercial ☐ Other Use ☐
   No. of Bedrooms 3 . Describe _____

3. Type of Individual Sewage Disposal System: Septic Tank ☑ ; Other ☐
   + Drainage Field.

4. Distance to public sewer: _____ ft.

M Rezac
Signature of Applicant (Owner or Lessee)

1830 West Burnham Lincoln 68522
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. 4/17/92. Date Frwd. 4/20/92. ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Hood

2. Supt. Bldg. Insp.: or Village Clerk Date Rec'd. 4/20/92. Date Frwd. 4/20/92. ACTION: Approved ☐ Disapproved ☐ Signature: _____

3. City or County Engineer: Date Rec'd. _____. Date Frwd. _____. ACTION: Approved ☒ Disapproved ☐ Signature: Jim Blaugh

REMARKS OR REASONS FOR DISAPPROVAL _____

Site Visits:
Date: 8/20/92 by: JR
Date: 8-21-92 by: PD
Date: _____ by: _____

5100 West Bear Crest

INSTALLATION FINAL WRITTEN APPROVAL *
Date: 10/29/92 By: John Hunt

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

* EXPERIMENTAL SYSTEM APPROVAL IS PROVISIONAL

FORM 23-43

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

D

DATE: _____

FILE NO: _____


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material PVC ; Diameter 4 in.
2. Distance above basement floor ____ in., or below basement floor 18 in.
3. Distance between dwelling and septic tank 76 ft.
4. Number of clean-outs None .
5. Distances to: Well or Suction Line 100+ ft.; Stream 100+ ft.; Pressure Line 20+ ft.; Property Line 20+ ft.

B. SEPTIC TANK:
1. Material Concrete ; No. of compartments 1 .
2. Capacity 1000 gals.;
3. Factory Built: Yes ☒ No ☐ (Company American Concrete)
4. Manholes: Over Inlet; diam. 16 in. Over Outlet; diam. 8 in. Riser Above ☒ Below ☐ Grade ☒ in.
5. Inlet: Baffle ☒ ; or Tee ☐
6. Outlet: Baffle ☒ ; or Tee ☐
7. Depth of top of tank below finished grade 18 in.
8. Distances to: Well or Suction Line 100+ ft.; Stream 100+ ft.; Pressure Line 20+ ft.; Property Line 20+ ft.

C. DISTRIBUTION BOX:
1. Material Concrete ; Number available outlets 5 .
2. Factory Built: Yes ☒ No ☐ (Company American Concrete)
3. Distance from Septic Tank 10' ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☐ Perforated Pipe ☒ Diameter of Half Round ____ or Perforated Pipe 4" . Material: fiberglass ☐ ; plastic ☒ ; concrete ☐ ; other ____ .
2. Lateral Lines: Number 2 ; Length of each line 100 , 100 , ____ , ____ , ____ ft.; Total length of laterals 200 ft.; Distance between lateral lines 10 ft.
3. Trench dimensions: Width 8' ft.; Slope 4 in/100 ft.; Average Depth 36 in.
4. Filter Material: Gravel Depth of Material 30 in.
5. Distances to: Well or Suction Line 100+ ft.; Stream 100+ ft.; Pressure Line 100+ ft.; Property Line 20+ ft.

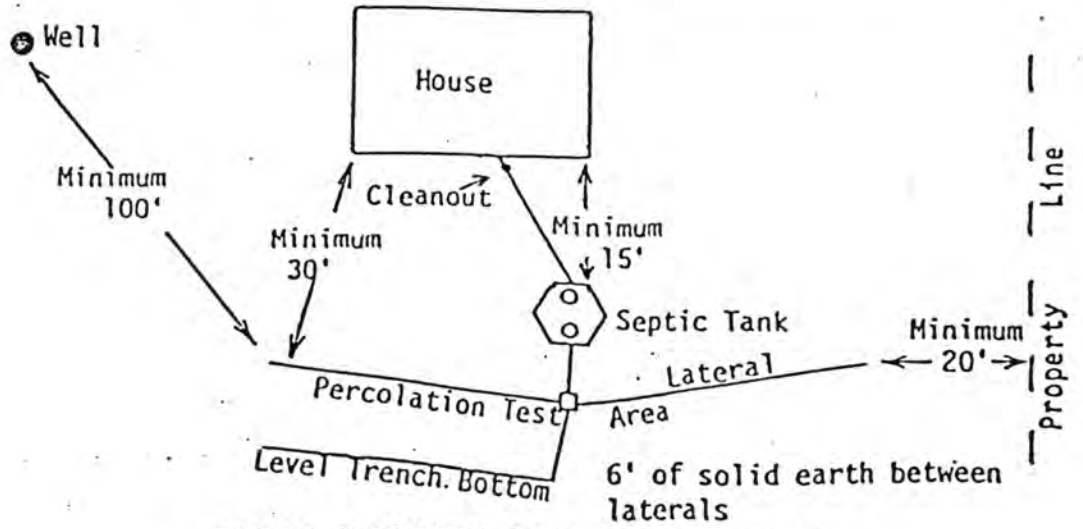

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

5100 Deercrest

Installed By Vogt T&T

N

