LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

ENVIRONMENTAL HEALTH DIVISION

2200 St. Marys Ave Lincoln, NE 68502-3785 (402) 441-8000

NON TRANSFERABLE

PERMIT

Permit
SEWAGE INSTALLATION

No. 93380098301

Issued 04/29/93
Expires 10/29/93
Revenue Code 18754

Establishment
MIKE REZAC
T9N R6E SEC 19
YANKEE HILL LAKE 1ST BLK 2 LOT 12
7343 SW HARTERS PLACE

FEES: $150.00

TOTAL $150.00

Permittee
MIKE REZAC
1830 W BURNHAM
LINCOLN NE 68522

Issued By M. Jane Ford
Health Director

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW
"POST IN A PROMINENT PLACE"

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

A

FILING FEE: $150.00

FILE NO. _____

DATE: _____

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 9N ; Range 6E ; Section 19 ;
   Block 2 : Lot 12 : Addition Yankee Hill Lake 1ST ADD.
   Street Address 7943 SW. Hampton Place.

2. Property Use: Residential ☒ ; Commercial ☐ Other Use ☐
   No. of Bedrooms 3 . Describe _____

3. Type of Individual Sewage Disposal System: Septic Tank ☒ ; Other ☐

4. Distance to public sewer: _____ ft.

WILL INSTALL WHATEVER SOIL PERCOLATION TEST INDICATES
EXPERIMENTAL

M K Zoc
Signature of Applicant (Owner or Lessee)

1830 West Burnham 68522
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. 4/29/93 . Date Frwd. 4/29/93 . ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Hood
2. Supt. Bldg. Insp.: or Village Clerk: Date Rec'd. 4/29/93 . Date Frwd. 4/29/93 . ACTION: Approved ☒ Disapproved ☐ Signature: [signature]
3. City or County Engineer: Date Rec'd. 4-29-93 . Date Frwd. 4-29-93 . ACTION: Approved ☒ Disapproved ☐ Signature: [signature]

REMARKS OR REASONS FOR DISAPPROVAL _____

Site Visits:
Date: 7-6-93 by: Paul D. Sewer Inspector
Date: 7/16/93 by: J.C.H.
Date: 8/5/96 by: J.C.H.

Hood Drawing

INSTALLATION FINAL WRITTEN APPROVAL
Date: 8/6/96 By: Jerrold C. Hood *

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

* EXPERIMENTAL SYSTEM
HENCE PROVISIONAL APPROVAL

FORM 23-43

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

D

DATE: _____

FILE NO. _____

7343 Hunters Place


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material PVC ; Diameter 4 in.
2. Distance above basement floor ____ in., or below basement floor 18 in.
3. Distance between dwelling and septic tank 70 ft.
4. Number of clean-outs Inside.
5. Distances to:
Well or Suction Line 100+ ft.; Stream NA ft.; Pressure Line 100+ ft.; Property Line 100+ ft.


B. SEPTIC TANK:
1. Material Concrete ; No. of compartments 1
2. Capacity 1000 gals.;
3. Factory Built: Yes ☒ No ☐
(Company American Concrete)
4. Manholes: Over Inlet; diam. 16 in.
Over Outlet; diam. 12 in.
Riser Above ☐ Below ☐ Grade ____ in.
5. Inlet: Baffle ☐ ; or Tee ☐
6. Outlet: Baffle ☐ ; or Tee ☐
7. Depth of top of tank below finished grade 14" in.
8. Distances to:
Well or Suction Line 100+ ft.; Stream NA ft.; Pressure Line 100+ ft.; Property Line 100+ ft.

C. DISTRIBUTION BOX:
1. Material Concrete ; Number available outlets 5.
2. Factory Built: Yes ☒ No ☐
(Company American Concrete)
3. Distance from Septic Tank 8 ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☒ Perforated Pipe ☐
Diameter of Half Round 22" or Perforated Pipe ____.
Material: fiberglass ☐ ; plastic ☐ ; concrete ☒ ; other ____.
2. Lateral Lines:
Number 2 ; Length of each line 100, 100, ____, ____, ____ ft.;
Total length of laterals 200 ft.;
Distance between lateral lines 20 ft.
3. Trench dimensions: Width 8 ft.;
Slope 2 in/100 ft.; Average Depth 36 in.
4. Filter Material: Gravel
Depth of Material 30 in.
5. Distances to:
Well or Suction Line 100+ ft.;
Stream NA ft.; Pressure Line 100+ ft.; Property Line 20 ft.

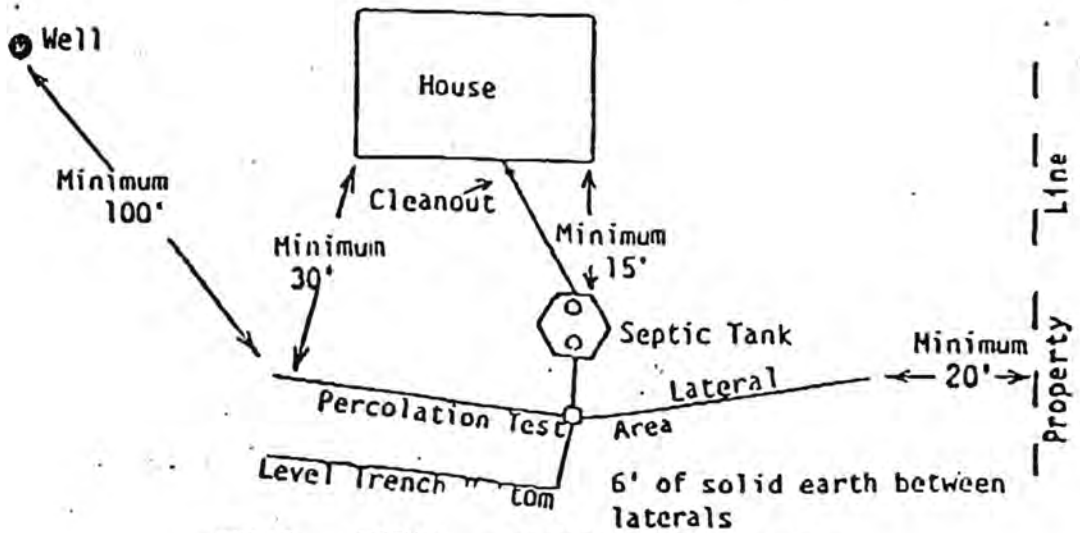

TYPIC INDIVI SEWAGE SYSTEM DESIGN

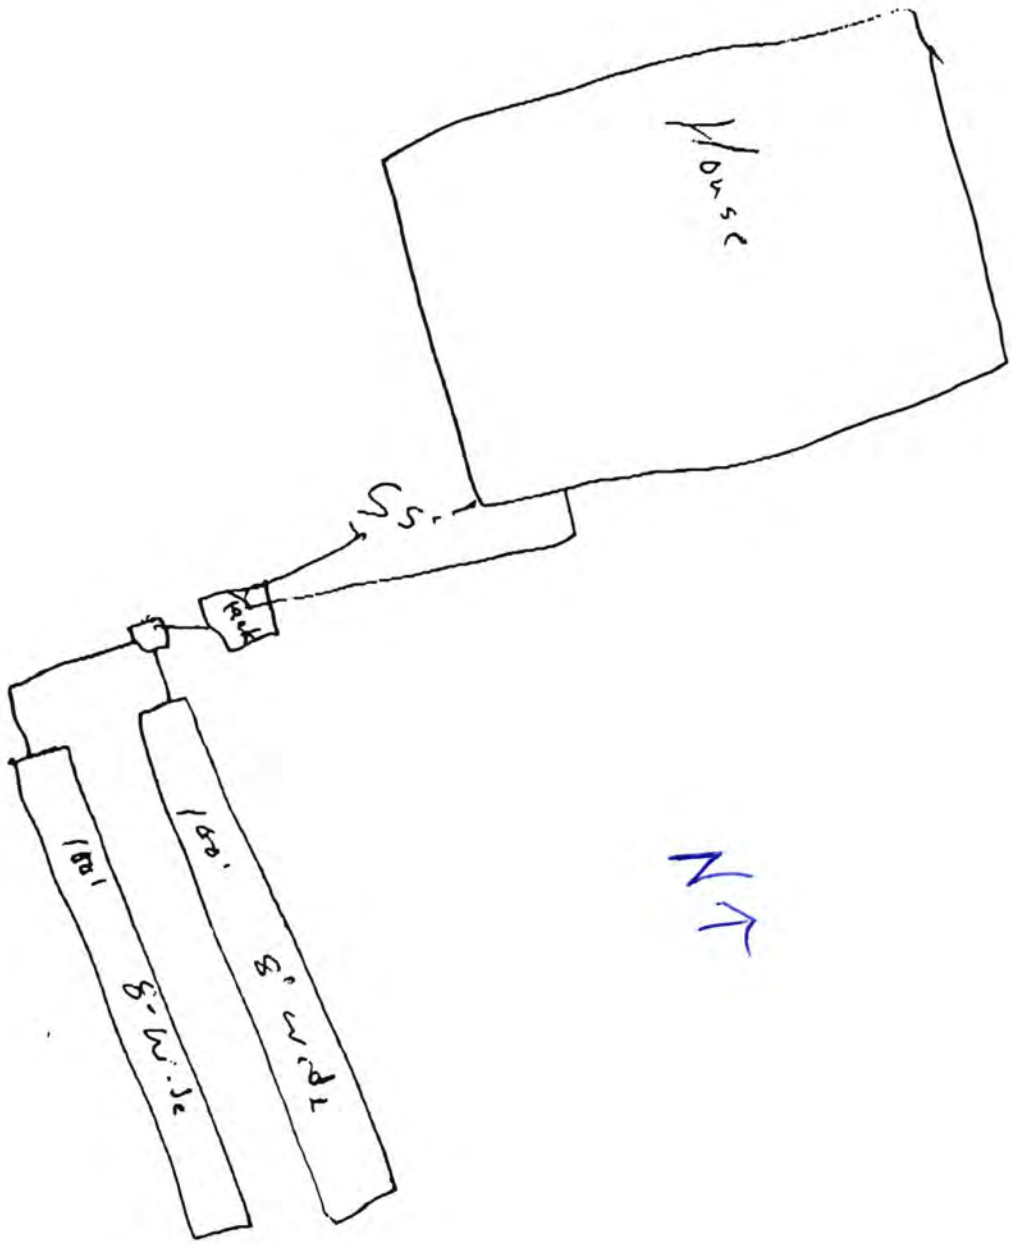
House
SS.
Septic Tank
100'
Leach Field
100'
N

011

Lincoln-Lancaster County Health Department

3140 "N" Street, Lincoln, Nebraska 68510 Phone: 441-8022

REAL ESTATE TRANSFER/LOAN APPROVAL FORM

FOR PROPERTY IN **LANCASTER COUNTY** ONLY

This form must be completed and returned with payment to request a real estate transfer inspection.

MAKE CHECK PAYABLE TO: "Lincoln-Lancaster County Health Department" or "LLCHD"

☑ Enclosed is $150.00. Allow two weeks for processing. Incomplete information will delay processing.

Legal Description of Property: Street Address 7343 S.W. Hunters Place

Twp 9N Range 6E Section 19 1/4 ___ 1/4 ___ Block 8 Lot 18 Addition ___

Directions to Property West on W Denton to 56th. 1 Block S. 1 Block E. - thru Brick

South appx. 100 Yds Brick Front 3 car garage W side of road (Yankee Hill Addition)

Location of Well N side of House Tap Location: Inside ☑ Outside ☐

Location of Sewage System S side Year Installed 93?

	NAME	ADDRESS	PHONE
Present Owner:	MAX MANES	7343 S.W. Hunters Place	797-2303
Tenant/Buyer:			
Return to:	Ted Givens	Nct Hybrids 3820 N 56th P.O. Box 4408 Lincoln 68504	467-2517

Signature of Applicant Ted Givens Address 206 S. Navasota Plainview TX 79072 Date 8/5/96

HEALTH DEPARTMENT USE ONLY

RECEIVED
Date 8/5/96
Initials T.C.H.
Amount $150.00
Check No. 6847

DATA ENTRY
Date ___/___/___
Case No. ___
Initials ___

PRELIMINARY STATUS--By Jerrold C. Hood **DATE:** 8/5/96

WATER SYSTEM:	Approved	Disapproved
Construction	☐	☒
Bacteria	☒ 0 /ml	☐ ___ /ml
Nitrate	☒ <0.1 ppm	☐ ___ ppm

SEWAGE SYSTEM
Approved ☐
Provisional ☒
Disapproved ☐

Additional Site Visits
Date 9/9/96 by J.C.H.
Date ___/___/___ by ___
Date ___/___/___ by ___

Comments: COLLAR BROKEN ON WELL HEAD. NEED AS BUILT DRAWING OF SEWAGE SYSTEM. SEWAGE SYSTEM IS OF AN EXPERIMENTAL VARIETY HENCE APPROVAL IS PROVISIONAL. NO EVIDENCE OF MALFUNCTION. 9/9/96 Collar replaced. J.C.H. See Attached Letter ☐

FINAL STATUS

WATER SYSTEM: Approved ☒ **SEWAGE DISPOSAL SYSTEM:** Approved ☐ Provisional Approval ☒

Approved by Jerrold C. Hood R.E.H.S. Date 9/9/96

Approval or disapproval is based on State and local standards for construction, location and water quality. Inspection is based on visible construction and operation at the time of inspection. Approval or provisional approval does not imply or express a guarantee of system operations.

White - Applicant after approval Yellow - Environmental Health Pink - Business Office

Revised/Reprint: 10-95
