LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

ENVIRONMENTAL HEALTH DIVISION

2200 St. Marys Ave Lincoln, NE 68502-3785 (402) 441-8000

NON TRANSFERABLE

P E R M I T

Permit
SEWAGE INSTALLATION

No. 93380103101

Issued 07/30/93
Expires 01/30/94
Revenue Code 18754

Establishment
ROBERT PACE
T9N R6E SEC 21
RIDGEWOOD ESTATES BLK 4 LOT 8

FEES: $150.00

TOTAL $150.00

Permittee
ROBERT PACE
1538 TRELAWNEY LN
LINCOLN NE 68512

Issued By M. Jane Ford
Health Director

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW
"POST IN A PROMINENT PLACE"

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☒
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

A

FILING FEE: $ 150.00

FILE NO. _____

DATE: 03/05/92

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 9N ; Range 6E ; Section 21 ;
   Block 4 : Lot 8 : Addition Ridgewood Estates
   Street Address 2201 Roxbury Lane, Lincoln, Ne

2. Property Use: Residential ☒ ; Commercial ☐ Other Use ☐
   No. of Bedrooms 3 . Describe _____

3. Type of Individual Sewage Disposal System: Septic Tank ☒ ; Other ☐

4. Distance to public sewer: _____ ft.

Robert Pace
Signature of Applicant (Owner or Lessee)
1538 Trelawney Lincoln, Ne 68512
~~5005 Vine #302 Lincoln, Ne 68504~~
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. 7/28/93. Date Frwd. 7/29/93. ACTION: Approved ☒ Disapproved ☐ Signature: Gerald C. Hoos
2. Supt. Bldg. Insp.: or Village Clerk Date Rec'd. 7/29/93. Date Frwd. 7/29/93. ACTION: Approved ☒ Disapproved ☐ Signature: Gary Spier
3. City or County Engineer: Date Rec'd. 7-29-93. Date Frwd. 7-29-93. ACTION: Approved ☒ Disapproved ☐ Signature: RD Mytham

REMARKS OR REASONS FOR DISAPPROVAL _____

Site Visits:
Date: 9-21-94 by: rm
Date: _____ by: _____
Date: _____ by: _____

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

INSTALLATION FINAL WRITTEN APPROVAL
Date: 9-21-94 By: Ron Maynard

FORM 23-43

FORM 20105-0477
SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150 and County Resolution No. 2832)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

B

FILE NO. _____

PROPERTY WHERE SOIL TESTED:

Location: Township 9 ; Range 6 ; Section & ¼ Section 21.
Property Dimensions: _____ ft. x _____ ft. Area: 3 acres. (Attach Sheet C with sketch of property).
Soil Type: Silty Clay ☐ ; Silty Clay Loam ☐ ; Sandy Loam ☐ ; Silt Loam ☐ ; Clay Loam ■ .
Dates of Tests: 6-1-89 to 6-2-89. Weather: Precip. 0 Temp. 70°.

Test Taken At Ridewood Ast. SW 27th

OWNER: Bruce Hocking
Address: 410 Teakwood 68510
483-2471

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
		Pre-Saturation Period				Percolation Readings						Results	
		Start		End		Start			End				
Hold No.	Hole Depth (in.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Water Level (in.)	Time (Hr./ Day)	Water Level (in.)	Elapsed Time (Min.)	Water Level Drop (in.)	Percolation Rates (Min./in.)
1	36"	6-1	7:30 pm	6-2	5:30 pm	6-2	5:30 pm	6"	9:30 pm	5"	30m	1"	
2	36"	6-1	7:30 pm	6-2	5:30 pm	6-2	5:30 pm	6"	9:30 pm	5¼"	"	¾"	
3	36"	6-1	7:30 pm	6-2	5:30 pm	6-2	5:30 pm	6"	9:30 pm	5"	"	1"	
4	36"	6-1	7:30 pm	6-2	5:30 pm	6-2	5:30 pm	6"	9:30 pm	5"	"	1"	
5	36"	6-1	7:30 pm	6-2	5:30 pm	6-2	5:30 pm	6"	9:30 pm	4¾"	"	1¼"	
6	36"	6-1	7:30 pm	6-2	5:30 pm	6-2	5:30 pm	6"	9:30 pm	4¾"	"	1¼"	

Sum of Percolation Rates: _____
Average of Rates: _____
Mean of Rates: _____

Mike Hoagland
Signature of Person Conducting Test

Address 2700 Dawn Ave Lincoln Phone 464-0638

Pre-Cast + Step Co.

(Do not write below this line)

Sharpsburg Silty Clay Loam or Wymore Silty Clay Loam

REVIEWING ACTION

Approved Percolation Rate (a) 28 MIN/IN min./inch

Remarks

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

D

DATE: _____

FILE NO. _____


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material Class 160; Diameter 4 in.
2. Distance above basement floor _____ in., or below basement floor 12 in.
3. Distance between dwelling and septic tank 100 ft.
4. Number of clean-outs 1.
5. Distances to:
Well or Suction Line 100'+ ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

B. SEPTIC TANK:
1. Material Precast; No. of compartments _____.
2. Capacity 1250 gals.;
3. Factory Built: Yes ☑ No ☐
(Company _____)
4. Manholes: Over Inlet; diam. _____ in.
Over Outlet; diam. _____ in.
Riser Above ☐ Below ☐ Grade ____ in.
5. Inlet: Baffle ☐ ; or Tee ☐
6. Outlet: Baffle ☐ ; or Tee ☐
7. Depth of top of tank below finished grade 8" in.
8. Distances to:
Well or Suction Line - ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

C. DISTRIBUTION BOX:
1. Material Precast; Number - available outlets _____.
2. Factory Built: Yes ☒ No ☐
(Company _____)
3. Distance from Septic Tank _____ ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☐ Perforated Pipe ☒
Diameter of Half Round _____ or Perforated Pipe 6.
Material: fiberglass ☐ ; plastic ☒ ; concrete ☐ ; other _____.
2. Lateral Lines:
Number 3 ; Length of each line 100, 100, 100, _____, _____ ft.;
Total length of laterals 300 ft.;
Distance between lateral lines 6 ft.
3. Trench dimensions: Width 3 ft.;
Slope 3 in/100 ft.; Average Depth 30 in.
4. Filter Material: Road Gravel
Depth of Material _____ in.
5. Distances to:
Well or Suction Line 100'+ ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line 20' ft.

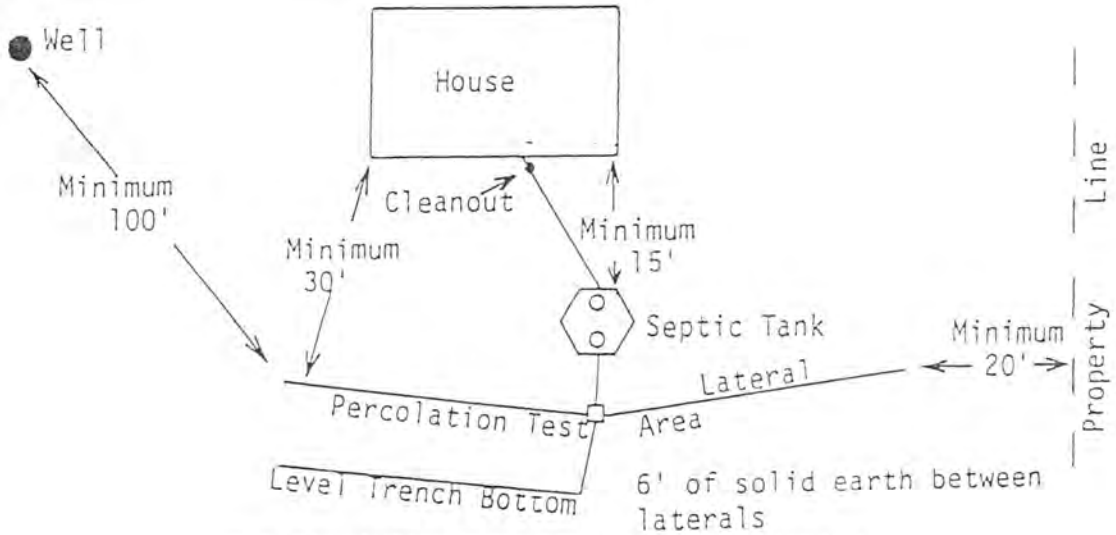

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

9-21-94

Larry Schwanck

