CITY OF LINCOLN NEBRASKA

DEPARTMENT OF LICENSES AND PERMITS

FILE NO. 1536

TYPE OF LICENSE OR PERMIT: INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION

THIS LICENSE OR PERMIT EXPIRES: NOVEMBER 10, 1978

LICENSEE OR PERMITTEE: MIKE FULTZ by Don Pentico, ADDRESS: 1520 Pioneers Blvd., Lincoln, NE 68502

NAME OF ESTABLISHMENT, IF ANY: T9N, R6E, Section 21, Block 6, Lot 5, Addition Ridgewood ADDRESS:

REMARKS: NON-TRANSFERABLE

PERMIT	INSPECTION FEE	OCCUPATION TAX	LICENSE	TOTAL
$ 60.00	$	$	$	$ 60.00

ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE
110.15	110.16	148.14	6-2

SERIAL NO.	DATE	AMOUNT
018754		

VALID RECEIPT ONLY IF MACHINE RECEIPTED IN THIS SPACE

APPLICATION
HEALTH

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☒
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

FILING FEE: $ 60.00

FILE NO. 1536

DATE: MAY 17 1979

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 9N ; Range 6E ; Section 21 ; Block 6 : Lot 5 : Addition RIDGEWOOD ADDITION
   Street Address 1900 w Foothills Road

2. Property Use: Residential ☒ ; Commercial ☐ Other Use ☐
   No. of Bedrooms 3 . Describe

3. Type of Individual Sewage Disposal System: Septic Tank ☒ ; Other ☐

4. Distance to public sewer: N/A ft.

Mike Fultz by Don Prentice
Signature of Applicant (Owner or Lessee)

1520 Pioneers Blvd.
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. 5/17/79. Date Frwd. 5/18/79. ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Hood

2. Supt. Bldg. Insp.: or Village Clerk Date Rec'd. 5/18/79 Date Frwd. 5/18/79. ACTION: Approved ☒ Disapproved ☐ Signature: Gaylon Sherwood

3. City ~~or County~~ Engineer : Date Rec'd. 5-18-79. Date Frwd. 5-18-79. ACTION: Approved ☒ Disapproved ☐ Signature: Al Haig

REMARKS OR REASONS FOR DISAPPROVAL

Site Visits:
Date: 7-30-79 by: jw
Date: by:
Date: by:

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

INSTALLATION FINAL WRITTEN APPROVAL
Date: 7-30-79 By: James Wierzba

, 20104-0477
.NS & SPECIFICATIONS FOR SEWAGE DISPOSAL
STEM (Annex to Application)
ity Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

D

DATE: _____

FILE NO. _____


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material PVC ; Diameter 4 in.
2. Distance above basement floor _____ in., or below basement floor 40 in.
3. Distance between dwelling and septic tank 70 ft.
4. Number of clean-outs 1 .
5. Distances to:
Well or Suction Line 100+ ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line 100+ ft.

B. SEPTIC TANK:
1. Material ~~Fiberglass~~; No. of compartments _____.
2. Capacity 1000 gals.;
3. Factory Built: Yes ☑ No ☐
(Company Conoglass)
4. Manholes: Over Inlet; diam. 6 in.
Over Outlet; diam. _____ in.
Riser Above ☑ Below ☐ Grade 4 in.
5. Inlet: Baffle ☐ ; or Tee ☑
6. Outlet: Baffle ☐ ; or Tee ☑
7. Depth of top of tank below finished grade 40 in.
8. Distances to:
Well or Suction Line 100+ ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line 100+ ft.

C. DISTRIBUTION BOX:
1. Material Plastic ; Number - available outlets 7 .
2. Factory Built: Yes ☑ No ☐
(Company Conoglass)
3. Distance from Septic Tank _____ ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☐ Perforated Pipe ☑
Diameter of Half Round _____ or Perforated Pipe 4" .
Material: fiberglass ☐ ; plastic ☑ ; concrete ☐ ; other _____.
2. Lateral Lines:
Number 2 ; Length of each line 100 FT 100 FT _____, _____, _____ ft.;
Total length of laterals 200 ft.;
Distance between lateral lines 20 ft.
3. Trench dimensions: Width 7 1/2 ft.;
Slope 6 in/100 ft.; Average Depth 40 in.
4. Filter Material: Gravel + Sand
Depth of Material (24 Gravel 6 Sand) in.
5. Distances to:
Well or Suction Line 100+ ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line 75 ft.

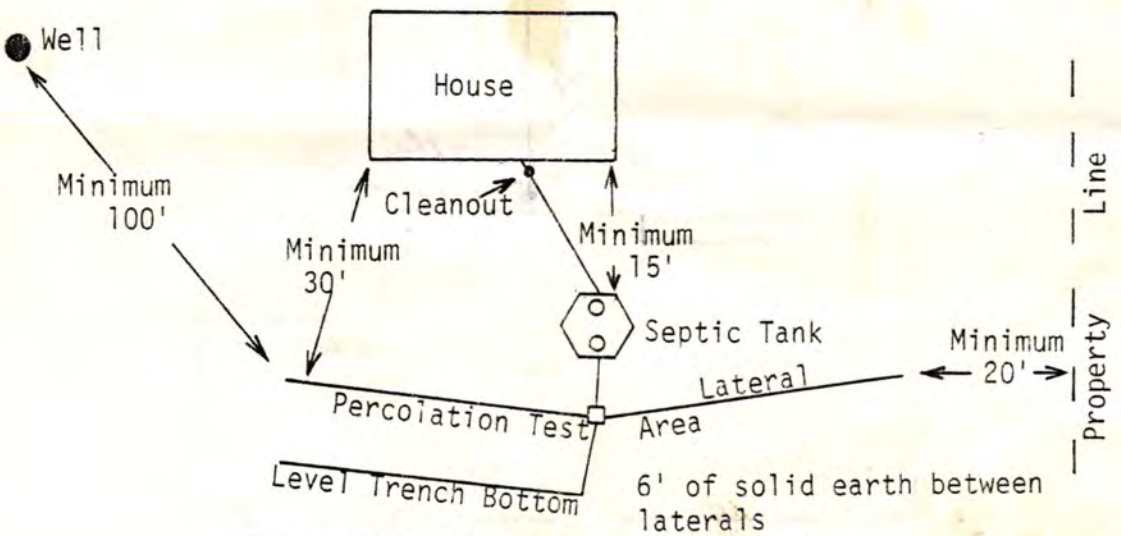

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

AS BUILT DRAWING OF SYSTEM

DATE 7-30-79 INSTALLER Roblyer Plumbing

N

