Lincoln-Lancaster County Health Department

ENVIRONMENTAL HEALTH DIVISION

3140 N STREET · LINCOLN, NE 68510-1514 (402) 441-8000

Permit

SEWAGE SYSTEM REPAIR
SEWER REPAIR-ALTER INFILTRATION

Permit # 00390068101

Issued 10/12/00
Expires 04/12/01
Revenue Code 3157

Establishment

TRINITY CHAPEL
T9N R6E SEC 27 QTR SE
SW1/4 OF SE1/4
~~800~~ W ROKEBY RD-ROKEBY

FEES: $100.00

Permitee 500

TRINITY CHAPEL C/O WAYNE PESTER
P O BOX 23053
LINCOLN NE 68542

TOTAL: $100.00

Leon F. Vinci, MPH, Health Director

• POST IN A PROMINENT PLACE • NOT TRANSFERABLE

013832

Application to Alter, Extend or Repair an Individual Sewage Disposal System

00390068

☐ Municipal Code 24.38 ☐ County Resolution Number 2832

The undersigned hereby applies for a permit to: ☒ **ALTER** ☐ **EXTEND** ☐ **REPAIR** an existing Individual Sewage Disposal System, in conformance with appropriate Ordinance or Resolution, as described in this application and drawings attached hereto.

1. **Legal description of property:**
   Township 9N Range 6E Section _____ 1/4 Section 27 SW/4 of SE/4
   Block _____ Lot _____ Addition _____
   Parcel ID ____-____-_____-_____-_____ (i.e. 99-99-999-999-999)
   Street Address 800 W. Rokeby Rd. Rokeby,

2. **Property use:** ☐ residential ☐ commercial ☐ other use
   Number of bedrooms _____ Describe Church (110 Seating Cap)

3. **Type of Present Individual Disposal System** ☒ septic tank ☐ lagoon ☐ other

4. **Description of proposed alteration, extension or repair** Remove existing crushed Lateral & Re Install 100' of Infiltrator in same place - As per Installer, the System is not failing. Onsite inspection does not indicate failure. D.S. 9/28/00

5. **Work to be done by:** ☐ owner ☒ contractor's name Southwick Sewer + Drain

6. **Estimated project:**
   a. Repair, replace or minor extension with a cost less than $400 (no fee required).
   b. Total cost is greater than $400 (Return fee with this application)
   c. A "construction permit" is required if the use, operation, location, or type of the system is being change.

Print Name Trinity Chapel Address Rokeby Phone 489-2609
Applicant Signature (owner or lessee) Wayne Pester 2100 W Denton Rd. P.O. Box 23053 Lincoln 68542

Please include the permit fee ($100) with this application
Fee must be included before the application will be processed. Incomplete information will delay processing

---

HEALTH DEPARTMENT USE ONLY

Date received 09/28/00 REVIEW: ☑ Approved ☐ Disapproved By: Doug Smith

Site visits
Date 9/28/00 By DS
Date ____/____/____ By _____
Date ____/____/____ By _____

Installation final written approval
Date 9/28/00 By DS

Return application to: Lincoln-Lancaster County Health Department - Environmental Health Division
3140 "N" Street, Lincoln, NE 68510
Phone: 441-8022

Business Office Use Only
Received: Date: 9/28/00 Amount $100.00 Check No. 4057 Initials CW

White - Division Copy Pink - Business Office Revised 9/00

Lincoln-Lancaster County Health Department
Environmental Health Division
3140 "N" Street • Lincoln, NE 68510-1514
Phone: 402-441-8022

D

Permit Number: 00390068l

Sewage Disposal System

As Built Plans & Specifications

Date 9-28-00

System Location (Indicate correct number and street)

Address W. Rokeby (no rural route) City Lincoln NE, Zip 68512

A. Building Sewer

1. Material: _____
   Diameter: _____ in.
2. Distance above basement floor: _____ in.
   or distance below basement floor: _____ in.
3. Distance between dwelling and septic tank: _____ ft.
4. Number of clean-outs: _____
5. Distances to: well or suction line _____ ft.
   stream _____ ft.
   pressure line _____ ft.
   property line _____ ft.

B. Septic Tank

1. Material: Concrete
   Number of compartments: 1
2. Capacity: 1005 gal.
3. Factory built: ☐ Yes ☒ No
4. Manholes: Over inlet, diameter 6 in.
   Over outlet, diameter — in.
   Riser: ☐ above ☐ below grade _____ in.
5. Inlet: ☐ baffle ☒ tee
6. Outlet: ☐ baffle ☒ tee
7. Depth to top of tank, below unfinished grade: 58 in.
8. Distances to: Well or suction line > 50 ft.
   Stream NA ft.
   Pressure line NA ft.
   Property line > 20 ft.

C. Distribution Box

1. Material: _____
   Number available outlets: _____
2. Factory built: ☐ Yes ☐ No
3. Distance from septic tank: _____ ft.

D. Absorption Field


(Provide as-built drawings on back of this form)

1. Type: ☒ Half rounds ☐ Perforated pipe
   Diameter of half round: 36
   or perforated pipe: _____
   Material: ☐ fiberglass ☐ plastic ☐ concrete
   ☐ other Infiltrator
2. Lateral lines: Number 1
   Length of each line: 25 ft. _____ ft.
   _____ ft. _____ ft., _____ ft.
3. Trench dimensions: Width 4 ft.
   Slope 4 in/100 ft.
   Average depth 47 in
4. Filter material: Road Gravel
   Depth of material _____ in.
5. Distances to: Well or suction line _____ ft.
   Stream _____ ft.
   Pressure line _____ ft.
   Property line _____ ft.

Indicate North with Arrow


Complete "As Built" drawing on back of this form.

Individual Sewage System Design (Example)

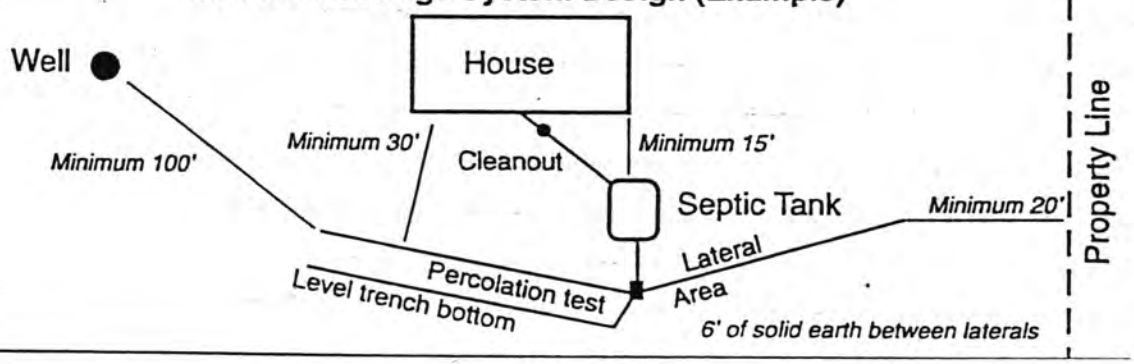

FORM 23-103 10-96

As Built Drawing

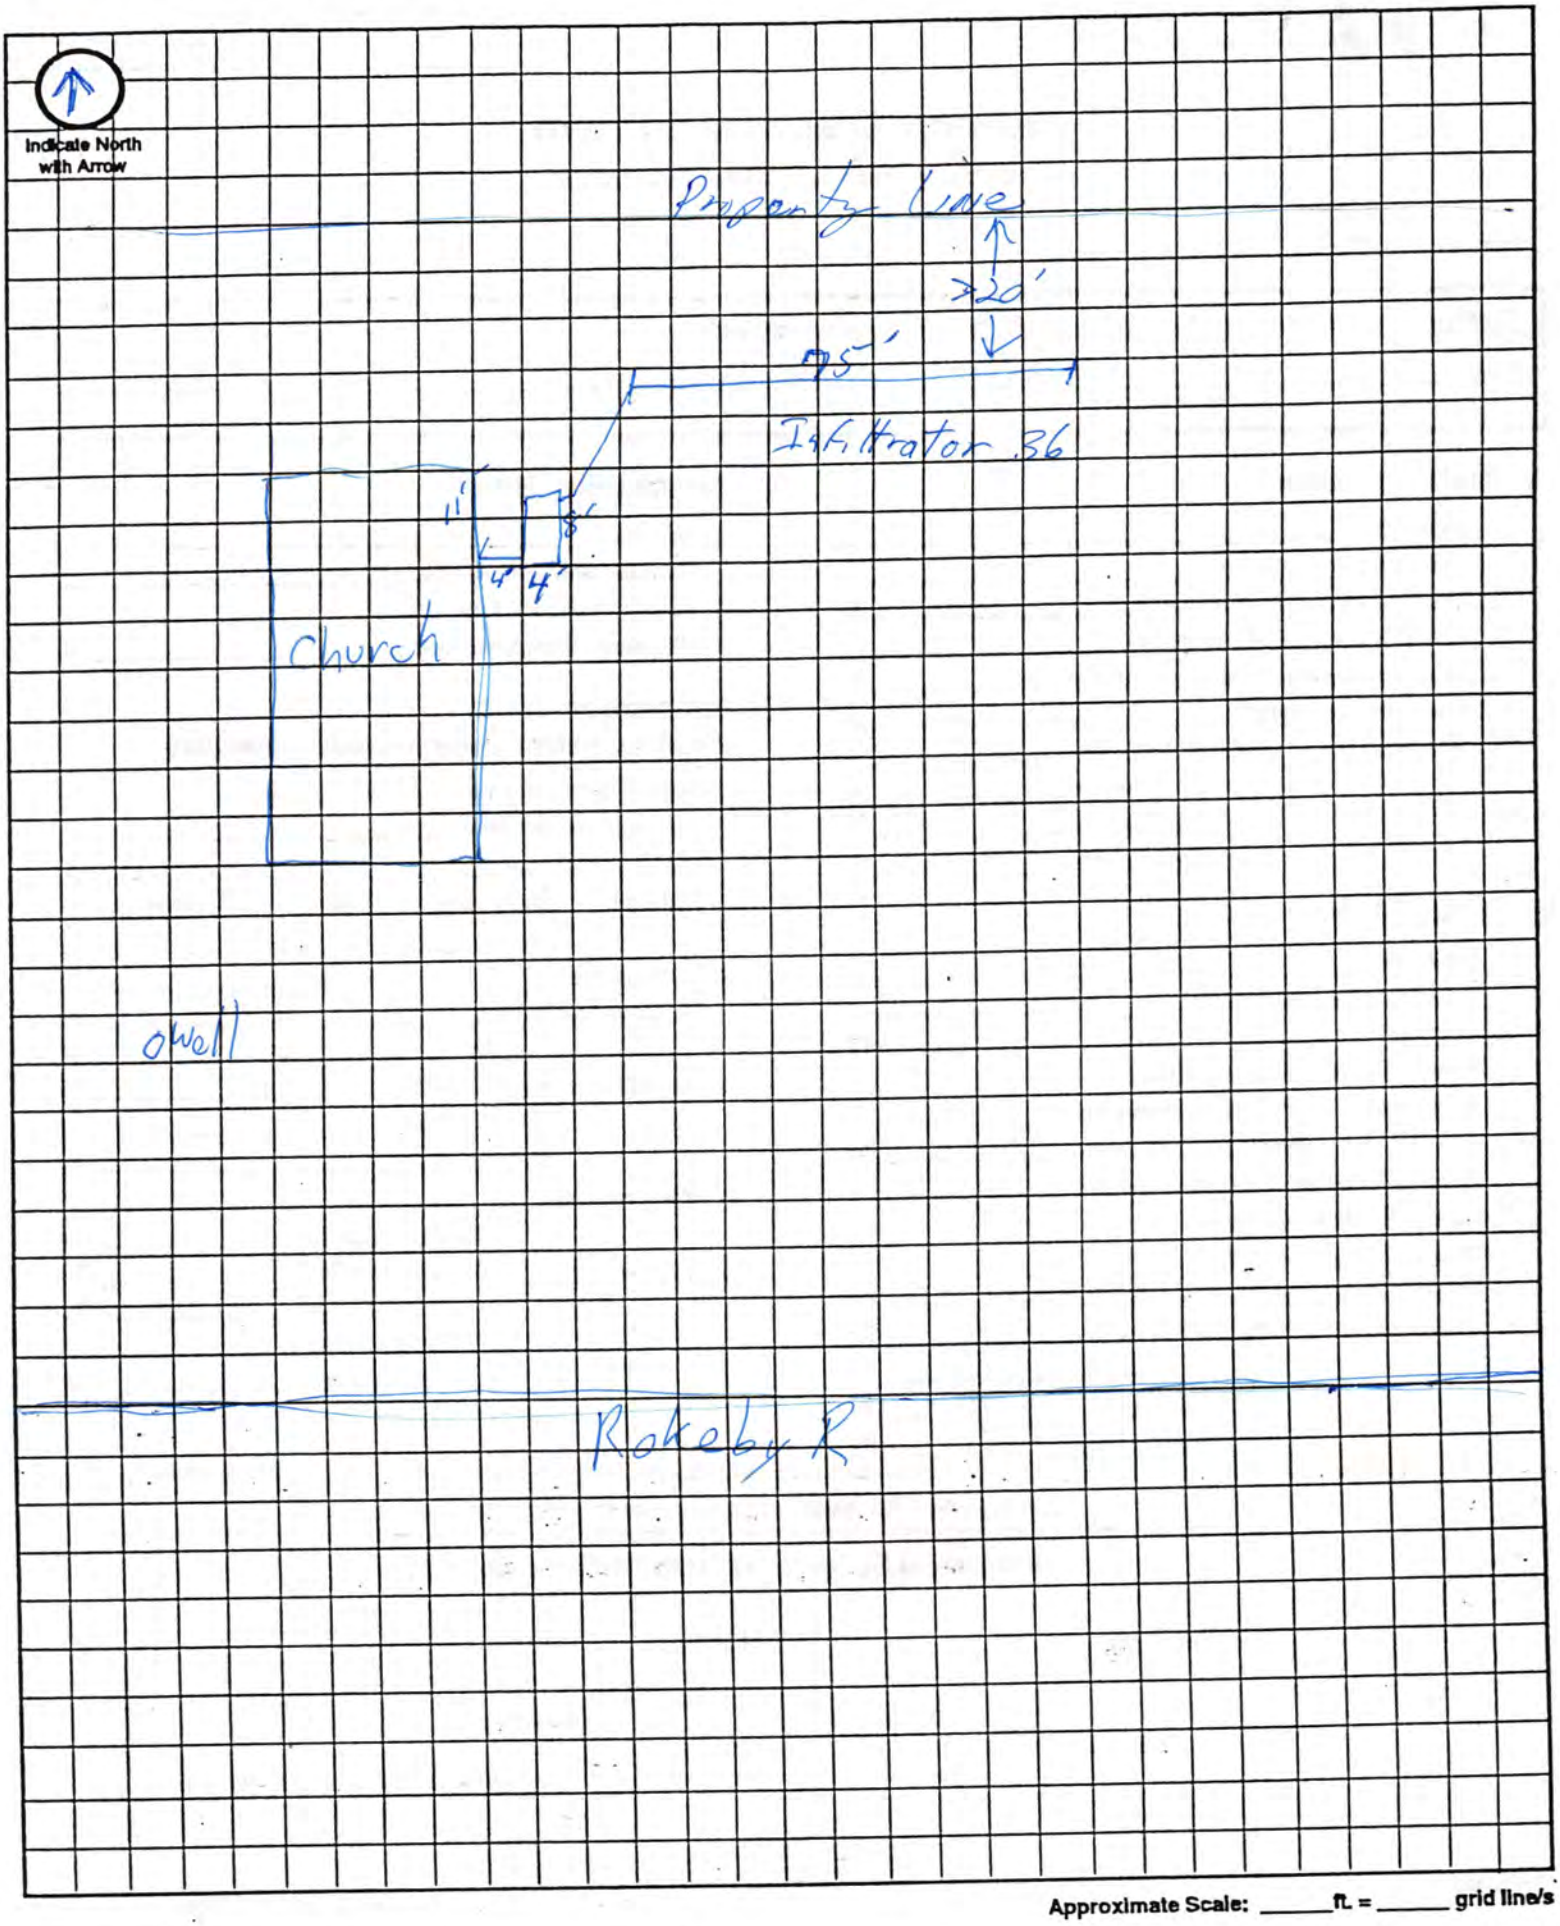

Approximate Scale: _____ ft. = _____ grid line/s
