LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

FILE NO. 1587-C

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION — TYPE OF PERMIT

February 23, 1980 — THIS PERMIT EXPIRES

Sintek Service Company — ISSUED TO

6710 North 7, Lincoln, NE — ADDRESS

T9N; R6E; Section 32; IT NW¼ of NE¼

LEGAL DESCRIPTION

REMARKS: NON-TRANSFERABLE

PERMIT	INSPECTION FEE	OCCUPATION TAX	TOTAL
$ 60.00	$	$	$ 60.00
ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE
	110.16	148.14	6-2

RECEIPTED BY — DATE — AMOUNT

VALID RECEIPT ONLY IF RECEIPTED IN THIS SPACE

HEALTH

ISSUING OFFICER

THIS PERMIT IS ISSUED AS PROVIDED BY COUNTY RESOLUTION NO. 2832

109-0977

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

A

FILING FEE: $ 60.00

FILE NO. 1587-C

DATE: 8-23-79

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 9N ; Range 6E ; Section 32 ; SEE ATTACHED
   Block _____ : Lot _____ : Addition _____
   Street Address _____

2. Property Use: Residential ☒ ; Commercial ☐ Other Use ☐
   No. of Bedrooms 3 . Describe _____

3. Type of Individual Sewage Disposal System: Septic Tank ☒ ; Other ☐

4. Distance to public sewer: _____ ft. ~~TO BE DETERMINED BY PERCOLATION TEST~~

Smith & Dennis Co
Signature of Applicant (Owner or Lessee)

6710 N 7th
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. 8/23/79. Date Frwd. 8/23/79. ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Hood

2. Supt. Bldg. Insp.: or Village Clerk: Date Rec'd. _____. Date Frwd. _____. ACTION: Approved ☐ Disapproved ☐ Signature: Dave S. Keese

3. City or County Engineer: Date Rec'd. 8-23-79. Date Frwd. 8-23-79. ACTION: Approved ☐ Disapproved ☐ Signature: Henry Graff

REMARKS OR REASONS FOR DISAPPROVAL _____

Site Visits:
Date: 9/20/79 by: J.C.H.
Date: _____ by: _____
Date: _____ by: _____

INSTALLATION FINAL WRITTEN APPROVAL
Date: 9/21/79 By: J. C. Hood *

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

* Provided water service is moved to 10' from sewer.

FORM 20105-0477
SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150 and County Resolution No. 2832)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

B

FILE NO. 1587-C

PROPERTY WHERE SOIL TESTED:

Location: Township_____; Range_____; Section & ¼ Section_____.
Property Dimensions: _____ft. x _____ft. Area:_____acres. (Attach Sheet C with sketch of property).
Soil Type: Silty Clay ☐ ; Silty Clay Loam ☒ ; Sandy Loam ☐ ; Silt Loam ☐ ; Clay Loam ☐ .
Dates of Tests: 9-14-79 to 9-15-79. Weather: Precip. NO Temp. 80.

OWNER: Sinclair Farms

Address: 6710 N 7th

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
		Pre-Saturation Period				Percolation Readings						Results	
		Start		End		Start			End				
Hold No.	Hole Depth (in.)	Date (Mo./Day)	Time (Hr./Min.)	Date (Mo./Day)	Time (Hr./Min.)	Date (Mo./Day)	Time (Hr./Min.)	Water Level (in.)	Time (Hr./Day)	Water Level (in.)	Elapsed Time (Min.)	Water Level Drop (in.)	Percolation Rates (Min./in.)
1	22	9-14	1 PM	9-14-79	5 PM	9-15	10 AM	6	11 AM	4 3/8	60	1 1/8	
2	22									4 3/8	60	1 1/8	
3	22									4 3/8	60	1 1/8	
4	22									5	60	1	
5	22									4 3/8	60	1 1/8	
6	22									4 3/8	60	1 1/8	

9-14-79 Bob 9-15-79 Larry Sinclair Farms Co.
Signature of Person Conducting Test

Sum of Percolation Rates: _____
Average of Rates: _____
Mean of Rates: _____

Address 6710 N 7 Phone 475-1486

(Do not write below this line)

REVIEWING ACTION

Remarks: _____

Soil Type (SCS): _____

Date: September 17, 1979

Approved Percolation Rate (a)
A. 56 min./inch
B. _____ min./inch
C. _____ min./inch

Jerrold C. Hood
Signature of Reviewing Official

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

D

DATE: 9-22-79

FILE NO. _____


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material Pla ; Diameter 4 in.
2. Distance above basement floor _____ in., or below basement floor 14 in.
3. Distance between dwelling and septic tank 148 ft.
4. Number of clean-outs 1 .
5. Distances to:
Well or Suction Line 20 ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line over 100 ft.

B. SEPTIC TANK:
1. Material Conc ; No. of compartments _____ .
2. Capacity 1000 gals.;
3. Factory Built: Yes ☒ No ☐
(Company Pre cast)
4. Manholes: Over Inlet; diam. 6 in. covers
Over Outlet; diam. 6 in. 24
Riser Above ☐ Below ☐ Grade 8 in.
5. Inlet: Baffle ☒ ; or Tee ☐
6. Outlet: Baffle ☒ ; or Tee ☐
7. Depth of top of tank below finished grade 8 in.
8. Distances to:
Well or Suction Line over 100 ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

C. DISTRIBUTION BOX:
1. Material Plastic ; Number - available outlets 7 .
2. Factory Built: Yes ☒ No ☐
(Company Hand Core)
3. Distance from Septic Tank 8 ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☐ Perforated Pipe ☒
Diameter of Half Round _____ or Perforated Pipe Yes .
Material: fiberglass ☐ ; plastic ☒ ; concrete ☐ ; other _____ .
2. Lateral Lines:
Number 4 ; Length of each line 60 , 80 , 80 , 100 , _____ ft.;
Total length of laterals 320 ft.;
Distance between lateral lines 20 ft.
3. Trench dimensions: Width 36 ft.; Slope 2 in/100 ft.; Average Depth 20 in.
4. Filter Material: Road Gravel
Depth of Material 12 in.
5. Distances to:
Well or Suction Line 110 ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

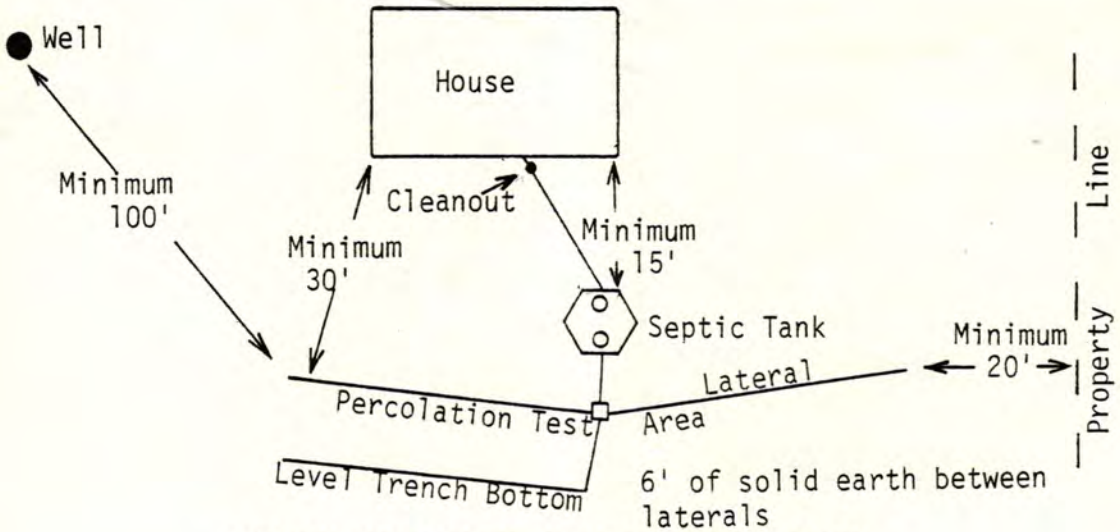

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

AS BUILT DRAWING OF SYSTEM

DATE 9-22-79 INSTALLER Smith, Inc

