LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

2200 ST. MARYS
LINCOLN, NEBRASKA 68502

FILE NO. 2619-C

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION — TYPE OF PERMIT

JULY 14, 1988 — THIS PERMIT EXPIRES

KENNETH W. SHERWOOD — ISSUED TO

2011 W. ROKEBY RD. LINCOLN, NE 68523 — ADDRESS

T9N; R6E; Sec 33; Lot 3 I.T.; 2011 W. Rokeby Rd, Lincoln
LEGAL DESCRIPTION

REMARKS: NON-TRANSFERABLE NEW CONSTRUCTION

PERMIT	INSPECTION FEE	OCCUPATION TAX	TOTAL
$ 60.00	$	$	$ 60.00
ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE
	110.16	148.14	6-2

RECEIPTED BY	DATE	AMOUNT
MG	1-15-88	

VALID RECEIPT ONLY IF RECEIPTED IN THIS SPACE

HEALTH
ISSUING OFFICER

THIS PERMIT IS ISSUED AS PROVIDED BY COUNTY RESOLUTION NO. 2832

20109-0977

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

A

FILING FEE: $ 60.00

FILE NO. 2619-C

DATE: Jan. 14, 1988

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 9 N. ; Range 6 E ; Section 33 ; Block _____ : Lot 3, I.T. : Addition _____
   Street Address 2011 W. ROKEBY ROAD LINCOLN, NE 68523

2. Property Use: Residential ☐ ; Commercial ☐ Other Use ☒
   No. of Bedrooms 0 . Describe Craft shop and summer Kitchen

3. Type of Individual Sewage Disposal System: Septic Tank ☒ ; Other ☐

4. Distance to public sewer: N/A ft.

Kenneth W. Sherwood
Signature of Applicant (Owner or Lessee)

2011 W. Rokeby Rd. Lincoln, Ne. 68523
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. 1/14/88 . Date Frwd. 1/14/88 . ACTION: Approved ☒ Disapproved ☐ Signature: Jerold C. Hood

2. Supt. Bldg. Insp.: or Village Clerk Date Rec'd. 1-14-88 . Date Frwd. 1-14-88 . ACTION: Approved ☒ Disapproved ☐ Signature: Paul Bouma

3. City or County Engineer : Date Rec'd. 1/14/88 . Date Frwd. _____ . ACTION: Approved ☐ Disapproved ☐ Signature: [illegible]

REMARKS OR REASONS FOR DISAPPROVAL _____

Site Visits:
Date: 5/5/88 by: J.C.H.
Date: _____ by: _____
Date: _____ by: _____

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

INSTALLATION FINAL WRITTEN APPROVAL *
Date: _____ By: _____

* C W/OI

FORM 23-43

FORM 20102-0477
PRELIMINARY PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒


LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

C

Sketch of property showing Percolation Test hole locations, well, residence, direction and property line.

FILE NO. 2619-C

Indicate on sketch if residence and well are exisiting or proposed.

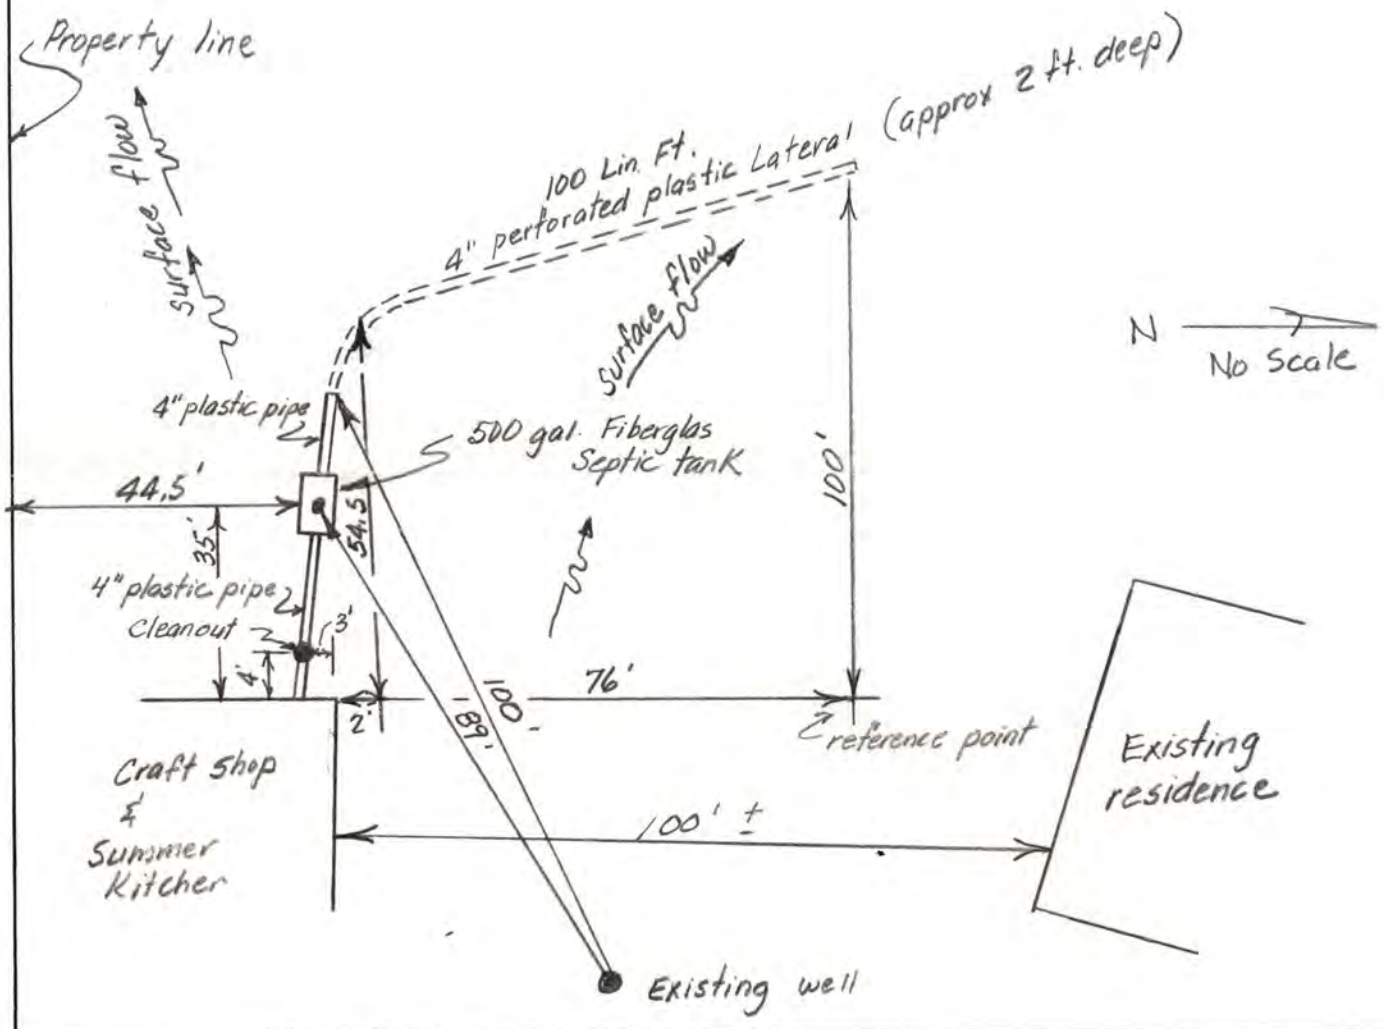

REVIEWING ACTION

Remarks: _____

_____

Date: _____

Minimum Design Requirement
1. Capacity of Septic Tank _____ gals.
2. Total Length of Laterals _____ ft.
3. With a Trench Width of _____ in.
4. Total Area of Lateral needed _____ sq.ft.

_____
Signature of Reviewing Official

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

D

DATE: 1/14/88

FILE NO. 2619-C


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material plastic ; Diameter 3" in.
2. Distance above basement floor ____ in., or below basement floor 12± in.
3. Distance between dwelling and septic tank 35 ft.
4. Number of clean-outs 1 .
5. Distances to: Well or Suction Line 50± ft.; Stream ____ ft.; Pressure Line ____ ft.; Property Line ____ ft.

B. SEPTIC TANK:
1. Material Fiberglas ; No. of compartments ____ .
2. Capacity 500 gals.;
3. Factory Built: Yes ☒ No ☐ (Company ____)
4. Manholes: Over Inlet; diam. ____ in. Over Outlet; diam. ____ in. Riser Above ☐ Below ☒ Grade 12± in.
5. Inlet: Baffle ☐ ; or Tee ☐
6. Outlet: Baffle ☐ ; or Tee ☐
7. Depth of top of tank below finished grade 12± in.
8. Distances to: Well or Suction Line 89 ft.; Stream ____ ft.; Pressure Line ____ ft.; Property Line 44.5 ft.

C. DISTRIBUTION BOX:
1. Material None ; Number - available outlets ____ .
2. Factory Built: Yes ☐ No ☐ (Company ____)
3. Distance from Septic Tank ____ ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☐ Perforated Pipe ☒ Diameter of Half Round ____ or Perforated Pipe 4" . Material: fiberglass ☐ ; plastic ☒ ; concrete ☐ ; other ____ .
2. Lateral Lines: Number 1 ; Length of each line 100 , ____ , ____ , ____ , ____ ft.; Total length of laterals 100 ft.; Distance between lateral lines ____ ft.
3. Trench dimensions: Width 2 ft.; Slope ____ in/100 ft.; Average Depth 24 in.
4. Filter Material: gravel Depth of Material 12± in. (used 16 tons)
5. Distances to: Well or Suction Line 100' min. ft.; Stream ____ ft.; Pressure Line ____ ft.; Property Line 50 ft.

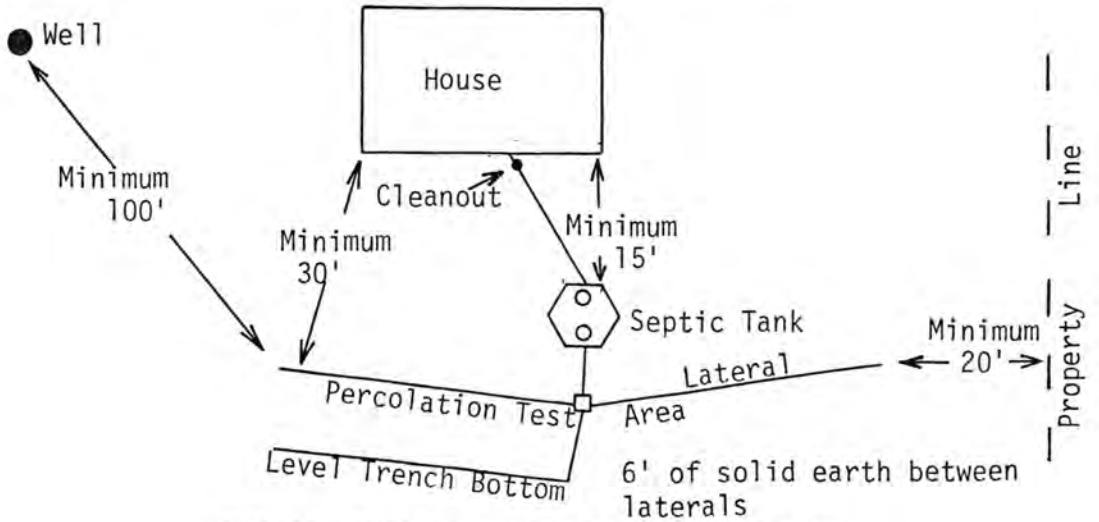

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN
