LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

ENVIRONMENTAL HEALTH DIVISION

2200 St. Marys Ave Lincoln, NE 68502-3785 (402) 441-8000

NON TRANSFERABLE

P E R M I T

Permit
SEWAGE INSTALLATION

No. 93380102201

Issued 07/12/93
Expires 01/12/94
Revenue Code 18754

Establishment
MIKE REZAC
T9N R6E SEC 33
LOT 21
10920 SW 27 STREET

FEES: $150.00

TOTAL $150.00

Permittee
MIKE REZAC
1830 W BURNHAM
LINCOLN NE 68522

Issued By M. Jane Ford
Health Director

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW
"POST IN A PROMINENT PLACE"

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

A

FILING FEE: $_____

FILE NO._____

Building permit # BC930062

DATE: 7/9/93

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. ~~33~~ 9N ; Range 6E ; Section 33 ;
   Block _____ : Lot 21 I.T. : Addition _____
   Street Address 10920 SW 27th ST.

2. Property Use: Residential ☑ ; Commercial ☐ Other Use ☐
   No. of Bedrooms 3 . Describe _____

3. Type of Individual Sewage Disposal System: Septic Tank ☑ ; Other ☐

4. Distance to public sewer: _____ ft. WILL INSTALL WHATEVER SOIL PERC TEST INDICATES

Mike Rezac
Signature of Applicant (Owner or Lessee)

1830 West Burnham.
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. 7/9/93. Date Frwd. 7/12/93. ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Hood

2. Supt. Bldg. Insp.: or Village Clerk: Date Rec'd. _____. Date Frwd. _____. ACTION: Approved ☑ Disapproved ☐ Signature: [illegible]

3. City or County Engineer: Date Rec'd. 7/12/93. Date Frwd. _____. ACTION: Approved ☒ Disapproved ☐ Signature: [illegible]

REMARKS OR REASONS FOR DISAPPROVAL _____

Site Visits:
Date: 1/12/94 by: J.C.H.
Date: _____ by: _____
Date: _____ by: _____

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

INSTALLATION FINAL WRITTEN APPROVAL X
Date: 1/12/94 By: Jerrold C. Hood

X EXPERIMENTAL SYSTEM HENCE PROVISIONAL APPROVAL.

FORM 23-43

10920 SW 27th
Rezac Constr.

Installed By Vogt Tilt
1-12-93



012

Lincoln-Lancaster County Health Department

2200 St. Mary's Avenue, Lincoln, Nebraska 68502 Phone: 441-8022

REAL ESTATE TRANSFER/LOAN APPROVAL FORM

This form must be completed and returned to request a real estate transfer inspection.

MAKE CHECK PAYABLE TO: Lincoln-Lancaster County Health Department or LLCHD

☑ Enclosed is $150.00. Allow two weeks for processing. Incomplete information will delay processing.

☐ Evaluation of the Individual Water System ☐ Evaluation of the Sewage Disposal System

Legal Description of Property: Street Address 10920 SW 27th

Twp 9N Range 6E Section 33 1/4 ___ 1/4 ROKEBY Block ___ Lot ___ Addition ___

Directions to Property 1/4 MILE south on ROKEBY RD & Right WEST 27th STREET INTERSECTION. EAST SIDE, DRIVE 1/4 mile Long. ADDRESS on Elect Pole.

Location of Well Back of Home Tap Location: Inside ☐ Outside ☑

Location of Sewage System ___ Year Installed 1994

	NAME	ADDRESS	PHONE
Present Owner:	REZAC CONST		423-2212 432-5080
Tenant/Buyer:	STEVE McDONALD		
Return to:			

Signature of Applicant M Rezac Address 1830 WEST BURNHAM Lincoln NE 68522 Date 1/11/94

HEALTH DEPARTMENT USE ONLY

Date Received 1/11/94 Received $150.00 Check ☒ Cash ☐

PRELIMINARY STATUS--By JERROLD HOOD **DATE:** 1/12/94

WATER SYSTEM:	Approved	Disapproved	SEWAGE SYSTEM	Additional Site Visits
Construction	☒	☐	Approved ☐	Date___/___/___by___
Bacteria	☒ 0 /ml	☐ ___ /ml	Provisional ☒	Date___/___/___by___
Nitrate	☒ 0.2 ppm	☐ ___ ppm	Disapproved ☐	Date___/___/___by___

Comments: SEWAGE SYSTEM IS OF AN EXPERIMENTAL VARIETY HENCE APPROVAL IS PROVISIONAL.

See Attached Letter ☐

FINAL STATUS

WATER SYSTEM: Approved: ☒ **SEWAGE DISPOSAL SYSTEM** Approved: ☐ Provisional Approval: ☑

Approved by Jerrold C. Hood R.E.H.S. Date 1/18/94

Approval or disapproval is based on State and local standards for construction, location and water quality. Inspection is based on visible construction and operation at the time of inspection. Approval or provisional approval does not imply or express a guarantee of system operations.

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

D

DATE: _____

FILE NO. _____


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material PVC ; Diameter 4 in.
2. Distance above basement floor _____ in., or below basement floor 18 in.
3. Distance between dwelling and septic tank 114 ft.
4. Number of clean-outs 2
5. Distances to:
Well or Suction Line 30 ft.; Stream NA ft.; Pressure Line 20 ft.; Property Line 100+ ft.

B. SEPTIC TANK:
1. Material Concrete ; No. of compartments 1 .
2. Capacity 1000 gals.;
3. Factory Built: Yes ☒ No ☐
(Company Pre-Cast)
4. Manholes: Over Inlet; diam. 16 in.
Over Outlet; diam. 10 in.
Riser Above ☐ Below ☐ Grade ___ in.
5. Inlet: Baffle ☑ ; or Tee ☐
6. Outlet: Baffle ☑ ; or Tee ☐
7. Depth of top of tank below finished grade 16 in.
8. Distances to:
Well or Suction Line 100+ ft.; Stream NA ft.; Pressure Line 100+ ft.; Property Line 100+ ft.

C. DISTRIBUTION BOX:
1. Material Concrete ; Number - available outlets 5 .
2. Factory Built: Yes ☒ No ☐
(Company Pre-Cast)
3. Distance from Septic Tank 23 ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☒ Perforated Pipe ☐
Diameter of Half Round 22" or
Perforated Pipe _____.
Material: fiberglass ☐ ; plastic ☐ ; concrete ☒ ; other _____.
2. Lateral Lines:
Number 2 ; Length of each line 100 , 100 , _____ , _____ , _____ ft.;
Total length of laterals _____ ft.;
Distance between lateral lines 16 ft.
3. Trench dimensions: Width 8 ft.; Slope 2 in/100 ft.; Average Depth 36 in.
4. Filter Material: ~~30~~ 6" Gravel - Scraped Bottom
Depth of Material 30 in.
5. Distances to:
Well or Suction Line 100+ ft.; Stream NA ft.; Pressure Line 100+ ft.; Property Line 80+ ft.

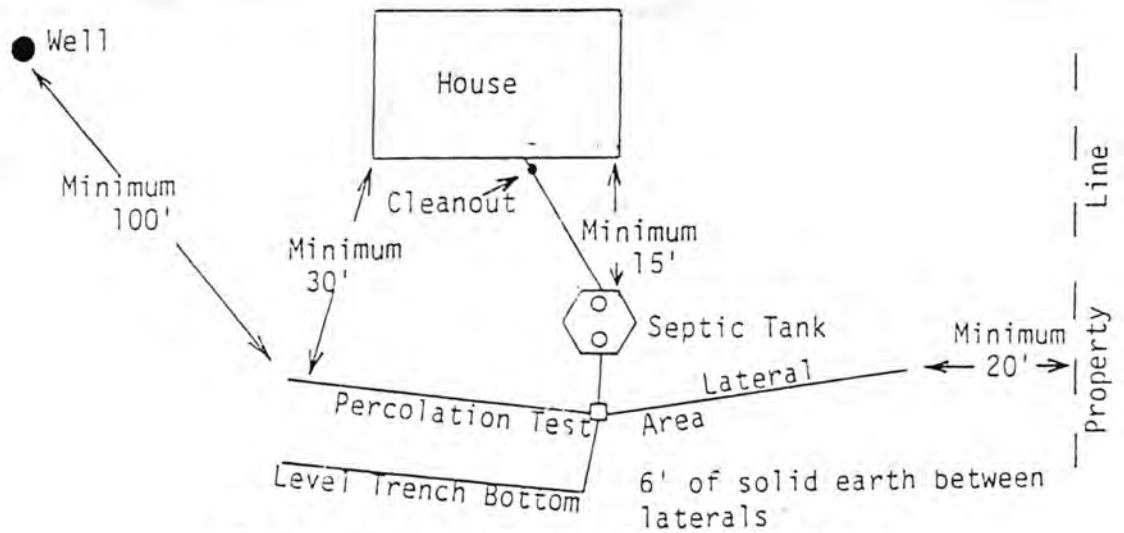

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN
