LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

3140 "N" STREET ENVIRONMENTAL HEALTH DIVISION (402) 441-8000
NON TRANSFERABLE Lincoln, NE 68510-1514
PERMIT

Permit No. 95380128201

SEWAGE INSTALLATION

Issued 03/10/95
Expires 09/10/96
Revenue Code 18754

CLOSED

Establishment

ROKEBY SCHOOL #152
T9N R[illegible]E SEC 3[illegible]
LOT 1

FEES: $150.00

TOTAL $150.00

Permittee

ROKEBY SCHOOL #152
RR0001
BOX 00419
LINCOLN NE 68523

Issued By M. Jane Ford
Health Director

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW "POST IN A PROMINENT PLACE"

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☒
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
~~2200 St. Marys Avenue~~ 3140 N
Lincoln, Nebraska ~~68502~~ 68510
Phone: ~~471-7800~~ 441-8029

A

FILING FEE: $ 150.00

FILE NO. RECEIVED JAN 19 1995

DATE: 1-10-95

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 9 N ; Range 6E ; Section 34 NW¼
   Block _____ : Lot 1 F.T. : Addition _____
   Street Address _____
2. Property Use: Residential ☐ ; Commercial ☐ ; Other Use ☒
   No. of Bedrooms _____. Describe School House, No Kitchen 25 people
3. Type of Individual Sewage Disposal System: Septic Tank ☒ ; Other ☐
4. Distance to public sewer: N A ft.

Brad Southwick
Signature of Applicant (Owner or Lessee)
ROKEBY SCHOOL DISTRICT #152
RR#1, Box 419
Address LINCOLN, NEBRASKA 68523

(Do not write below this double line)

1. Health Department: Date Rec'd. 3/10/95. Date Frwd. 3/10/95. ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Hood
2. Supt. Bldg. Insp.: or Village Clerk Date Rec'd. 3/10/95. Date Frwd. 3/10/95. ACTION: Approved ☒ Disapproved ☐ Signature: [signature]
3. City or County Engineer: Date Rec'd. 3-10-95. Date Frwd. 3-10-95. ACTION: Approved ☒ Disapproved ☐ Signature: [signature]

REMARKS OR REASONS FOR DISAPPROVAL _____

Site Visits:
Date: 12-2-95 by: P.D. am
Date: 12-2-95 by: P.D. pm
Date: _____ by: _____

INSTALLATION FINAL WRITTEN APPROVAL
Date: 3-27-95 By: [signature]

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

FORM 23 43

FORM 20105-0477
SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150 and County Resolution No. 2832)

RECEIVED MAR 3 1995
LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

B

FILE NO: _____

PROPERTY WHERE SOIL TESTED:

Location: Township 9N ; Range 6E ; Section & ¼ Section 34.
Property Dimensions: _____ ft. x _____ ft. Area: _____ acres. (Attach Sheet C with sketch of property).
Soil Type: Silty Clay ☐ ; Silty Clay Loam ☒ ; Sandy Loam ☐ ; Silt Loam ☐ ; Clay Loam ☐ .
Dates of Tests: 3-28 to 3-29-94. Weather: Precip. 0 Temp. 40s. wtr

OWNER: Rokeby School
Address: Rokeby, Ne 68522

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
Hold No.	Hole Depth (in.)	Pre-Saturation Period Start Date (Mo./Day)	Start Time (Hr./Min.)	End Date (Mo./Day)	End Time (Hr./Min.)	Percolation Readings Start Date (Mo./Day)	Start Time (Hr./Min.)	Start Water Level (in.)	End Time (Hr./Day)	End Water Level (in.)	Elapsed Time (Min.)	Results Water Level Drop (in.)	Percolation Rates (Min./in.)
1	36	3-28	7:30	3-29	8:30						30	½	
2	↓		AM		AM							¾	
3												⅝	
4												¾	
5												⅝	
6												⅝	

Sum of Percolation Rates: 3.875
Average of Rates: .646
Mean of Rates: _____

Brad Southwell
Signature of Person Conducting Test

Address 17201 S 72 Hickman Phone 475-2462

(Do not write below this line)

REVIEWING ACTION

Remarks: _____
Soil Type (SCS): Wymore Silty Clay Loam
Date: March 10, 1995

Approved Percolation Rate (a)
A. 48 min./inch
B. _____ min./inch
C. _____ min./inch

Gerrold C. Hood
Signature of Reviewing Official

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

D

DATE: _____

FILE NO. _____


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material CPVC ; Diameter 4" in.
2. Distance above basement floor _____ in., or below basement floor _____ in.
3. Distance between dwelling and septic tank 60 ft.
4. Number of clean-outs 1 .
5. Distances to: Well or Suction Line >100' ft.; Stream N/A ft.; Pressure Line _____ ft.; Property Line >5' ft.


B. SEPTIC TANK:
1. Material Concrete ; No. of compartments 1 .
2. Capacity 1000 gals.;
3. Factory Built: Yes ☒ No ☐ (Company Pre Cast Products)
4. Manholes: Over Inlet; diam. 10 in. Over Outlet; diam. 15 in. Riser Above ☐ Below ☐ Grade _____ in.
5. Inlet: Baffle ☒ ; or Tee ☐
6. Outlet: Baffle ☒ ; or Tee ☐
7. Depth of top of tank below finished grade 12-15 in.
8. Distances to: Well or Suction Line _____ ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

C. DISTRIBUTION BOX:
1. Material PVC ; Number available outlets 5 .
2. Factory Built: Yes ☒ No ☐ (Company _____)
3. Distance from Septic Tank 38 ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☐ Perforated Pipe ☒ Diameter of Half Round _____ or Perforated Pipe 4" . Material: fiberglass ☐ ; plastic ☒ ; concrete ☐ ; other _____ .
2. Lateral Lines: Number 2 ; Length of each line 100 , 70 , _____ , _____ , _____ ft.; Total length of laterals _____ ft.; Distance between lateral lines 15 ft.
3. Trench dimensions: Width 3 ft.; Slope _____ in/100 ft.; Average Depth _____ in.
4. Filter Material: Road Gravel Depth of Material 14 in.
5. Distances to: Well or Suction Line >100 ft.; Stream N/A ft.; Pressure Line _____ ft.; Property Line 20 ft.

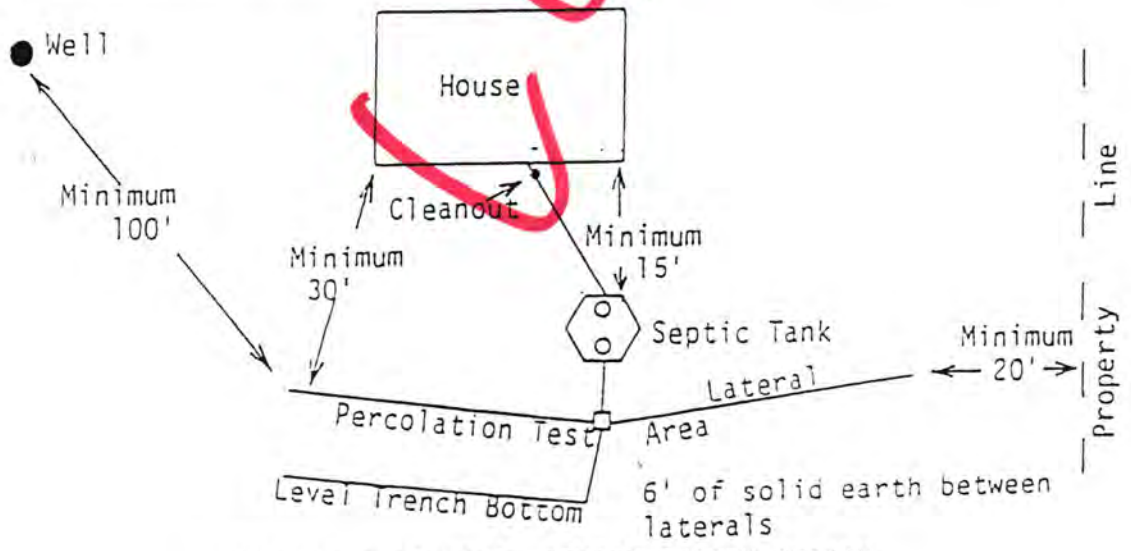

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

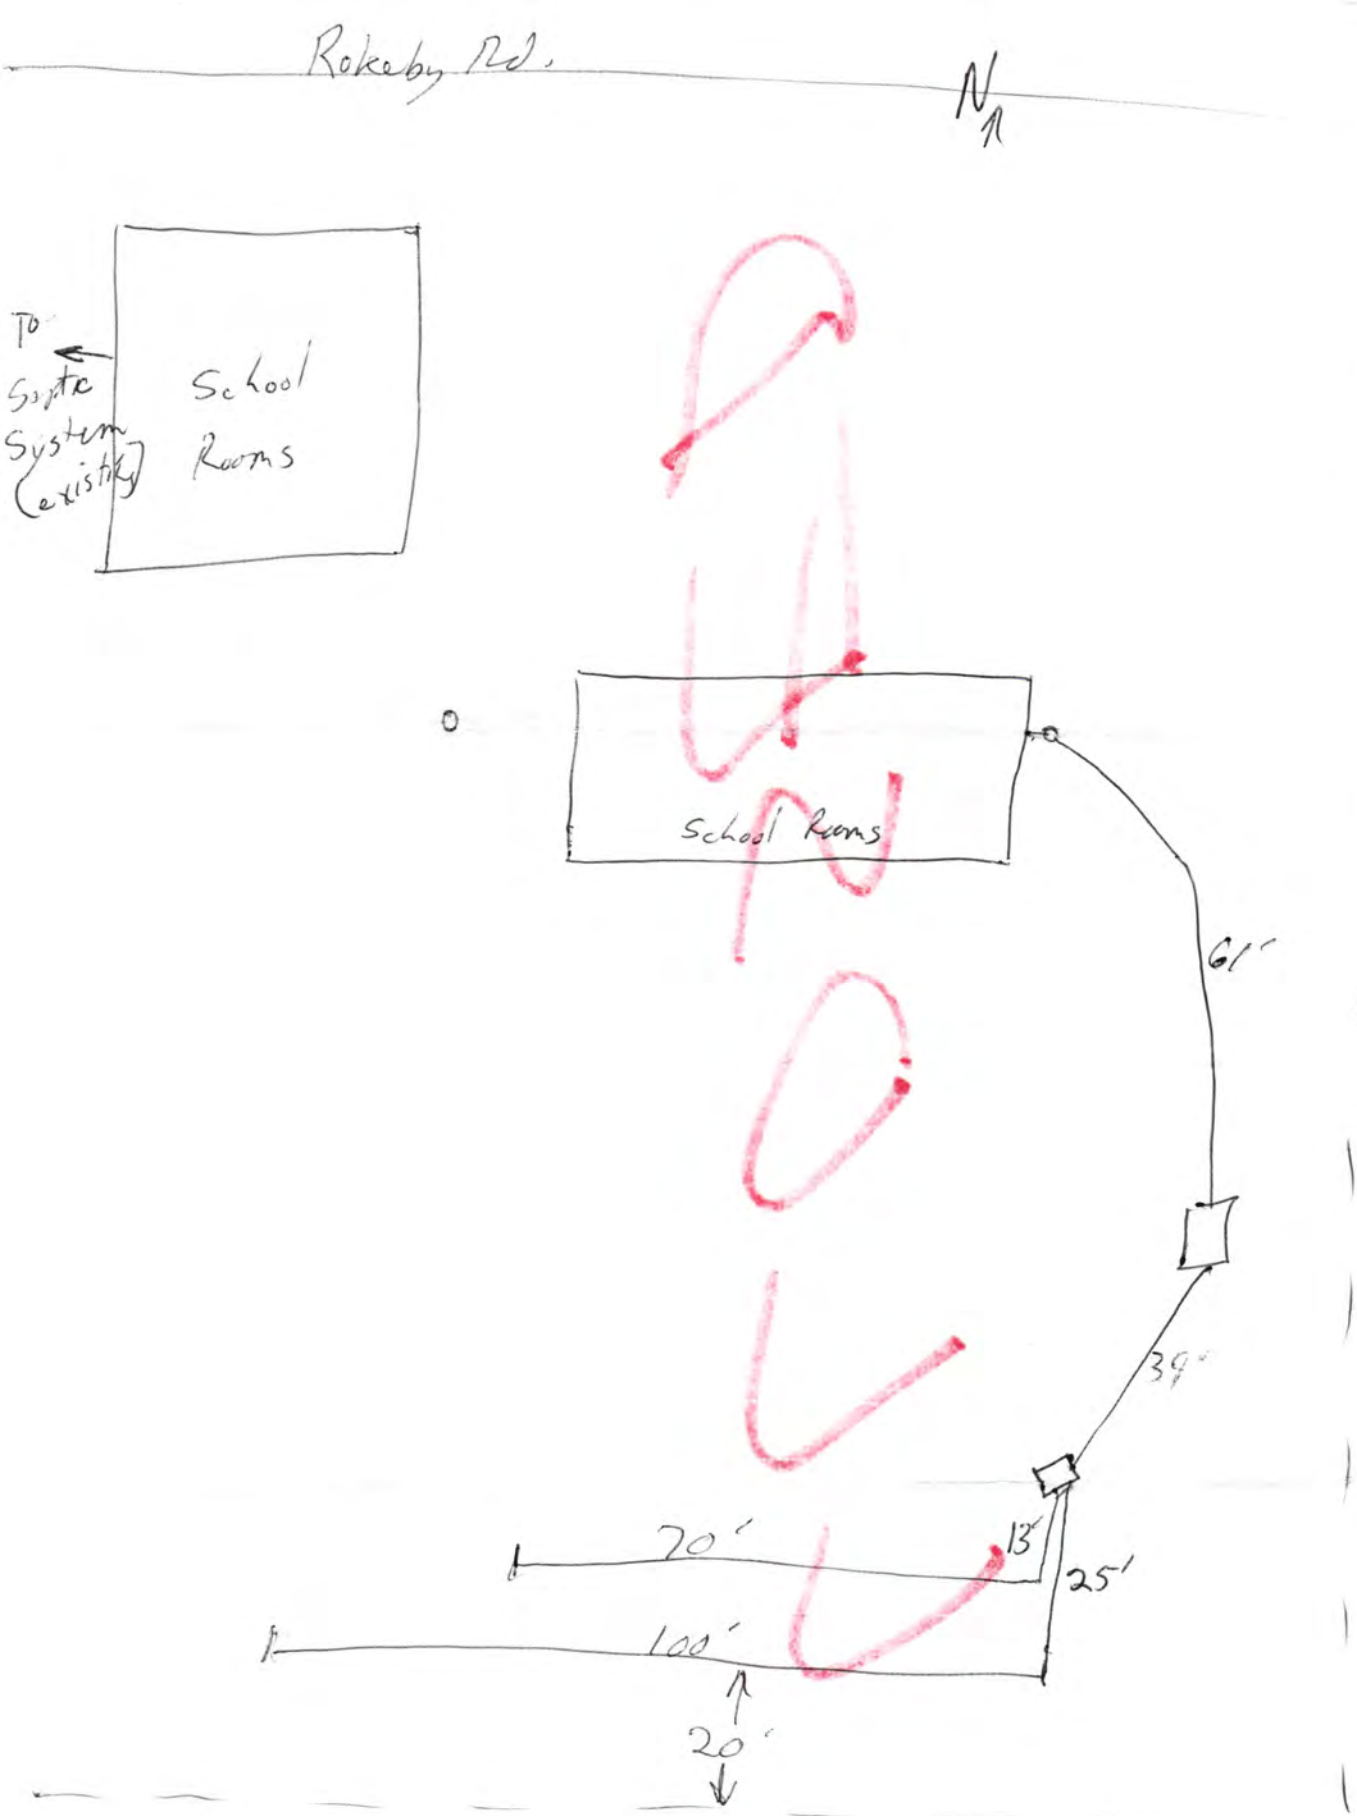
Rokeby Rd.
N
To Septic System (existing)
School Rooms
School Rooms
61'
39'
13'
70'
25'
100'
20'
