Lincoln-Lancaster County Health Department

ENVIRONMENTAL HEALTH DIVISION

3140 N STREET · LINCOLN, NE 68510-1514 (402) 441-8000

Permit

SEWAGE SYSTEM REPAIR
SEWAGE REPAIR

Permit # 00390068601

Issued 11/21/00
Expires 05/21/01
Revenue Code 3157

Establishment

QUALITY WATER SERVICES
T9N R6E SEC 36
1700 SALTILLO RD--ROCA

FEES: $100.00

Permitee

QUALITY WATER SERVICES
1700 SALTILLO RD
ROCA NE 68430

TOTAL: $100.00

Leon F. Vinci, MPH, Health Director

• POST IN A PROMINENT PLACE • NOT TRANSFERABLE

013924

Application to Alter, Extend or Repair an Individual Sewage Disposal System

☒ Municipal Code 24.38 ☐ County Resolution Number 2832

The undersigned hereby applies for a permit to: ☐ **ALTER** ☒ **EXTEND** ☐ **REPAIR** an existing Individual Sewage Disposal System, in conformance with appropriate Ordinance or Resolution, as described in this application and drawings attached hereto.

1. **Legal description of property:**
   Township 9N Range 6E Section 36 1/4 Section _____
   Block _____ Lot _____ Addition _____
   Parcel ID ____-____-_____-_____-_____ (i.e. 99-99-999-999-999)
   Street Address 1700 Saltillo Rd.

2. **Property use:** ☐ residential ☒ commercial ☐ other use
   Number of bedrooms _____ Describe _____

3. **Type of Present Individual Disposal System** ☒ septic tank ☐ lagoon ☐ other

4. **Description of proposed alteration, extension or repair** extend laterals with 200' of Infiltrator Eq 24 X 4' wide.

5. **Work to be done by:** ☐ owner ☒ contractor's name Southwick Sewer & Drain

6. **Estimated project:**
   a. Repair, replace or minor extension with a cost less than $400 (no fee required).
   b. Total cost is greater than $400 (Return fee with this application)
   c. A "construction permit" is required if the use, operation, location, or type of the system is being change.

Print Name Quality Water Services Address 1700 Saltillo Rd. Phone 423-0909
Applicant Signature (owner or lessee) _____

Please include the permit fee ($100) with this application
Fee must be included before the application will be processed. Incomplete information will delay processing

---

HEALTH DEPARTMENT USE ONLY

Date received 11/16/00 REVIEW: ☒ Approved ☐ Disapproved By: Jerrold C. Hood

OK BECOUSE REGULATION

Site visits
Date 11/16/00 By JCH
Date 11/17/00 By J.C.H.
Date ____/____/____ By _____

Installation final written approval
Date 12/4/00 By Jerrold C. Hood

Return application to: Lincoln-Lancaster County Health Department - Environmental Health Division
3140 "N" Street, Lincoln, NE 68510
Phone: 441-8022

Business Office Use Only
Received: Date: 11/16/00 Amount $100.00 Check No. 4113 Initials ns

White - Division Copy Pink - Business Office Revised 9/00

Lincoln-Lancaster County Health Department
Environmental Health Division
3140 "N" Street • Lincoln, NE 68510-1514
Phone: 402-441-8022

D

Permit Number:

Sewage Disposal System

As Built Plans & Specifications

Date 11-23-00

System Location (Indicate correct number and street)

Address 1700 Saltillo (no rural route) City Roca NE, Zip 68430

A. Building Sewer

1. Material: PVC
   Diameter: 4" in.
2. Distance above basement floor: _____ in.
   or distance below basement floor: _____ in.
3. Distance between dwelling and septic tank: 60 ft.
4. Number of clean-outs: 1
5. Distances to: well or suction line _____ ft.
   stream _____ ft.
   pressure line _____ ft.
   property line _____ ft.

B. Septic Tank

1. Material: Fiberglass
   Number of compartments: 1
2. Capacity: 1,000 gal.
3. Factory built: ☒ Yes ☐ No
4. Manholes: Over inlet, diameter 12 in.
   Over outlet, diameter _____ in.
   Riser: ☒ above ☐ below grade _____ in.
5. Inlet: ☒ baffle ☐ tee
6. Outlet: ☐ baffle ☒ tee
7. Depth to top of tank, below unfinished grade: 30 in.
8. Distances to: Well or suction line _____ ft.
   Stream _____ ft.
   Pressure line _____ ft.
   Property line _____ ft.

C. Distribution Box

1. Material: PVC
   Number available outlets: 5
2. Factory built: ☒ Yes ☐ No
3. Distance from septic tank: 4' ft.

D. Absorption Field


(Provide as-built drawings on back of this form)

1. Type: ☒ Half rounds ☐ Perforated pipe
   Diameter of half round: _____
   or perforated pipe: _____
   Material: ☒ fiberglass ☒ plastic ☐ concrete
   ☐ other _____
2. Lateral lines: Number 3
   Length of each line: 25' ft. 100 ft.
   100 ft. _____ ft., _____ ft.
3. Trench dimensions: Width 4' ft.
   Slope 3 in/100 ft.
   Average depth 40 in
4. Filter material: Road Gravel
   Depth of material _____ in.
5. Distances to: Well or suction line >100' ft.
   Stream NA ft.
   Pressure line NA ft.
   Property line ≈ 20' ft.

Complete "As Built" drawing on back of this form.


Indicate North with Arrow

Individual Sewage System Design (Example)

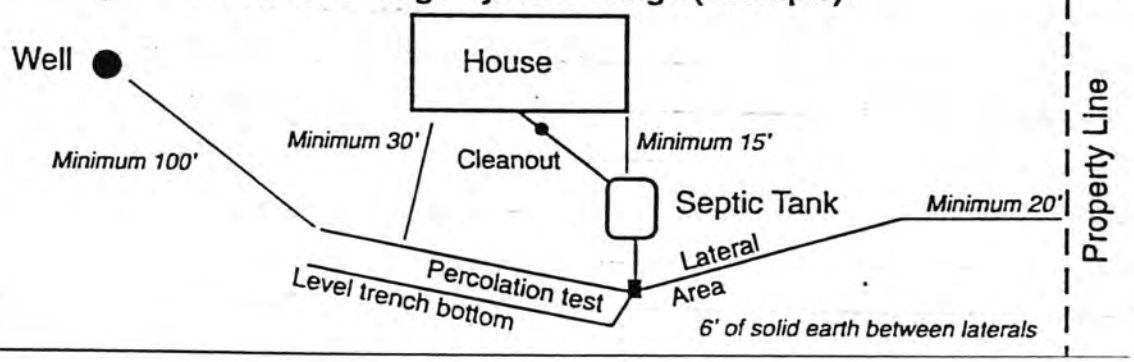

FORM 23-103 10-96

As Built Drawing

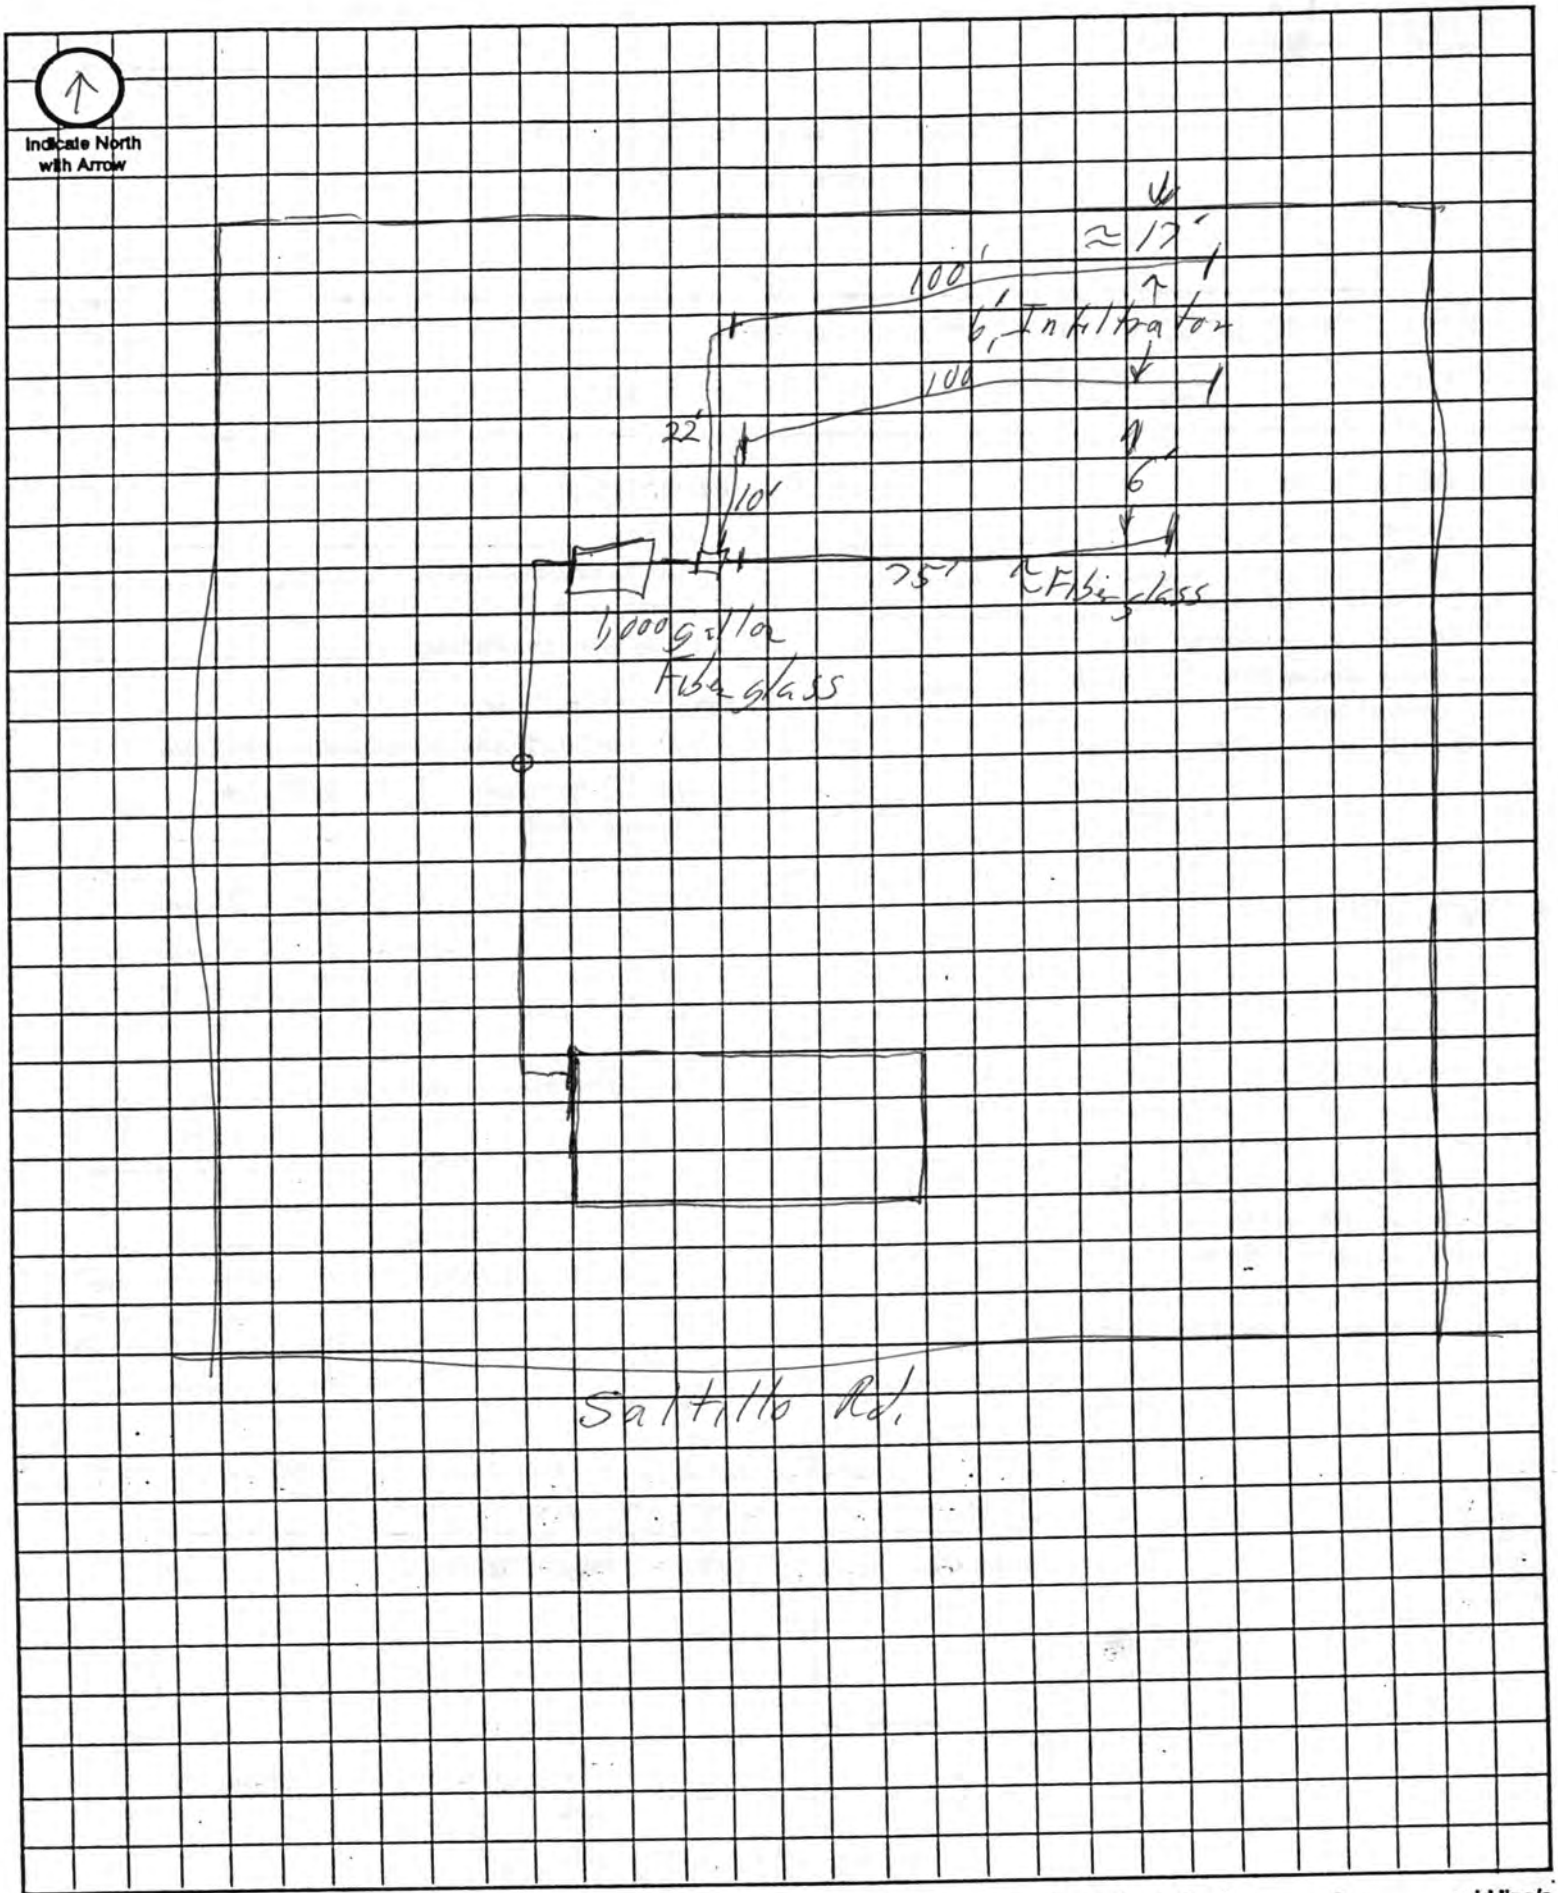

Approximate Scale: _____ ft. = _____ grid line/s
