CITY OF LINCOLN NEBRASKA

DEPARTMENT OF LICENSES AND PERMITS

FILE NO. 1455

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION — May 9, 1979

TYPE OF LICENSE OR PERMIT — THIS LICENSE OR PERMIT EXPIRES

Rick Nider — 5221 South 49 Street, Lincoln, NE

LICENSEE OR PERMITTEE — ADDRESS

T9N, R7E, Section 10, Block 1, Lot 4, Add. Mar-Lo-Heights —

NAME OF ESTABLISHMENT, IF ANY — ADDRESS

REMARKS: NON-TRANSFERABLE

PERMIT	INSPECTION FEE	OCCUPATION TAX	LICENSE	TOTAL
$ 30.00	$	$	$	$ 30.00

ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE
110.15	110.16	148.14	6-2

SERIAL NO.	DATE	AMOUNT
018754		

VALID RECEIPT ONLY IF MACHINE RECEIPTED IN THIS SPACE

APPLICATION

HEALTH

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☒
County Resolution No. 2832 ☐

LINCOLN-LANCAS[illegible] COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

FILING FEE: $ 30 00

FILE NO. 1455

DATE: 10-24-78

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 9 N ; Range 7 EAST ; Section 10 ;
Block 1 : Lot 4 : Addition Mar-bo-Heights
Street Address 4500 So 84th

2. Property Use: Residential ☒ ; Commercial ☐ Other Use ☐
No. of Bedrooms 3 . Describe

3. Type of Individual Sewage Disposal System: Septic Tank ☒ ; Other ☐

4. Distance to public sewer: 1 mile ft.

EXPERIMENTAL SYSTEM

Signature of Applicant (Owner or Lessee)

5221 So 49th
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. 11/9/78 . Date Frwd. 11/9/78 . ACTION: Approved ☒ Disapproved ☐ Conditional only
Signature: Jerrold C. Hood

2. Supt. Bldg. Insp.: or Village Clerk: Date Rec'd. 11/9/78 . Date Frwd. 11/9/78 . ACTION: Approved ☑ Disapproved ☐
Signature: Bob Sorensen

3. City or County Engineer: Date Rec'd. 11-9-78 . Date Frwd. 11-9-78 . ACTION: Approved ☒ Disapproved ☐
Signature: Glenn Bartels

REMARKS OR REASONS FOR DISAPPROVAL

Site Visits:
Date: 12/20/78 by: L.C.H.
Date: 12/21/78 by: L.C.H.
Date: / / by:

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

INSTALLATION FINAL WRITTEN APPROVAL *
Date: 12/21/78 By: Jerrold C. Hood

* Conditional approval only

FORM 20105-0477
SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150 and County Resolution No. 2832)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

B

FILE NO. 1455

PROPERTY WHERE SOIL TESTED:

Location: Township 9N ; Range 7E ; Section & ¼ Section 10.
Property Dimensions: 283 ft. x 160 ft. Area: 2 ± acres. (Attach Sheet C with sketch of property).
Soil Type: Silty Clay ☒ ; Silty Clay Loam ☐ ; Sandy Loam ☐ ; Silt Loam ☐ ; Clay Loam ☐ .
Dates of Tests: 10-24-78 to _____. Weather: Precip. No Temp. No.

OWNER: Rick Nider

Address: 5221 So 49th

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
		Pre-Saturation Period				Percolation Readings						Results	
		Start		End		Start			End				
Hold No.	Hole Depth (in.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Water Level (in.)	Time (Hr./ Day)	Water Level (in.)	Elapsed Time (Min.)	Water Level Drop (in.)	Percolation Rates (Min./in.)
											one at 18"		
			Demolished										
							O.K.	10-24-78					

Sum of Percolation Rates: _____
Average of Rates: _____
Mean of Rates: _____

Smith Sewer Co.
Signature of Person Conducting Test

Address 2425 South Phone 475-1480

(Do not write below this line)

REVIEWING ACTION

Remarks: _____

Soil Type (SCS): _____

Date: _____

Approved Percolation Rate (a)
A. _____ min./inch
B. _____ min./inch
C. _____ min./inch

_____
Signature of Reviewing Official

FORM 20102-0477
PRELIMINARY PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐


LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

C

Sketch of property showing Percolation Test hole locations, well, residence, direction and property line.

FILE NO. 1455

Indicate on sketch if residence and well are exisiting or proposed.

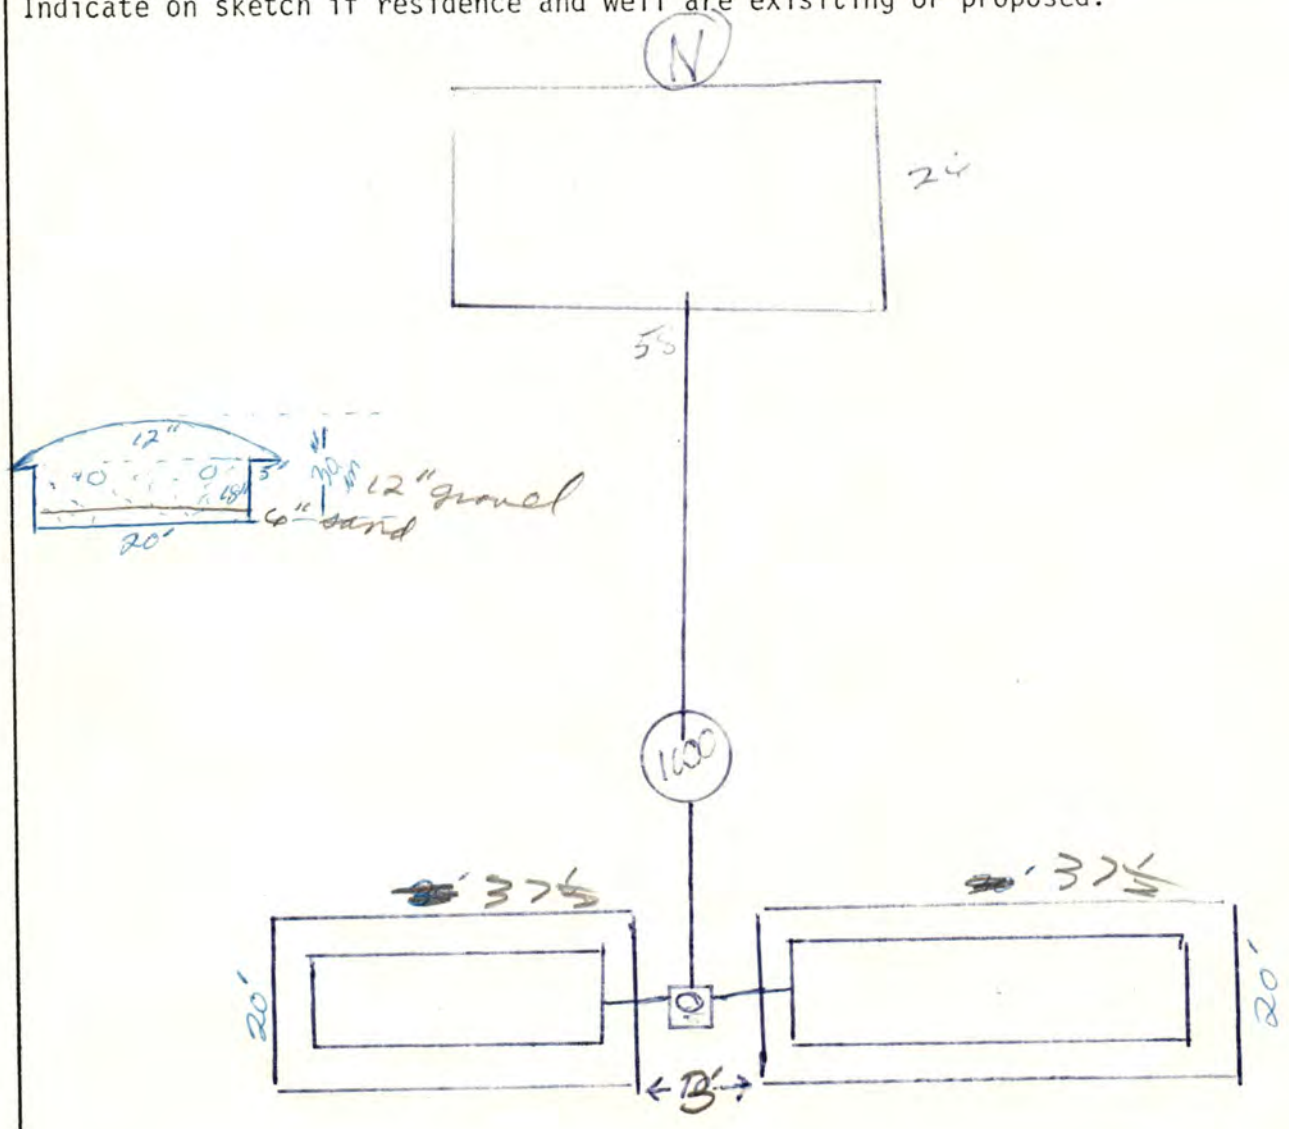

REVIEWING ACTION

Remarks: _____

_____

Date: _____

Minimum Design Requirement
1. Capacity of Septic Tank 1000 gals.
2. Total Length of Laterals _____ ft.
3. With a Trench Width of _____ in.
4. Total Area of Lateral needed 1200 sq.ft.

_____
Signature of Reviewing Official

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

D

DATE: 12-20-78

FILE NO. _____


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material Pla ; Diameter 4 in.
2. Distance above basement floor _____ in., or below basement floor 12 in.
3. Distance between dwelling and septic tank 90 ft.
4. Number of clean-outs 1 .
5. Distances to:
Well or Suction Line _____ ft.;
Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

B. SEPTIC TANK:
1. Material Conc ; No. of compartments 1 .
2. Capacity 1000 gals.;
3. Factory Built: Yes ☒ No ☐
(Company Rue)
4. Manholes: Over Inlet; diam. 6 in.
Over Outlet; diam. 6 in.
Riser Above ☐ Below ☐ Grade ~~24~~ in.
5. Inlet: Baffle ☐ ; or Tee ☐
6. Outlet: Baffle ☐ ; or Tee ☐
7. Depth of top of tank below finished grade 8 in.
8. Distances to:
Well or Suction Line _____ ft.;
Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

C. DISTRIBUTION BOX:
1. Material Pla ; Number - available outlets 7 .
2. Factory Built: Yes ☒ No ☐
(Company Hand)
3. Distance from Septic Tank 40 ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☐ Perforated Pipe ☒
Diameter of Half Round _____ or
Perforated Pipe 4" .
Material: fiberglass ☐ ; plastic ☒ ;
concrete ☐ ; other _____ .
2. Lateral Lines:
Number ___ ; Length of each line 150 ft.
_____, _____, _____, _____ ft.
Total length of laterals 75 x 20 ft.;
Distance between lateral lines 3 ft.
3. Trench dimensions: Width 20 ft.;
Slope 2 in/100 ft.; Average Depth 22 in.
4. Filter Material: Road Gravel
Depth of Material 12 in.
5. Distances to:
Well or Suction Line _____ ft.;
Stream _____ ft.; Pressure Line _____ ft.; Property Line 20 ft.

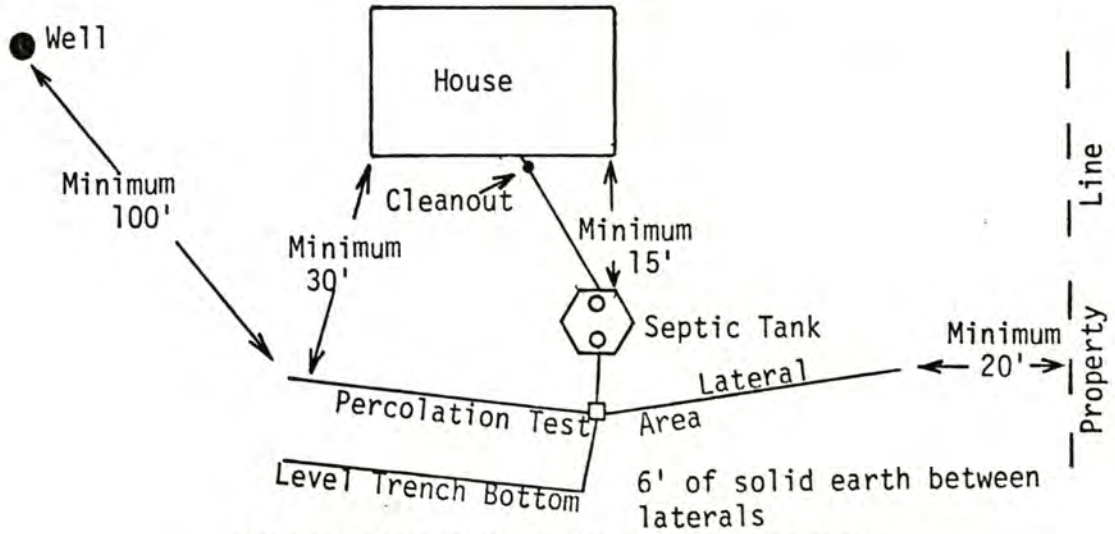

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

BUILT DRAWING OF SYSTEM

DATE 12-20-78 INSTALLER [illegible]

