LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

ENVIRONMENTAL HEALTH DIVISION

2200 St. Marys Ave Lincoln, NE 68502-3785 (402) 441-8000

NON TRANSFERABLE

PERMIT

Permit
SEWAGE INSTALLATION

No. 93380097501

Issued 04/13/93
Expires 10/13/93
Revenue Code 18754

Establishment
JAMES TOMASEK
T9N R7E SEC 13 QTR SE
HIDDEN VALLEY ACRES BLK 5 LOT 6

FEES: $150.00

TOTAL $150.00

Permittee
JAMES TOMASEK
5724 CULWELLS RD
LINCOLN NE 68516

Issued By M. Jane Ford
Health Director

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW
"POST IN A PROMINENT PLACE"

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

A

FILING FEE: $_____

FILE NO._____

DATE: 7-12-93

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 9N ; Range 7E ; Section 13 ; Block 5 : Lot 6 : Addition Hidden Valley Acres
   Street Address 6700 ~~&~~ Prairie Rim Rd.
2. Property Use: Residential ☒ ; Commercial ☐ Other Use ☐
   No. of Bedrooms 3 . Describe_____
3. Type of Individual Sewage Disposal System: Septic Tank ☒ ; Other ☒ experimental wide seepage bed
4. Distance to public sewer: _____ft.

Jann C Tank
Signature of Applicant (Owner or Lessee)
437-6246
5729 Culwells
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. 4/13/93. Date Frwd. 4/13/93. ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Hood
2. Supt. Bldg. Insp.: or Village Clerk Date Rec'd. 4/13/93. Date Frwd. 4/13/93. ACTION: Approved ☒ Disapproved ☐ Signature: Gary Spur
3. City or County Engineer : Date Rec'd. 4/13/93. Date Frwd. 4/13/93. ACTION: Approved ☒ Disapproved ☐ Signature: Dennis Bowdish

REMARKS OR REASONS FOR DISAPPROVAL_____

Site Visits:
Date: 6/29/93 by: J.C.H. ~~Tank, pipe~~
Date: 7/2/93 by: J.C.H.
Date:_____ by:_____

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

INSTALLATION FINAL WRITTEN APPROVAL*
Date: 7/2/93 By: Jerrold C. Hood

* EXPERIMENTAL SYSTEM
HENCE PROVISIONAL APPROVAL

FORM 23-43

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

D

DATE: 7-2-93

FILE NO. _____

SPECIFICATIONS AS BUILT


A. BUILDING SEWER:
1. Material Schedule 40; Diameter 4 in.
2. Distance above basement floor _____ in., or below basement floor 12 in.
3. Distance between dwelling and septic tank 57 ft.
4. Number of clean-outs 1.
5. Distances to:
Well or Suction Line — ft.; Stream — ft.; Pressure Line 100 ft.; Property Line 125 ft.

B. SEPTIC TANK:
1. Material Concrete; No. of compartments 3.
2. Capacity 1000 gals.;
3. Factory Built: Yes ☑ No ☐
(Company Precast)
4. Manholes: Over Inlet; diam. — in.
Over Outlet; diam. — in.
Riser Above ☐ Below ☑ Grade 6 in.
5. Inlet: Baffle ☑; or Tee ☐
6. Outlet: Baffle ☑; or Tee ☐
7. Depth of top of tank below finished grade 8 in.
8. Distances to:
Well or Suction Line — ft.; Stream — ft.; Pressure Line 100 ft.; Property Line 125 ft.

C. DISTRIBUTION BOX:
1. Material plastic; Number - available outlets 5.
2. Factory Built: Yes ☑ No ☐
(Company ?)
3. Distance from Septic Tank 35 ft.

Experimental


D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☐ Perforated Pipe ☑
Diameter of Half Round _____ or Perforated Pipe 4".
Material: fiberglass ☐; plastic ☑; concrete ☐; other _____.
2. Lateral Lines:
Number 2; Length of each line 100, 100, _____, _____, _____ ft.;
Total length of laterals 200 ft.;
Distance between lateral lines 12 ft.
3. Trench dimensions: Width 8 ft.;
Slope 0 in/100 ft.; Average Depth ~~9~~ 36 in.
4. Filter Material: Gravel
Depth of Material 24 in.
5. Distances to:
Well or Suction Line — ft.; Stream — ft.; Pressure Line 150 ft.; Property Line 23 ft.

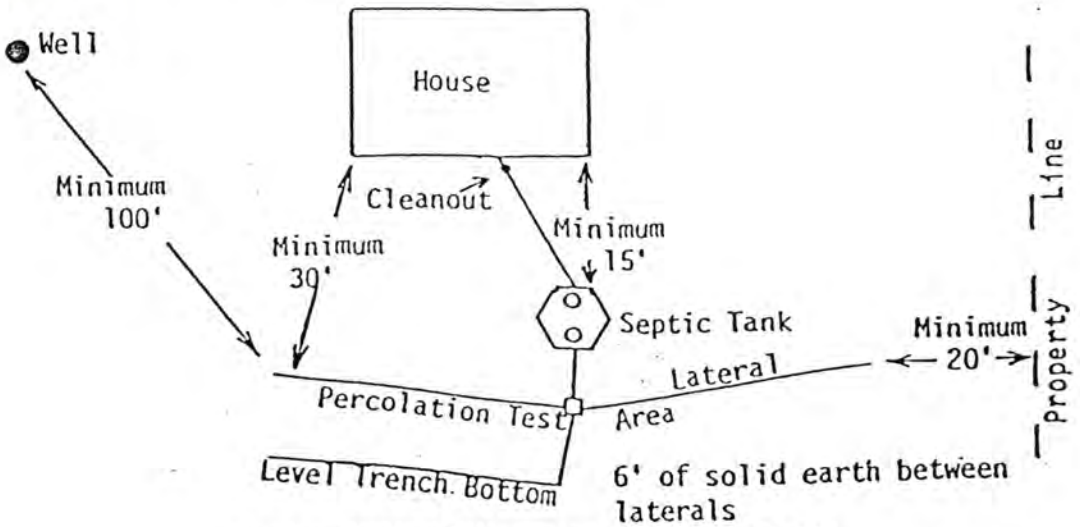

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

East

6700 Prairee Rim Road

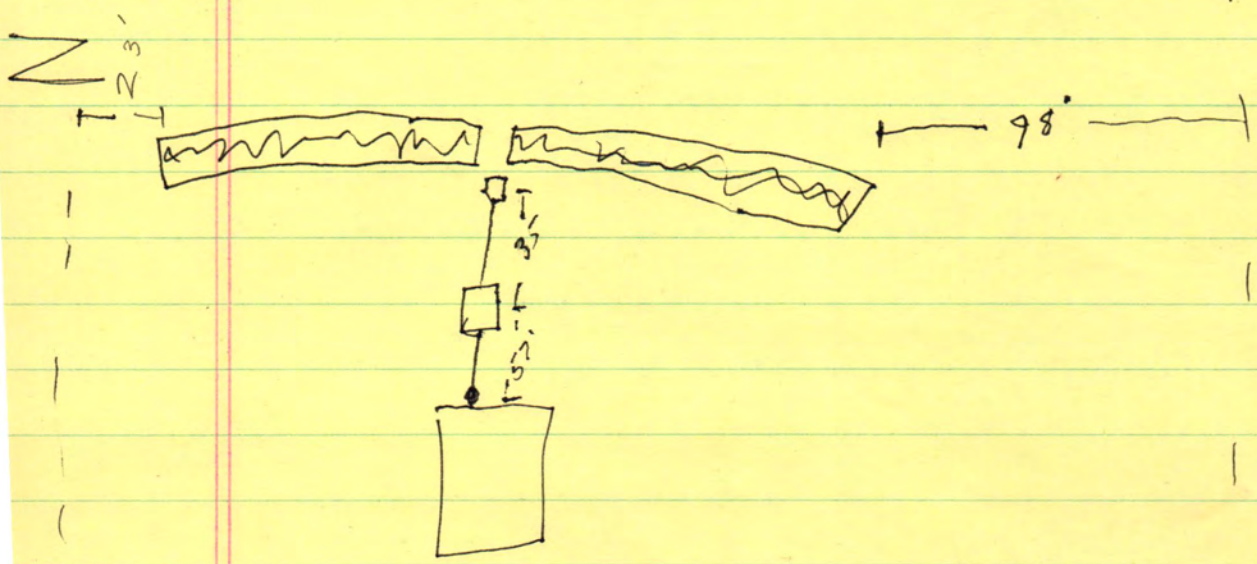

5'

W

Prairee Rim Rd.
