CITY OF LINCOLN NEBRASKA

DEPARTMENT OF LICENSES AND PERMITS

FILE NO. 1500

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION
TYPE OF LICENSE OR PERMIT

September 23, 1979
THIS LICENSE OR PERMIT EXPIRES

Paul von Gillern — 3308 North Cotner, Lincoln, NE
LICENSEE OR PERMITTEE — ADDRESS

T9N, R7E, Section 15, Lot 27 ILT, SW¼
NAME OF ESTABLISHMENT, IF ANY — ADDRESS

REMARKS: NON-TRANSFERABLE (BEREAN FUNDAMENTAL CHURCH)

PERMIT	INSPECTION FEE	OCCUPATION TAX	LICENSE	TOTAL
$ 60.00	$	$	$	$ 60.00

ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE
110.15	110.16	148.14	6-2

SERIAL NO.	DATE	AMOUNT
018754		

VALID RECEIPT ONLY IF MACHINE RECEIPTED IN THIS SPACE

APPLICATION
HEALTH

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☒
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

A

FILING FEE: $ ~~60~~ 00

FILE NO. 1500

DATE: 12-26-78

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 9N ; Range 7E ; Section 15 ;
   Block ~~Waterlace~~ : Lot 2 I.T. : Addition Southwest ¼
   Street Address 70th & Highway 2
2. Property Use: Residential ☐ ; Commercial ☒ Other Use ☐
   No. of Bedrooms _____. Describe Church
3. Type of Individual Sewage Disposal System: Septic Tank ☒ ; Other ☐
4. Distance to public sewer: 3 Miles ft.

Berean Fundamental Church Raymond Gilmore
Signature of Applicant (Owner or Lessee)

3308 N Nebraska Blvd
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. 3/22/79. Date Frwd. 3/23/79. ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Nead
2. Supt. Bldg. Insp.: or Village Clerk Date Rec'd. _____. Date Frwd. 3/23-79. ACTION: Approved ☐ Disapproved ☐ Signature: [illegible]
3. City ~~or County~~ Engineer: Date Rec'd. 3-23-79. Date Frwd. 3-23-79. ACTION: Approved ☒ Disapproved ☐ Signature: [illegible]

REMARKS OR REASONS FOR DISAPPROVAL _____

Site Visits:
Date: 11/5/80 by: L.C.H.
Date: 12-5-80 by: rm
Date: 12-6-80 by: [illegible]

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

EXPERIMENTAL SYSTEM*

INSTALLATION ~~FINAL~~ WRITTEN APPROVAL
Date: 12-6-80 By: Ron Marquart

* See drawing of large seepage bed.

FORM 20105-0477
SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150 and County Resolution No. 2832)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

B

FILE NO. 1500

Church 70th & 2nd highway

PROPERTY WHERE SOIL TESTED:

Location: Township 9 ; Range 7 ; Section & ¼ Section 15 .
Property Dimensions: _____ ft. x _____ ft. Area: 25 acres. (Attach Sheet C with sketch of property).
Soil Type: Silty Clay ☐ ; Silty Clay Loam ☐ ; Sandy Loam ☐ ; Silt Loam ☐ ; Clay Loam ☐ .
Dates of Tests: Nov 27 to Nov 28, 1978 Weather: Precip. Light Snow Temp. 35 .

OWNER: _____

Address: 70th & Highway 2nd

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
		Pre-Saturation Period				Percolation Readings						Results	
		Start		End		Start			End				
Hold No.	Hole Depth (in.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Water Level (in.)	Time (Hr./ Day)	Water Level (in.)	Elapsed Time (Min.)	Water Level Drop (in.)	Percolation Rates (Min./in.)
1	24	Nov 27	6:30	Nov 28	9:30	Nov 28	6:30	8"	Nov 28	6"			1⅛ 60 min
2													1⅛
3													1⅛
4													1
5													1⅛
6													1

Sum of Percolation Rates: 6.81
Average of Rates: 1.135
Mean of Rates: 60 Min

Paul Wm Gilmore
Signature of Person Conducting Test

Address 3308 N Antares Phone 467-4792

(Do not write below this line)

REVIEWING ACTION

Remarks: _____

Soil Type (SCS): Wymore Silty Clay Loam

Date: March 23, 1979

Approved Percolation Rate (a)
A. 3 min./inch
B. _____ min./inch
C. _____ min./inch

Gerald C. Hood
Signature of Reviewing Official

FORM 20102-0477
PRELIMINARY PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐


LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

C

Sketch of property showing Percolation Test hole locations, well, residence, direction and property line.

FILE NO. 1500

Indicate on sketch if residence and well are exisiting or proposed.

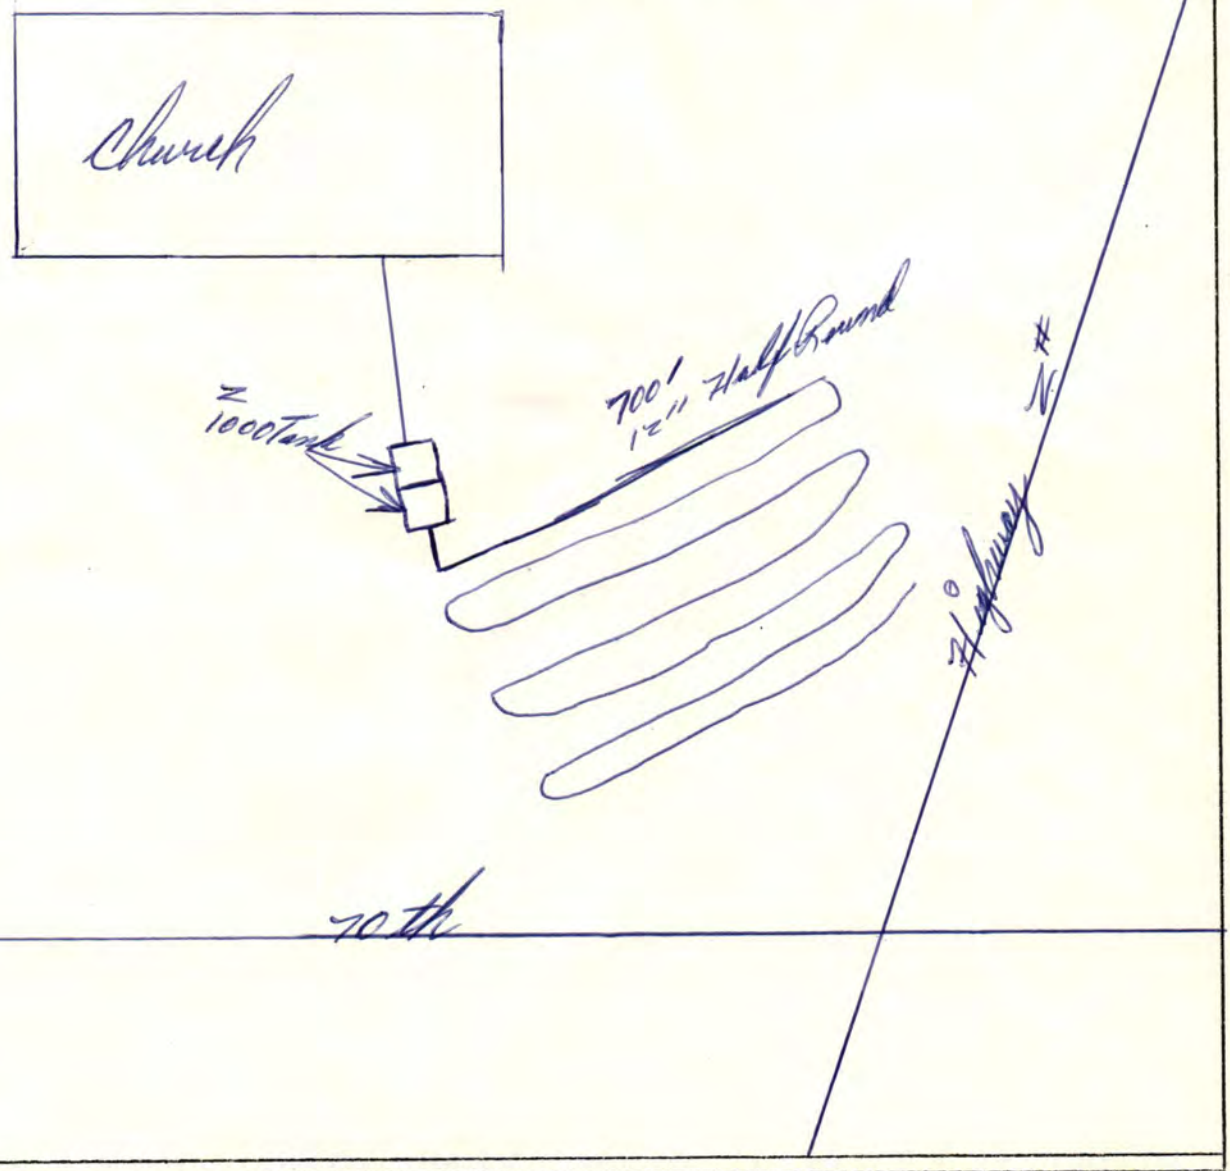

REVIEWING ACTION

Remarks: _____

Date: March 23, 1979

Minimum Design Requirement 1575
1. Capacity of Septic Tank ~~1000~~ gals.
2. Total Length of Laterals ~~800~~ 382 ft.
3. With a Trench Width of 48 in.
4. Total Area of Lateral needed ~~800~~ 1529 sq.ft.

Jerrold C. Hood
Signature of Reviewing Official

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 474-1541

D

DATE: _____

FILE NO. _____


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material plastic ; Diameter 6" in.
2. Distance above basement floor _____ in., or below basement floor 10 in.
3. Distance between dwelling and septic tank 144' ft.
4. Number of clean-outs 2 .
5. Distances to:
Well or Suction Line 100'+ ft.;
Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

B. SEPTIC TANK:
1. Material Concrete ; No. of compartments _____.
2. Capacity 2100 gals.;
3. Factory Built: Yes ☑ No ☐
(Company Pre-cast)
4. Manholes: Over Inlet; diam. _____ in.
Over Outlet; diam. _____ in.
Riser Above ☑ Below ☐ Grade ____ in.
5. Inlet: Baffle ☐ ; or Tee ☐
6. Outlet: Baffle ☐ ; or Tee ☐
7. Depth of top of tank below finished grade 24" in.
8. Distances to:
Well or Suction Line 100'+ ft.;
Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

C. DISTRIBUTION BOX:
1. Material Concrete ; Number - available outlets 6 .
2. Factory Built: Yes ☑ No ☐
(Company Pre-cast)
3. Distance from Septic Tank _____ ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☐ Perforated Pipe ☐
Diameter of Half Round _____ or
Perforated Pipe ✓ _____.
Material: fiberglass ☐ ; plastic ☑ ;
concrete ☐ ; other _____.
2. Lateral Lines:
Number 5 ; Length of each line 75 , _____, _____, _____, _____ ft.;
Total length of laterals _____ ft.;
Distance between lateral lines ____ ft.
3. Trench dimensions: Width _____ ft.;
Slope 2 in/100 ft.; Average Depth 18-36" in.
4. Filter Material: Road Gravel
Depth of Material 14" in.
5. Distances to:
Well or Suction Line 100'+ ft.;
Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

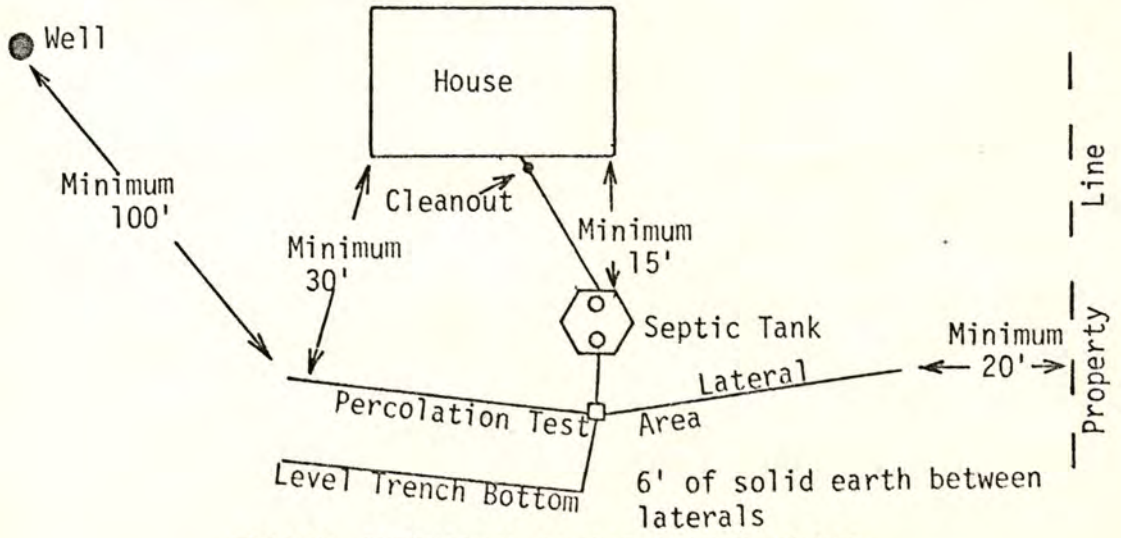

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

AS BUILT DRAWING OF SYSTEM

DATE Jan 5, 1981 INSTALLER Strahmyer

