FILE # 2822

CITY OF LINCOLN NEBRASKA

DEPARTMENT OF LICENSES AND PERMITS

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION — THIS LICENSE OR PERMIT EXPIRES

TYPE OF LICENSE OR PERMIT

MARK L. SOUTHWICK 1020 NO. 52ND ST. LINCOLN, NE 68504

LICENSEE OR PERMITTEE — ADDRESS

T9N; R7E; Sec. 17; Lot 7; Colonial Acres 2nd Addition

NAME OF ESTABLISHMENT, IF ANY — ADDRESS

REMARKS: NON TRANSFERABLE

ALTER EXTENDOOR REPAIR

PERMIT	ACCOUNTING NUMBER	TOTAL
$ 30.00	019754	$ 30.00

Valid Receipt Only if Machine Receipted In This Space

Serial No. — Date and Amount

APPLICATION

HEALTH

ISSUING OFFICER OR DEPARTMENT

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW

FORM HD-41(73) APPLICATION FOR PERMIT TO ALTER, EXTEND OR REPAIR INDIVIDUAL SEWAGE DISPOSAL SYSTEM

City Ordinance No. 9150 ☒
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Ave.
Lincoln, Nebraska 68502 (Phone: 471-7800)

FILE NO. 2822

TO: Division of Environmental Health
Lincoln-Lancaster County Health Dept.

DATE: April 9, 1989

The undersigned hereby applies for a permit to ALTER ☐, EXTEND ☒, or REPAIR ☐ an existing Individual Sewage Disposal System, in conformance with appropriate Ordinance or Resolution, as described in this application and drawings attached hereto.

1. Legal description of property: Twp. 9N ; Range 7E ; Section 17 ;
Block ; Lot 7 ; Addition COLONIAL ACRES 2ND ADD.
Street Address 5301 Cornell Colonial Acres

2. Property Use: Residential ☒; Commercial ☐
No. Bedrooms 4 Describe

Other Use ☐
Describe

3. Type of existing Individual Sewage Disposal System: Septic Tank ☒; Other ☐

4. Description of proposed alteration, extension or repair: Add a Distribution Box and 100'x6' of Perforated Pipe Lateral

5. Work to be done by: Owner ☐ ; or Contractor ☒, Big Clyde
Contractor's Name

6. Estimated cost of project:

a. Materials	$
b. Labor	$
c. Other	$
TOTAL	$

Mark Goodwin
Signature of Applicant (owner or lessee)

1020 U.S. 77 Lincoln, Nebr. 68504
Address

(Do not write below this line)

REVIEWING ACTION

1. Date Rec'd:
Filing Fee: $

2. Site Visits:
Date: 4/12/89 by: J.C.H.
Date: by:
Date: by:

3. Date: Approved ☒; Disapproved ☐
by: Jerrold C. Hood

4. INSTALLATION FINAL WRITTEN APPROVAL ✗
Date: by:

✗ PROVISIONAL APPROVAL EXPERIMENTAL SYSTEM.

001

Lincoln-Lancaster County Health Department

2200 St. Mary's Avenue, Lincoln, Nebraska 68502 Phone: 441-8022

REAL ESTATE TRANSFER/LOAN APPROVAL FORM

This form must be completed and returned to request a real estate transfer inspection.

MAKE CHECK PAYABLE TO: Lincoln-Lancaster County Health Department or LLCHD

☒ Enclosed is $150.00. Allow two weeks for processing. Incomplete information will delay processing.

☒ Evaluation of the Individual Water System ☒ Evaluation of the Sewage Disposal System

Legal Description of Property: Street Address 5301 Cornell Rd.

Twp 9N Range 7E Section 17 1/4 ___ 1/4 ___ Block ___ Lot 7 Addition Colonial Acres-2nd Addition

Directions to Property _____

Location of Well Community Tap Location: Inside ☐ Outside ☐

Location of Sewage System SW of House Year Installed _____

	NAME	ADDRESS	PHONE
Present Owner:	Ron Scheinost	5301 Cornell Rd Lincoln, NE 68516	421-1506
Tenant/Buyer:	Same		
Return to:			

Signature of Applicant Ron Scheinost Address 5301 Cornell Rd Lincoln, NE 68516 Date 9/23/93

HEALTH DEPARTMENT USE ONLY

Date Received 9/27/93 Received $150.00 Check ☒ Cash ☐

PRELIMINARY STATUS--By Gerald C. Hood **DATE:** 9/28/93

WATER SYSTEM:	Approved	Disapproved	SEWAGE SYSTEM	Additional Site Visits
Construction	☒	☐	Approved ☐	Date 10/5/93 by L.C.H.
Bacteria	☒ 0 /ml	☒ 1 /ml	Provisional ☐	Date 10/28/93 by L.C.H.
Nitrate	☒ 1.1 ppm	☐ ___ ppm	Disapproved ☒	Date 11/3/93 by L.C.H.

Comments: SEPTIC SYSTEM IS LEAKING. 10/28/93 Ø Bleeding lateral Bleeding all appears better. Recheck 11/3/93 Yard dried up. L.C.H. Ø bleeding lateral was experimental See Attached Letter ☐

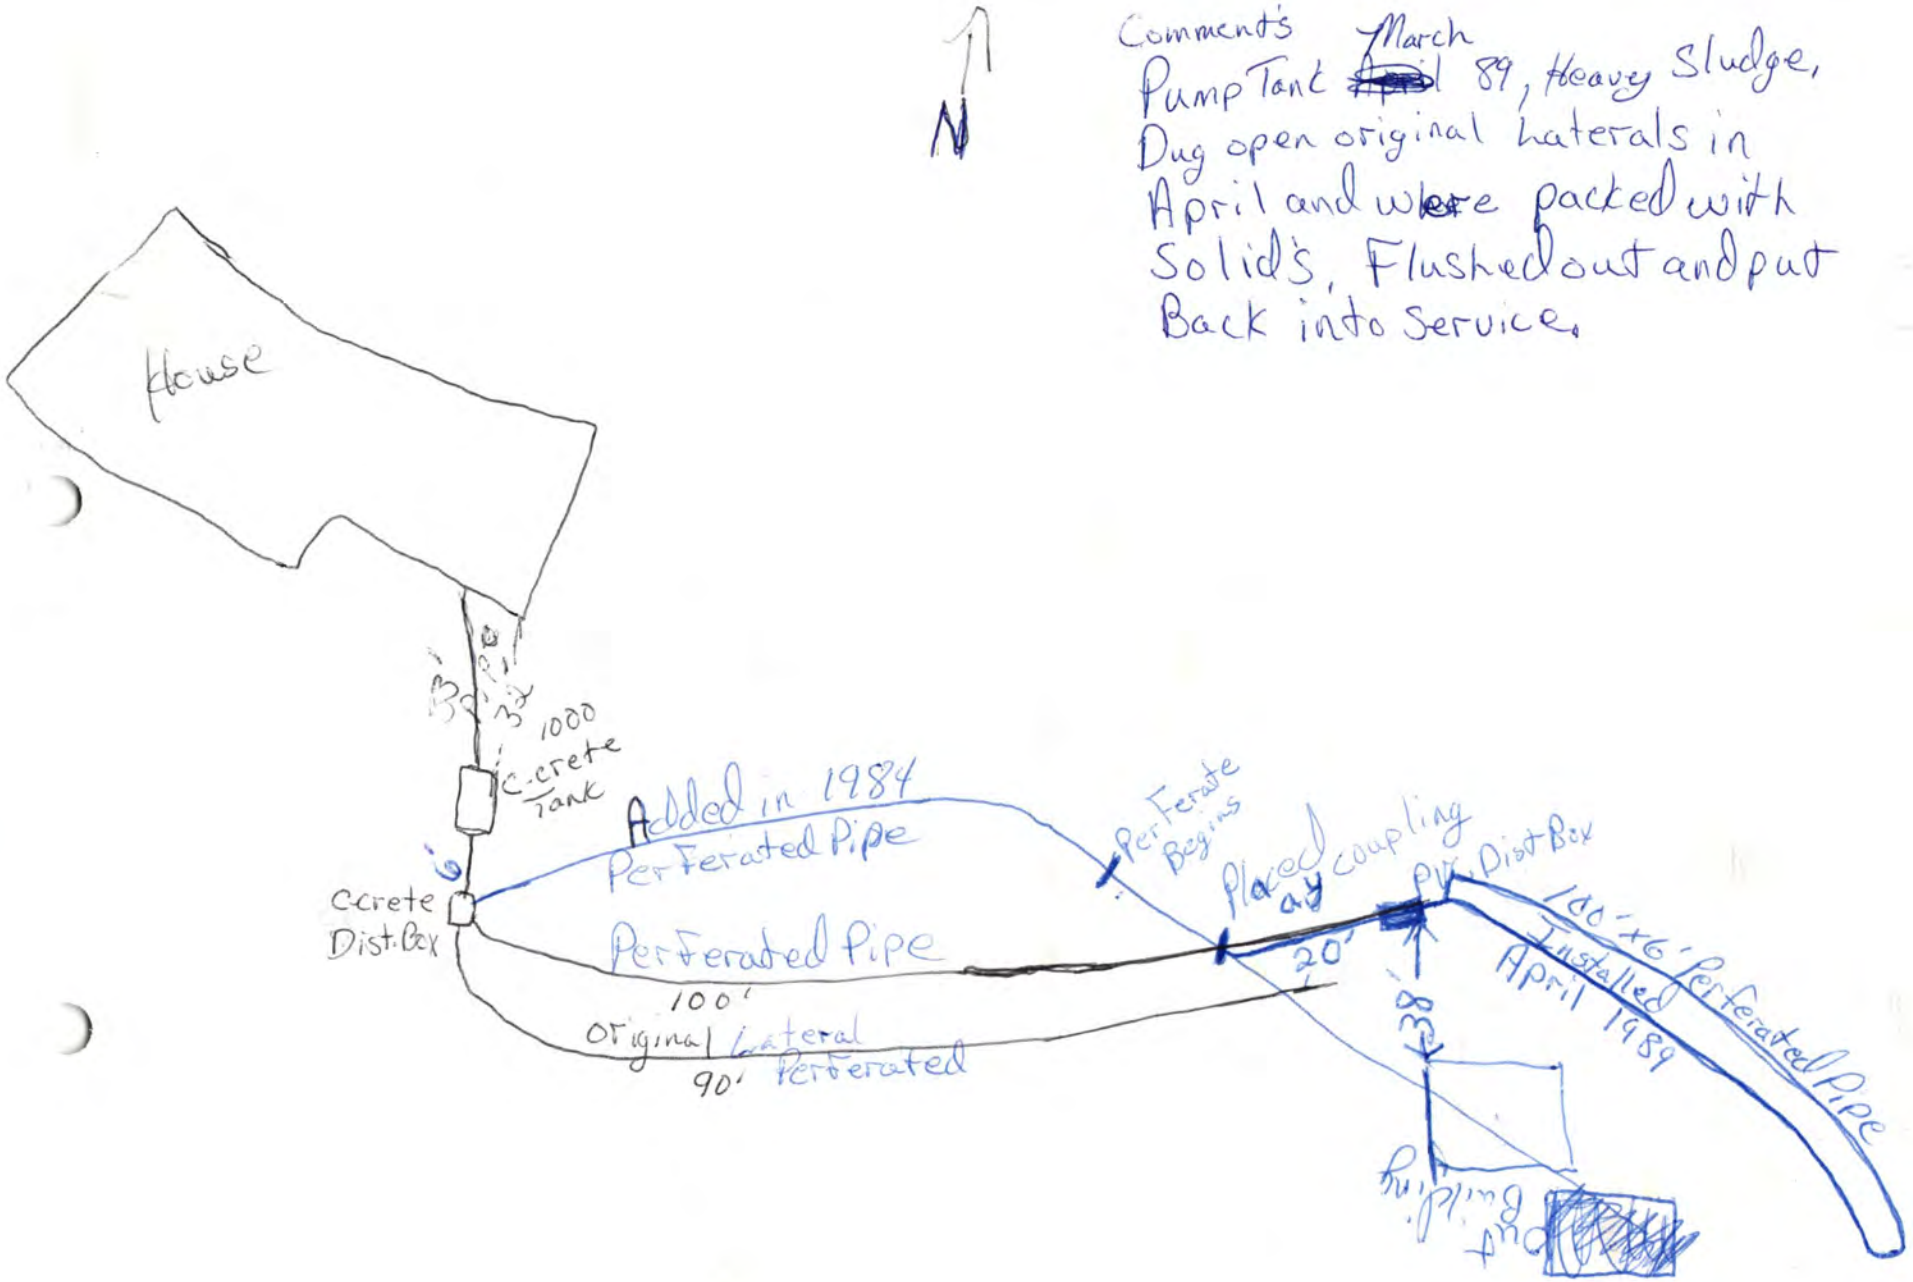
FINAL STATUS

WATER SYSTEM: Approved: ☒ **SEWAGE DISPOSAL SYSTEM** Approved: ☐ Provisional Approval: ☒

Approved by Gerald C. Hood R.E.H.S. Date 11/3/93

Approval or disapproval is based on State and local standards for construction, location and water quality. Inspection is based on visible construction and operation at the time of inspection. Approval or provisional approval does not imply or express a guarantee of system operations.

145


Comments March
Pump Tank ~~April~~ 89, Heavy Sludge,
Dug open original laterals in
April and were packed with
Solid's, Flushed out and put
Back into Service.
N
House
1000
Concrete
Tank
Added in 1984
Perforated Pipe
Perforate
Begins
Placed at coupling
PVC Dist Box
100' x 6' Perforated Pipe
Installed
April 1989
Concrete
Dist. Box
Perforated Pipe
100'
20'
Original Lateral
90' Perforated
Building
