. 360

CITY OF LINCOLN NEBRASKA

DEPARTMENT OF LICENSES AND PERMITS

NDIVIDUAL SEWAGE SYSTEM CONSTRUCTION — April 2, 1974

E OF LICENSE OR PERMIT — THIS LICENSE OR PERMIT EXPIRES

Foster Woodruff — 510 Terminal Building

LICENSEE OR PERMITTEE — ADDRESS

T9N; R7E; Sec. 20; Bl. 2; Lot 3; Country Acres Add.

NAME OF ESTABLISHMENT, IF ANY — ADDRESS

LEGAL DESCRIPTION

REMARKS: NON-TRANSFERABLE

PERMIT	INSPECTION FEE	OCCUPATION TAX	LICENSE	TOTAL
$ 30.00	$	$	$	$ 30.00

ACCOUNTING NO.	ACCOUNTING NO.	ACCOUNTING NO.	CODE
624-2525 110.15	110.16	148.14	6-2

SERIAL NO.	DATE	AMOUNT

APPLICATION

VALID RECEIPT ONLY IF MACHINE RECEIPTED IN THIS SPACE

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW

FORM HD-30(67) REQUEST FOR SITE CLEARANCE FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 432-7611)

FILE NO. 360

TO: Division of Environmental Health
Lincoln-Lancaster County Health Dept.

The undersigned hereby requests SITE CLEARANCE to construct an Individual Sewage Disposal System in conformance with Lincoln City Ordinance No. 9150, as described herein:

1. Legal description of property: Twp. 9N ; Range ~~X~~ 7E ; Section N½SE¼ 20 ;
Block ~~X~~ 2 ; Lot 3 ; Addition "Country Acres"
Street Address Cavvy Road .

2. Property Use: Residential ____ [x]; Commercial ____ [ ]
No. of Bedrooms 3 . Describe: ____
Other Use ____ [ ]
Describe: ____

3. Type of Individual Sewage Disposal System: Septic Tank [x]; Other [ ]

4. Distance to public sewer: None/rural ft.

Foster Woodruff
Signature of Applicant (owner or lessee)
Foster Woodruff
510 Terminal Bldg., Lincoln, Nebr.
Address

(Do not write below this double line)

REVIEWING ACTION

1. Health Department: Date Rec'd. 10/2/73 . ACTION: Approved [X] Disapproved [ ]
Date Frwd. 10/2/73 . Signature: Jerrold C. Hoot

2. Supt. Bldg. Insp.: Date Rec'd. 10/3/73 . ACTION: Approved [X] Disapproved [ ]
Date Frwd. ____ . Signature: Chas. Seale By RH.

3. City Engineer: Date Rec'd. 10/3/73 . ACTION: Approved [X] Disapproved [ ]
Date Frwd. ____ . Signature: H. Ress Smith

REMARKS OR REASONS FOR DISAPPROVAL ____

FINAL ACTION ON SITE CLEARANCE: Approved [ ] Disapproved [ ]

Date Applicant Notified: ____ Signature ____

FORM HD-32a(67) PLANS & SPECIFICATIONS
SEWAGE DISPOSAL SYSTEM
(Annex to Application)
Ordinance No. 9150

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502 (Phone: 432-7611)

FILE NO. 360

SPECIFICATIONS

DATE: 9/27/73


A. BUILDING SEWER:
1. Material cast i; Diameter 4 in.
2. Distance above basement floor ___ in.; or below basement floor 4 in. plus
3. Distance between dwelling and septic tank 20 ft.
4. Number of clean-outs 1.
5. Distances To:
Well or Suction Line no well ft.;
Stream xxx ft.; Pressure Line 150 ft.;
Property Line 105 ft.

B. SEPTIC TANK (Provide construction drawings.)
1. Material conc; No. of compartments 1.
2. Capacity 1500 gals.; Liquid depth 74 in.
3. Factory Built: Yes [X] (Company PRE-CAST STEP Co.) No [ ]
4. Manholes: Over Inlet; diam. 16 in. OVER CENTER
Over Outlet; diam. ___ in.
Below Grade 12 in.
5. Inlet: Baffle [ ]; or Tee [ ] neither
6. Outlet: Baffle [ ]; or Tee [X]
Depth of outlet below inlet 1 in.
7. Depth of top of tank below finished grade 12 in.
8. Distances To:
Well or Suction Line — ft.;
Stream — ft.; Pressure Line ___ ft.;
Property Line 96 ft.


C. DISTRIBUTION BOX
1. Material conc; No. available outlets 2.
2. Factory Built: Yes [X], (Company PRE-CAST STEP Co.) No [ ]
3. Dimension: Length 18 in.; Width 12 in. Depth 18 in.
4. Distance from Septic Tank 14 ft.
5. Serial Distribution: Yes [ ], No [ ] (If yes, show detailed plans.)

D. ABSORPTION FIELD: (Provide drawings.)
1. Type: 1/2 round pre-cast
2. Lateral Lines: Depth below grade ~~18~~ in. Number 2; Length of each line ~~92~~ ft Total length of Laterals ~~184~~ ft.; Slope ~~2/4~~ in/100 ft. Diameter of pipe ___ in.; Shape ~~1/2 round~~
Material: concrete [ ]; fiber asbestos [ ]; clay [ ]; other ___
Distance between lateral lines ___ ft.
3. Trench Dimensions: Depth ~~24~~ in.; to 30 Width ~~48~~ in.
4. Filter Material: GRAVEL.
Depth of material from trench bottom 12 in. + 6" PEA GRAVEL & 6" SAND
5. Distances To:
Well or Suction Line — ft.;
Stream ___ ft.; Pressure Line ___ ft.
Property Line 75 ft.
6. Percolation Rate: 28 minutes/inch

TYPICAL SKETCHES

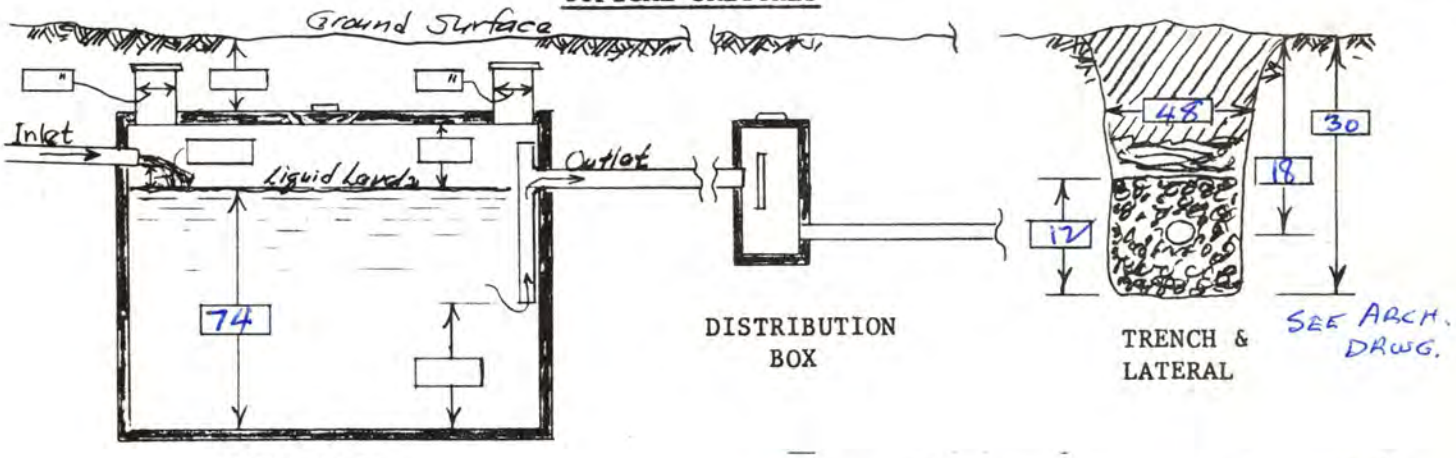

Signature of Applicant

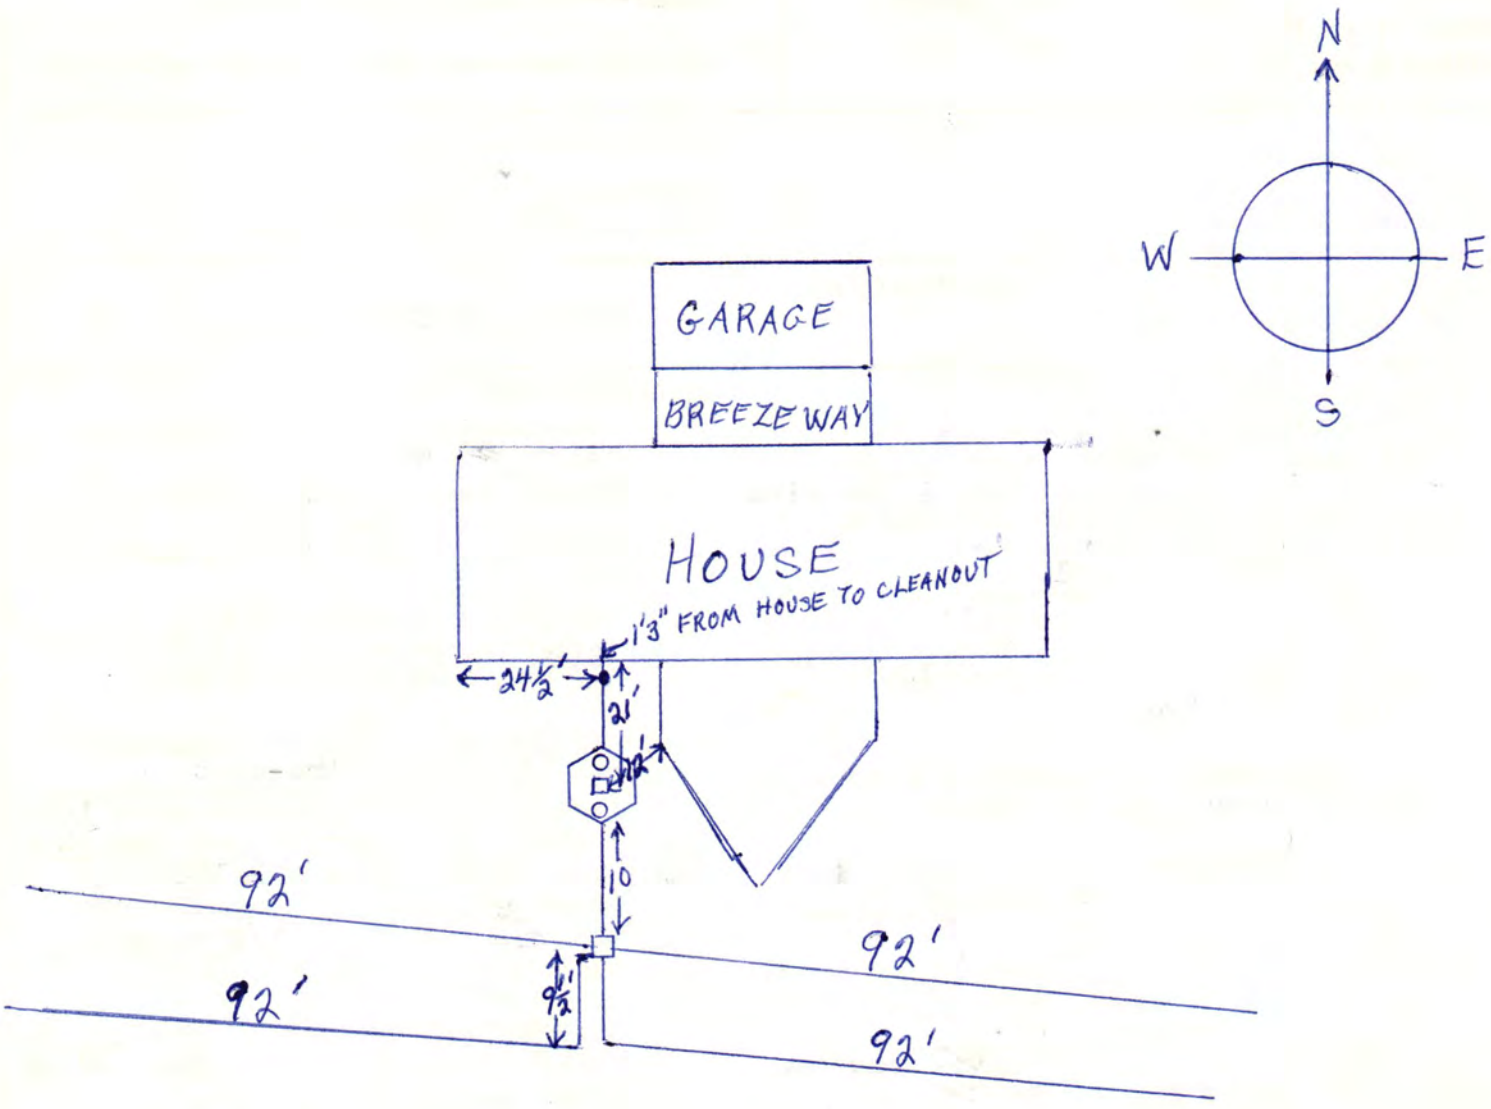
N
W
E
S
GARAGE
BREEZEWAY
HOUSE
1'3" FROM HOUSE TO CLEANOUT
24½'
2'
10
92'
92'
92'
92'
9½'
