FILE #2191

CITY OF LINCOLN NEBRASKA

DEPARTMENT OF LICENSES AND PERMITS

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION — TYPE OF LICENSE OR PERMIT

OCTOBER 23, 1985 — THIS LICENSE OR PERMIT EXPIRES

JHON BELL — LICENSEE OR PERMITTEE

3201 PIONEERS BLVD. LINCOLN, NE 68502 — ADDRESS

T9N; R7E; Sec 20; Bk 3; Lot 1; Country Acres Addition; 56th & Covey Rd. — NAME OF ESTABLISHMENT, IF ANY / ADDRESS

REMARKS: NON TRANSFERABLE NEW CONSTRUCTION

PERMIT	ACCOUNTING NUMBER	TOTAL
$ 60.00	018754	$ 60.00

Valid Receipt Only if Machine Receipted In This Space

Serial No. — Date and Amount

APPLICATION

HEALTH

ISSUING OFFICER OR DEPARTMENT

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☒
County Resolution No. 2832 ☐

LINCOLN-LANCAST COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

A

FILING FEE: $ 60.00

FILE NO. 2191

DATE: 4-22-85

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 9N ; Range 7E ; Section 20 ; Block 3 : Lot 1 : Addition County acres
   Street Address 56th + Coney Rd
2. Property Use: Residential ☑ ; Commercial ☐ Other Use ☐
   No. of Bedrooms 4 . Describe
3. Type of Individual Sewage Disposal System: Septic Tank ☐ ; Other ☑
4. Distance to public sewer: ~~1 mile~~ 4 ft. EXPERIMENTAL SYSTEM

John Bell
Signature of Applicant (Owner or Lessee)

3201 Pioneer Blvd
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. 4/22/85. Date Frwd. 4/23/85. ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Hood
2. Supt. Bldg. Insp.: or Village Clerk Date Rec'd. 4/23/85. Date Frwd. 4/23/85. ACTION: Approved ☑ Disapproved ☐ Signature:
3. City or County Engineer : Date Rec'd. 4-23-85. Date Frwd. 4-23-85. ACTION: Approved ☒ Disapproved ☐ Signature: Dennis Bartels

REMARKS OR REASONS FOR DISAPPROVAL COMMUNITY WATER SYSTEM

Site Visits:
Date: 9/18/85 by: J.C.H.
Date: by:
Date: by:

INSTALLATION FINAL WRITTEN APPROVAL *
Date: 9/26/85 By: Jerrold Hood

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

* PROVISIONAL APPROVAL EXPERIMENTAL SYSTEM

FORM 20105-0477
SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150 and County Resolution No. 2832)

LINCOLN-LANCAS[illegible] COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

B

FILE NO. 2191

PROPERTY WHERE SOIL TESTED:

Location: Township_____; Range_____; Section & ¼ Section_____.
Property Dimensions: _____ft. x _____ft. Area:_____acres. (Attach Sheet C with sketch of property).
Soil Type: Silty Clay ☐ ; Silty Clay Loam ☐ ; Sandy Loam ☐ ; Silt Loam ☐ ; Clay Loam ■ .
Dates of Tests: 3-5-85 to 3-6-85. Weather: Precip. 0 Temp. 45°.


ALL HOLES STILL FULL FROM PRE-TEST

OWNER:_____

Address:_____

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
		Pre-Saturation Period				Percolation Readings						Results	
		Start		End		Start			End				
Hold No.	Hole Depth (in.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Water Level (in.)	Time (Hr./ Day)	Water Level (in.)	Elapsed Time (Min.)	Water Level Drop (in.)	Percolation Rates (Min./in.)
1	36"	3-5	3:00 pm	3-6	3:00 pm								
2	36"	3-5	3:00 pm	3-6	3:00 pm								
3	36"	3-5	3:00 pm	3-6	3:00 pm								
4	36"	3-5	3:00 pm	3-6	3:00 pm								
5	36"	3-5	3:00 pm	3-6	3:00 pm								
6	36"	3-5	3:00 pm	3-6	3:00 pm								

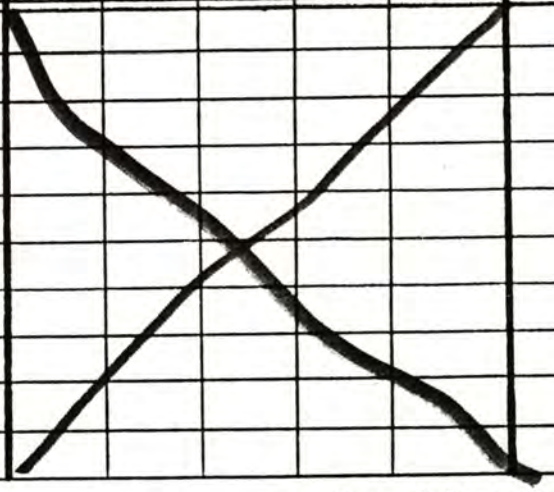

Sum of Percolation Rates: _____
Average of Rates: _____
Mean of Rates: _____

[signature]
Signature of Person Conducting Test

Address 2701 [illegible] 27th Apt 22 Phone_____

(Do not write below this line)

REVIEWING ACTION

Remarks:_____

Soil Type (SCS):_____

Date:_____

Approved Percolation Rate (a)
A._____min./inch
B._____min./inch
C._____min./inch

_____
Signature of Reviewing Official

RECD SEP 26 1985

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

D

DATE: 9-23-85

FILE NO. _____

Jack Bell 5501 Cavy Rd.


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material Plastic ; Diameter 4" in.
2. Distance above basement floor _____ in., or below basement floor 48 in.
3. Distance between dwelling and septic tank 40 ft.
4. Number of clean-outs 1 .
5. Distances to:
Well or Suction Line _____ ft.;
Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

B. SEPTIC TANK:
1. Material concrete ; No. of compartments one .
2. Capacity _____ gals.;
3. Factory Built: Yes ☑ No ☐
(Company Pre-cast)
4. Manholes: Over Inlet; diam. 24 in.
Over Outlet; diam. _____ in.
Riser Above ☑ Below ☐ Grade ___ in.
5. Inlet: Baffle ☐ ; or Tee ☐
6. Outlet: Baffle ☐ ; or Tee ☐
7. Depth of top of tank below finished grade 20 in.
8. Distances to:
Well or Suction Line _____ ft.;
Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

C. DISTRIBUTION BOX:
1. Material Concrete ; Number - available outlets _____ .
2. Factory Built: Yes ☑ No ☐
(Company Pre-cast)
3. Distance from Septic Tank 26' ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☑ Perforated Pipe ☐
Diameter of Half Round _____ or
Perforated Pipe _____ .
Material: fiberglass ☐ ; plastic ☐ ; concrete ☑ ; other _____ .
2. Lateral Lines:
Number 2 ; Length of each line 100 , _____ , _____ , _____ , _____ ft.;
Total length of laterals _____ ft.;
Distance between lateral lines 20 ft.
3. Trench dimensions: Width 8' ft.;
Slope 1 in/100 ft.; Average Depth 36 in.
4. Filter Material: Gravel
Depth of Material 24" in.
5. Distances to:
Well or Suction Line _____ ft.;
Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

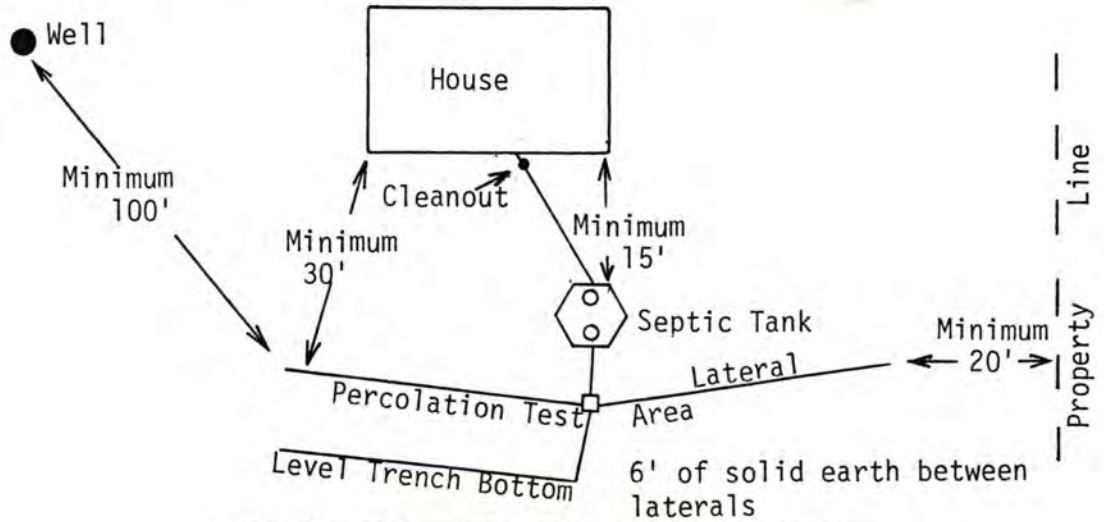

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

AS BUILT DRAWING OF SYSTEM

DATE 9-23-85 INSTALLER Strohmyer

