LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

ENVIRONMENTAL HEALTH DIVISION

2200 St. Marys Ave Lincoln, NE 68502-3785 (402) 441-8000

NON TRANSFERABLE

PERMIT

Permit
SEWAGE INSTALLATION

No. 93380095801

Issued 03/03/93
Expires 09/03/93
Revenue Code 18754

Establishment
MANN CUSTOM HOMES INC
T9N R7E SEC 20
COUNTRY ACRES SOUTH
5001 BRIDAL LANE

FEES: $150.00

TOTAL $150.00

Permittee
MANN CUSTOM HOME INC
6101 S 25 ST
LINCOLN NE 68512

Issued By M. Jane Ford
Health Director

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW
"POST IN A PROMINENT PLACE"

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☒
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

A

FILING FEE: $ 150.00

FILE NO. _____

DATE: 3-2-93

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 9N ; Range 7E ; Section 20 ;
   Block 4 : Lot 3 : Addition Country Acres South
   Street Address 5001 Bridal Lane.

2. Property Use: Residential ☒ ; Commercial ☐ ; Other Use ☐
   No. of Bedrooms 4 . Describe _____

3. Type of Individual Sewage Disposal System: Septic Tank ☒ ; Other ☐

4. Distance to public sewer: _____ ft. ~~WILL INSTALL WHATEVER SOIL PERCOLATION TEST INDICATES~~ EXPERIMENTAL SYSTEM

Manke Customs Inc.
Signature of Applicant (Owner or Lessee)

6101 S 25th, Lincoln NE 68512
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. 3/3/93 . Date Frwd. 3/5/93 . ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Hood

2. Supt. Bldg. Insp.: or Village Clerk: Date Rec'd. 3/5/93 . Date Frwd. 3/5/93 . ACTION: Approved ☐ Disapproved ☐ Signature: Dale

3. City or County Engineer: Date Rec'd. 3-5-93 . Date Frwd. 3-5-93 . ACTION: Approved ☒ Disapproved ☐ Signature: Glenn Daniels

REMARKS OR REASONS FOR DISAPPROVAL A 1000 GALLON SEPTIC TANK WAS INSTALLED HERE FILLED & COVERED BEFORE THE SIZING ERROR WAS DISCOVERED. IT WAS LEFT IN PLACE.

Site Visits:
Date: 6/17/93 by: J.C.H. Pipe only
Date: 7/9/93 by: J.C.H. ~~Hood Draining~~
Date: 7/21/93 by: J.C.H.

INSTALLATION FINAL WRITTEN APPROVAL
Date: 10/28/93 By: Jerrold C. Hood

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

RECEIVED OCT 2 8 1993

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

D

DATE: _____

FILE NO. _____


SPECIFICATIONS AS BUILT

A. BUILDING SEWER:
1. Material PVC; Diameter 4 in.
2. Distance above basement floor ____ in., or below basement floor 36 in.
3. Distance between dwelling and septic tank 129 ft.
4. Number of clean-outs 2.
5. Distances to:
Well or Suction Line 100+ ft.; Stream 100+ ft.; Pressure Line 100+ ft.; Property Line 100+ ft.

B. SEPTIC TANK:
1. Material Concrete; No. of compartments 1.
2. Capacity 1000 gals.;
3. Factory Built: Yes ☒ No ☐
(Company Pre-Cast)
4. Manholes: Over Inlet; diam. 6 in.
Over Outlet; diam. 12 in.
Riser Above ☐ Below ☐ Grade ___ in.
5. Inlet: Baffle ☒; or Tee ☐
6. Outlet: Baffle ☒; or Tee ☐
7. Depth of top of tank below finished grade 12 in.
8. Distances to:
Well or Suction Line 100+ ft.; Stream 100+ ft.; Pressure Line 100+ ft.; Property Line 30+ ft.

C. DISTRIBUTION BOX:
1. Material Concrete; Number available outlets 5.
2. Factory Built: Yes ☒ No ☐
(Company Pre-Cast)
3. Distance from Septic Tank 8 ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☒ Perforated Pipe ☐
Diameter of Half Round 22" or Perforated Pipe ____.
Material: fiberglass ☐; plastic ☐; concrete ☒; other ____.
2. Lateral Lines:
Number 3; Length of each line 100, 100, 50, ____, ____ ft.;
Total length of laterals 250 ft.;
Distance between lateral lines 12 ft.
3. Trench dimensions: Width 8 ft.;
Slope 4 in/100 ft.; Average Depth 36 in.
4. Filter Material: Gravel
Depth of Material 30 in.
5. Distances to:
Well or Suction Line 100+ ft.; Stream 100+ ft.; Pressure Line 100+ ft.; Property Line 25 ft.

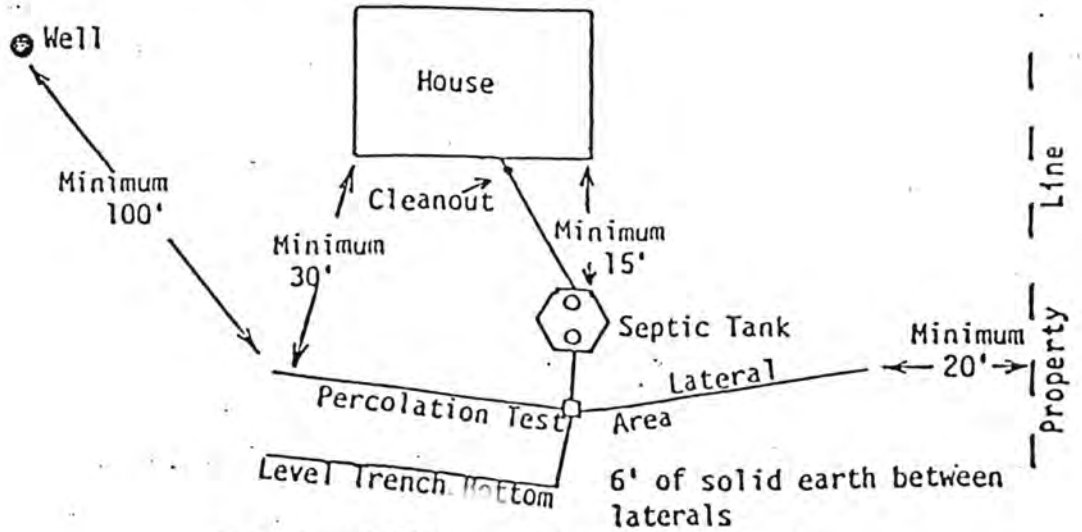

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

~~5101~~ Bridle Lane
5001
Mann Custom Homes

Installed By Vogt Tot

