FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☒

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: ~~471-7800~~ 441

A

FILING FEE: $ 150.00

FILE NO. _____

DATE: _____

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. ~~24~~ 9N ; Range ~~29~~ 7E ; Section ~~2~~ 2 ;
   Block 1 : Lot 4 : Addition PORTSCHE HEIGHTS THIRD ADDITION
   Street Address 7800 PORTSCHE LANE

2. Property Use: Residential ☒ ; Commercial ☐ ; Other Use ☐
   No. of Bedrooms 3 . Describe _____

3. Type of Individual Sewage Disposal System: Septic Tank ☒ ; Other ☐

4. Distance to public sewer: 6000 + ft.

Signature of Applicant (Owner or Lessee)

3140 South 74TH St., Lincoln, NE. 68506
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. 6/20/94. Date Frwd. 6/20/94. ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Nood
2. Supt. Bldg. Insp.: or Village Clerk Date Rec'd. _____. Date Frwd. 6-20-94. ACTION: Approved ☒ Disapproved ☐ Signature: _____
3. City or County Engineer : Date Rec'd. 6-20-94. Date Frwd. 6-20-94. ACTION: Approved ☒ Disapproved ☐ Signature: _____

REMARKS OR REASONS FOR DISAPPROVAL _____

Site Visits: 11:30
Date: 7-5-94 by: P.D
Date: 7-5-94 1:15 by: P.D
Date: 12-1-97 by: P.D

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

INSTALLATION FINAL WRITTEN APPROVAL
Date: 12-1-97 By: _____

FORM 20105-0477
SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150 and County Resolution No. 2832)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

B

FILE NO. _____

PROPERTY WHERE SOIL TESTED:

Location: Township 9N ; Range 9 ; Section & ¼ Section 7 .
Property Dimensions: 425 ft. x 539 ft. Area: 3 acres. (Attach Sheet C with sketch of property).
Soil Type: Silty Clay ☐ ; Silty Clay Loam ☐ ; Sandy Loam ☐ ; Silt Loam ☐ ; Clay Loam ☐ .
Dates of Tests: Nov. 21, 193 to Nov. 22, 1993 . Weather: Precip. No. Temp. 50°

OWNER: RICHARD E. REEVES
Address: 7800 PORTCHE LANE 68506

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
		Pre-Saturation Period				Percolation Readings						Results	
		Start		End		Start			End				
Hold No.	Hole Depth (in.)	Date (Mo./Day)	Time (Hr./Min.)	Date (Mo./Day)	Time (Hr./Min.)	Date (Mo./Day)	Time (Hr./Min.)	Water Level (in.)	Time (Hr./Day)	Water Level (in.)	Elapsed Time (Min.)	Water Level Drop (in.)	Percolation Rates (Min./in.
1	36"	11-21	12:30	11-22	11:30	11-22	4:38	29	5:08	31½	30 min	1½"	20/IN
2	36"	11-21	12:31	11-22	11:31		4:39	28	5:09	29		1"	30/IN
3	36"	11-21	12:32	11-22	11:32		4:40	29	5:10	30½		1½"	20/IN
4	36"	11-21	12:33	11-22	11:33		4:41	27	5:11	28½		1½"	20/IN
5	36"	11-21	12:34	11-22	11:34		4:42	29	5:12	30½		1½"	20/IN
6	36"	11-21	12:35	11-22	11:35		4:43	26	5:13	27¼		1¼"	24/IN
7	36"	11-21	12:36	11-22	11:36		4:44	26	5:14	27¼		1¼"	24/IN
8	36"	11-21	12:39	11-22	11:37	11-22	4:45	26	5:15	27½	30 min.	1½"	20/IN

Sum of Percolation Rates: 178/IN.
Average of Rates: 22.25/IN.
Mean of Rates: 25/MIN.

Signature of Person Conducting Test

Address 3140 S. 74TH ST. LINCOLN, NE Phone 432-1599

(Do not write below this line)

REVIEWING ACTION

Approved Percolation Rate (a)
A. 22 min./inch
B. _____ min./inch
C. _____ min./inch

Remarks:
Soil Type (SCS): Sharpsburg Silty Clay Loam
Date: June 20, 1994

Gerrold C. Hood
Signature of Reviewing Official

FORM 20102-0477
PRELIMINARY PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐


LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

C

Sketch of property showing Percolation Test hole locations, well, residence, direction and property line.

FILE NO._____

Indicate on sketch if residence and well are exisiting or proposed.

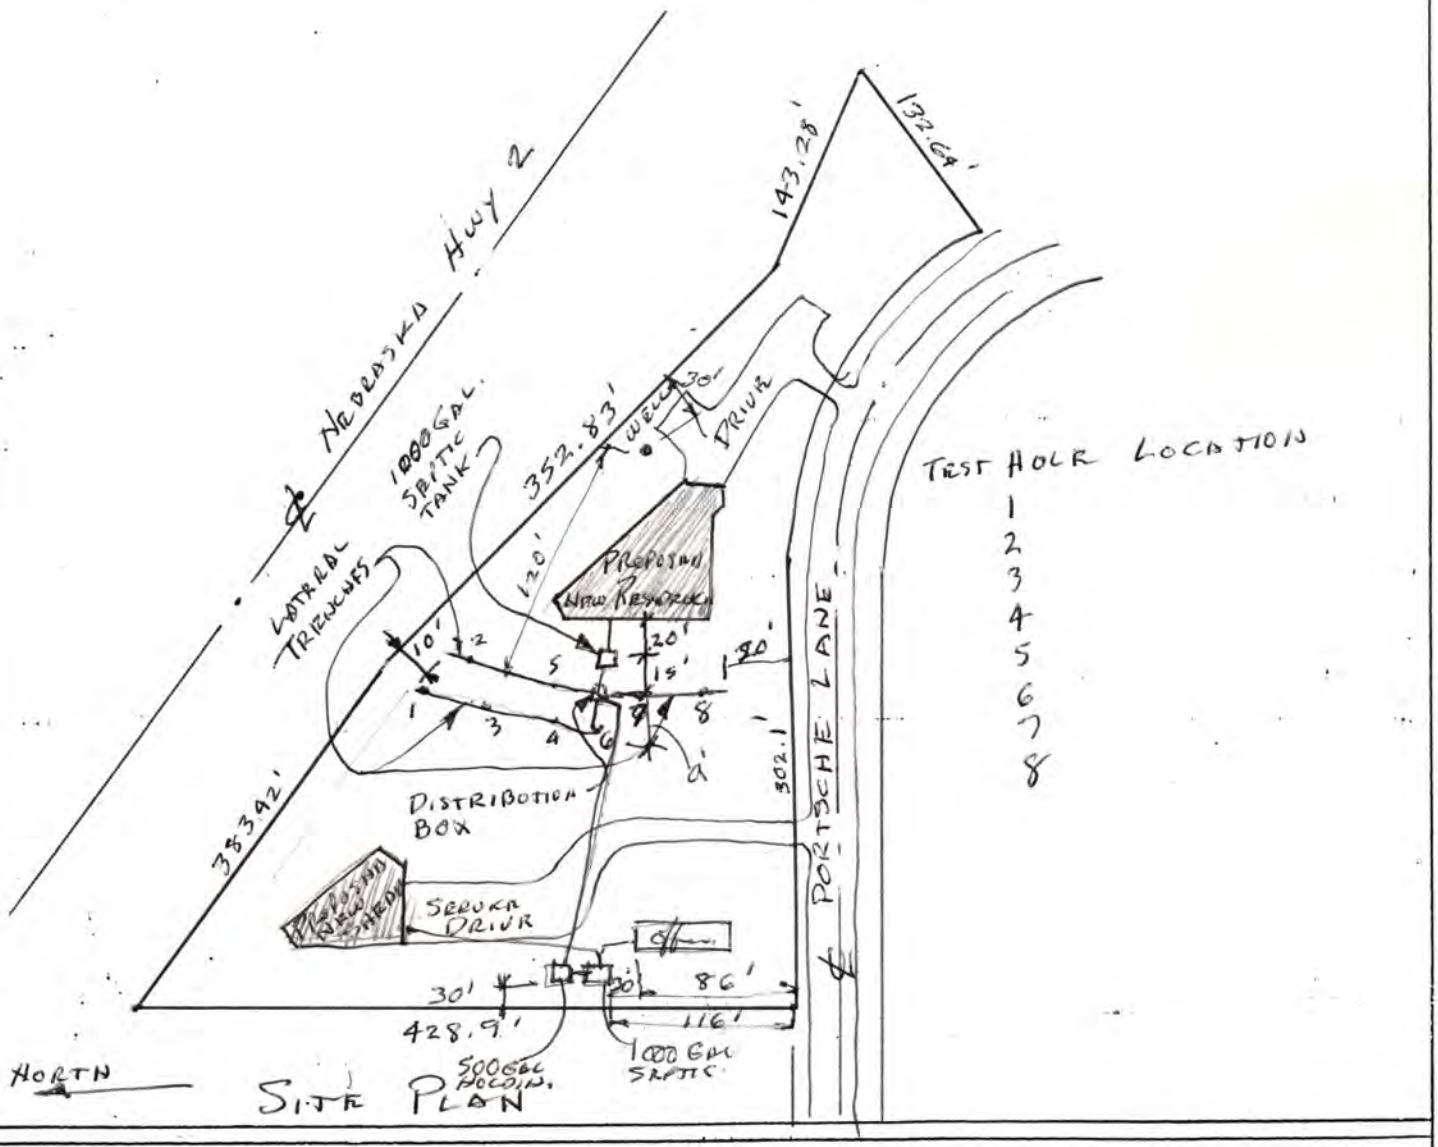

REVIEWING ACTION

Remarks: _____

_____

Date: _____

Minimum Design Requirement
1. Capacity of Septic Tank 1000 gals.
2. Total Length of Laterals _____ ft.
3. With a Trench Width of _____ in.
4. Total Area of Lateral needed 653 sq.ft.

_____
Signature of Reviewing Official

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

D

DATE: 7-5-94

FILE NO: _____


SPECIFICATIONS AS BUILT

A. BUILDING SEWER: 5' Cut, #160
1. Material 40 ; Diameter 4 in.
2. Distance above basement floor _____ in., or below basement floor _____ in.
3. Distance between dwelling and septic tank 40 ft.
4. Number of clean-outs 3
5. Distances to: Well or Suction Line 120' ft.; Stream 200 ft.; Pressure Line 120 ft.; Property Line 120' ft.

B. SEPTIC TANK:
1. Material Precast ; No. of compartments _____
2. Capacity ~~1000~~ 1250 gals.;
3. Factory Built: Yes ☒ No ☐ (Company _____)
4. Manholes: Over Inlet; diam. _____ in. Over Outlet; diam. _____ in. Riser Above ☐ Below ☐ Grade ___ in.
5. Inlet: Baffle ☒ ; or Tee ☐
6. Outlet: Baffle ☒ ; or Tee ☐
7. Depth of top of tank below finished grade 10" in.
8. Distances to: Well or Suction Line 135 ft.; Stream 175 ft.; Pressure Line 145 ft.; Property Line 120 ft.

C. DISTRIBUTION BOX:
1. Material Precast ; Number available outlets _____
2. Factory Built: Yes ☒ No ☐ (Company _____)
3. Distance from Septic Tank 15 ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☒ Perforated Pipe ☐ Diameter of Half Round 16 or Perforated Pipe _____. Material: fiberglass ☐ ; plastic ☐ ; concrete ☒ ; other _____
2. Lateral Lines: Number 3 ; Length of each line 64, 64, 48, _____, _____ ft.; Total length of laterals _____ ft.; Distance between lateral lines _____ ft.
3. Trench dimensions: Width 4 ft.; Slope 6 in/100 ft.; Average Depth 36 in.
4. Filter Material: Road Gravel Depth of Material 20 in.
5. Distances to: Well or Suction Line ~~—~~ ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

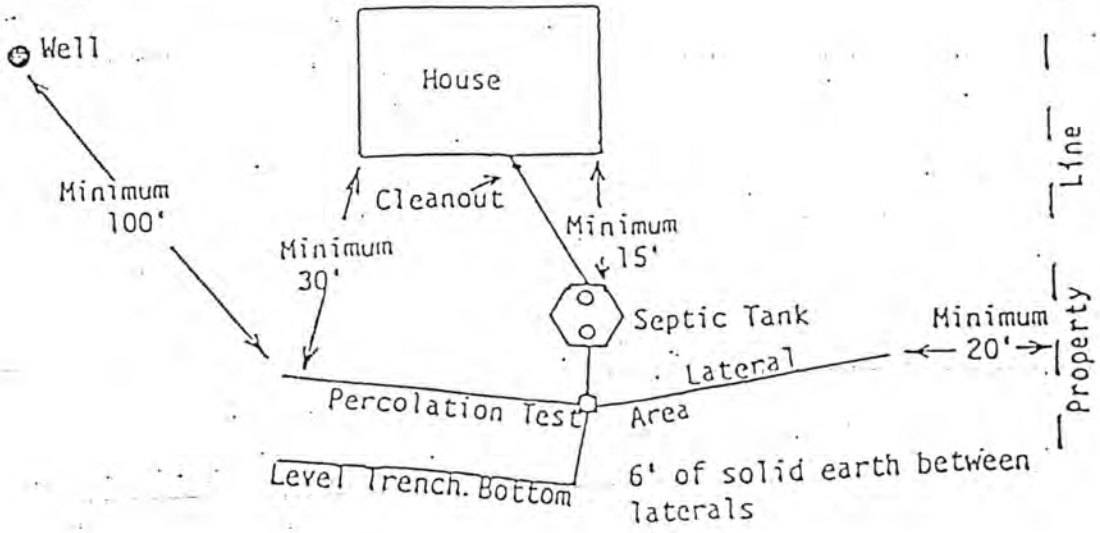

Larry Schwarck 7-5-94

