LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT

Division of Environmental Health
2200 St. Marys Ave Lincoln, NE 68502 (402) 471-8000

NON TRANSFERABLE

PERMIT

SEWAGE SYSTEM REPAIR

No. 91390023001

Issued 04/30/91
Expires 10/30/91

ESTABLISHMENT

MARK SOUTHWICK
T9N R7E SEC 26 QTR SE

FEES: Permit 018754 $50.00

Total $50.00

PERMITTEE

MARK SOUTHWICK
1020 N 52 ST
LINCOLN NE 68504

Issued By COUNTY HEALTH

VALID RECEIPT ONLY IF RECEIPTED IN THIS SPACE

DATE	AMOUNT
5/6/91	PAID

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW

FORM HD-41(73) APPLICATION FOR PERMIT TO ALTER, EXTEND OR REPAIR INDIVIDUAL SEWAGE DISPOSAL SYSTEM

City Ordinance No. 9150 [X]
County Resolution No. 2832 [ ]

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Ave.
Lincoln, Nebraska 68502 (Phone: 471-7800)

FILE NO._____

TO: Division of Environmental Health
Lincoln-Lancaster County Health Dept.

DATE: April 23, 1991

The undersigned hereby applies for a permit to ALTER [X], EXTEND [ ], or REPAIR [ ] an existing Individual Sewage Disposal System, in conformance with appropriate Ordinance or Resolution, as described in this application and drawings attached hereto.

1. Legal description of property: Twp. 9N ; Range 7E ; Section 26 SE¼ ;
Block _____ ; Lot _____ ; Addition _____
Street Address 9705 S. 98

2. Property Use: Residential _____ [X]; Commercial _____ [ ]
No. Bedrooms 3
Describe _____
Other Use [ ]
Describe _____

3. Type of existing Individual Sewage Disposal System: Septic Tank [X]; Other [ ]

4. Description of proposed alteration, extension or repair: ADD Dist. Box and 100' of 4" wide Half-moon

5. Work to be done by: Owner [ ] ; or Contractor [X] , Big Clyde Sanitation / J. S. Installation
Contractor's Name

6. Estimated cost of project:
a. Materials $_____
b. Labor $_____
c. Other $_____
TOTAL over $ 400

Mary Southwick
Signature of Applicant (owner or lessee)

1020 N. 52, Lincoln Nebr. 68504
Address

(Do not write below this line)

REVIEWING ACTION

1. Date Rec'd:_____
Filing Fee: $ 50.00

2. Site Visits:
Date: 4/22/91 by: L.C.H.
Date:_____ by:_____
Date:_____ by:_____

3. Date: Approved [X]; Disapproved [ ]
by: Lerold E. Nobbe

4. INSTALLATION FINAL WRITTEN APPROVAL
Date: 4/29/91 by: L. E. Nobbe

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

D

DATE: _____

FILE NO. _____

SPECIFICATIONS AS BUILT


New. April 22, 1991

A. BUILDING SEWER:
1. Material _____; Diameter _____ in.
2. Distance above basement floor _____ in., or below basement floor _____ in.
3. Distance between dwelling and septic tank _____ ft.
4. Number of clean-outs _____.
5. Distances to:
Well or Suction Line _____ ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

B. SEPTIC TANK:
1. Material C-Crete; No. of compartments 1.
2. Capacity 1000 gals.;
3. Factory Built: Yes ☒ No ☐
(Company Pre-Cast)
4. Manholes: Over Inlet; diam. 6 in.
Over Outlet; diam. _____ in.
Riser Above ☐ Below ☐ Grade ___ in.
5. Inlet: Baffle ☐ ; or Tee ☐
6. Outlet: Baffle ☐ ; or Tee ☐
7. Depth of top of tank below finished grade 3' 6" in. - 54 in
8. Distances to:
Well or Suction Line _____ ft.; Stream _____ ft.; Pressure Line _____ ft.; Property Line _____ ft.

C. DISTRIBUTION BOX:
1. Material Poly; Number - available outlets 7.
2. Factory Built: Yes ☒ No ☐
(Company _____)
3. Distance from Septic Tank 6 in ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☒ Perforated Pipe ☐
Diameter of Half Round 16" or Perforated Pipe _____.
Material: fiberglass ☐ ; plastic ☐ ; concrete ☒ ; other _____.
2. Lateral Lines:
Number 2; Length of each line 100, _____, _____, _____, _____ ft.;
Total length of laterals 200 ft.;
Distance between lateral lines 10 ft.
3. Trench dimensions: Width 4 ft.; Slope _____ in/100 ft.; Average Depth _____ in.
4. Filter Material: Gravel
Depth of Material 20 in.
5. Distances to:
Well or Suction Line over 100 ft.; Stream N.A. ft.; Pressure Line 90 ft.; Property Line 40 ft.

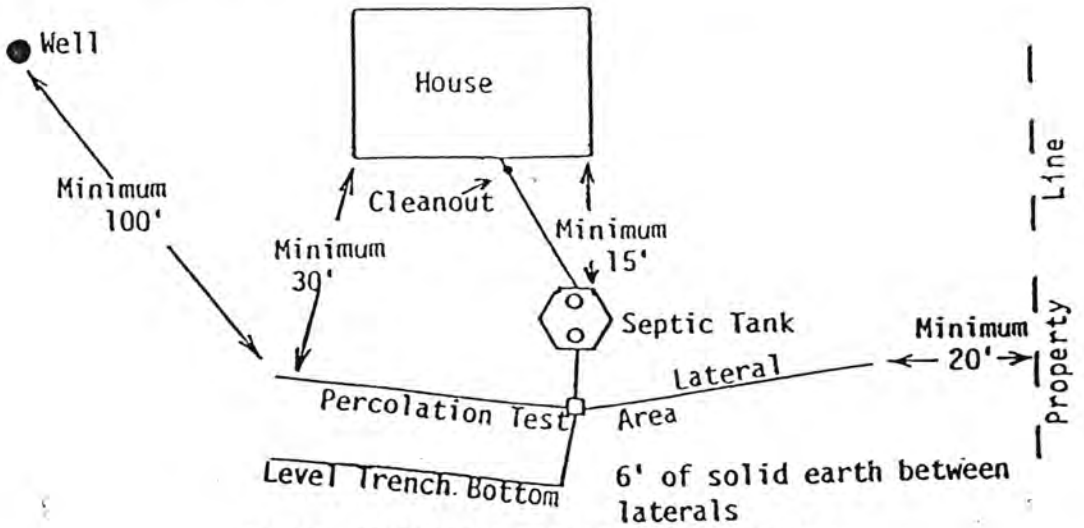

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

N
House
Location of Sewer
line is Not Diffinent
Treeline
Power going to well
Well is Located
Several Hundred
Feet South
6"
riser on
Inlet
4'6" Deep
1972
10Ft
Dist. Box
5-ft Deep
5 ft Deep
C-Crete Half-moon - Installed April 22, 1991
C-Crete Half-moon - Installed 1972
rural water Line
Ditch in this Area
road
