FILE #2627

CITY OF LINCOLN NEBRASKA

DEPARTMENT OF LICENSES AND PERMITS

INDIVIDUAL SEWAGE SYSTEM CONSTRUCTION — TYPE OF LICENSE OR PERMIT

AUGUST 23, 1988 — THIS LICENSE OR PERMIT EXPIRES

DAN LOECK CONTRACTING — 1553 SO. 2 STREET — LINCOLN, NE 68502

LICENSEE OR PERMITTEE — ADDRESS

T9N; R7E; Sec 28; Blk 2; Lot 1; 8601 So. 63 Street — ADDRESS

NAME OF ESTABLISHMENT, IF ANY

REMARKS: NON TRANSFERABLE

NEW CONSTRUCTION

PERMIT	ACCOUNTING NUMBER	TOTAL
$ 60.00	018754	$ 60.00

Valid Receipt Only if Machine Receipted In This Space

Serial No. — Date and Amount

APPLICATION

HEALTH

ISSUING OFFICER OR DEPARTMENT

THIS LICENSE OR PERMIT IS ISSUED SUBJECT TO REVOCATION AS PROVIDED BY LAW

FORM 20103-0477
REQUEST FOR SITE CLEARANCE AND PERMIT
FOR INDIVIDUAL SEWAGE DISPOSAL SYSTEM
City Ordinance No. 9150 ☒
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

A

FILING FEE: $ 60.00

FILE NO. 2627

DATE: FEB 23, 1988

The undersigned hereby requests SITE CLEARANCE and PERMIT to construct an Individual Sewage Disposal System in conformance with appropriate resolution or ordinance, as described herein:

1. Legal description of property: Twp. 9N ; Range 7E ; Section 28 ;
   Block 2 : Lot 1 : Addition YANKEE RIDGE ESTATES 1ST ADD
   Street Address 8601 SO 63 ST.

2. Property Use: Residential ☒ ; Commercial ☐ Other Use ☐
   No. of Bedrooms 4 . Describe

3. Type of Individual Sewage Disposal System: Septic Tank ☒ ; Other ☐

4. Distance to public sewer: — ft.

D. R Roberts (CONTRACTOR)
Signature of Applicant (Owner or Lessee)

1553 SO 2nd 68502
Address

(Do not write below this double line)

1. Health Department: Date Rec'd. 2/23/88. Date Frwd. 2/23/88. ACTION: Approved ☒ Disapproved ☐ Signature: Jerrold C. Hood

2. Supt. Bldg. Insp.: or Village Clerk Date Rec'd. 2/23/88. Date Frwd. 2/23/88. ACTION: Approved ☒ Disapproved ☐ Signature: Walter Stuart

3. City or County Engineer: Date Rec'd. 2/23/88. Date Frwd. 2/23/88. ACTION: Approved ☒ Disapproved ☐ Signature: H B Mohan

REMARKS OR REASONS FOR DISAPPROVAL DON'T KNOW IF INTEND TO HAVE WELL NO WELL PERMIT RECIEVED,

Site Visits:
Date: June-88 by: mm probed 40ft lateral
Date: by:
Date: by:

INSTALLATION FINAL WRITTEN APPROVAL
Date: July 5-88 By: Ron Marquardt

White: Health Dept. Copy
Yellow: Engineers Copy
Pink: Bldg. Inspector's Copy

FORM 23-43

FORM 20105-0477
SOIL ABSORPTION TEST DATA REPORT
(Annex to Application)
(Reference: City Ordinance No. 9150 and County Resolution No. 2832)

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

B

FILE NO. 2627

PROPERTY WHERE SOIL TESTED: Yankee Ridge Estates

Location: Township T9N; Range R7E; Section & ¼ Section 28 NW/4.
Property Dimensions: _____ ft. x _____ ft. Area: _____ acres. (Attach Sheet C with sketch of property).
Soil Type: Silty Clay ☐; Silty Clay Loam ☐; Sandy Loam ☐; Silt Loam ☐; SHO2 Clay Loam ☐.
Dates of Tests: 11-9 to 11-11-87. Weather: Precip. 0 Temp. 20°-50°

OWNER: Dwayne Dvorak

Address: 3333 S. 28 - Lincoln

PERCOLATION TEST DATA TABLE

a.	b.	c.	d.	e.	f.	g.	h.	i.	j.	k.	l.	m.	n.
		Pre-Saturation Period				Percolation Readings						Results	
		Start		End		Start			End				
Hold No.	Hole Depth (in.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Date (Mo./ Day)	Time (Hr./ Min.)	Water Level (in.)	Time (Hr./ Day)	Water Level (in.)	Elapsed Time (Min.)	Water Level Drop (in.)	Percolation Rates (Min./in.)
1	36	11/9	4:00	11/11	8:30	11/11	12:30	22¾	1:00	23	30	¼	
2			PM		AM		PM	20¼	PM	20¾		½	
3								23¾		24½		¾	
4								21¼		21⅝		⅜	
5								23⅞		24¾		⅞	
6								29⅞		31		1⅛	
7								20¾		21¾		1	
8	↓							20¾		22		1¼	
												6⅛	
											8	.765	

Brad Southwick
Signature of Person Conducting Test

Address 701 E 4 Hickman Phone 792-2462

Sum of Percolation Rates: _____
Average of Rates: .765
Mean of Rates: _____

(Do not write below this line)

REVIEWING ACTION

Remarks: _____
Soil Type (SCS): Sharpsburg Silty Clay Loam
Date: FEBRUARY 23, 1988

Approved Percolation Rate (a)
A. 40 min./inch
B. _____ min./inch
C. _____ min./inch

Terrold C. Hood
Signature of Reviewing Official

FORM 20104-0477
PLANS & SPECIFICATIONS FOR SEWAGE DISPOSAL SYSTEM (Annex to Application)
City Ordinance No. 9150 ☐
County Resolution No. 2832 ☐

LINCOLN-LANCASTER COUNTY HEALTH DEPARTMENT
Division of Environmental Health
2200 St. Marys Avenue
Lincoln, Nebraska 68502
Phone: 471-7800

D

DATE: 6-27-88

FILE NO. _____


SPECIFICATIONS AS BUILT 5801 S. 63 Dewayne Dvorak

A. BUILDING SEWER:
1. Material PVC ; Diameter 4 in.
2. Distance above basement floor ____ in., or below basement floor 4 in.
3. Distance between dwelling and septic tank 142 ft.
4. Number of clean-outs 2 .
5. Distances to: Well or Suction Line NA ft.; Stream NA ft.; Pressure Line NA ft.; Property Line over 25 ft.

B. SEPTIC TANK:
1. Material Concrete ; No. of compartments 1 .
2. Capacity 1500 gals.;
3. Factory Built: Yes ☒ No ☐ (Company Pre Cast Step)
4. Manholes: Over Inlet; diam. 8 in. Over Outlet; diam. 10 in. Riser Above ☐ Below ☐ Grade ___ in.
5. Inlet: Baffle ☒ ; or Tee ☐
6. Outlet: Baffle ☒ ; or Tee ☐
7. Depth of top of tank below finished grade 18 in.
8. Distances to: Well or Suction Line NA ft.; Stream NA ft.; Pressure Line NA ft.; Property Line over 75 ft.

C. DISTRIBUTION BOX:
1. Material Plastic ; Number - available outlets 7 .
2. Factory Built: Yes ☒ No ☐ (Company _____)
3. Distance from Septic Tank 21 ft.

D. ABSORPTION FIELD: (Provide as built drawings on back of this form)
1. Type: Half Rounds ☐ Perforated Pipe ☒ Diameter of Half Round _____ or Perforated Pipe 4" . Material: fiberglass ☐ ; plastic ☒ ; concrete ☐ ; other _____.
2. Lateral Lines: Number 4 ; Length of each line 100 , 100 , 100 , 100 , _____ ft.; Total length of laterals 400 ft.; Distance between lateral lines 10 ft.
3. Trench dimensions: Width 3 ft.; Slope 4-6 in/100 ft.; Average Depth 38 in.
4. Filter Material: Road Gravel Depth of Material 14 in.
5. Distances to: Well or Suction Line NA ft.; Stream NA ft.; Pressure Line over 100 ft.; Property Line over 60 ft.

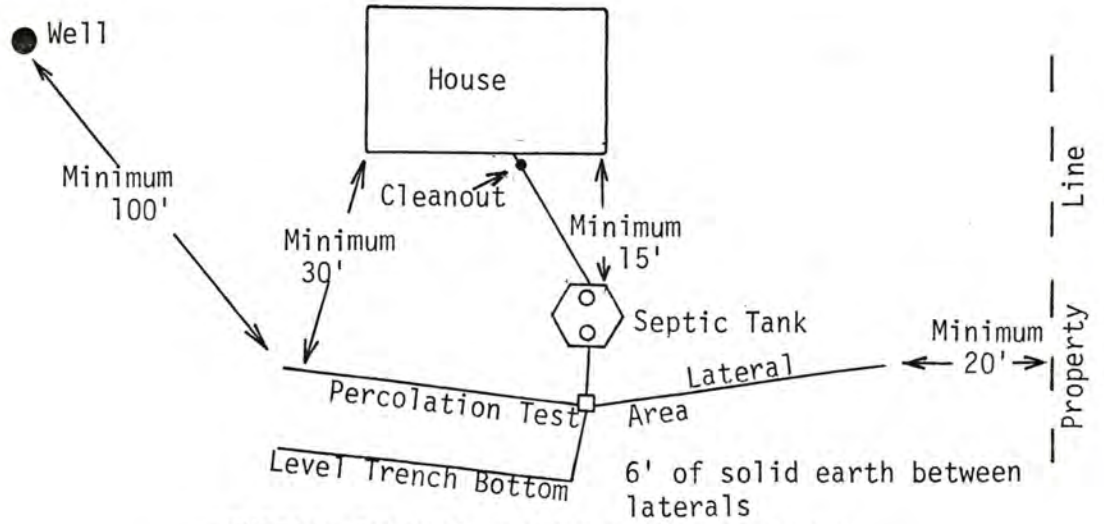

TYPICAL INDIVIDUAL SEWAGE SYSTEM DESIGN

AS BUILT DRAWING OF SYSTEM

DATE 6-27-88 INSTALLER Southwick Sewer & Drain

